


PROJECT REFERENCE NO.	SHEET NO.
<i>R-5739</i>	<i>EC-26A/CONST.26</i>
RW SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

CULVERT CONSTRUCTION SEQUENCE STA. 324+27 -L-

$$1'' = 20'$$

PHASE I

1. INSTALL IMPERVIOUS DIKES #1, #2, #3, & #4 AND 24 INCH TEMPORARY PIPES #1 & #2.
2. DEWATER CONSTRUCTION AREA INTO SKIMMER BASINS #26.2, #26.3, AND SPECIAL STILLING BASIN(S) AS REQUIRED.
3. REMOVE EXISTING HEADWALLS AND WINGWALLS.

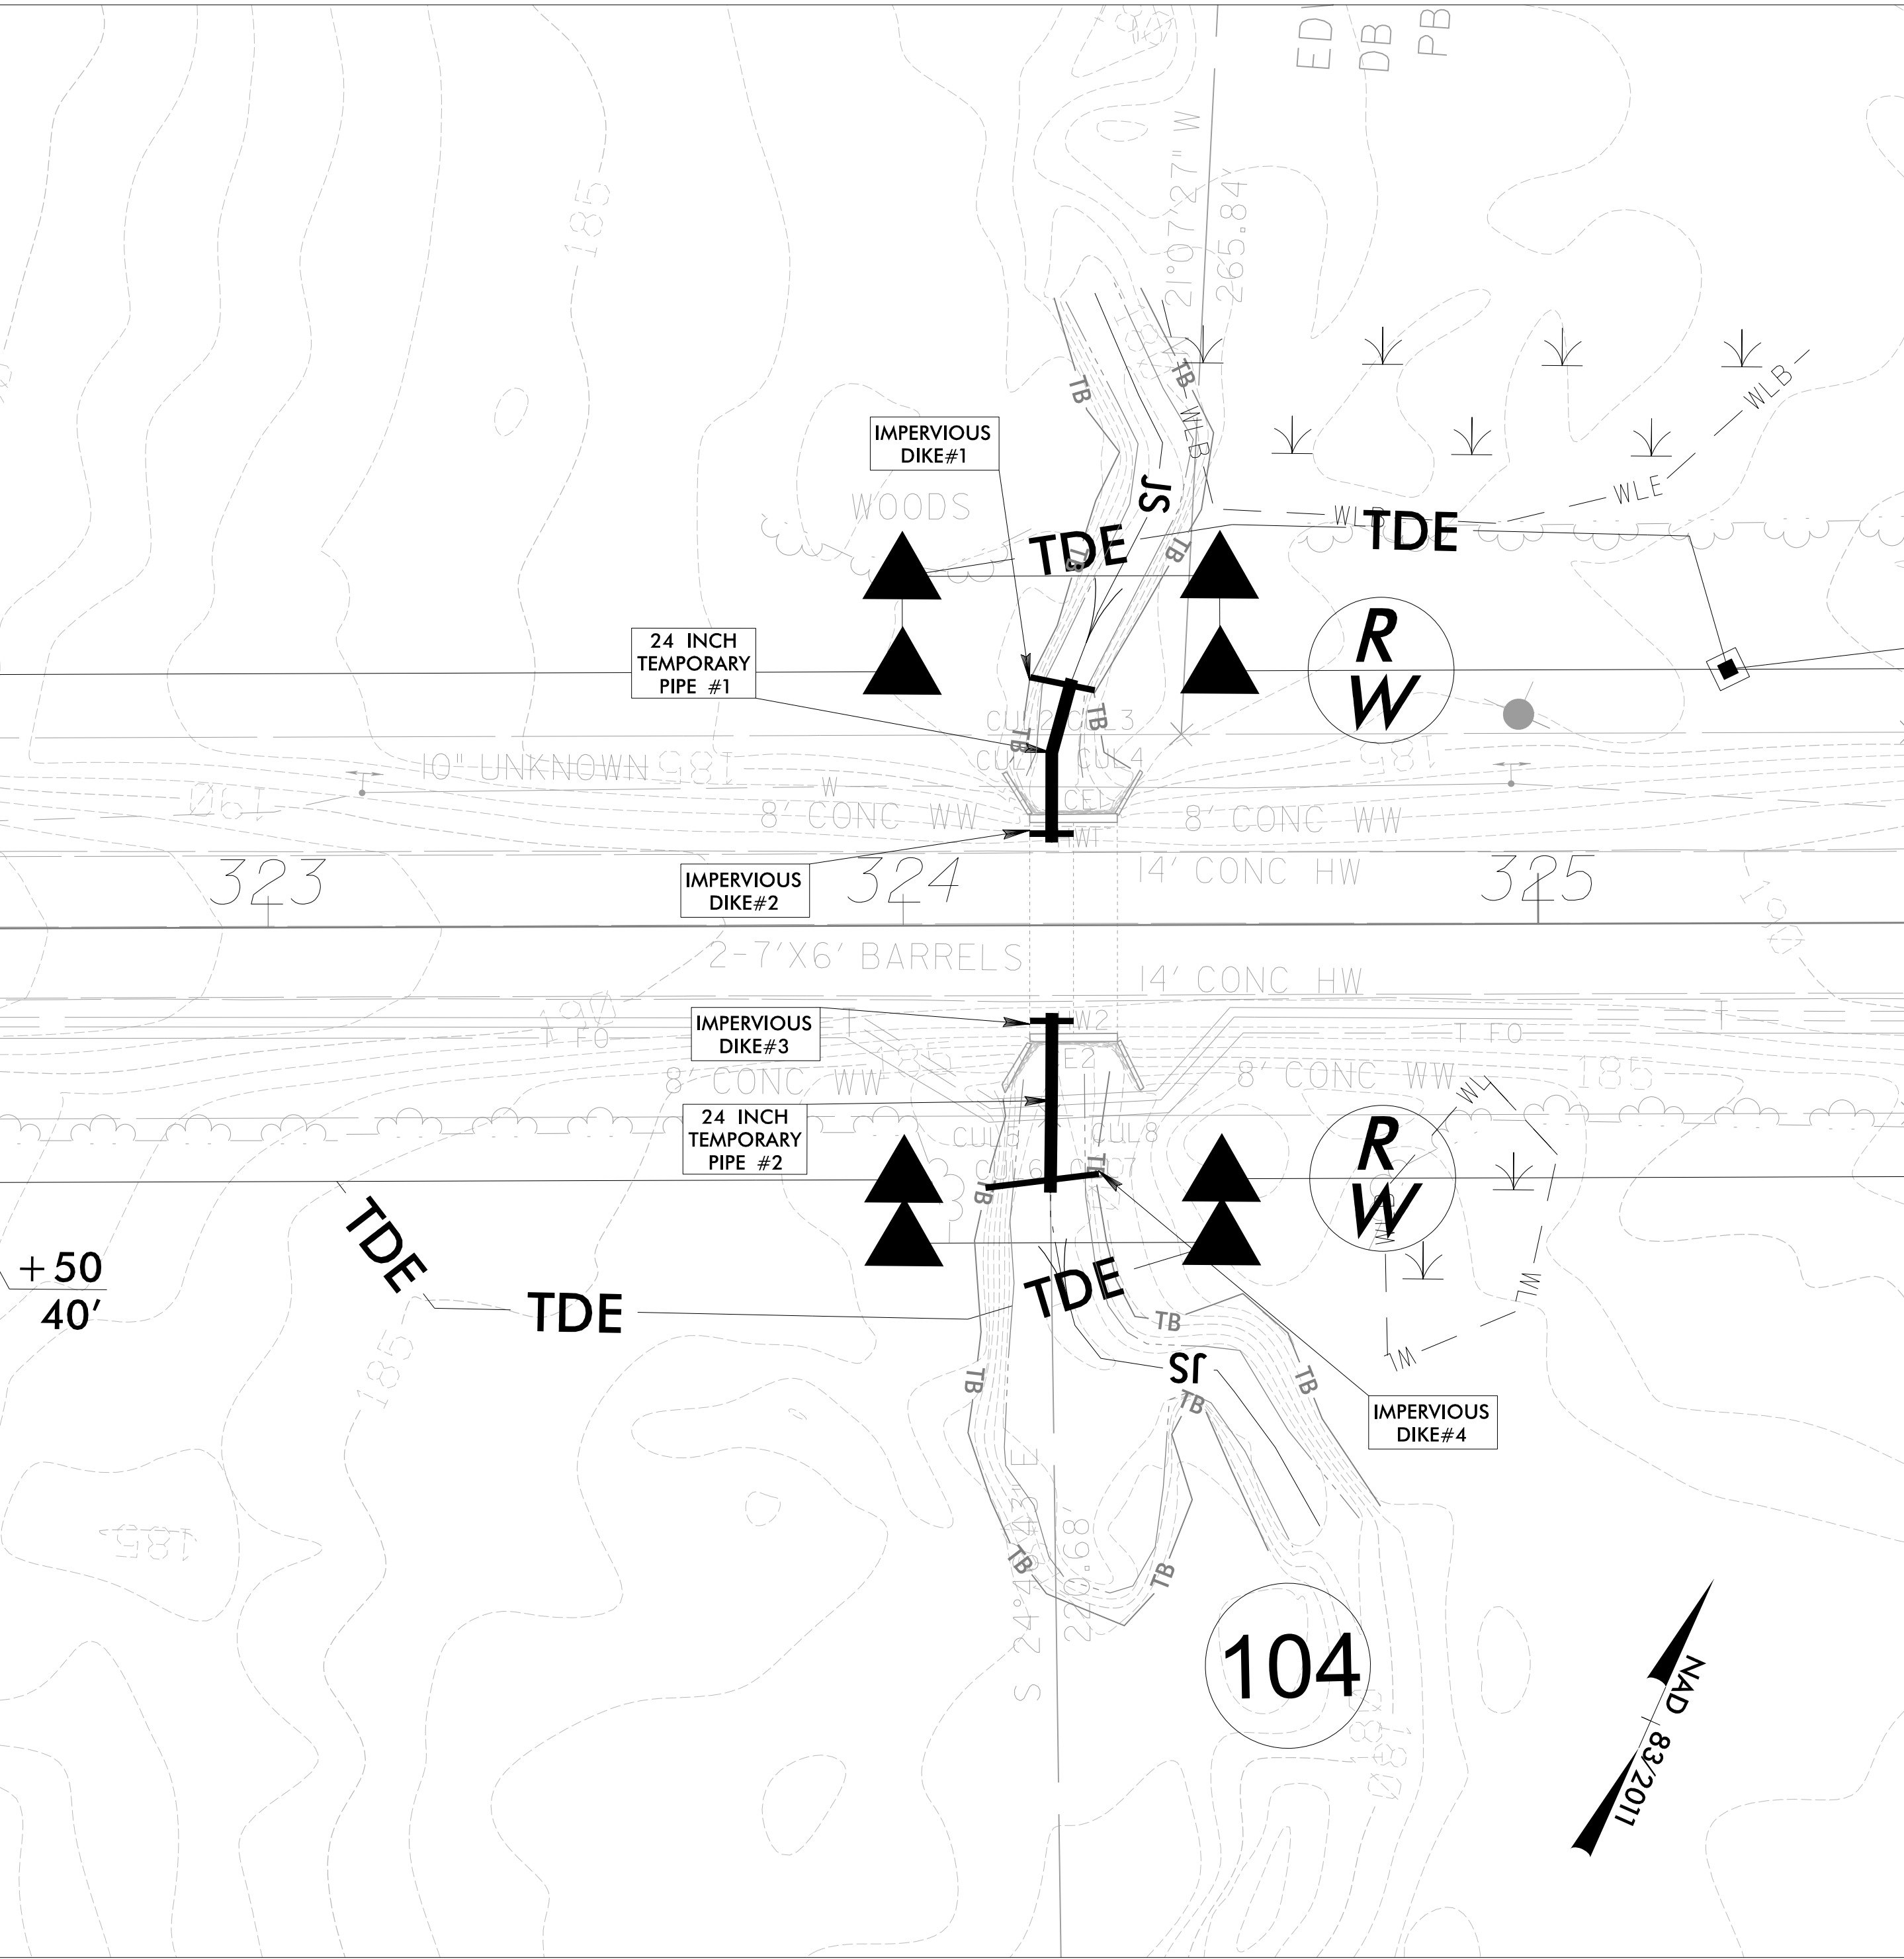

PHASE II

1. CONSTRUCT PROPOSED CULVERT EXTENSIONS, HEADWALLS, AND WINGWALLS.
2. INSTALL PROPOSED CLASS 'I' RIP-RAP AT CULVERT INLET AND OUTLET.
3. REMOVE IMPERVIOUS DIKES #1, #2, #3, & #4 AND 24 INCH TEMPORARY PIPES #1 & #2.

