

## CULVERT CONSTRUCTION SEQUENCE

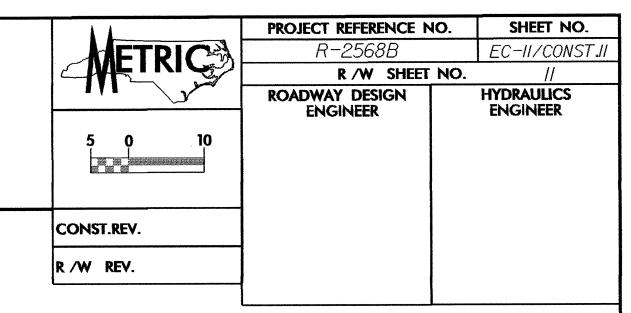

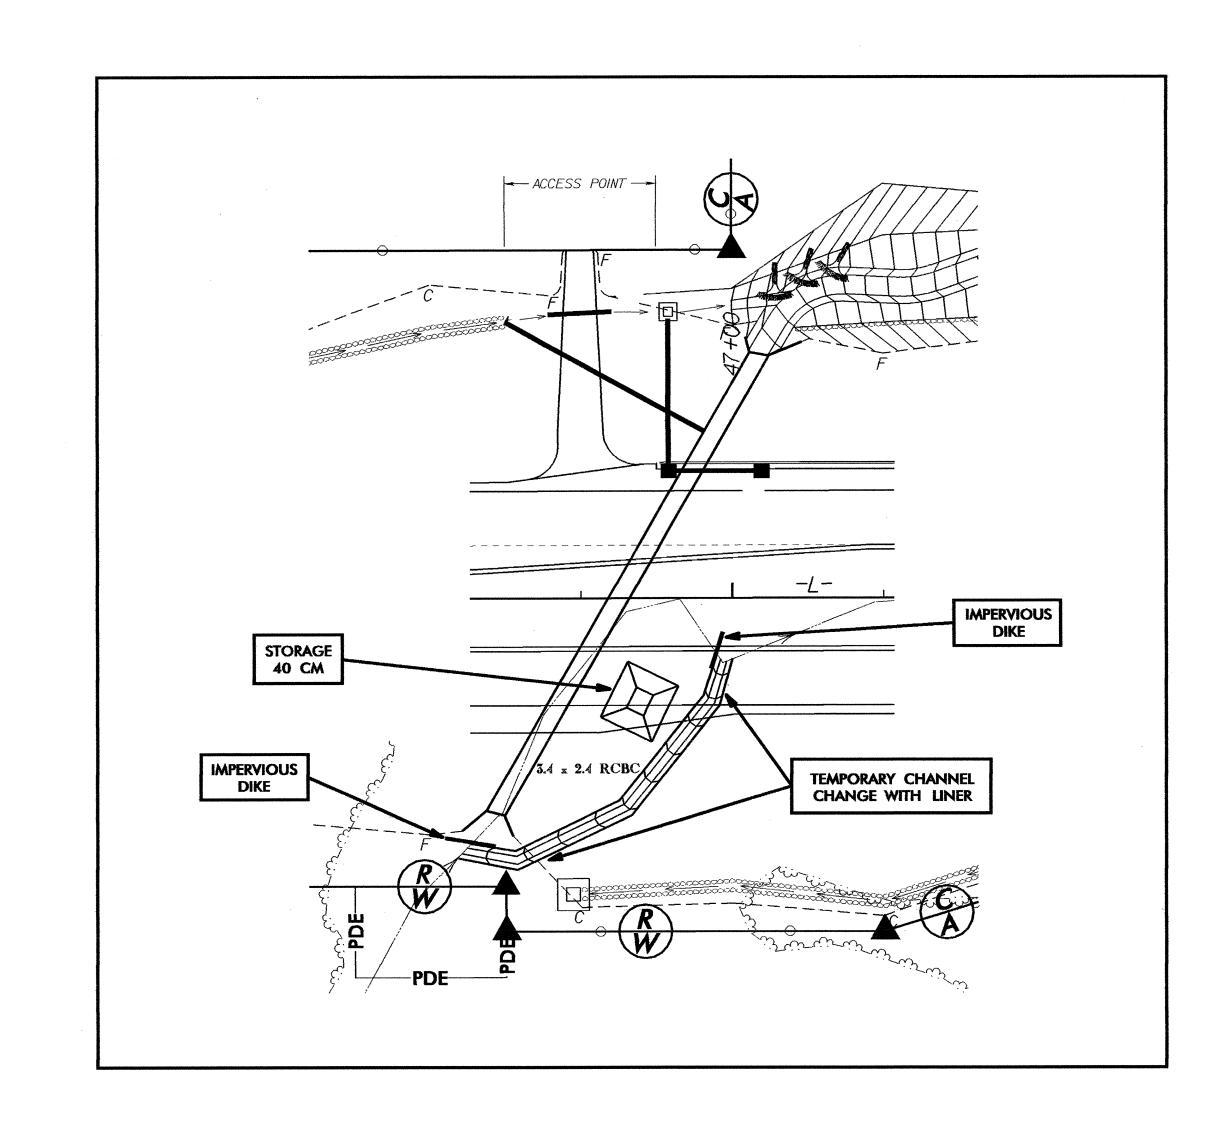

## CONSTRUCTION SEQUENCE (STA. 46+80)

- 1. CONSTRUCT STILLING BASIN (40 CM).
- 2. CONSTRUCT TEMPORARY CHANNEL CHANGE WITH LINER (2:1 SIDE SLOPES, 2 M BASE, 1 M DEPTH).
- 3. CONSTRUCT IMPERVIOUS DIKES.
- 4. CONSTRUCT CULVERT AND STREAM RELOCATION AT OUTLET.
- 5. DIVERT WATER THROUGH CULVERT.
- 6. COMPLETE ROADWAY.
