


# AREA II



PROJ. REFERENCE NO.	SHEET NO.
R-2206C	TCP-10

SEE TCP-12 FOR OFFSITE DETOUR AND SIGNING

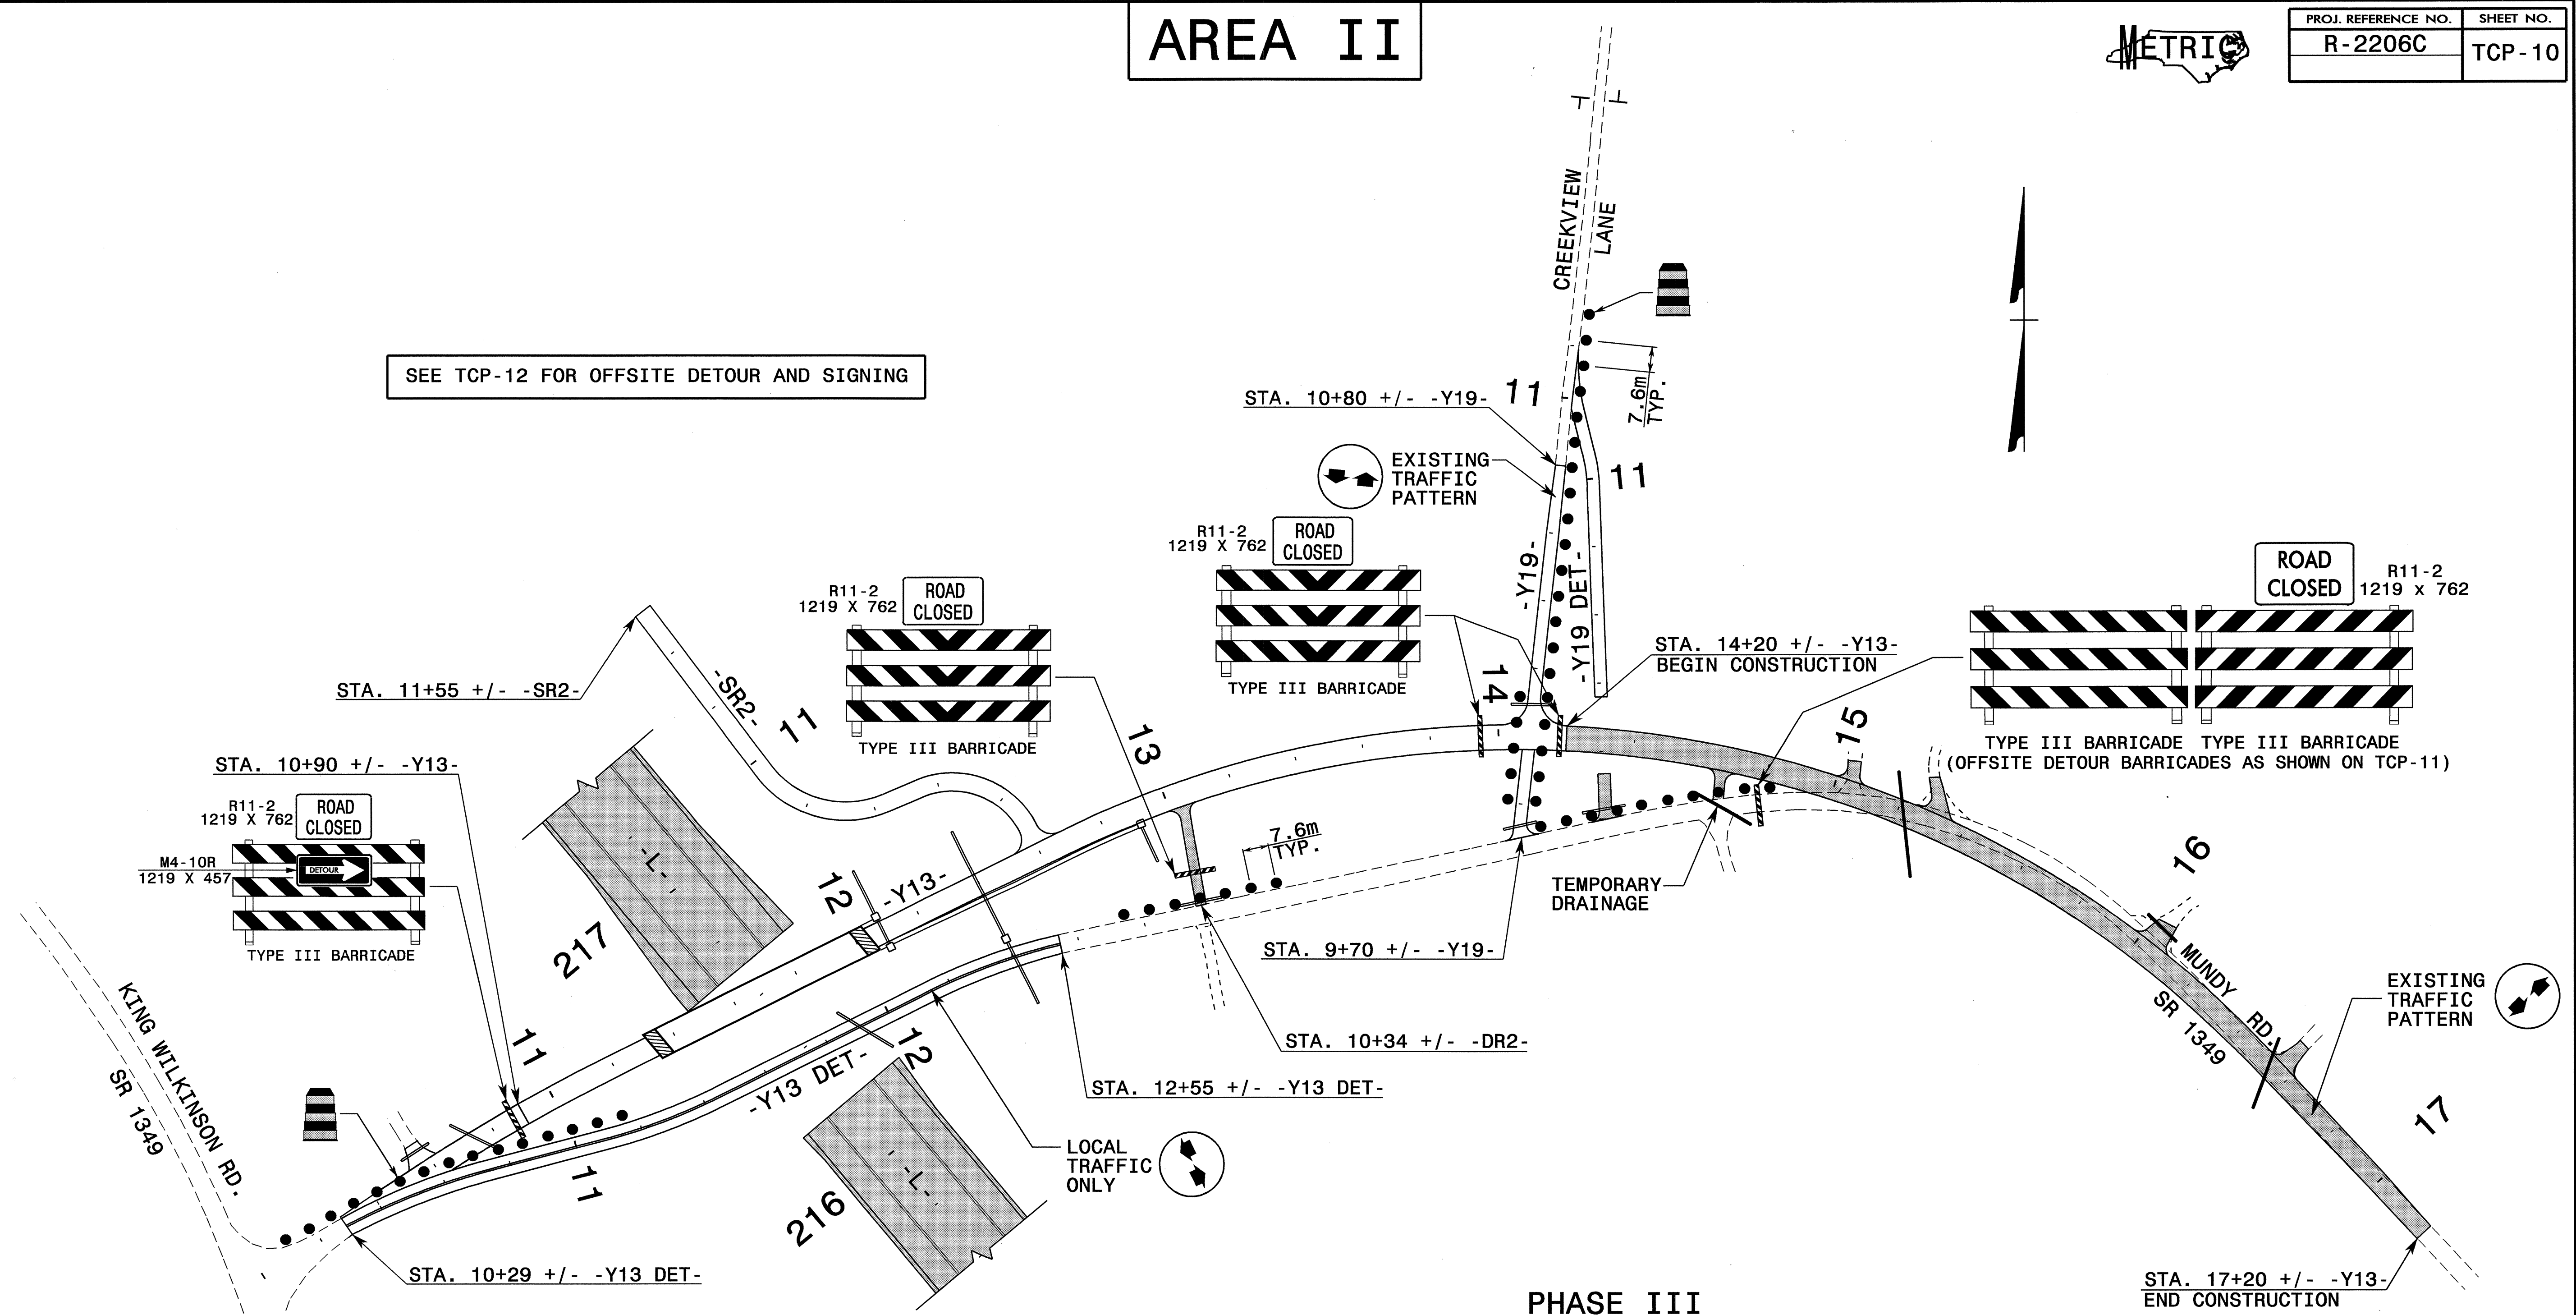

## PHASE III

- NOTE: THE CONTRACTOR SHALL NOT CLOSE -Y13- (MUNDY ROAD) AND -Y11- (FORNEY HILL ROAD) SIMULTANEOUSLY.
- STEP 1. INSTALL ALL OFFSITE DETOUR SIGNING (SEE TCP-12) FOR MUNDY RD. (SR 1349). REMOVE ADVANCED WARNING SIGNS INSTALLED IN PHASE I, STEP 1.

THE CONTRACTOR SHALL COMPLETE THE WORK REQUIRED OF PHASE III, STEPS 2 THRU 6 IN 21 CONSECUTIVE CALENDER DAYS. (SEE INTERMEDIATE CONTRACT TIME AND LIQUIDATED DAMAGES).

- STEP 2. USING SIGNS AS SHOWN ON INSET "A", TCP-12, CLOSE MUNDY ROAD (SR 1349) FROM STA. 10+29 +/- -Y13- TO STA. 17+20 +/- -Y13-. REOPEN -Y19- AND TEMPORARY CONNECTION TO EXISTING TRAFFIC. MAINTAIN ACCESS TO ALL DRIVEWAYS WITHIN PROJECT LIMITS.
- STEP 3. CONSTRUCT -Y13- FROM STA. 14+20 +/- TO STA. 17+20 +/-, INCLUDING DRAINAGE, UP TO BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE.

09-JUL-2004 14:25 J:\TCP\AREA2\R2206C-TC-AREA2-Tcp10.dgn SBC00FS AT TETC206428

EXISTING TRAFFIC PATTERN

APPROVED: *[Signature]* DATE: 7/2/04

SEAL

**AREA 2  
PHASE III DETAILS  
AND PHASING**

SCALE: 1:1000		REVISIONS
DATE: 05-10-04		
DWG. BY: SBC		
DESIGN BY: SBC		
REVIEWED BY: CLM		
