


PROJ. REFERENCE NO.	SHEET NO.
U-5775	TMP-4
 TGS ENGINEERS 201 W. MARION ST. STE 200 SHELBY, NC 28150 PH (704) 476-0003 CORP. LICENSE NO.: C-0275	

PHASE II

STEP 1:

USING TEMPORARY LANE CLOSURES AND FLAGGERS AS NEEDED PLACE TEMPORARY PAVEMENT MARKINGS AS FOLLOWS:
 -L- STA. 19+46.00 TO 30+00.00
 -Y- STA 11+00.00 TO 26+28.00
 (SEE TMP-4, 5 & 6, SEE NCDOT RDY STD DRAWING 1101.02, SHEET 1 OF 14)

SHIFT THE PEACH ST TRAFFIC ONTO THE NEW ALIGNMENT AND OPEN ALL NEW LANES ON E MARION/US 74 BUS (-L-) AND CHERRYVILLE RD (-Y-) TO TRAFFIC.

ACTIVATE THE NEW SIGNAL.

STEP 2:

USING TEMPORARY LANE CLOSURES AND FLAGGERS AS NEEDED CONSTRUCT THE REMAINING SECTION OF -Y- FROM -Y- STA. 25+57+/- TO 26+78.00.
 (SEE TMP-4 & 5, SEE NCDOT RDY STD DRAWING 1101.02, SHEET 1 OF 14)

CONSTRUCT THE ADJACENT CURB & GUTTER, SIDEWALK AND DRIVES AS SHOWN ON PLAN. (SEE TMP-4 & 5).

PLACE THE REMAINING SECTION OF CURB AND GUTTER FROM -L- STA. 22+19+/- LT TO THE PEACH ST TURNOUT. COMPLETE THE ADJACENT SIDEWALK. (SEE TMP-4 & 5)

REMOVE THE OLD PEACH STREET PAVEMENT INCLUDING THE TEMPORARY PAVEMENT PLACE IN PHASE 1. (SEE TMP-4)

STEP 3:

USING TEMPORARY LANE CLOSURES AND FLAGGERS AS NEEDED PLACE THE FINAL LAYER OF SURFACE COURSE AS FOLLOWS:



- L- STA. 19+46.00 TO 30+00.00
 - Y- STA 11+00.00 TO 26+28.00
 - SVC- STA. 10+55.00 TO 12+02.51
 - SVC- STA. 12+40.66 TO 15+10.00
- (SEE TMP-4, SEE NCDOT RDY STD DRAWING 1101.02, SHEET 1 OF 14)

PLACE CONCRETE ISLANDS AS SHOWN ON PLAN (TMP-4)


USING TEMPORARY LANE CLOSURES AND FLAGGERS AS NEEDED PLACE FINAL PAVEMENT MARKINGS AND MARKERS AS FOLLOWS:

- L- STA. 19+46.00 TO 30+00.00
 - Y- STA 11+00.00 TO 26+28.00
 - SVC- STA. 10+55.00 TO 12+02.51
 - SVC- STA. 12+40.66 TO 15+10.00
- (SEE PAVEMENT MARKING PLANS, SEE NCDOT RDY STD DRAWING 1101.02, SHEET 1 OF 14)

OPEN MULTI-USE PATH.
 REMOVE ALL TRAFFIC CONTROL DEVICES.

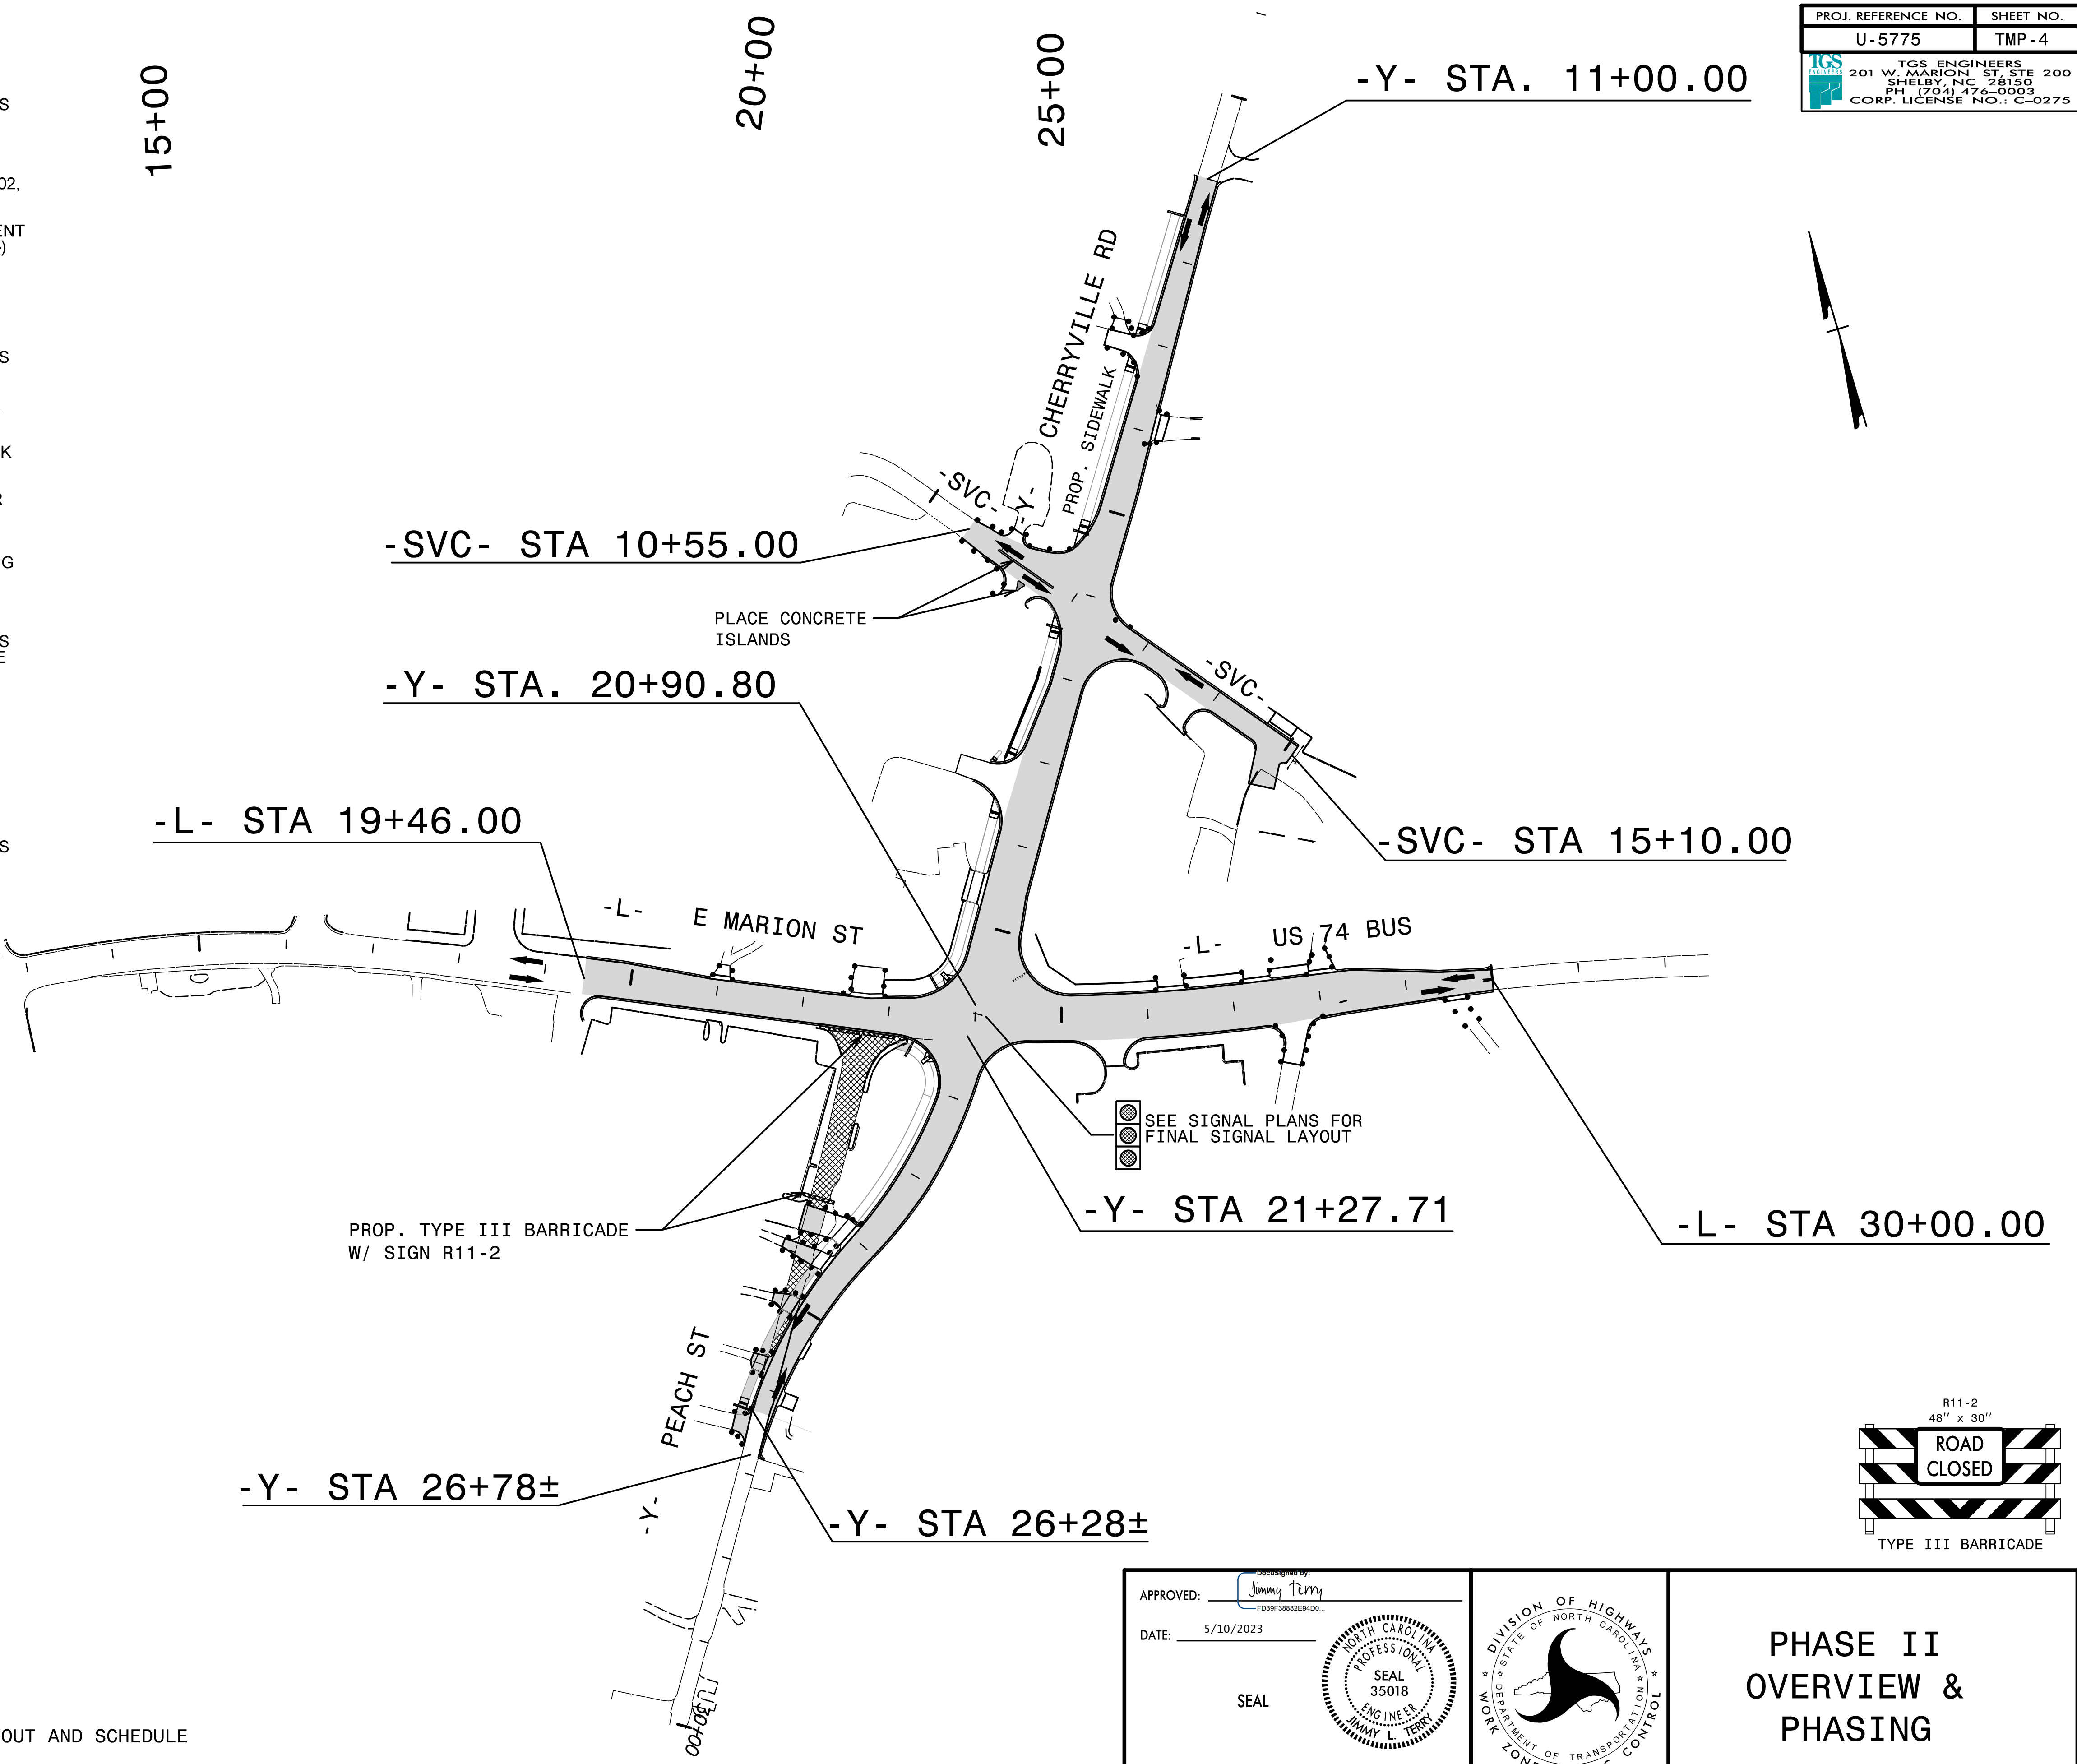


FOR TEMPORARY PAVEMENT MARKING LAYOUT AND SCHEDULE SEE TMP-5 & TMP-6

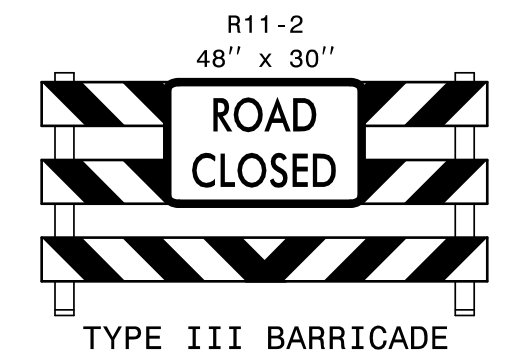


APPROVED: Jimmy Terry
Professional Engineer
 DATE: 5/10/2023

SEAL

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED

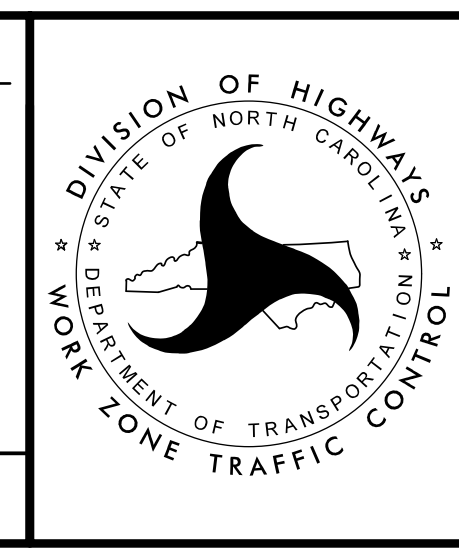

PHASE II OVERVIEW & PHASING



4/24/2023 11:57:55 AM \\Traf\TrafficControl\TCP\U-5775-TC-TMP-04(0V02).dgn
 User: jsmelvin
