


CULVERT INSTALLATION SEQUENCE STA. 17 + 26 -Y2-

- 1. INSTALL FOUR SEDIMENT BASINS AROUND CULVERT LOCATION
- 2. INSTALL IMPERVIOUS DIKES AND APPROXIMATELY 190 LF OF OF TEMPORARY CHANNEL CHANGE W/LINER AS SHOWN IN DETAIL.
- 3. DIVERT FLOW THROUGH TEMPORARY CHANNEL.
- 4. INSTALL STILLING BASIN.
- 5. CONSTRUCT PROPOSED CULVERT.
- 6. REMOVE IMPERVIOUS DIKES AND TEMPORARY CHANNEL CHANGE.
- 7. DIVERT FLOW THROUGH NEW CULVERT.



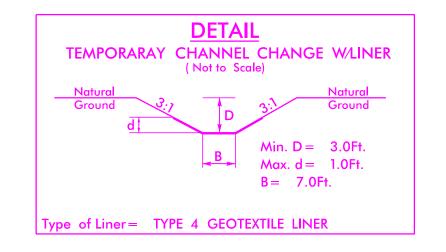

Engineers | Construction Managers | Planners | Scientists
www.rkk.com

Responsive People | Creative Solutions
