

# PIPE INSTALLATION SEQUENCE

## STA. 30+53 -L1-

PROJECT REFERENCE NO. U-5907  
SHEET NO. EC-8A

**Kimley»Horn**



200 SOUTH TRYON, SUITE 200  
CHARLOTTE, N.C. 28202

### PIPE INSTALLATION SEQUENCE

#### Stage I

1. INSTALL CLEAN WATER DIVERSIONS AND TEMPORARY PIPES 1 AND 2.
2. CONSTRUCT IMPERVIOUS DIKES AND DIVERT FLOW THROUGH TEMP PIPES 1 AND 2 UTILIZING EXISTING 18" RCPS W/CB'S UNDER SLOAN STREET.
3. REMOVE EXISTING 48" UNDER SLOANE STREET.
4. DEWATER ENTRAPPED AREA. INSTALL PIPES AND STORM STRUCTURES PER PLANS FROM 810 TO 809, 809 TO 807, 804 TO 802 AND 805, 802 TO 801 AND 700.

### STAGE I

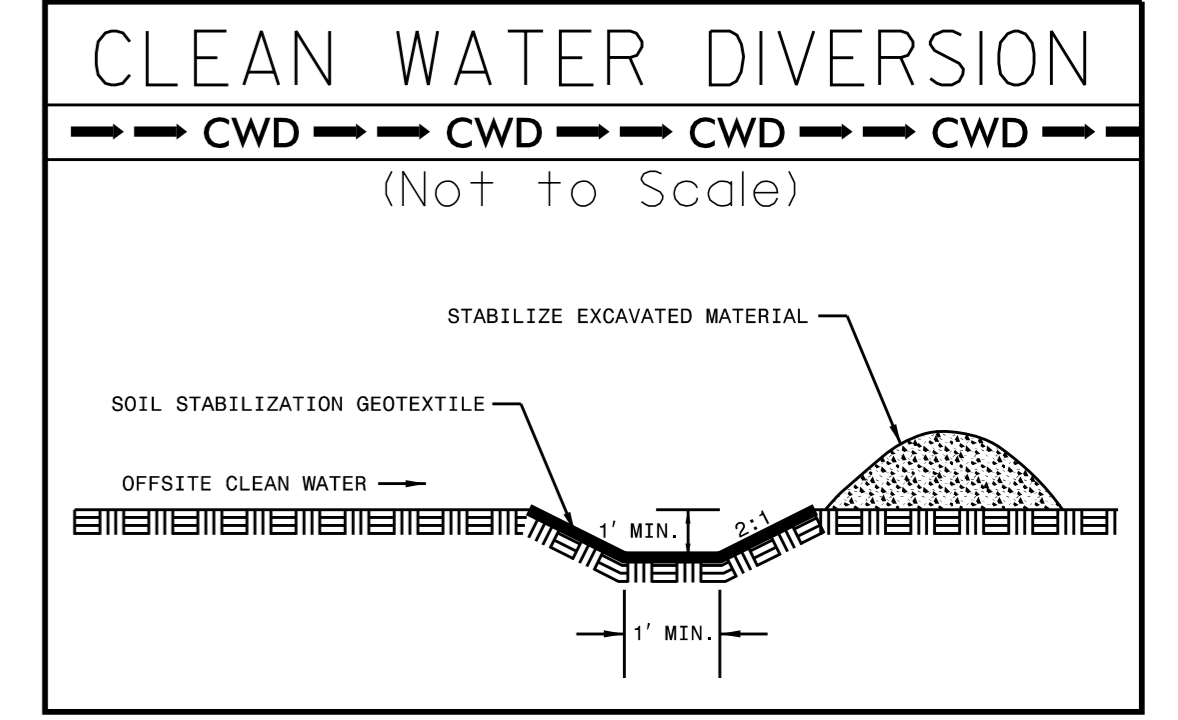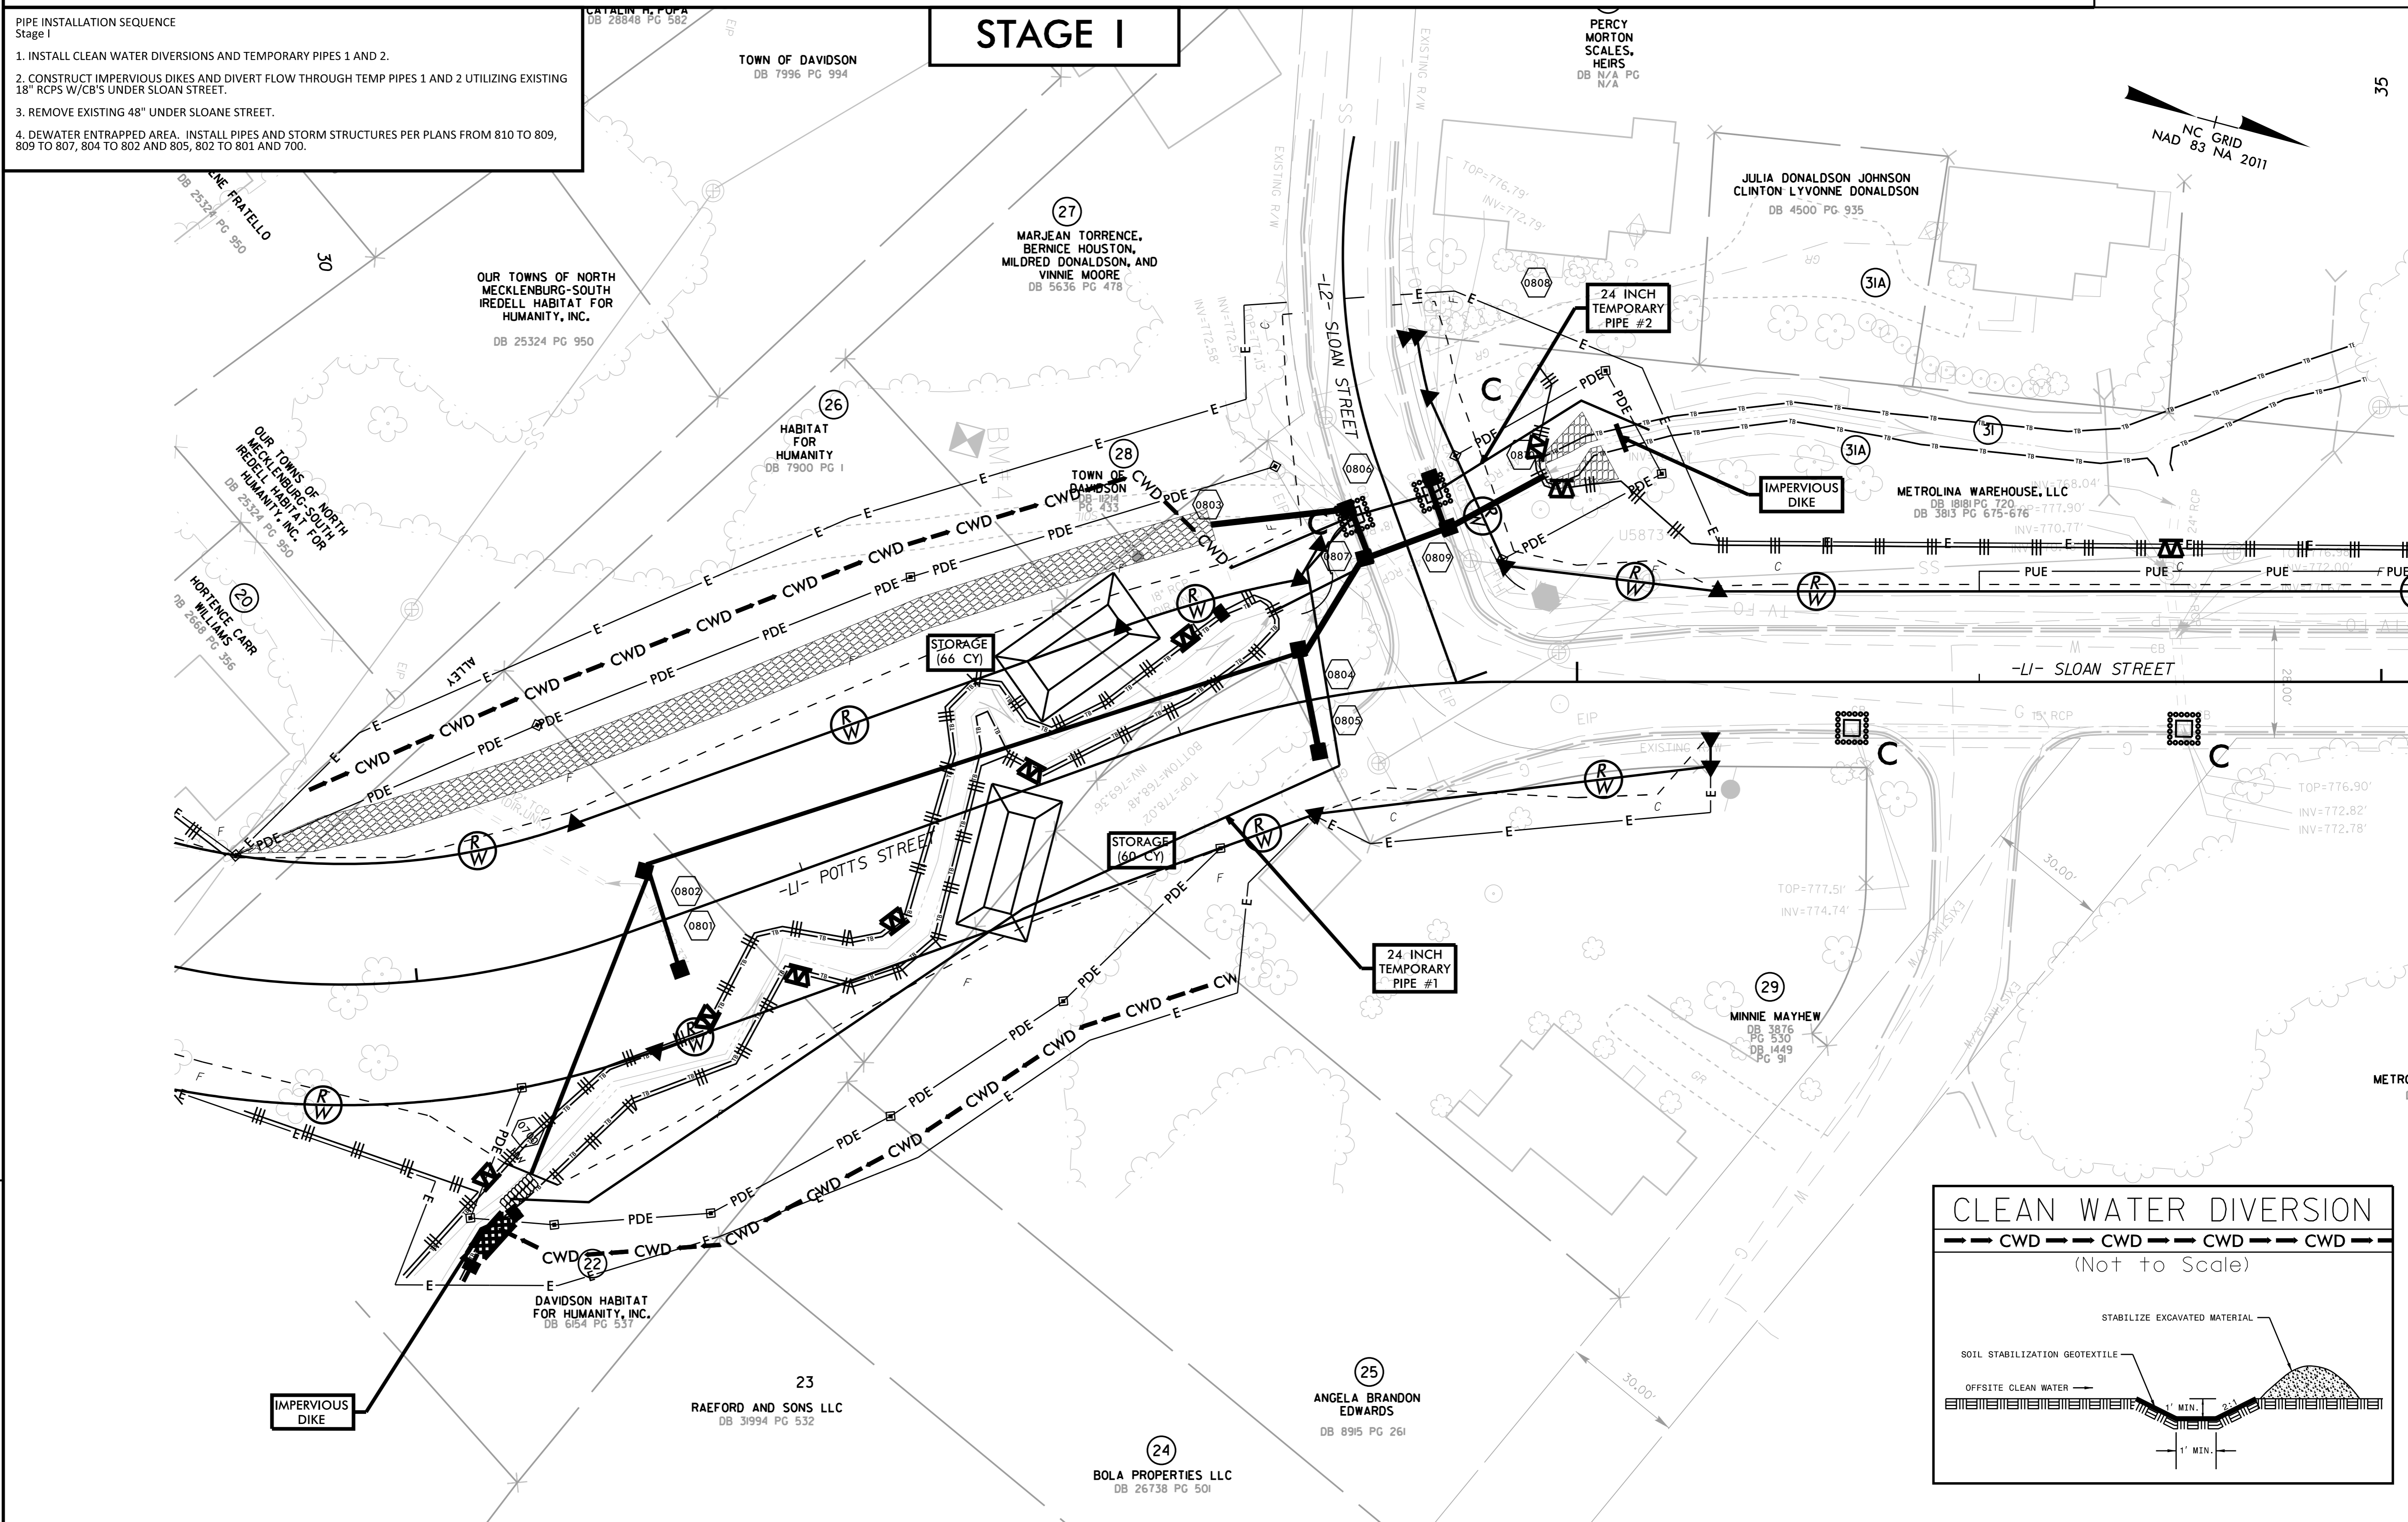

REVISIONS

5/14/199

9/8/2023
