


## CROSS-PIPE INSTALLATION SEQUENCE -Y14- STA. 13 + 27 PHASE 1

- UTILIZE TRAFFIC CONTROL AS SEEN FIT IN FIELD.
- . UTILIZE SPECIAL STILLING BASIN(S) DURING PIPE INSTALLATION AS NEEDED.
- 4. INSTALL TEMPORARY SILT FENCE AROUND THE JURISDICTIONAL STREAMS, UPSTREAM AND DOWNSTREAM, AS SHOWN.
- 5. INSTALL PUMP AROUND AND IMPERVIOUS DIKES AS SHOWN ON PLAN.
- 6. MAINTAIN FLOW THROUGH PUMP AROUND AND EXISTING 30" HDPE.
- 7. CONSTRUCT TRENCH FOR 60" RCP-III.
- . CONSTRUCT JUNCTION BOX AND HEAD WALL INSTALL BOTH RCP-III'S, CONNECTING UPSTREAM PIPE TO BOTH HEADWALL AND JB AND DOWNSTREAM PIPE TO JB.
- 9. CONSTRUCT CHANNEL IMPROVEMENTS ON UPSTREAM AND DOWNSTREAM SIDE AND TIE JS STREAM TO INLET END OF PROPOSED 60" RCP—III. REMOVE IMPERVIOUS DIKES AND PUMP AROUND.
- 10. CONSTRUCT PROPOSED ROADWAY PAVEMENT, SLOPES, AND DITCHES PER ROADWAY PLANS.

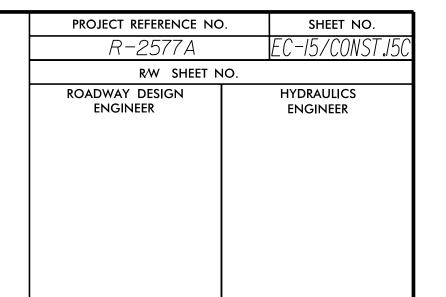

P: (919) 878-9560 8601 Six Forks Road, Forum 1,Suite 700 Raleigh, North Carolina 27615-3960

Engineers | Construction Managers | Planners | Scientists www.rkk.com

Responsive People | Creative Solutions
