


CULVERT CONSTRUCTION SEQUENCE STA. 16+37 -L-


PROJECT REFERENCE NO.	SHEET NO.
HL-0033	EC-4A/CONST.04
R/W SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

PHASE I

1. CONSTRUCT SPECIAL STILLING BASIN(S).
2. INSTALL IMPERVIOUS DIKES A AND D AND CONSTRUCT TEMPORARY CHANNEL IN THE DRY UTILIZING PUMP AROUND OPERATIONS AS NEEDED.
3. INSTALL IMPERVIOUS DIKES B AND C AND REMOVE IMPERVIOUS DIKES A AND D TO DIRECT WATER INTO THE TEMPORARY CHANNEL.
4. BEGIN PHASE II.

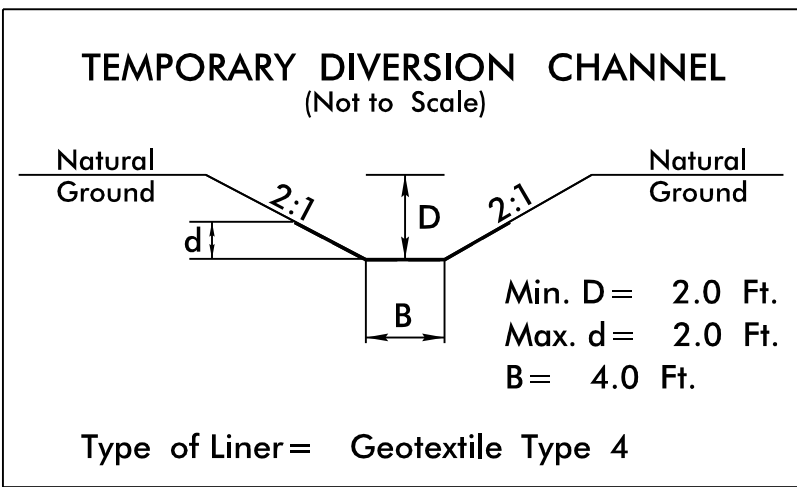


NAD 83/2011

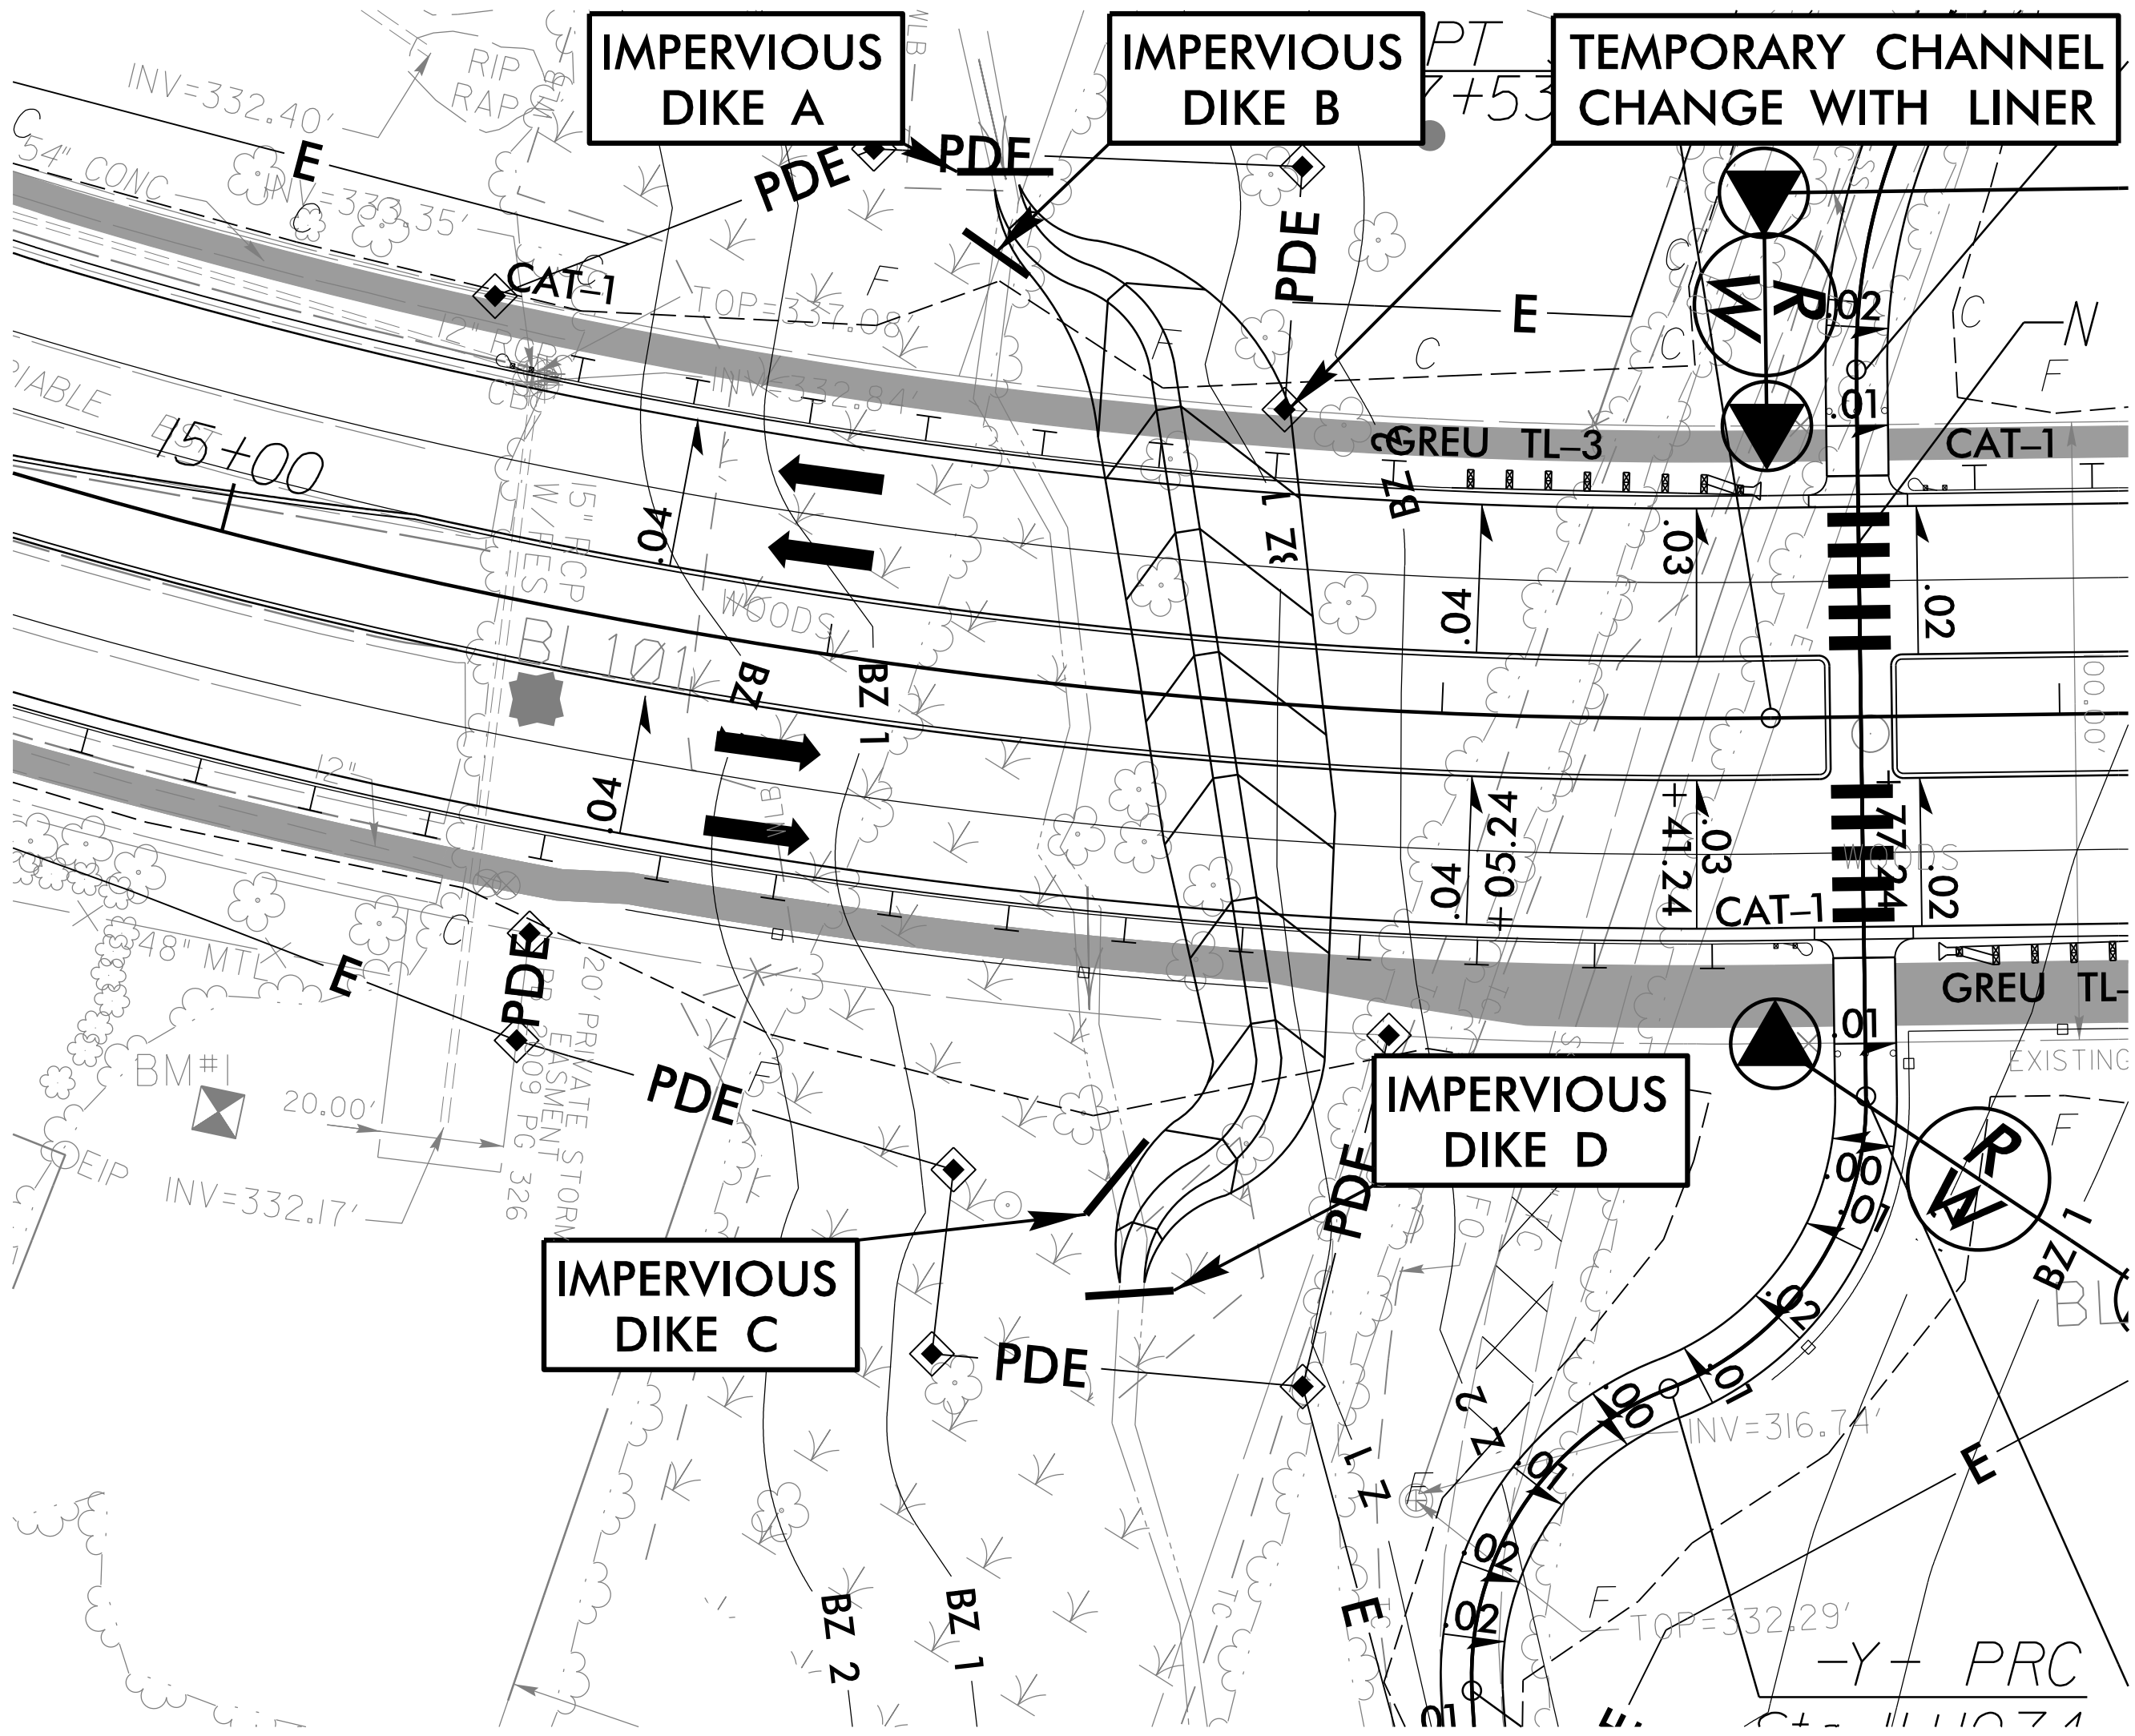


PHASE II

1. INSTALL PROPOSED 78" RCP W/HW AND PIPE INLET/OUTLET CHANNEL WORK IN THE DRY UTILIZING PUMP AROUND OPERATIONS AS NEEDED.
2. REMOVE REMAINING IMPERVIOUS DIKES AND TEMPORARY CHANNEL TO ALLOW WATER TO FLOW THROUGH 78" RCP.
3. COMPLETE ROADWAY.

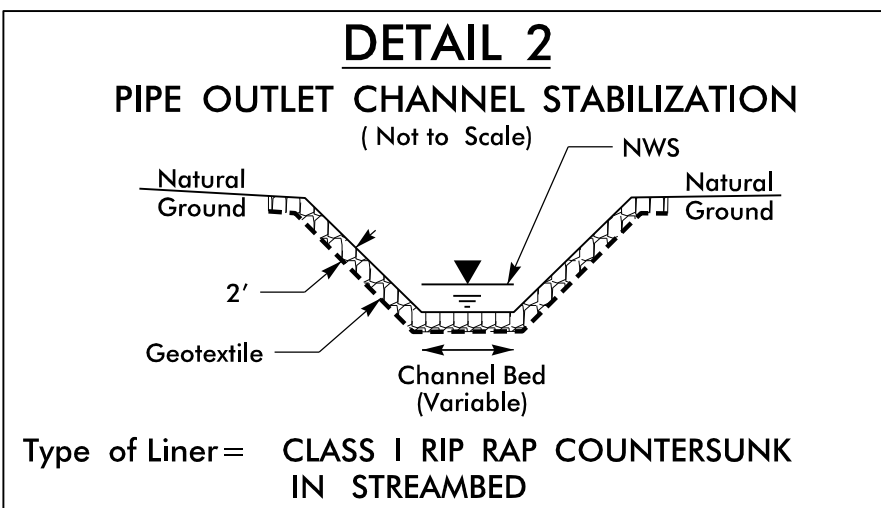

AT STA. 16+54 -L- RT

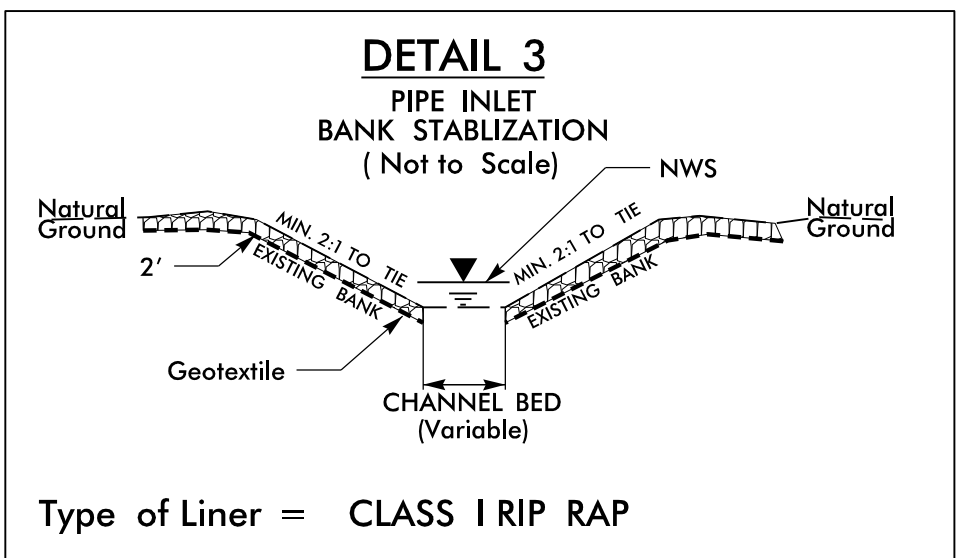

AT STA. 16+20 -L- LT

NAD 83/2011

