
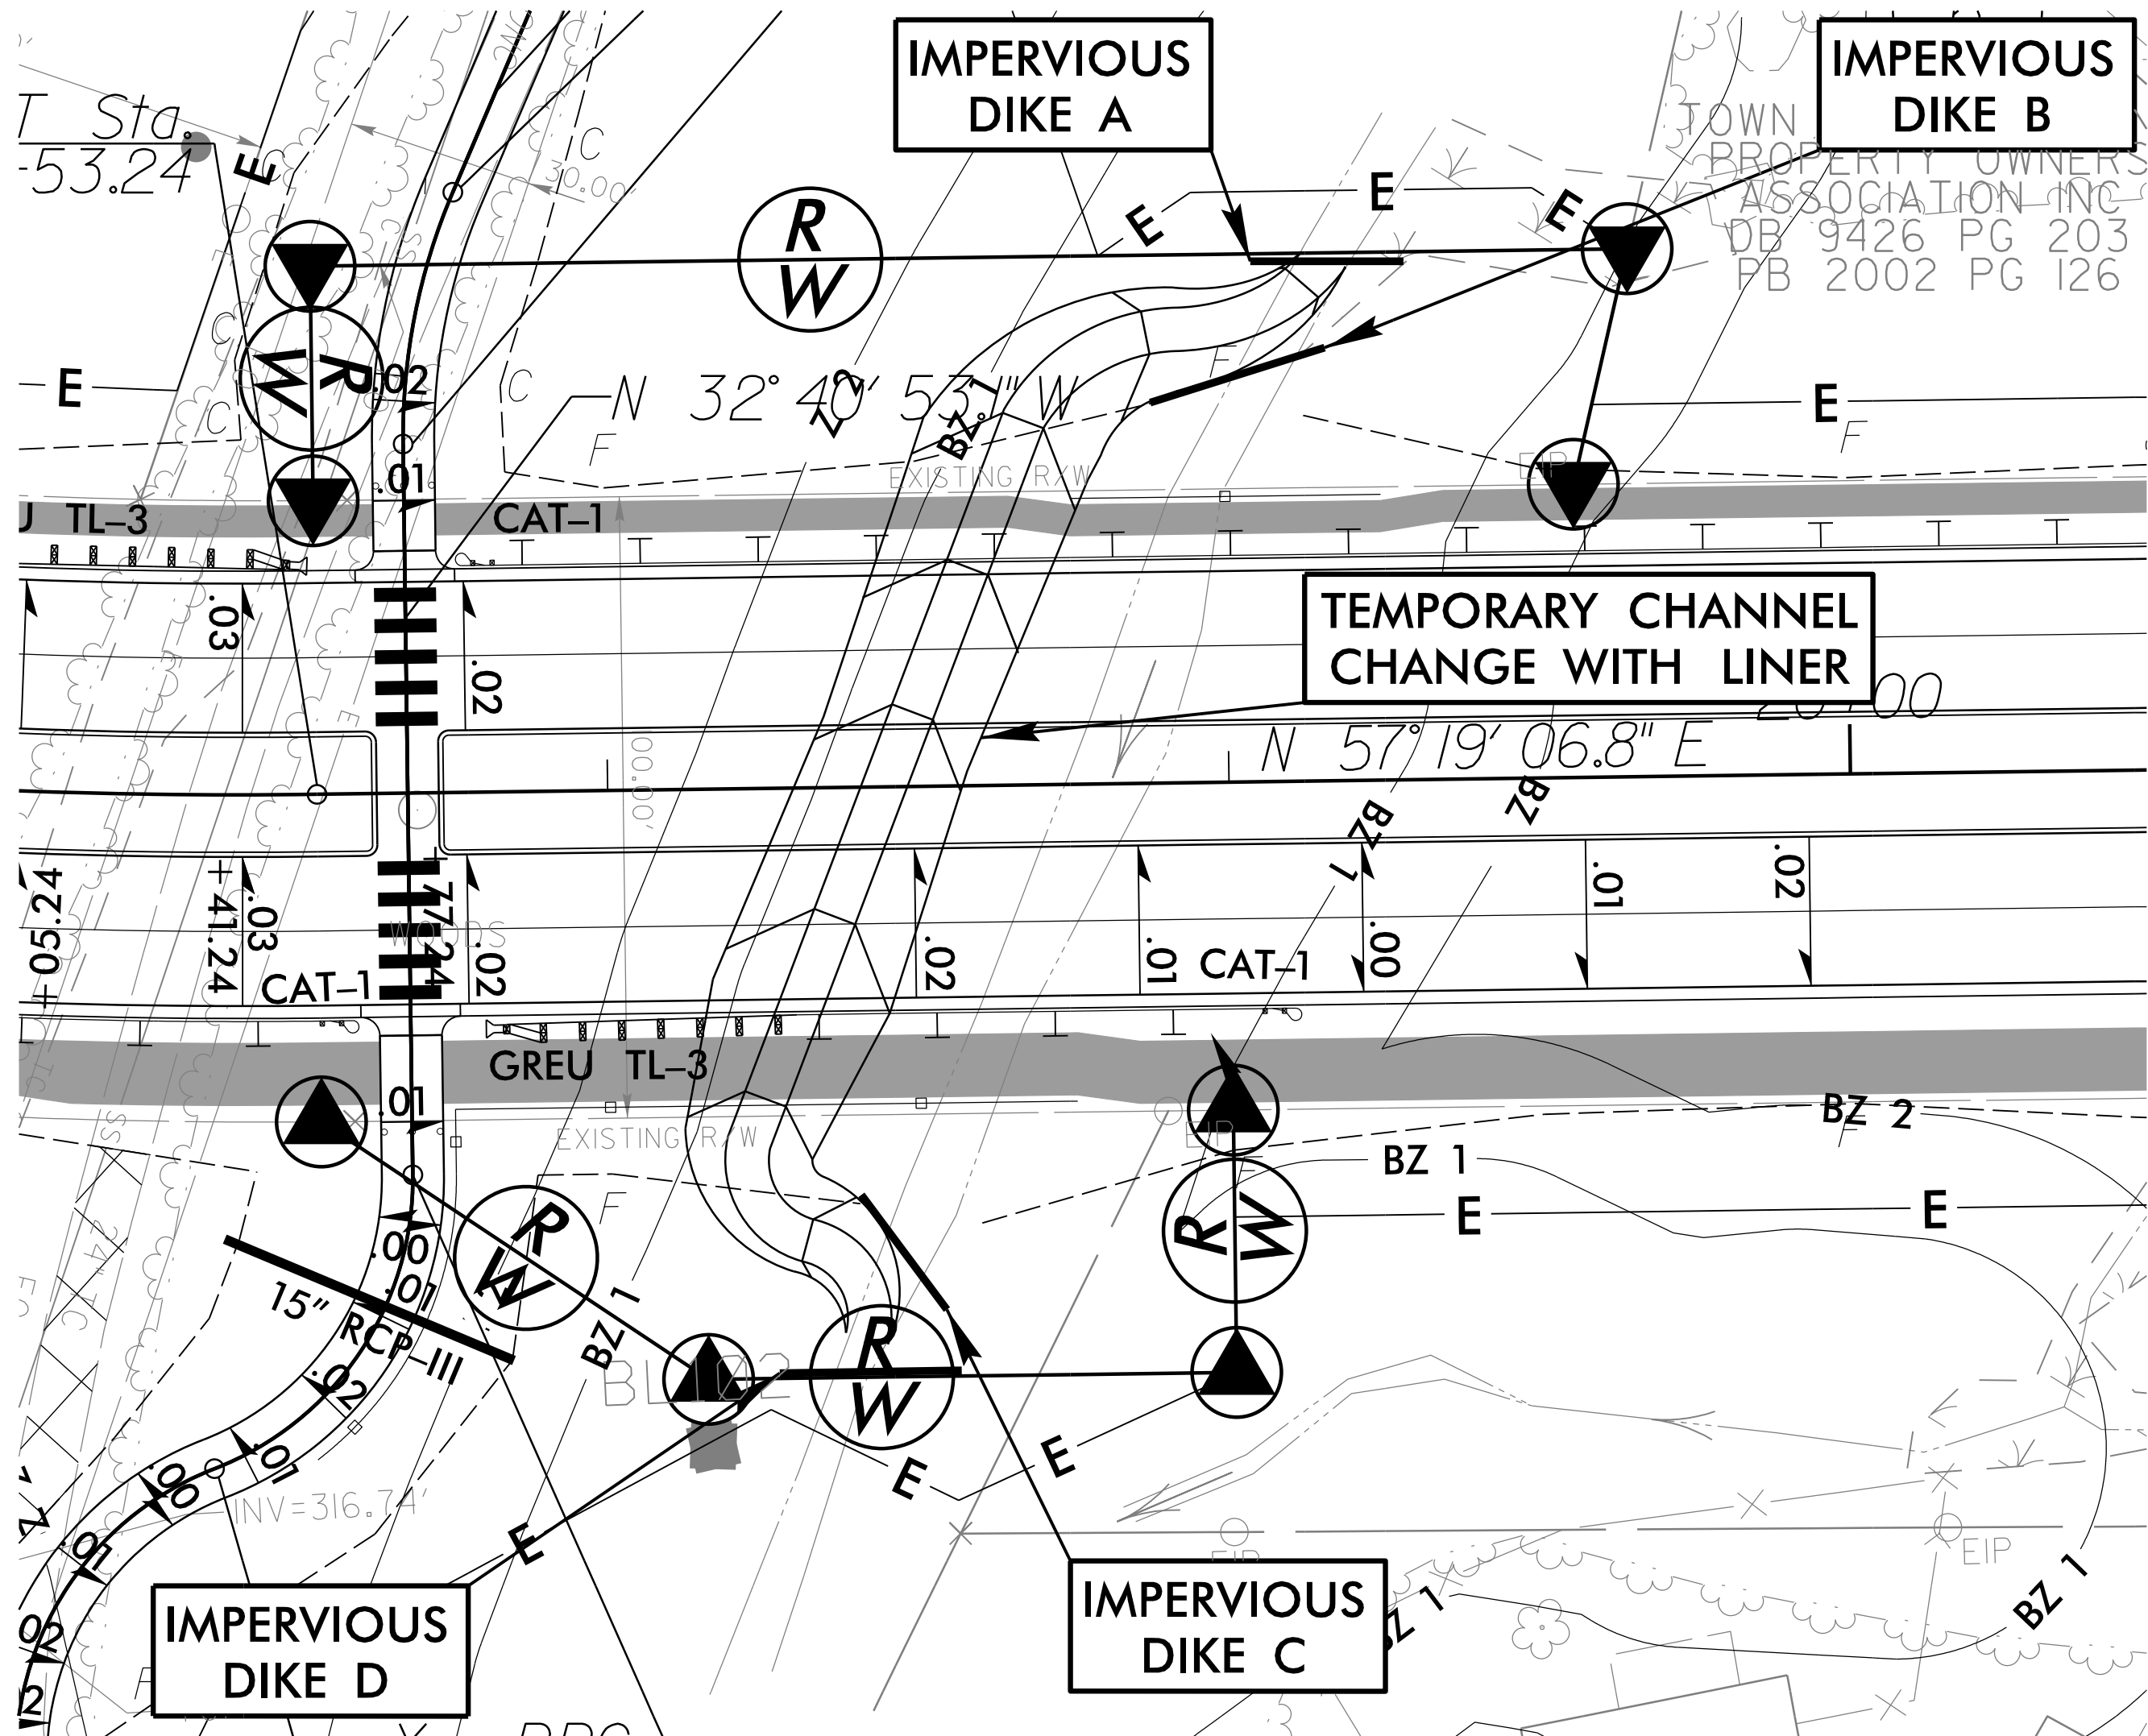


CULVERT CONSTRUCTION SEQUENCE STA. 18+78 -L-

PROJECT REFERENCE NO.	SHEET NO.
HL-0033	EC-4B/CONST.04
R/W SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

PHASE I

1. CONSTRUCT SPECIAL STILLING BASIN(S).
2. INSTALL IMPERVIOUS DIKES A AND D AND CONSTRUCT TEMPORARY CHANNEL IN THE DRY UTILIZING PUMP AROUND OPERATIONS AS NEEDED.
3. INSTALL IMPERVIOUS DIKES B AND C AND REMOVE IMPERVIOUS DIKES A AND D TO DIRECT WATER INTO THE TEMPORARY CHANNEL.
4. BEGIN PHASE II.

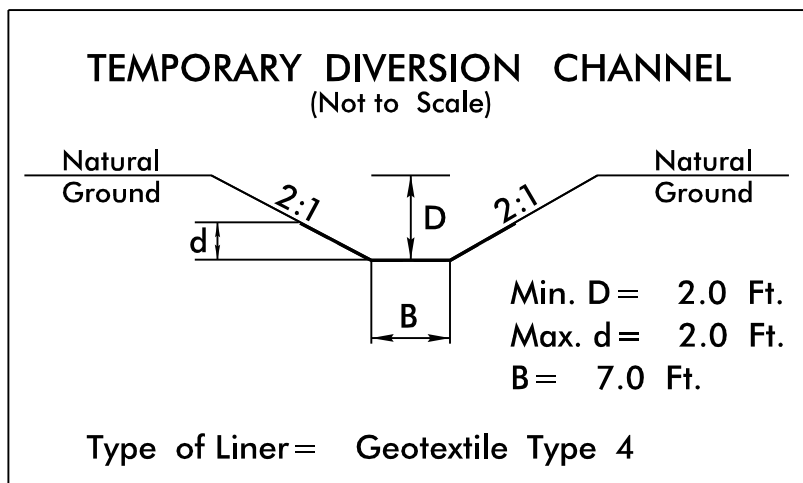

PHASE II

1. INSTALL PROPOSED 1@8'x7' RCBC AND INLET/OUTLET BANK STABILIZATION IN THE DRY UTILIZING PUMP AROUND OPERATIONS AS NECESSARY.
2. REMOVE REMAINING IMPERVIOUS DIKES AND TEMPORARY CHANNEL TO ALLOW WATER TO FLOW THROUGH RCBC.
3. COMPLETE ROADWAY.

