

# AREA III





PROJ. REFERENCE NO.	SHEET NO.
R-2206C	TCP-14A

## PHASE II (CONT.)

THE CONTRACTOR SHALL COMPLETE THE WORK REQUIRED OF PHASE II, STEPS 2 THRU 4 FROM 6:00 P.M. FRIDAY THRU 7:00 A.M. MONDAY. (SEE INTERMEDIATE CONTRACT TIME AND LIQUIDATED DAMAGES).

- STEP 2. USING RSD NO. 1101.02 (SHEET 1 OF 7), PLACE ONE LANE, TWO-WAY TRAFFIC ONTO EXISTING NC 150 WESTBOUND LANE (SEE SECTIONS B-B AND C-C). CONSTRUCT -Y14DET- TIE-IN (RIGHT LANE) FROM STA. 10+31+/- TO STA. 11+80+/- AND FROM STA. 18+20+/- TO STA. 19+87+/-, UP TO FINAL LAYER OF SURFACE COURSE. PLACE TEMPORARY PAVEMENT MARKINGS AS MUCH AS POSSIBLE ON -Y14DET- (SEE TCP-15). REFER TO RSD 1205.01 AND 1205.02 WHEN PLACING TEMPORARY PAVEMENT MARKINGS, SEE TCP-1 FOR TEMPORARY MARKING SCHEDULE.
- STEP 3. USING FLAGGERS, PLACE ONE LANE, TWO-WAY TRAFFIC ONTO -Y14DET- EASTBOUND LANE (SECTIONS B-B AND C-C). CONSTRUCT -Y14DET- TIE-IN (LEFT LANE) FROM STA. 10+31+/- TO STA. 11+80+/- AND FROM STA. 18+20+/- TO STA. 19+87+/-, UP TO FINAL LAYER OF SURFACE COURSE. PLACE REMAINING TEMPORARY PAVEMENT MARKINGS ON -Y14DET-.
- STEP 4. OPEN -Y14DET- TO A 2-LANE, TWO-WAY TRAFFIC PATTERN.

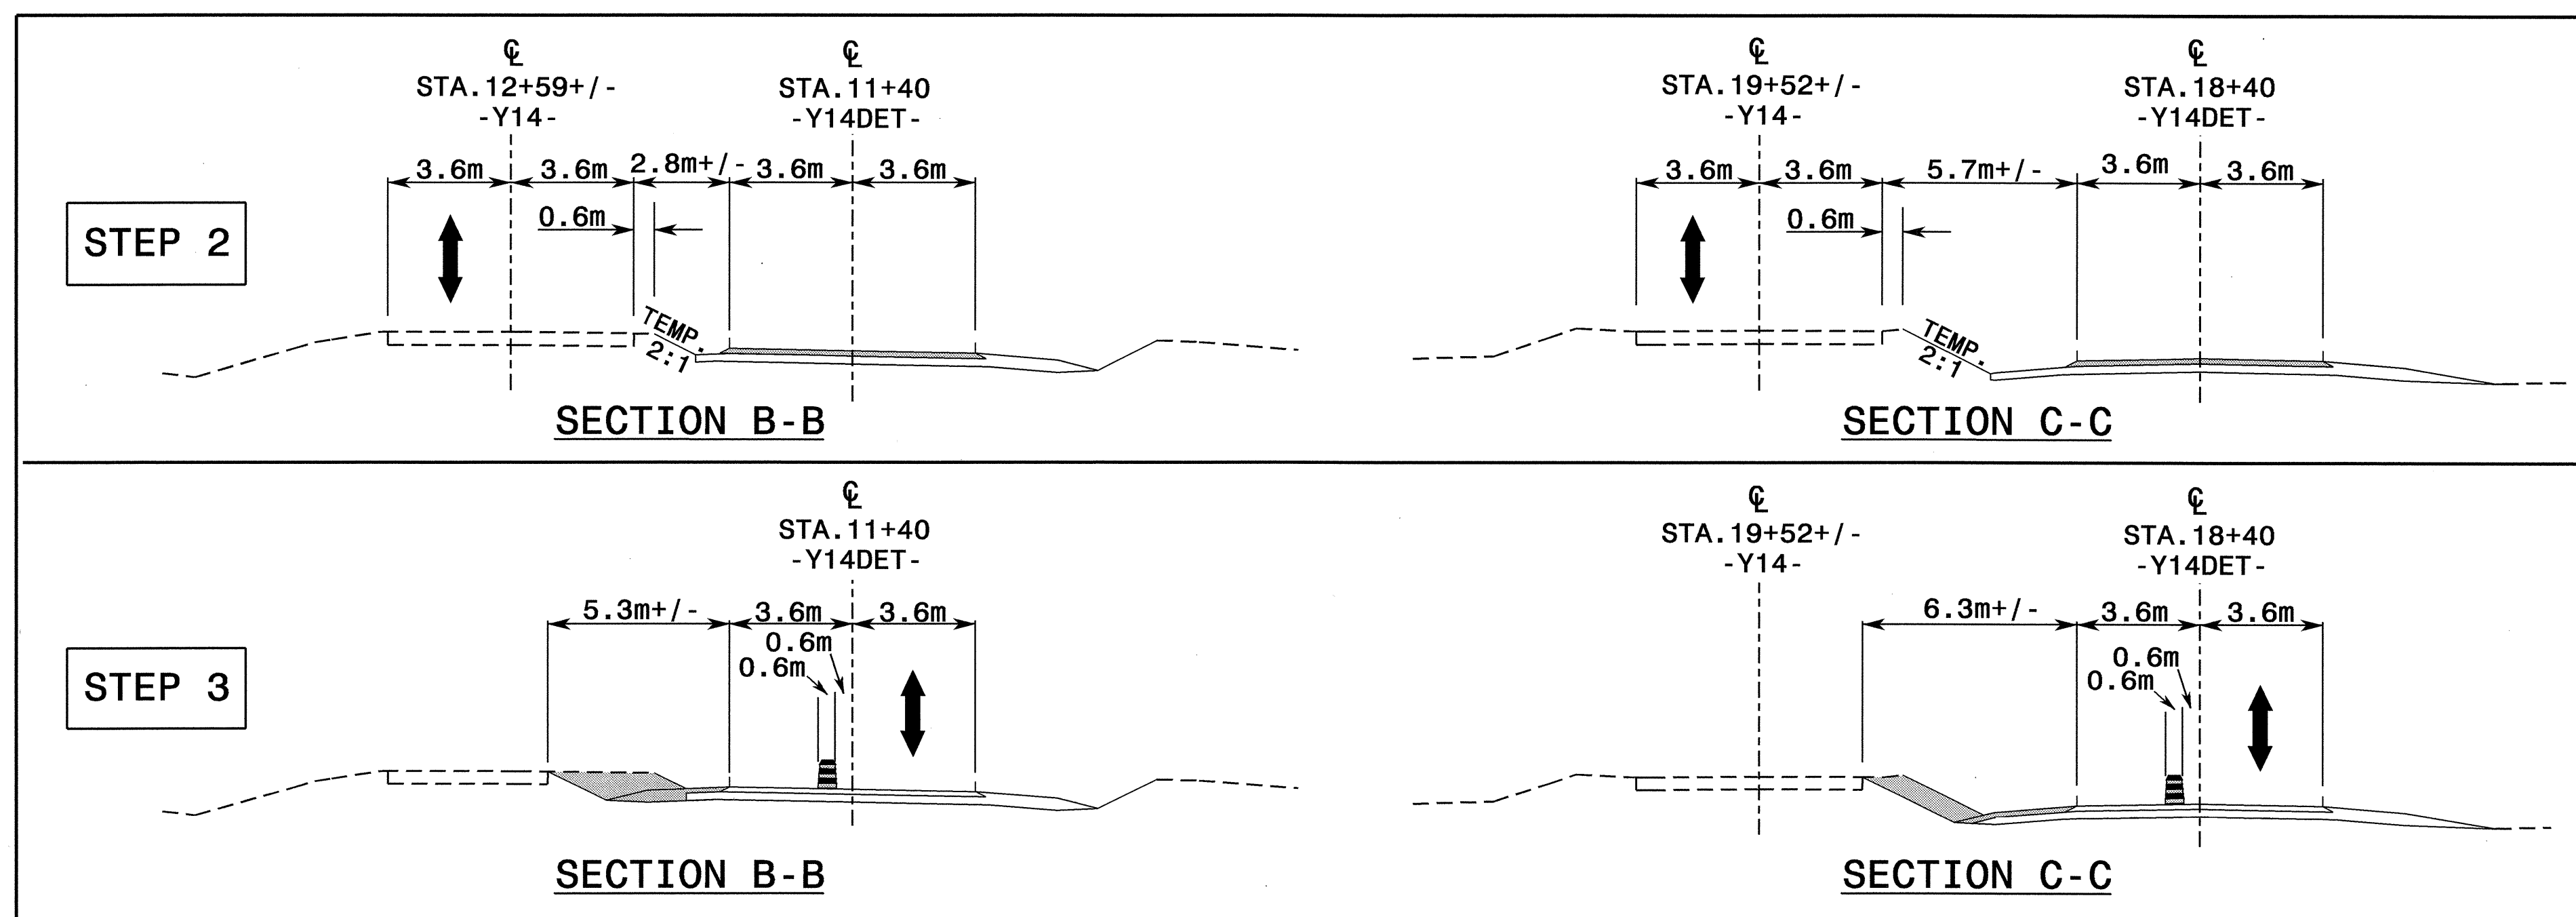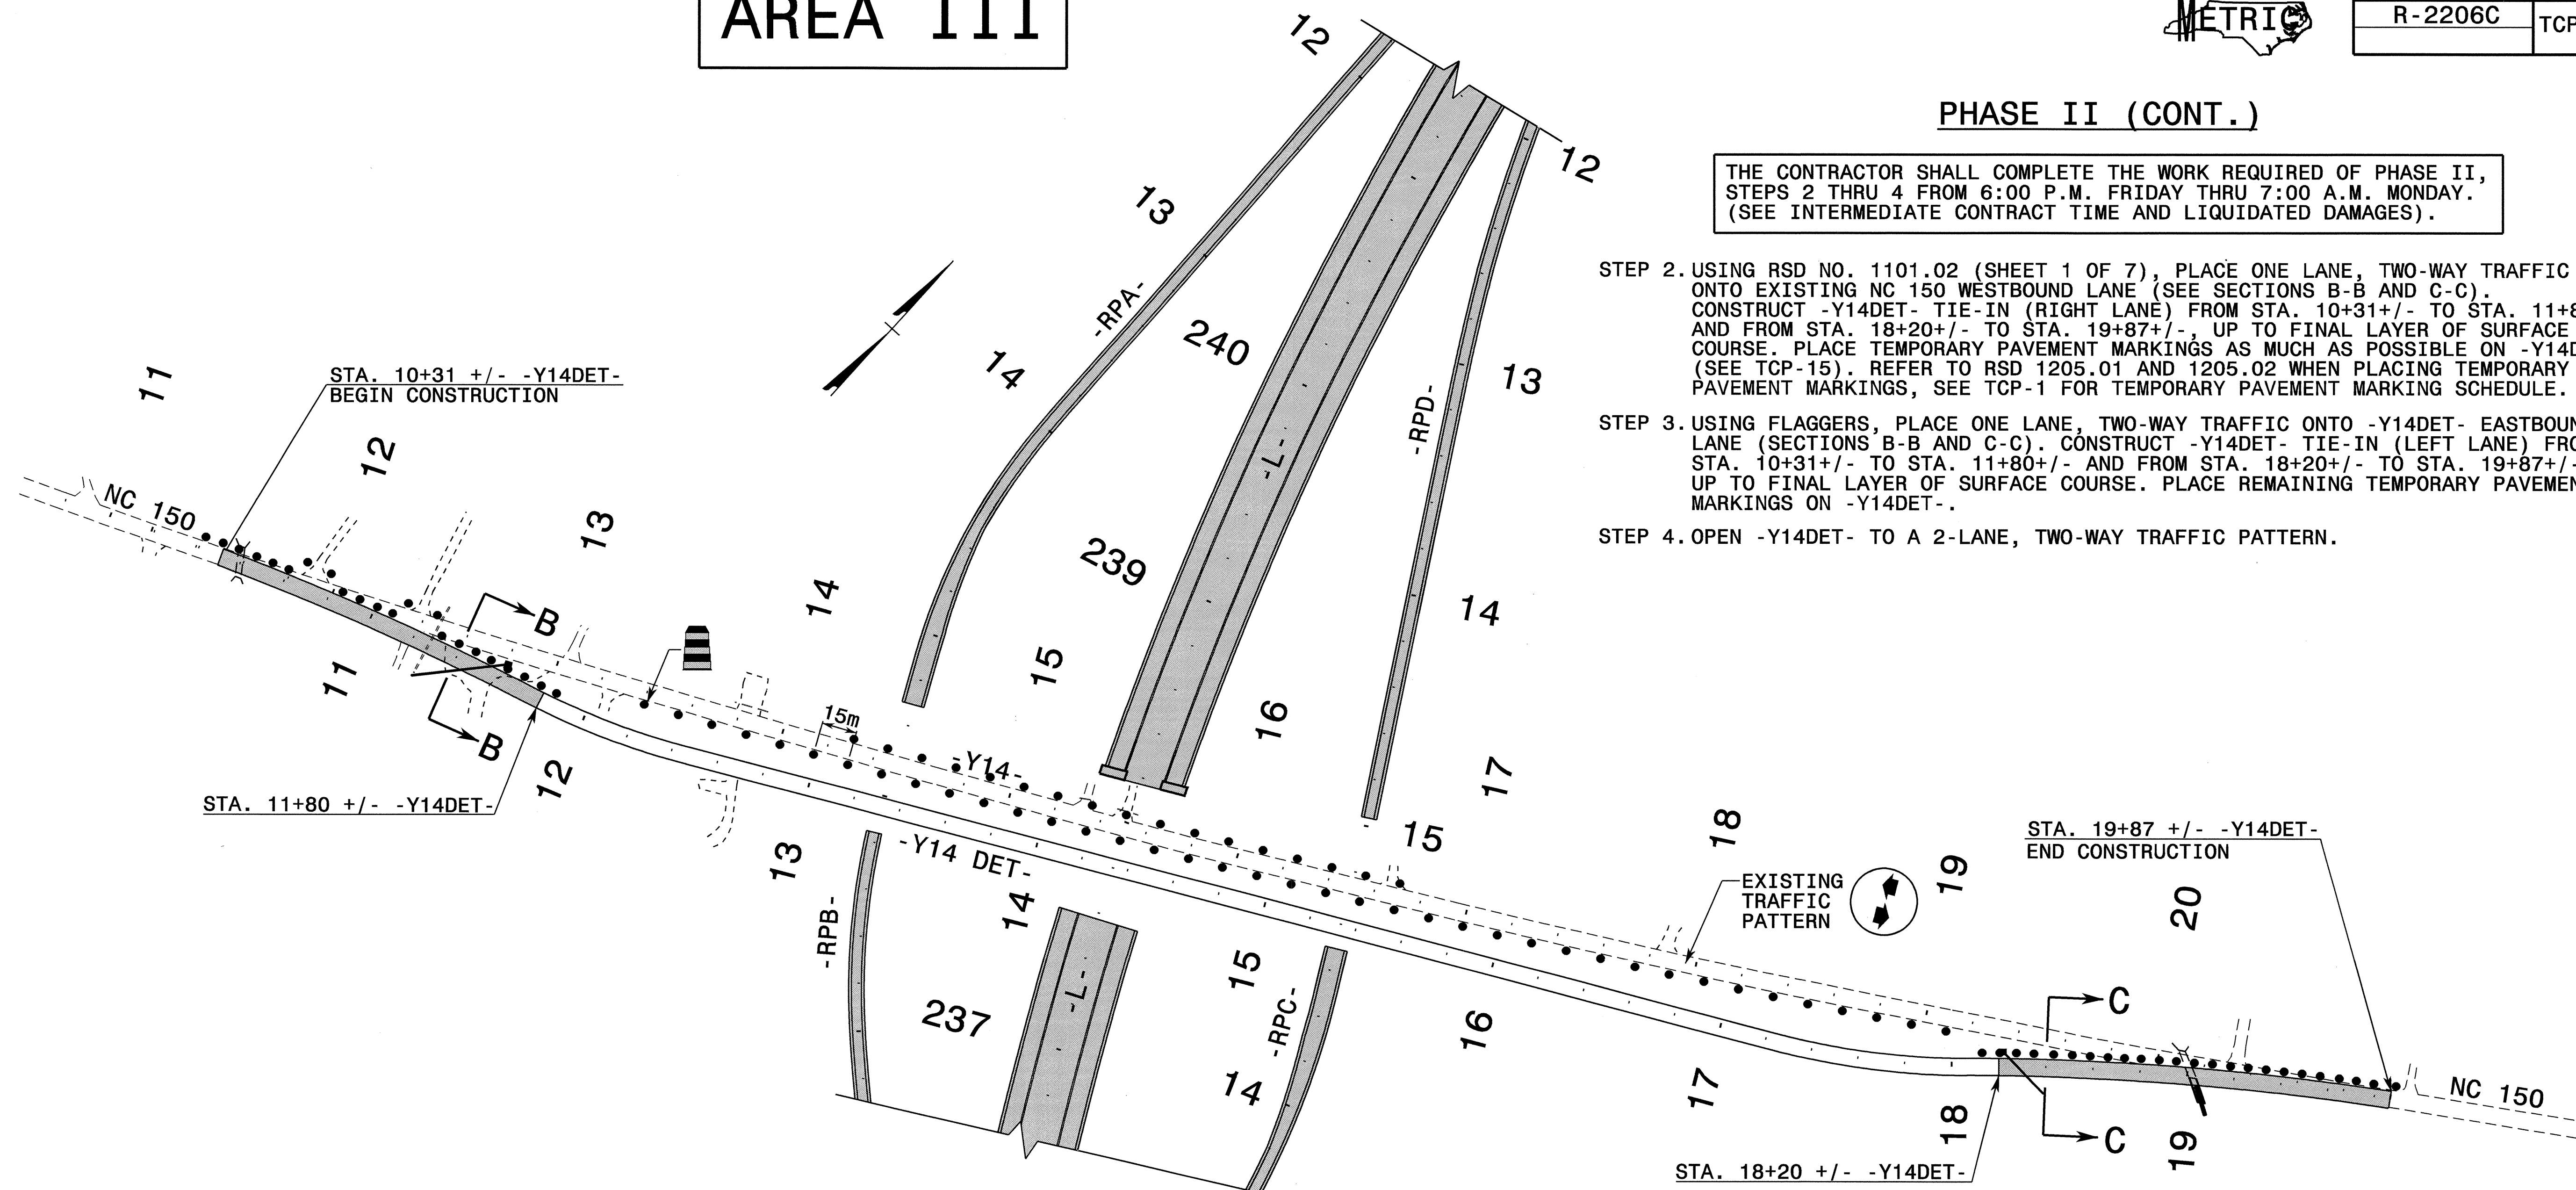

APPROVED: <i>[Signature]</i> DATE: <i>11/14/04</i>	<h3>AREA 3</h3> <h3>PHASE II (CONT.) DETAILS AND PHASING</h3>		REVISIONS					
			SCALE: 1:1500 DATE: 05-10-04 DWG. BY: SBC DESIGN BY: SBC REVIEWED BY: CLM	<table border="1"> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> </table>				

12-JUL-2004 15:50  
 R:\TCP\AREA3\REF\2206C.TC\AREA3-Tcp14A.dgn  
 SBC\GIS AT TELC206428
