


CULVERT PHASE I
CONSTRUCTION SEQUENCE (-Y-1 STA. 17 +48)

1. Construct channel relocation upstream of culvert, including all vanes and cross vanes, and install vegetation
2. Construct stilling basin #1 (120 CY volume)
3. Construct upstream most 94 feet of culvert

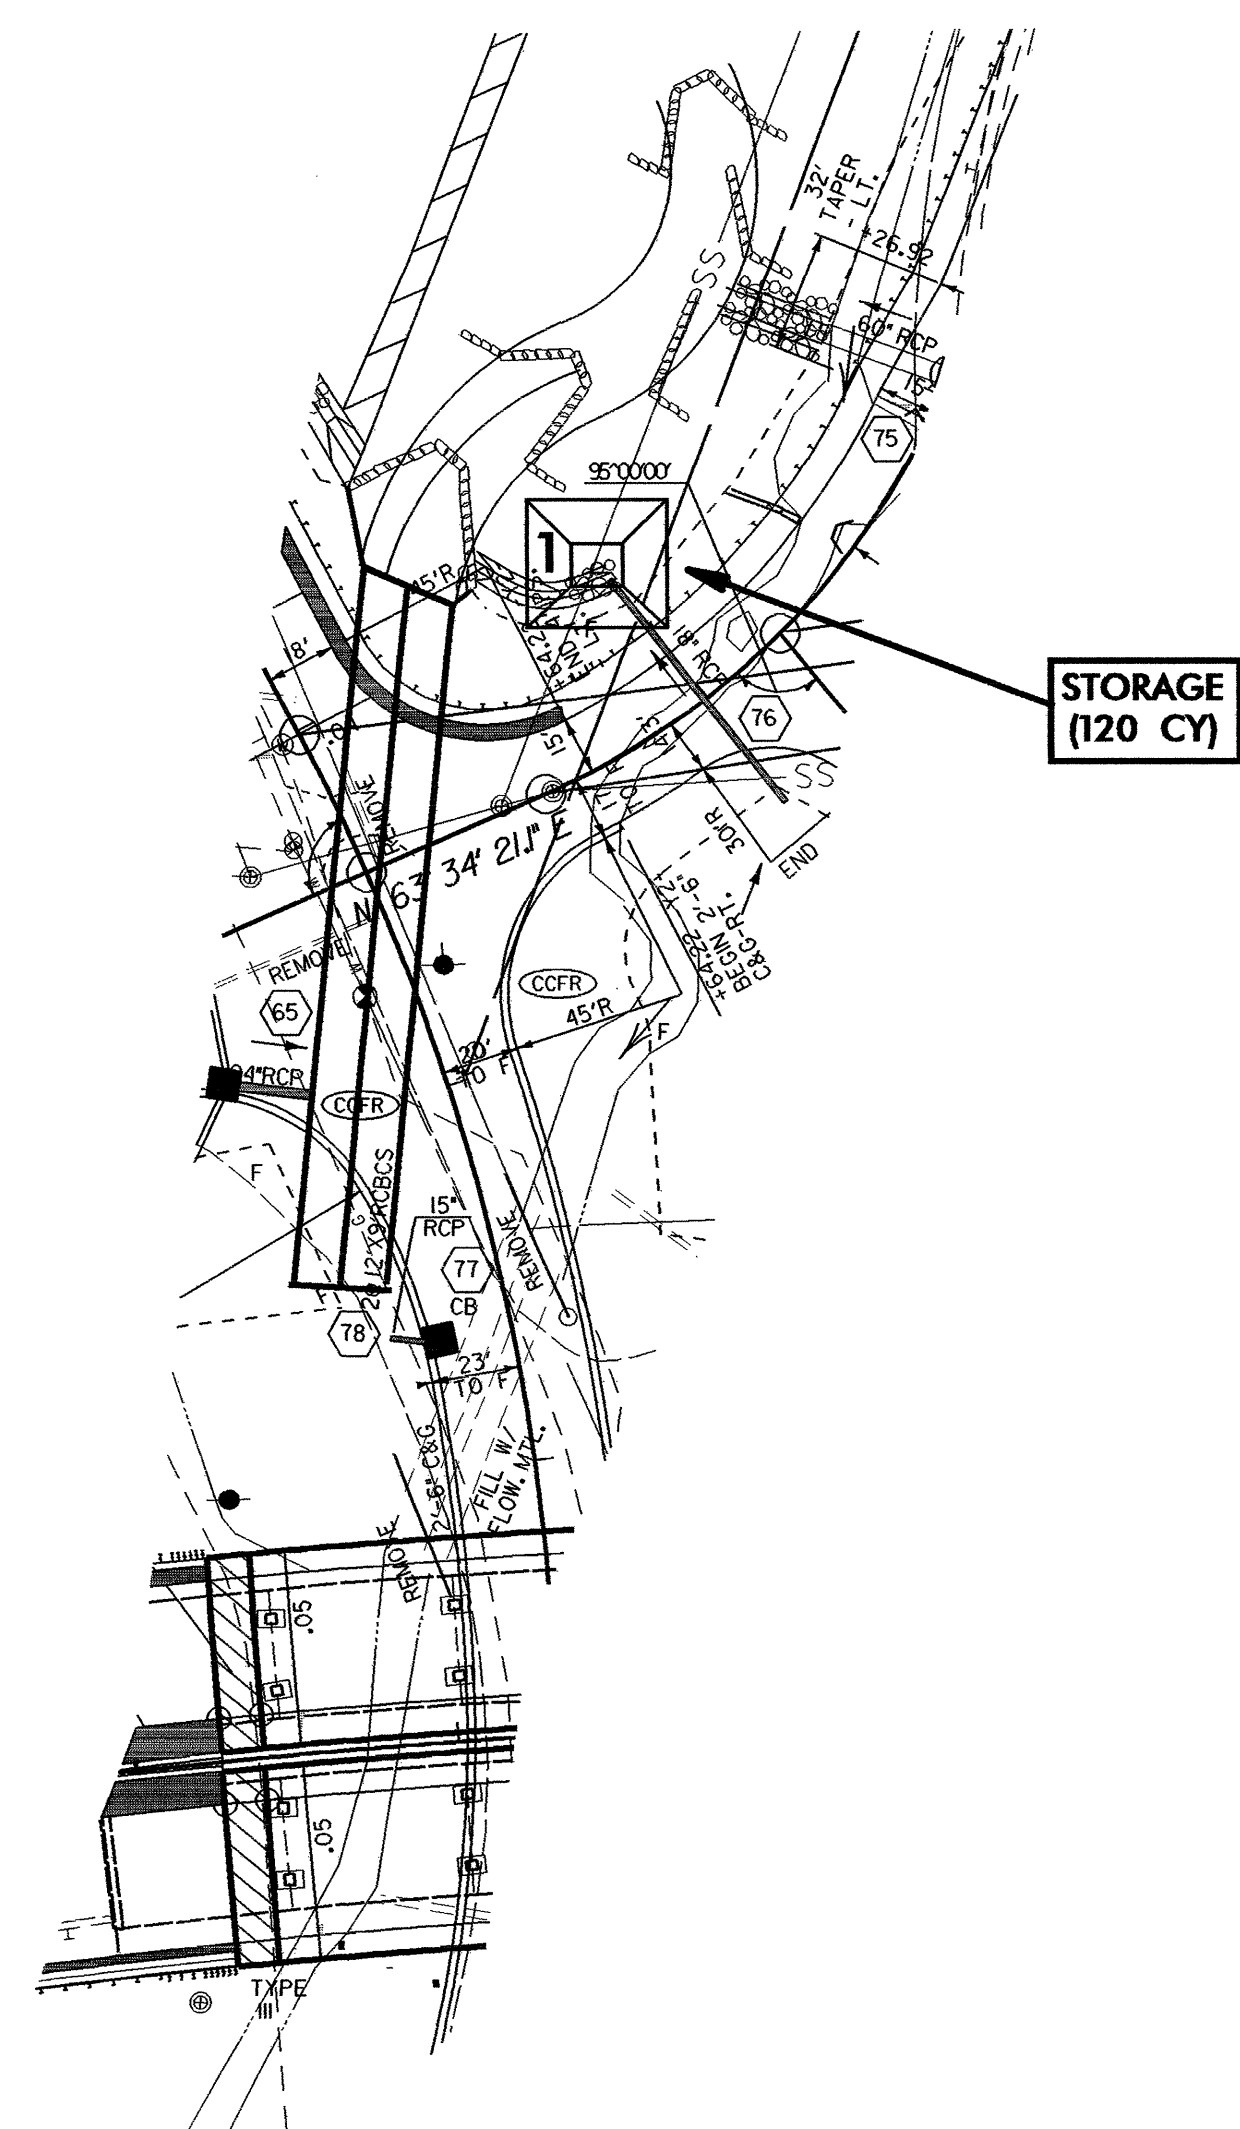

CULVERT PHASE I
CONSTRUCTION SEQUENCE (-Y-1 STA. 17 +48)

1. Install impervious dikes #1 and # 2
2. Install temporary 24" pipe
3. Once vegetation is established in channel relocation, divert water through the new channel and the newly constructed portion of the culvert
4. Construct temporary detour over new culvert
5. Construct stilling basin # 2 (600 CY volume)
6. Construct remainder of culvert
7. Complete roadway

