

# CULVERT CONSTRUCTION SEQUENCE


## -L- 104+66

### CULVERT CONSTRUCTION SEQUENCE - STAGE 1

1. CONSTRUCT TEMPORARY SKIMMER SEDIMENT BASINS.
2. UTILIZE SPECIAL STILLING BASIN(S) DURING CULVERT CONSTRUCTION AS NEEDED.
3. DIVERT WATER USING CLEAN WATER DIVERSIONS TO SYSTEM INSTALLED DURING CLEARING AND GRUBBING.
4. ENSURE BOXES INSTALLED DURING CLEARING AND GRUBBING ARE NOT ALLOWED TO RECEIVE FLOW.

### CULVERT CONSTRUCTION SEQUENCE - STAGE 2

1. UTILIZE SPECIAL STILLING BASIN(S) DURING CULVERT CONSTRUCTION AS NEEDED.
2. CONSTRUCT PROPOSED SYSTEM IN ACCORDANCE WITH THE PLANS.
3. REMOVE/RESHAPE CLEAN WATER DIVERSION TO NEWLY CONSTRUCTED PIPE AND ADJUST EROSION CONTROL MEASURES AS NECESSARY.
4. REMOVE ANY SPECIAL STILLING BASIN(S) AND STABILIZE AREAS AS NECESSARY.

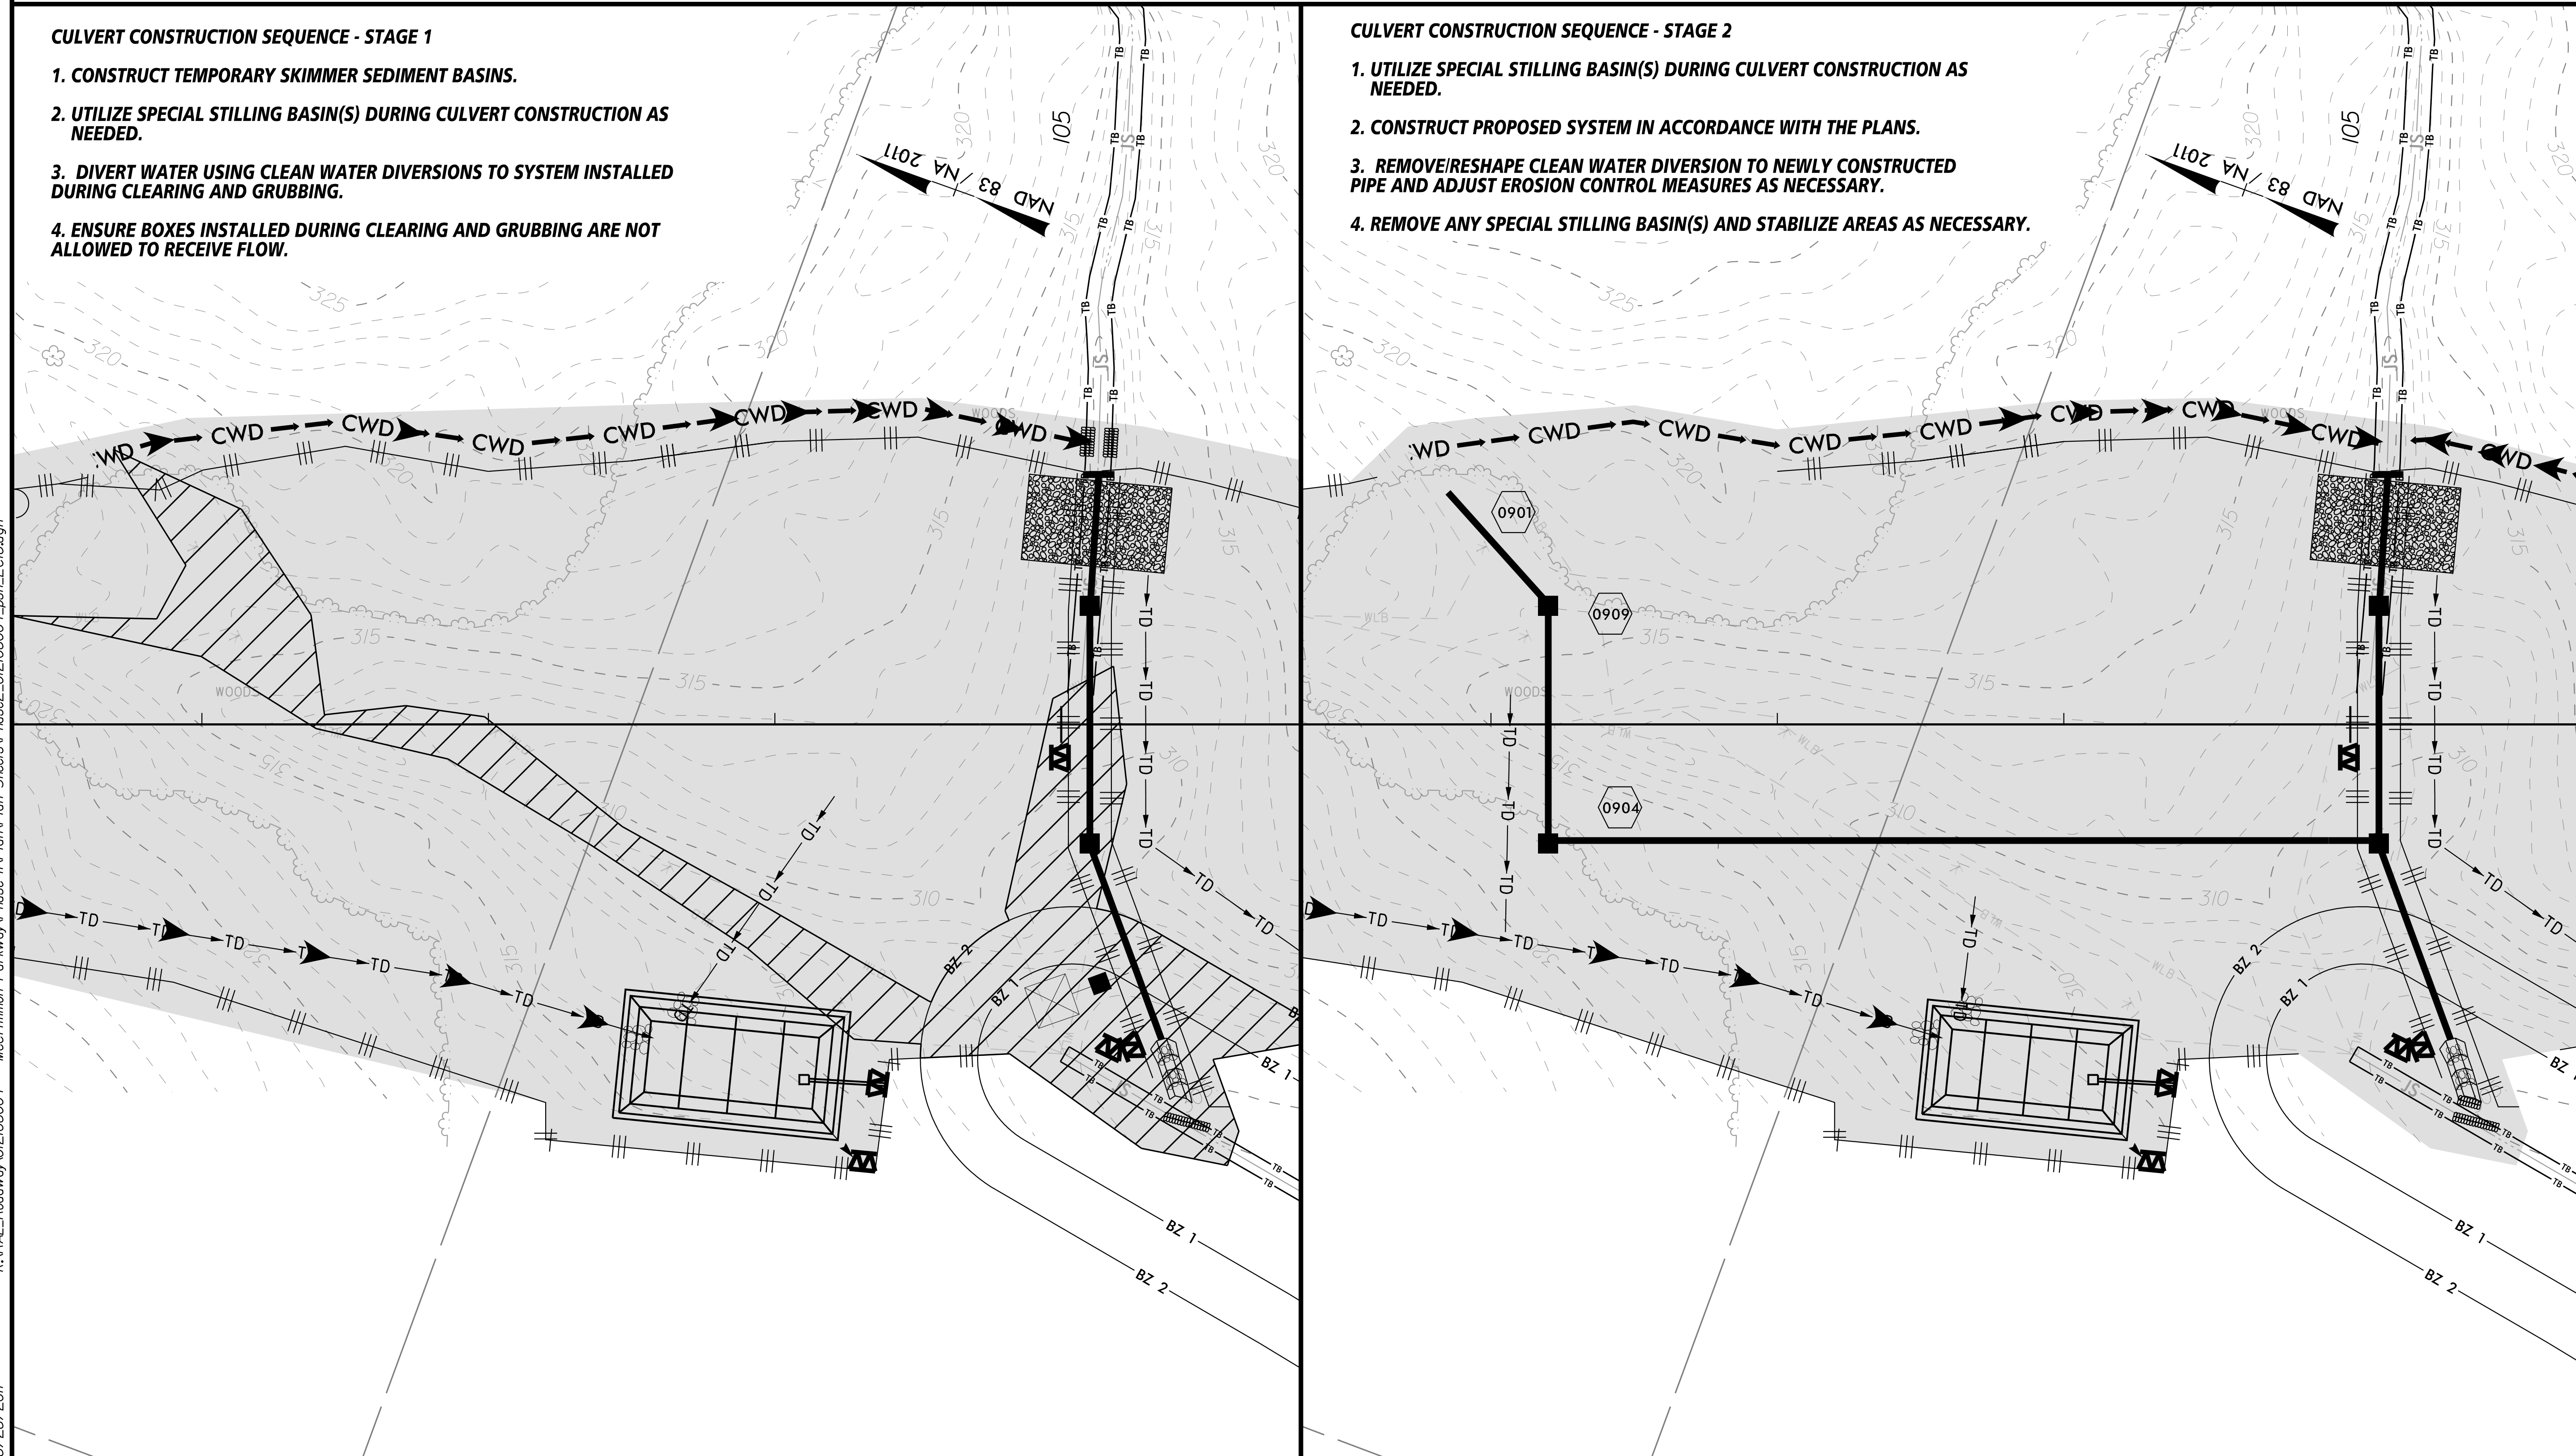

K:\RAL\_Roadway\012108004 - McCrimmon Parkway\Phase I\Plan\Plan Sheets\Phase2\_012108004\_posh\_EC18.dgn

8/28/2017
