


DATE: 2/27/2020
TIME: 3:46:03 PM

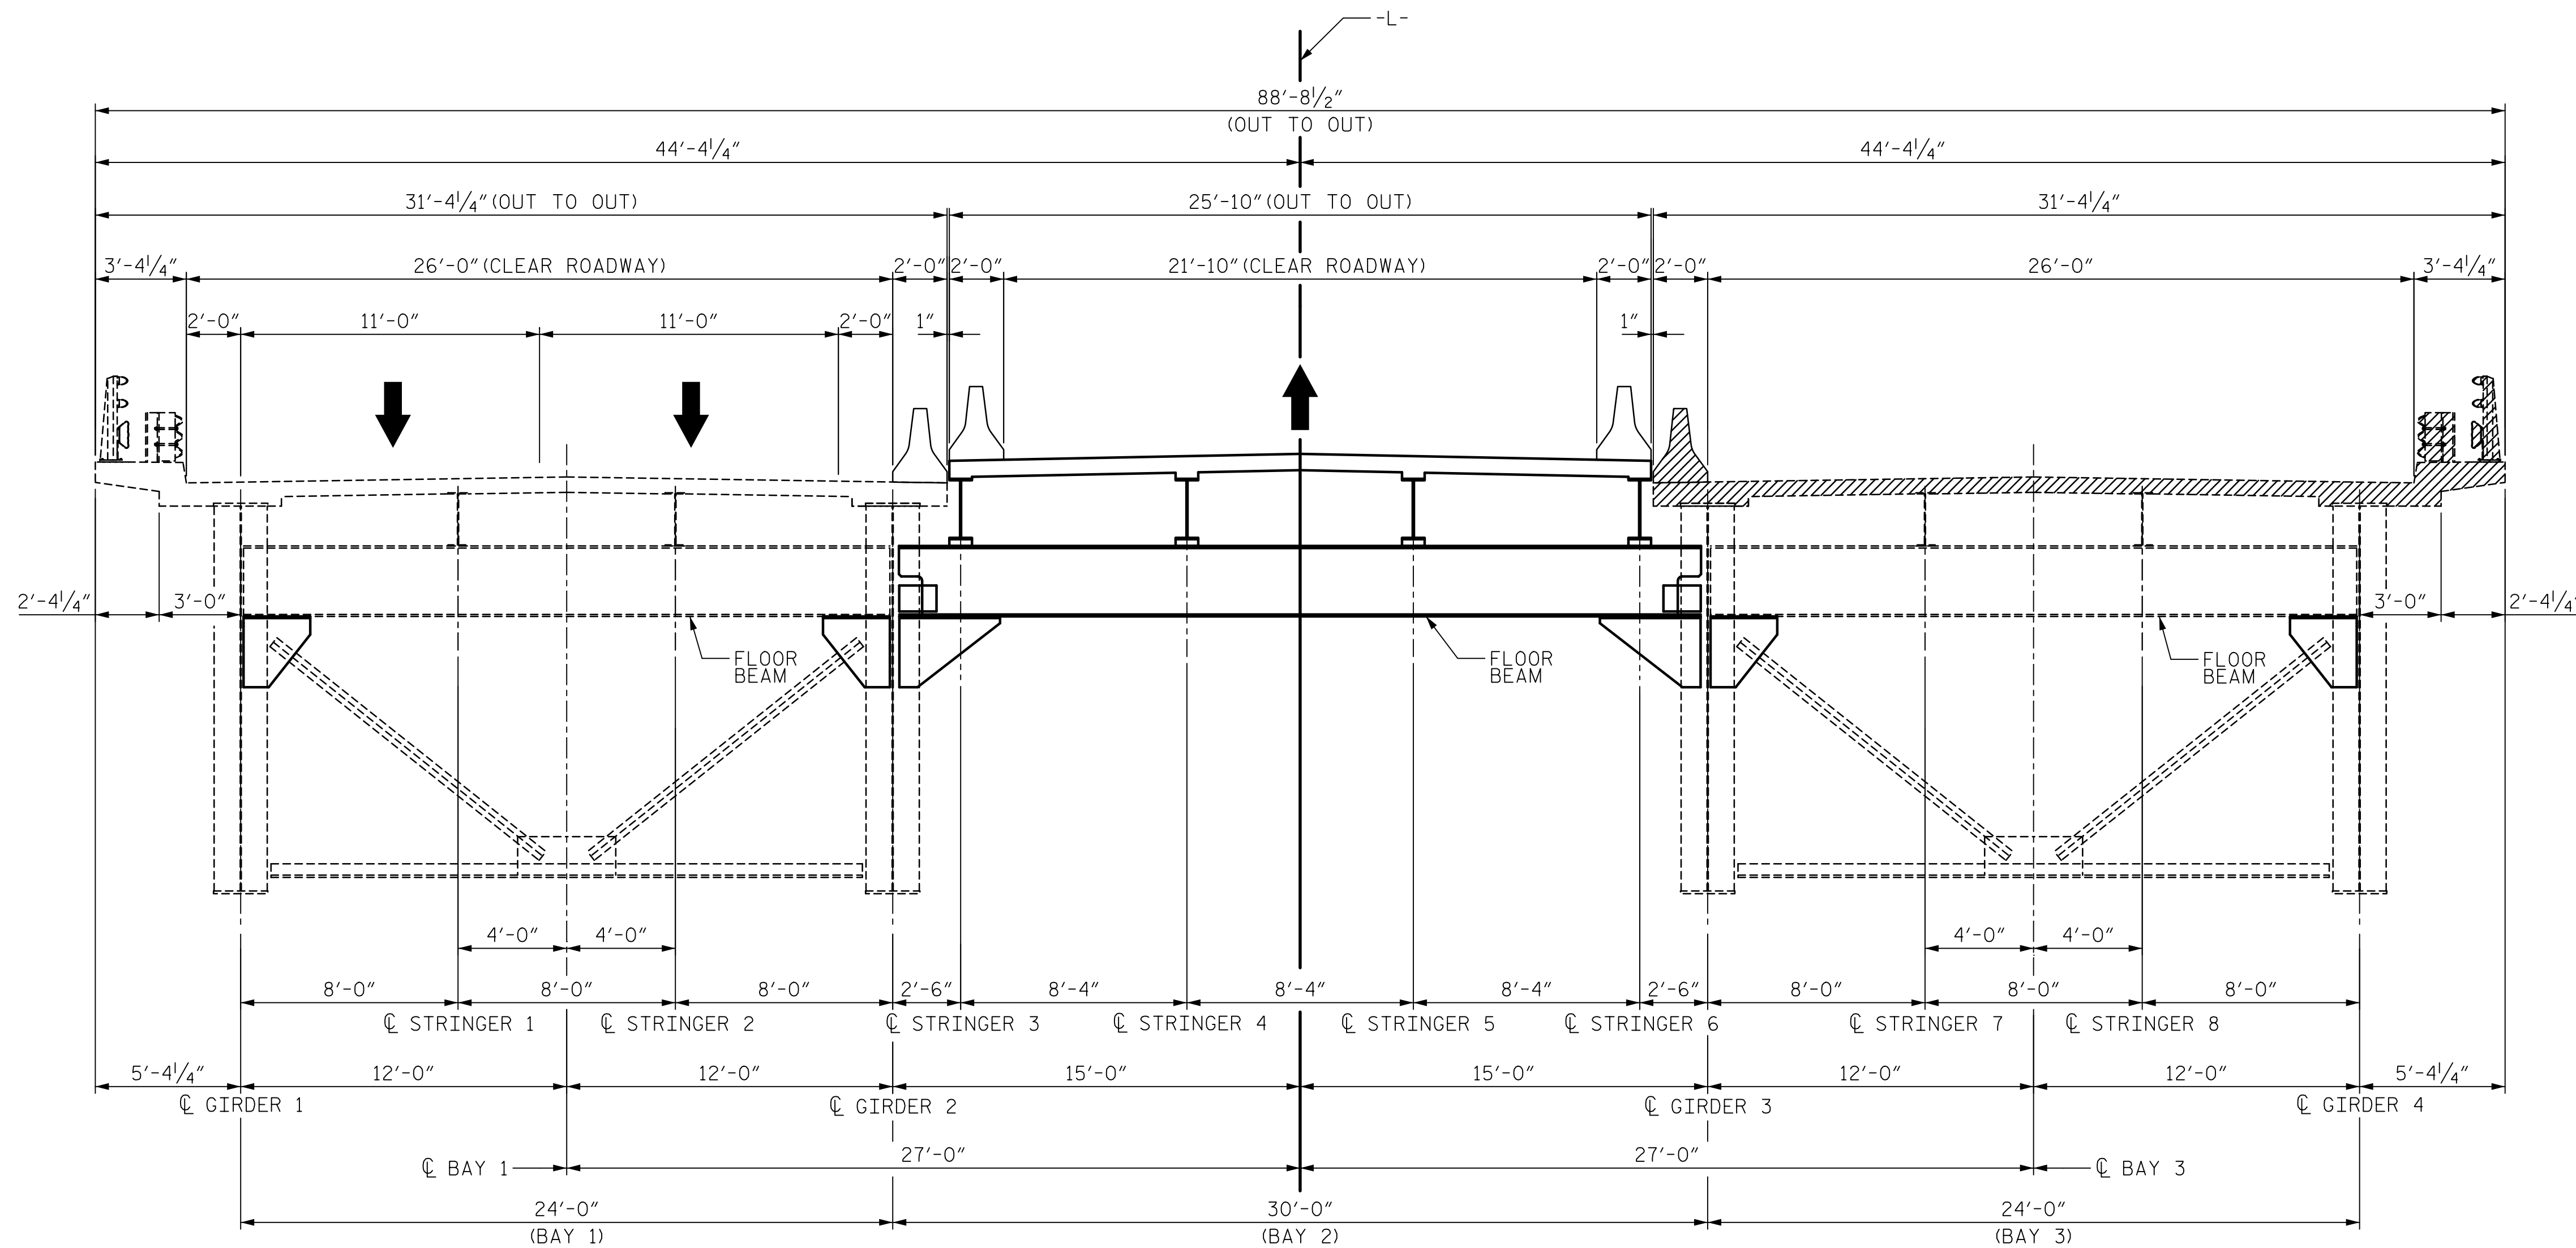

STAGE IIA CONSTRUCTION

5. INSTALL STRINGERS 3 AND 6. COMPLETE GIRDERS 2 AND 3 REHAB AND STRENGTHENING PRIOR TO PLACING BAY 2 DECK FORMWORK. COMPLETE WELD REPAIR #W3 ON GIRDER 4.
6. POUR BAY 2 CONCRETE DECK.
7. INSTALL ANCHORED TEMPORARY BARRIERS AT STRINGERS 3 AND 6.
8. SHIFT WESTBOUND TRAFFIC TO A SINGLE LANE IN BAY 2.
9. REMOVE ANCHORED TEMPORARY BARRIER IN BAY 3 THAT WAS INSTALLED IN STAGE IA. DEMOLISH EXISTING BARRIER AND CONCRETE DECK IN BAY 3.

PROJECT NO. 15BPR.20

HENDERSON COUNTY


STATION: 35+30.22 -L-

SHEET 6 OF 12

LEGEND

- EXISTING
- PROPOSED
- ▨ DEMOLITION

DRAWN BY : H.T. ROSEMOND DATE : 11/2018
 CHECKED BY : J.E. SLOAN DATE : 11/2018
 DESIGNED BY : N. BROWN/D. TUTTLE DATE : 11/2018
 DESIGN CHECKED BY : J. SLOAN/J. LIU DATE : 11/2018



STATE OF NORTH CAROLINA
DEPARTMENT OF TRANSPORTATION
RALEIGH

SUPERSTRUCTURE
& CONSTRUCTION
SEQUENCE
STAGE IIA

REVISIONS

NO.	BY:	DATE:	NO.	BY:	DATE:
1			3		
2			4		

SHEET NO.

S-16

TOTAL SHEETS
129

DOCUMENT NOT CONSIDERED
FINAL UNLESS ALL
SIGNATURES COMPLETED

USER: Hrc@rosemond.com Drawings\401_031_15BPR20_SML\DCS6.dgn
