

PHASING - BRIDGES 45 & 46

STAGE I

- STEP 1 - USING ROADWAY STANDARD DRAWINGS (RSD) 1101.01, SHEET 2 OF 3, PLACE ADVANCE WARNING SIGNS.
- STEP 2 - USING RSD 1101.02, SHEET 3 OF 14, CLOSE A SINGLE LANE AND ADJUST PAVEMENT MARKINGS ON BRIDGE AND APPROACHES AS NECESSARY FOR STAGE I SINGLE LANE PATTERN.
- STEP 3 - USING RSD 1101.02, SHEET 3 OF 14, CLOSE A SINGLE LANE AND PERFORM STAGE I BRIDGE WORK.
- STEP 4 - UPON COMPLETION OF BRIDGE WORK, INSTALL TEMPORARY MARKINGS AS NEEDED FOR STAGE II SINGLE LANE PATTERN.

STAGE II

- STEP 1 - USING RSD 1101.02, SHEET 3 OF 14 AND PEDESTRIAN CHANNELIZING DEVICES, CLOSE A SINGLE LANE AND SIDEWALK, IF NECESSARY, AND PERFORM STAGE II BRIDGE WORK.
- STEP 2 - UPON COMPLETION OF BRIDGE WORK, INSTALL TEMPORARY MARKINGS AS NEEDED TO RETURN TRAFFIC TO EXISTING PATTERN.
- STEP 3 - REMOVE ALL STAGE II TRAFFIC CONTROL DEVICES AND RETURN TRAFFIC TO EXISTING PATTERN.
- STEP 4 - USING RSD 1101.02, SHEET 12 OF 14, INSTALL FINAL PAVEMENT MARKING AND MARKERS.
- STEP 5 - REMOVE ANY REMAINING ADVANCE WARNING SIGNS AND DEVICES.

PHASING - BRIDGE 52


- STEP 1 - USING RSD 1101.01, SHEET 3 OF 3, PLACE ADVANCE WARNING SIGNS.
- STEP 2 - USING RSD 1101.02, SHEET 1 OF 14, CLOSE A SINGLE DIRECTION OF TRAFFIC USING FLAGGERS.
- STEP 3 - COMPLETE BRIDGE WORK REQUIRED. REPEAT STEP 2 AS NEEDED.
- STEP 4 - UPON COMPLETION OF BRIDGE WORK, REMOVE ALL ADVANCE WARNING SIGNS AND DEVICES.

I:\12\2022
 \dot\dfs\Root\0\NSPProj\Special\15BPR34\TrafficControl\15BPR34_TC_TMP_2.dgn
 User: jdbeaver1

APPROVED: *Kenneth C. Thornwell, Jr., P.E.*
 DATE: 01/12/2022

SEAL

DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED

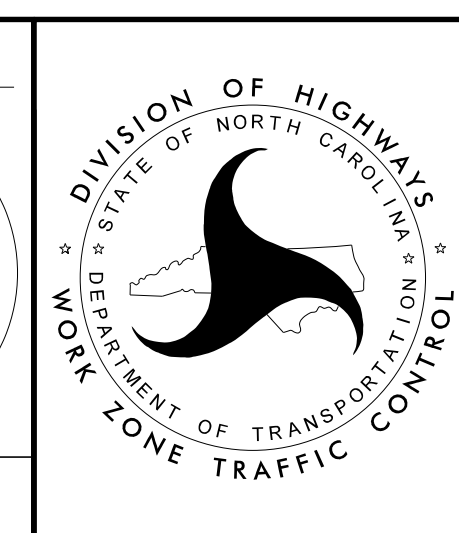

BRIDGE NOS. 45, 46, & 52

TRAFFIC CONTROL
PHASING
