

PHASE IV

NOTE: COMPLETE WORK DESCRIBED IN PHASE IV, SECTION 1 STEP 1 AND PHASE I, SECTION 2 STEP 1 CONCURRENTLY

SECTION 1 - -L- STA 465+00 TO STA 650+00, -Y4- AND -Y5

SECTION 2 - -L- FROM STA 650+00 TO STA 915+07, -Y1B-, -Y6- AND -Y7-

SECTION 1, PHASE IV, STEP 2 (TMP-95 TO TMP-102)

NOTE: STEP 2.A, 2.B AND 2.C MAY BE COMPLETED CONCURRENTLY

- A. 1. BEHIND BARRIER, PLACE TEMPORARY PCB ON THE OUTSIDE SHOULDER OF -DET-Y5RPB- AS SHOWN ON TMP-98
 - 2. USING RSD 1101.04, SHEET 4 OF 14 AS NEEDED, RESET TEMPORARY PCB ON THE OUTSIDE SHOULDER OF SB -L- FROM STA 687+75+/- TO -DET-Y5RPC- A SHOWN ON TMP-97 AND TMP-98
 - 3. USING RSD 1101.04, SHEET 4 AND 10 OF 14 AS NEEDED, PERFORM THE FOLLOWING:
 - * REMOVE TEMPORARY ANCHORED PCB FROM -Y5RPB- SHOWN ON TMP-90
 - * PLACE TEMPORARY PAVEMENT MARKINGS ON -DET-Y5RPB- AND SB -L- AS SHOWN ON TMP-96 THRU TMP-99
 - * SHIFT -5RPB- TRAFFIC TO TEMPORARY RAMP -DET-Y5RPB-
 - 4. USING RSD 1101.04, SHEET 4 OF 10 AS NEEDED, PERFORM THE FOLLOWING: (TMP-95 & TMP-96)
 - * EXTEND TEMPORARY PCB ON THE OUTSIDE SHOULDER OF SB -L- FROM STA 579+20 TO STA 574+60+/- AS SHOWN
 - * PLACE TEMPORARY PAVEMENT MARKING ON SB -L- FROM STA 563+15+/- TO 577+85+/- AS SHOWN
 - 4. BEHIND BARRIER, PERFORM THE FOLLOWING:
 - * CONSTRUCT SB -L- FROM STA 574+80+/- TO STA 603+00+/- AS SHOWN ON TMP-95 THRU TMP-97
 - * REMOVE EXISTING SB STRUCTURE AT BIG MARSH SWAMP (TMP-96)
 - * CONSTRUCT STAGE 3 OF PROPOSED STRUCTURE 770156 INCLUDING PROPOSED MEDIAN BARRIER (TMP-96)
 - * REMOVE TEMPORARY PAVEMENT ON THE OUTSIDE SHOULDER OF -Y5RPB- AND SB -L- AS SHOWN ON TMP-97 AND TMP-98
 - B. 1. BEHIND BARRIER, PLACE TEMPORARY ANCHORED PCB ON THE OUTSIDE SHOULDER OF -Y5RPA- FROM STA 10+00+/- TO STA 23+52+/- AS SHOWN ON TMP-99 AND TMP-100
 - 2. USING TRAFFIC SHIFTS, PERFORM THE FOLLOWING:
 - * RESET TEMPORARY ANCHORED PCB FROM STA 632+50+/- TO 635+55+/- AS SHOWN ON TMP-100 AND TMP-101 AT -Y5RPA-
 - * PLACE TEMPORARY PAVEMENT MARKINGS FOR TEMPORARY RAMP -Y5RPA- AS SHOWN ON TMP-99 THRU TMP-101
 - * SHIFT -Y5RPA- TO NEW TEMPORARY TRAFFIC PATTERN
 - 3. BEHIND BARRIER, CONSTRUCT THE FOLLOWING:
 - * RIGHT SIDE OF -Y5RPA- AS SHOWN ON TMP-99 AND TMP-100
 - * LEFT SIDE OF SB -L- FROM STA 632+51+/- TO STA 634+00+/- AS SHOWN ON TMP-100 TO TMP-101
 - * "GAS", "FOOD" AND "LODGING" SIGNS (TMP-99 AND TMP-100) (SEE FINAL SIGNING PLANS)
 - * OVERHEAD SIGN ASSEMBLY "E" (TMP-100) (SEE FINAL SIGNING PLANS)
- BEHIND BARRIER AND USING RSD 1101.02, SHEETS 1 AND 2 AND FLAGGERS AS NEEDED, COMPLETE CONSTRUCTION OF -Y5RAB- (TMP-99)
- AWAY FROM TRAFFIC BEGIN INSTALLATION OF PROPOSED GUIDE SIGNS FOR PROPOSED ROUNDABOUT (TMP-99 AND TMP-113) (SEE FINAL SIGNING PLANS)
- C. BEHIND BARRIER, COMPLETE CONSTRUCTION OF THE FOLLOWING:
 - * MEDIAN OF -L- FROM STA 605+30+/- TO STA 608+00+/- AS SHOWN ON TMP-98
 - * MEDIAN AND SB -L- FROM STA 608+00+/- TO BRIDGE APPROACH SLAB AT STRUCTURE 770159 AS SHOWN ON TMP-98 AND TMP-99
 - * MEDIAN AND SB -L- FROM BRIDGE APPROACH SLAB AT STRUCTURE 770159 TO STA 625+00+/- AS SHOWN ON TMP-98 AND TMP-99


PHASE IV, SECTION 1, STEP 3 CONTINUED ON TMP-3V

PLANS PREPARED FOR THE NCDOT BY:

M MOTT MACDONALD 1 & E, LLC
1101 HAYNES STREET, SUITE 101
RALEIGH, NC 27604


M MOTT MACDONALD NC LICENSE NO. F-0669

APPROVED: *Lori D. Stoucho*
DATE: 4/29/2022



DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED


APPROVED: *J.W. Woolard, Jr.*
DATE: 4/29/2022



DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED



Stantec Consulting Services Inc.
801 Jones Franklin Road
Suite 300
Raleigh, NC 27606
Tel. 919.851.6866
Fax. 919.851.7024
www.stantec.com
License No. F-0672

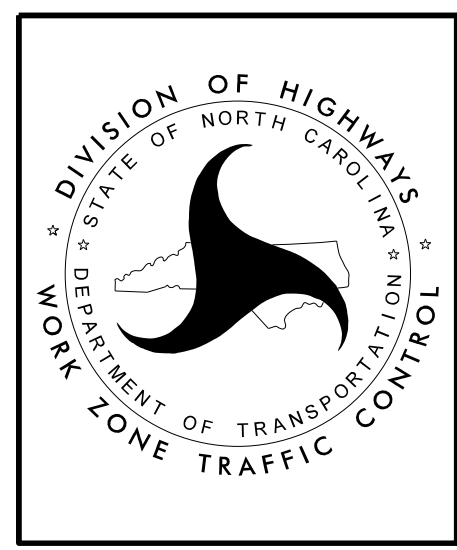

TEMPORARY TRAFFIC CONTROL PHASING PHASE IV

3/29/2022 G:\50100191_NV5_1-5987B\TrafficControl\Tc\200_088_1-5987B-TMP-3U_Phase IV_220315.dgn User:ST086227
