


PHASE III

- STEP 1:** USING RSD 1101.02, SHEET 3 OF 14 AND TMP-10 THRU TMP 13 REMOVE THE TEMPORARY ROAD CLOSURE FOR NORTHBOUND TRAFFIC AND SHIFT TRAFFIC TO THE OUTSIDE LANES ON US 13 NORTH AND SOUTH BOUND. THIS STEP WILL INVOLVE: REMOVAL OF TEMPORARY ROAD CLOSURE DEVICES & MARKINGS FROM PHASE II, INSTALLATION OF TEMPORARY PAVEMENT MARKINGS SAME PATTERN AS PHASE 1, RELAP EXISTING GUARD RAIL AT -L- STA 24+35+/- AND -L- STA 30+79 +/-, AND ADJUSTMENT OF SOUTHBOUND MEDIAN GUARDRAIL TO ITS FINAL LOCATION.
- STEP 2:** USING RSD 1101.04, PERFORM THE FINAL GRADING AND DRAINAGE WORK IN THE MEDIAN. USING RSD 1101.02, MILL (1.5") NORTHBOUND PAVEMENT FROM -L- STA. 18+78+/- TO 22+96+/- AND -L- STA. 33+21+/- TO 36+39+/-.
- STEP 3:** USING RSD 1101.02 SHEET 3 OF 14, PLACE THE FINAL LIFT OF SURFACE COURSE AND FINAL PAVEMENT MARKINGS PER B-4786 ROADWAY PLANS AND FINAL PAVEMENT MARKING PLANS RETURN THE TRAFFIC SIGNAL BACK TO ITS INITIAL CONDITION REMOVE ALL REMAINING TRAFFIC CONTROL DEVICES AND OPEN -L- TO THE FINAL TRAFFIC PATTERN.

APPROVED: _____
DATE: 3/21/2022 | 10:43

DocuSign
SEAL
03392
REGISTERED PROFESSIONAL ENGINEER
CLAYTON T. REGISTER

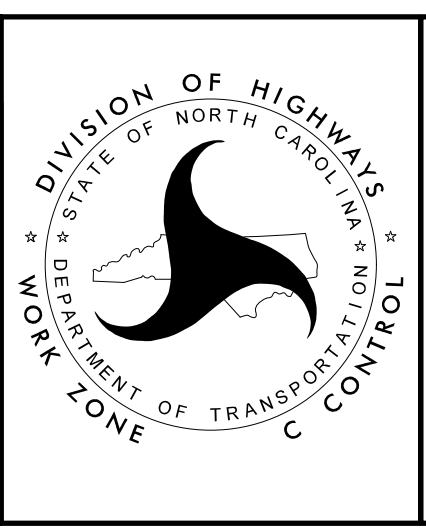

**OVERVIEW
AND PHASING
PHASE III
DETAIL**

**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**
