


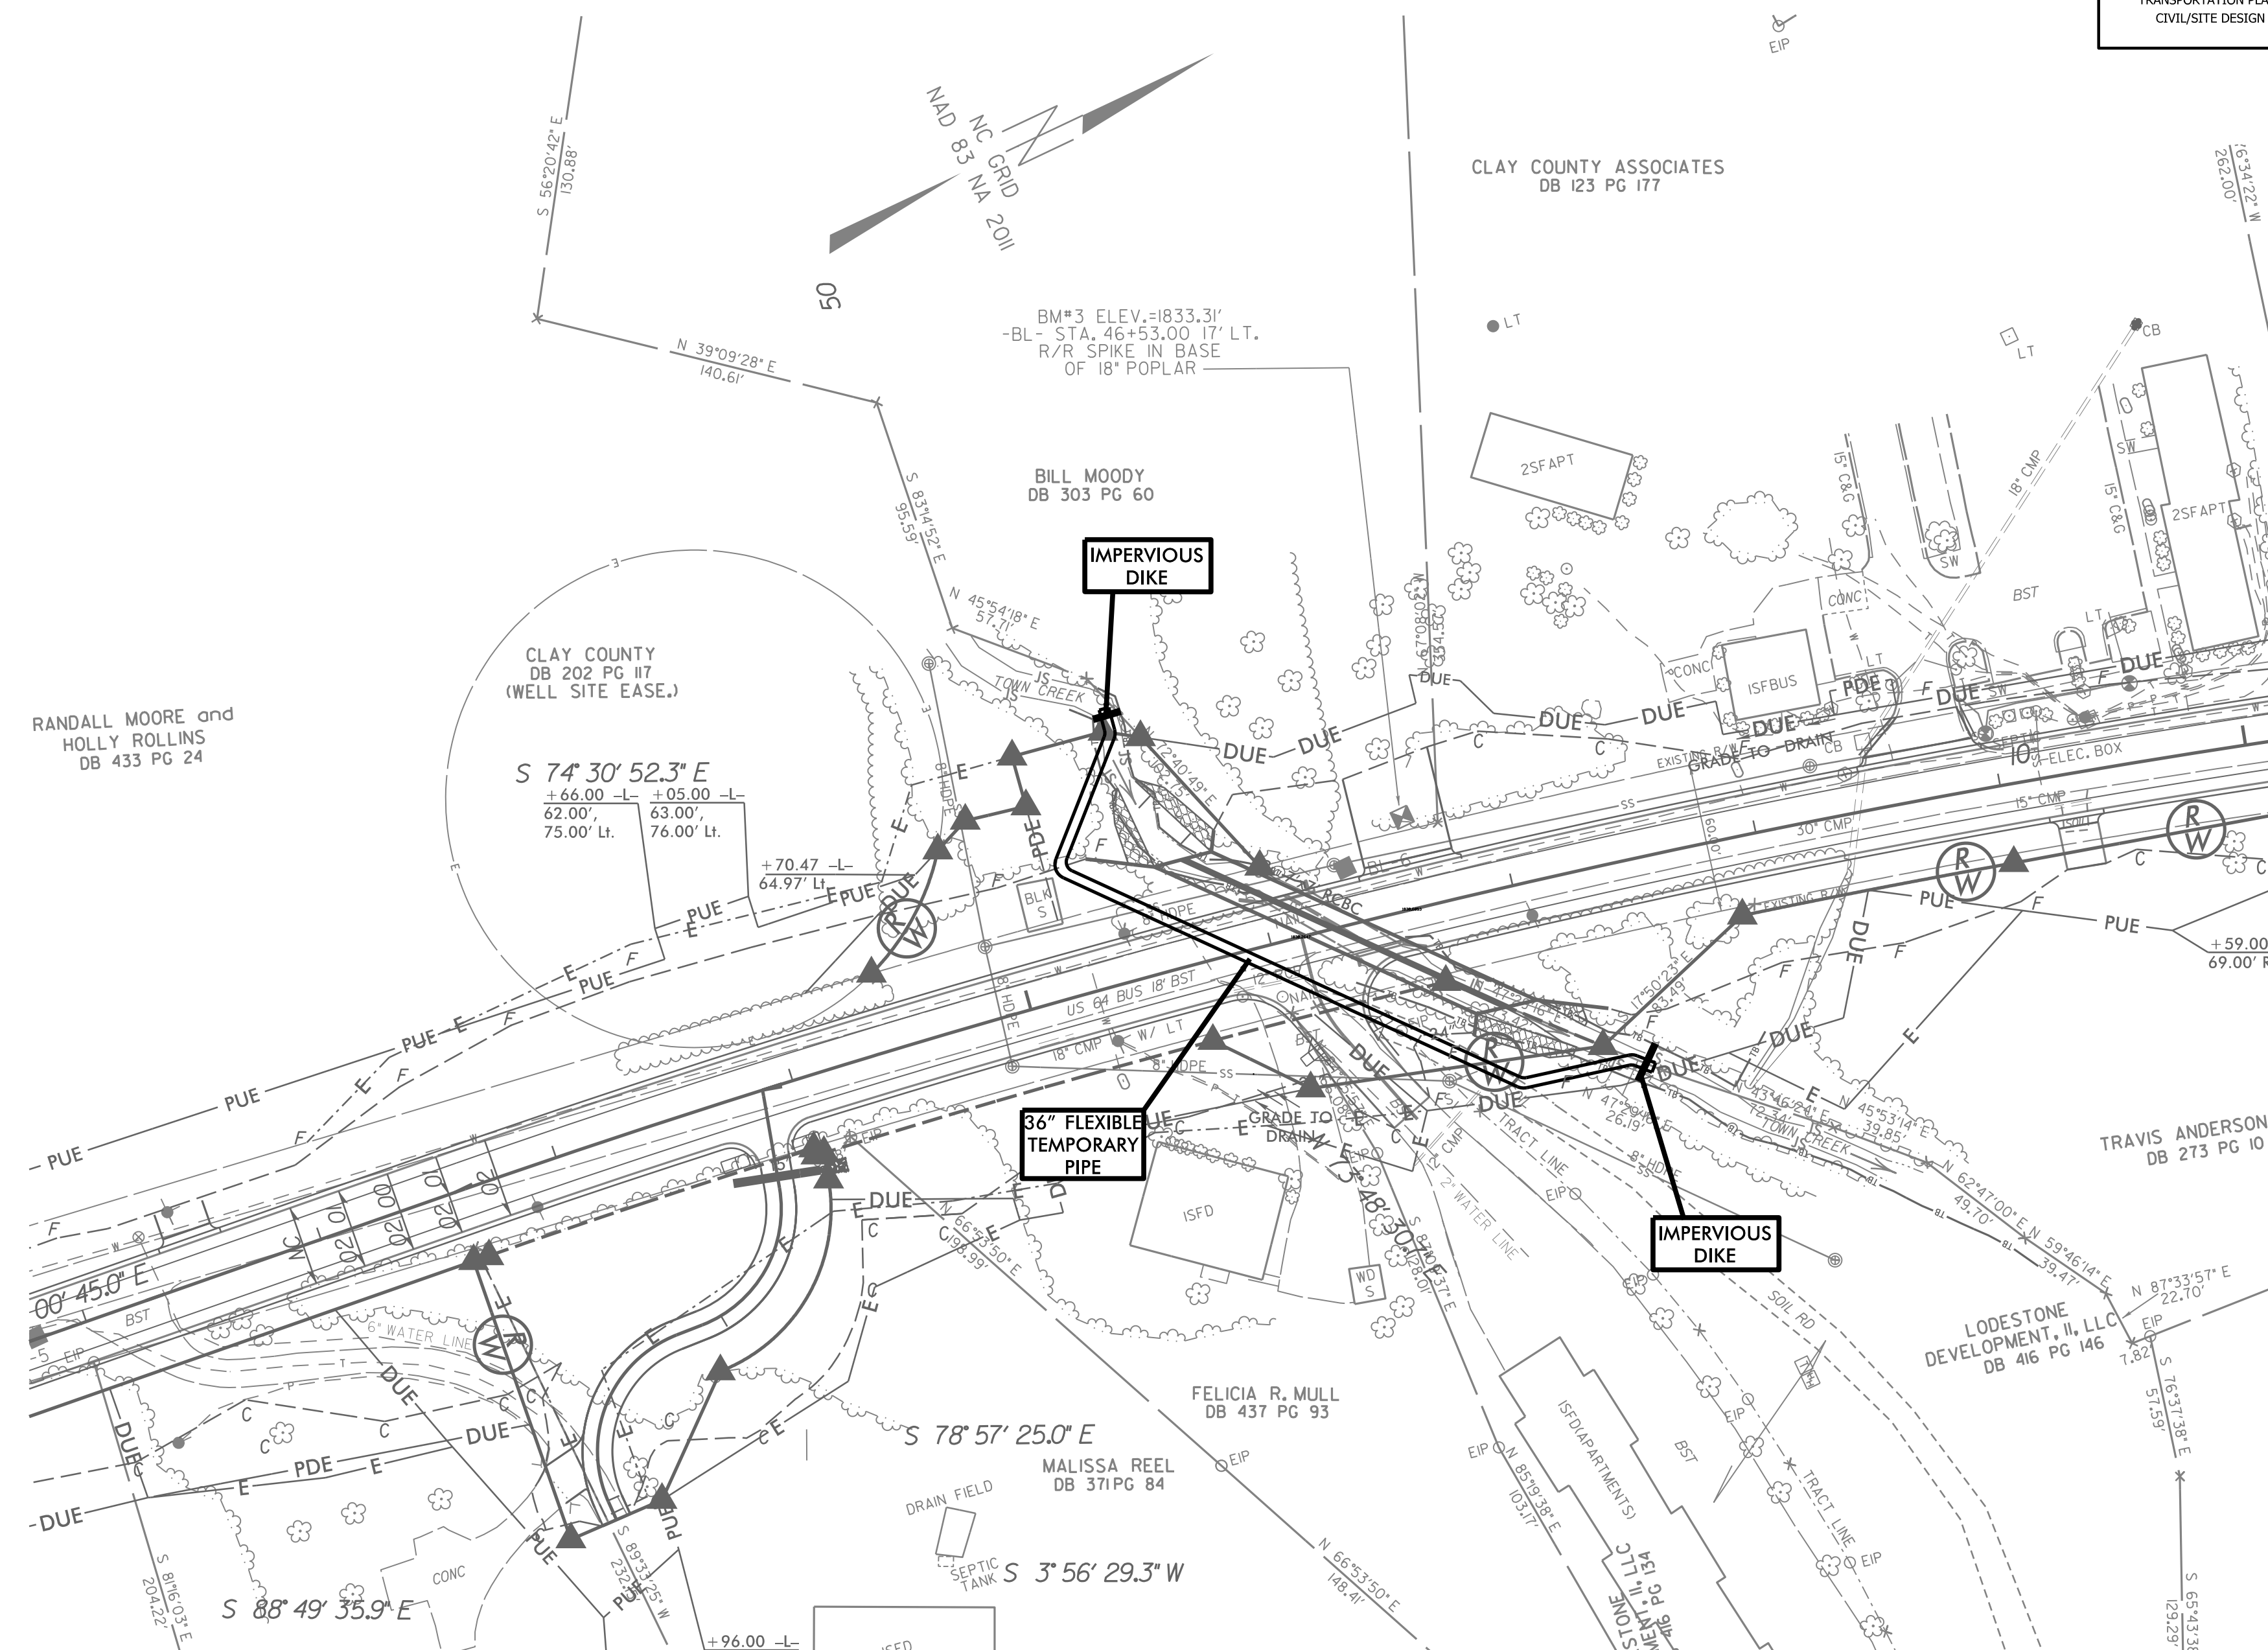

CULVERT CONSTRUCTION SEQUENCE STA. 51+26 -L-

INSTALL EROSION CONTROL C&G PHASE MEASURES FOR THIS SITE
PRIOR TO COMMENCING CULVERT WORK. (NOT SHOWN FOR CLARITY).

1. UTILIZE SPECIAL STILLING BASIN(S) AS NEEDED THROUGHOUT CULVERT CONSTRUCTION.
2. CONSTRUCT IMPERVIOUS DIKES AND INSTALL 36" FLEXIBLE TEMPORARY PIPE, DIVERTING FLOW.
3. REMOVE EXISTING CULVERT
4. CONSTRUCT PROPOSED CULVERT BARRELS, WING WALLS AND UPSTREAM AND DOWNSTREAM CHANNEL IMPROVEMENTS
5. REMOVE IMPERVIOUS DIKES AND TEMPORARY PIPE, ALLOWING NORMAL FLOW THROUGH THE CULVERT.
6. BACKFILL AND COMPLETE ROADWAY CONSTRUCTION
