


CULVERT CONSTRUCTION SEQUENCE STA. 38+74 -L-

1"=20'

PROJECT REFERENCE NO.		SHEET NO.
R-5739		EC-6A/CONST.6
RW SHEET NO.		
ROADWAY DESIGN ENGINEER		HYDRAULICS ENGINEER

PHASE I

1. INSTALL IMPERVIOUS DIKES #1, #2, #3, & #4 AND 15 INCH TEMPORARY PIPES #1 & #2.
2. DEWATER CONSTRUCTION AREA INTO SKIMMER BASINS #6.1, #6.2, #6.3, AND SPECIAL STILLING BASIN(S) AS REQUIRED.
3. REMOVE EXISTING HEADWALLS AND WINGWALLS.

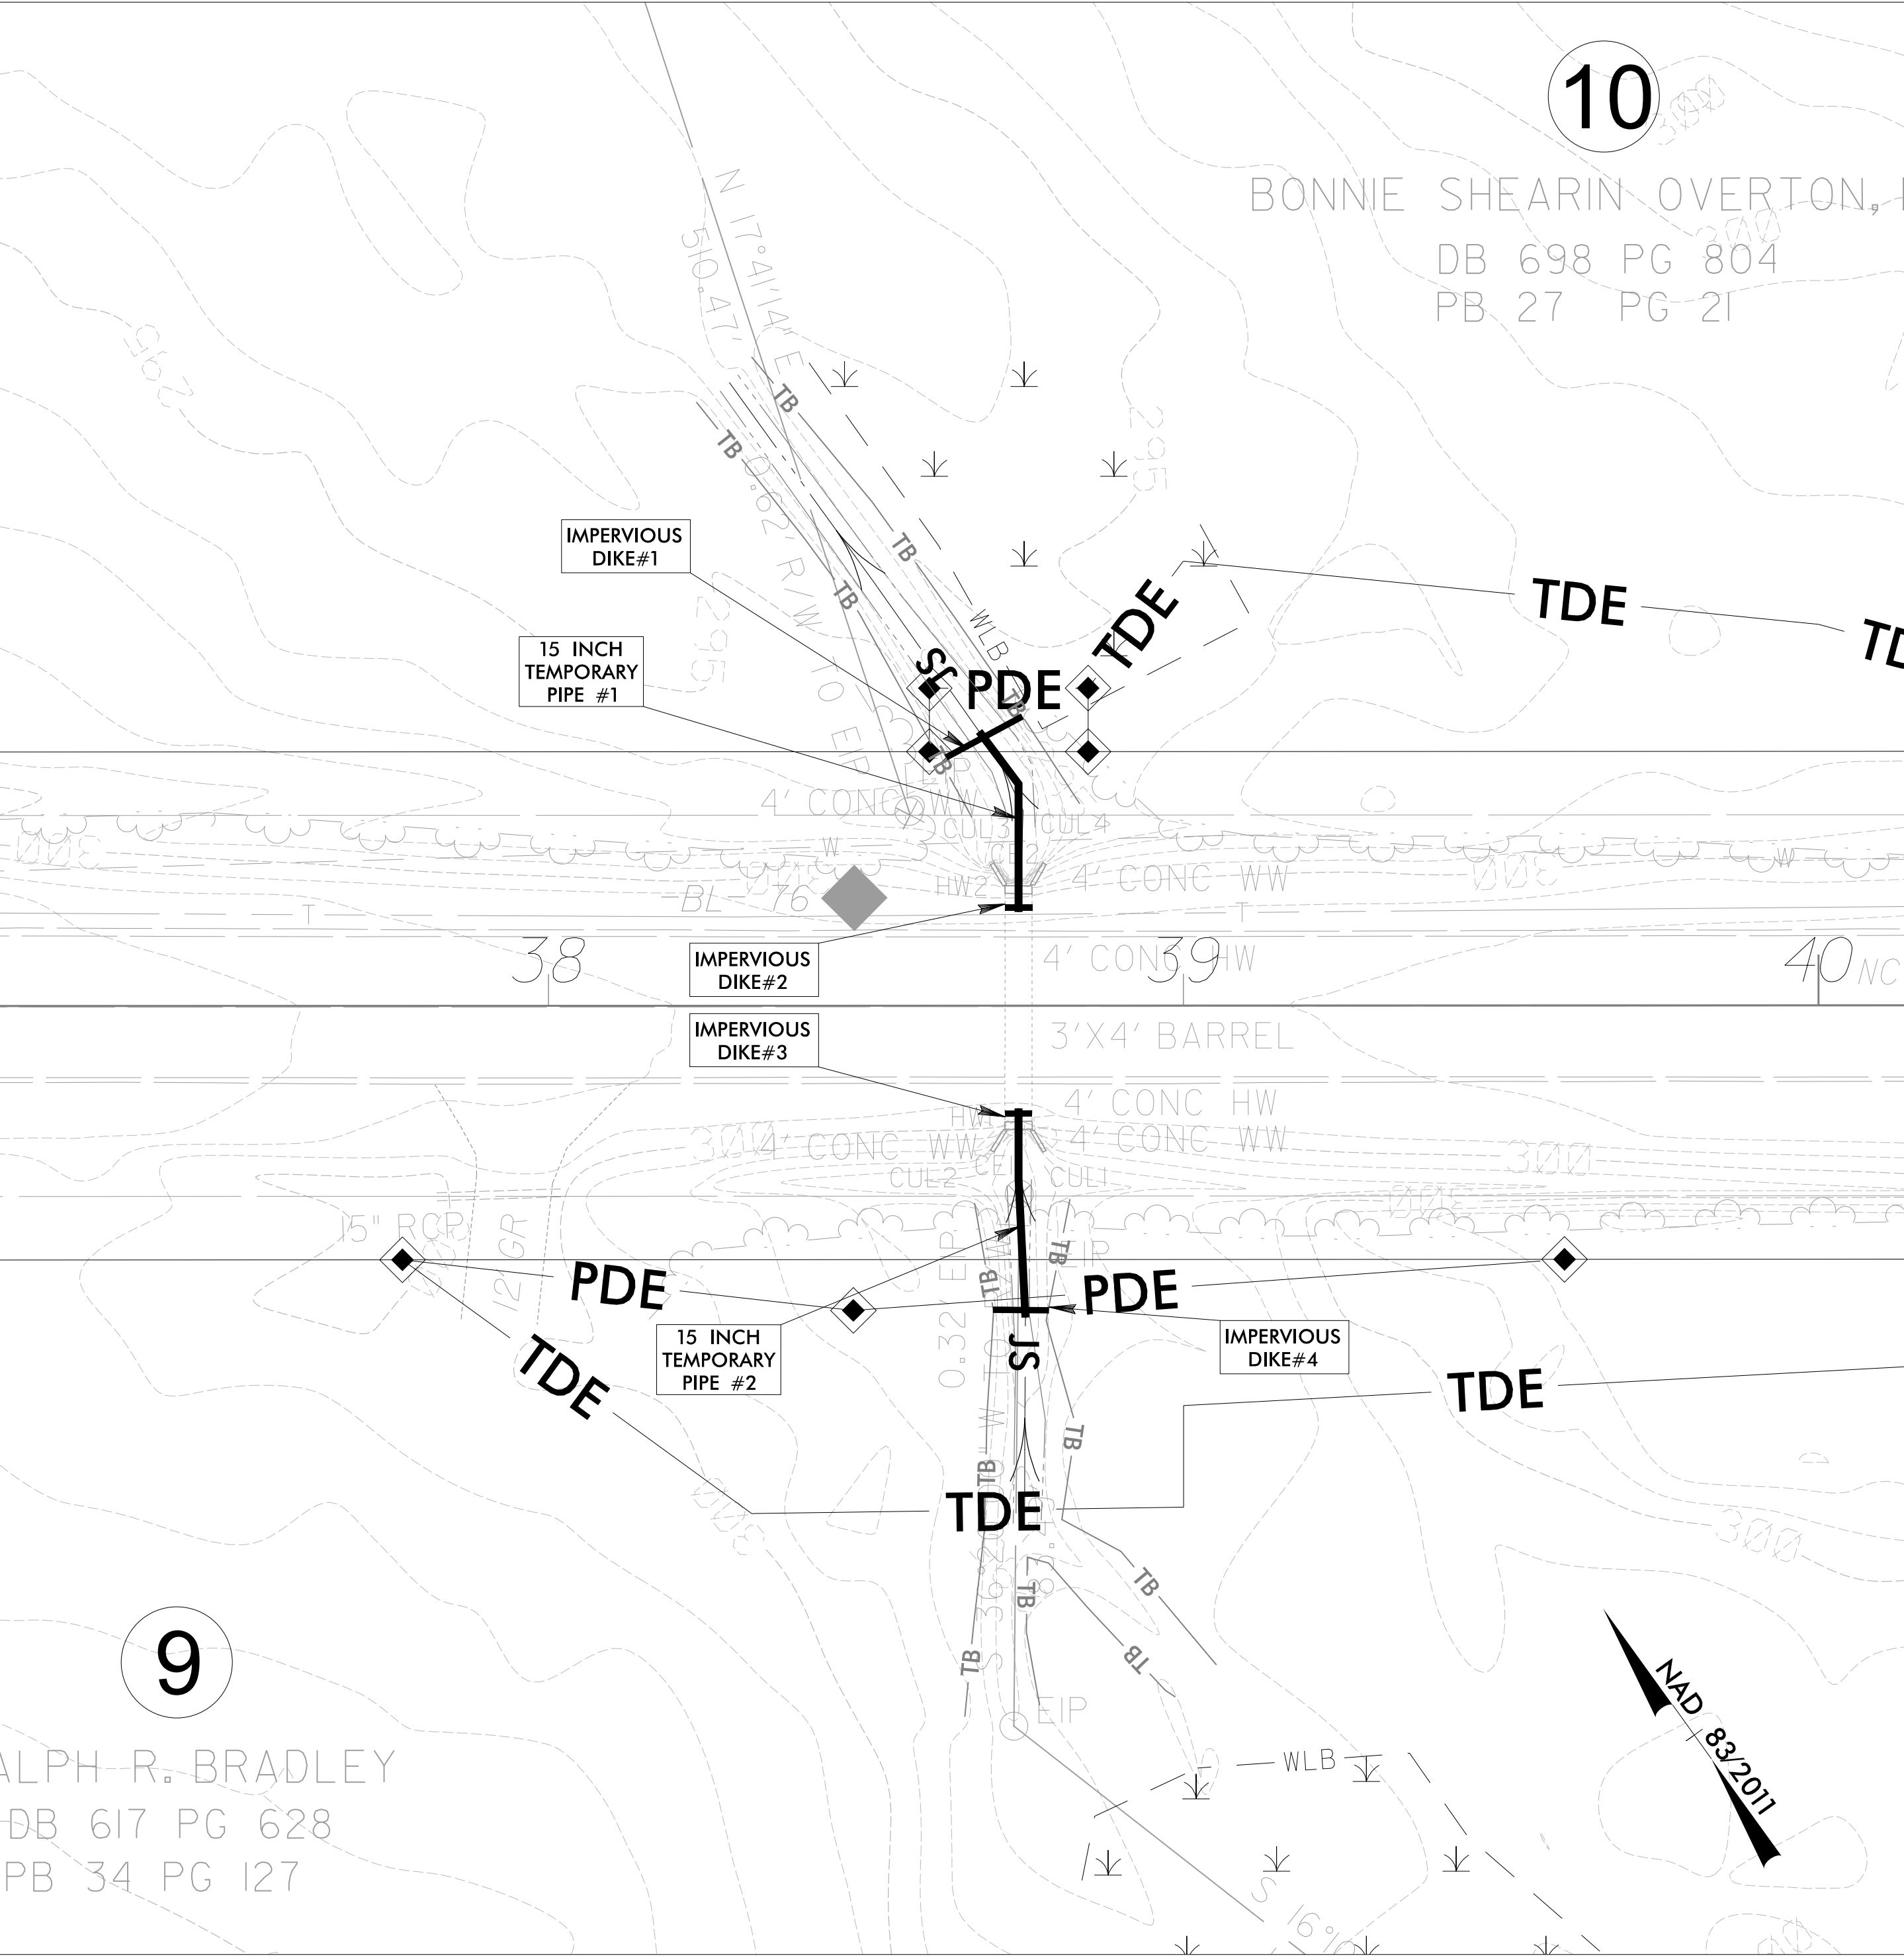

PHASE II

1. CONSTRUCT PROPOSED CULVERT EXTENSIONS, HEADWALLS, AND WINGWALLS.
2. INSTALL PROPOSED CLASS 'I' RIP-RAP AT CULVERT INLET AND OUTLET.
3. REMOVE IMPERVIOUS DIKES #1, #2, #3, & #4 AND 15 INCH TEMPORARY PIPES #1 & #2.

