


PROJECT REFERENCE NO.	SHEET NO.
<i>R-5739</i>	<i>EC-36A/CONST.36</i>
RW SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

CULVERT CONSTRUCTION SEQUENCE STA. 451+96 -L-

$$1'' = 20'$$

PHASE I

1. INSTALL IMPERVIOUS DIKES #1, #2, #3, #4, & #5, 24 INCH TEMPORARY PIPES #1 & #2, AND 15 INCH TEMPORARY PIPE #1.
2. DEWATER CONSTRUCTION AREA INTO SKIMMER BASINS #35.1, #36.1, AND SPECIAL STILLING BASIN(S) AS REQUIRED.
3. REMOVE EXISTING HEADWALLS AND WINGWALLS.

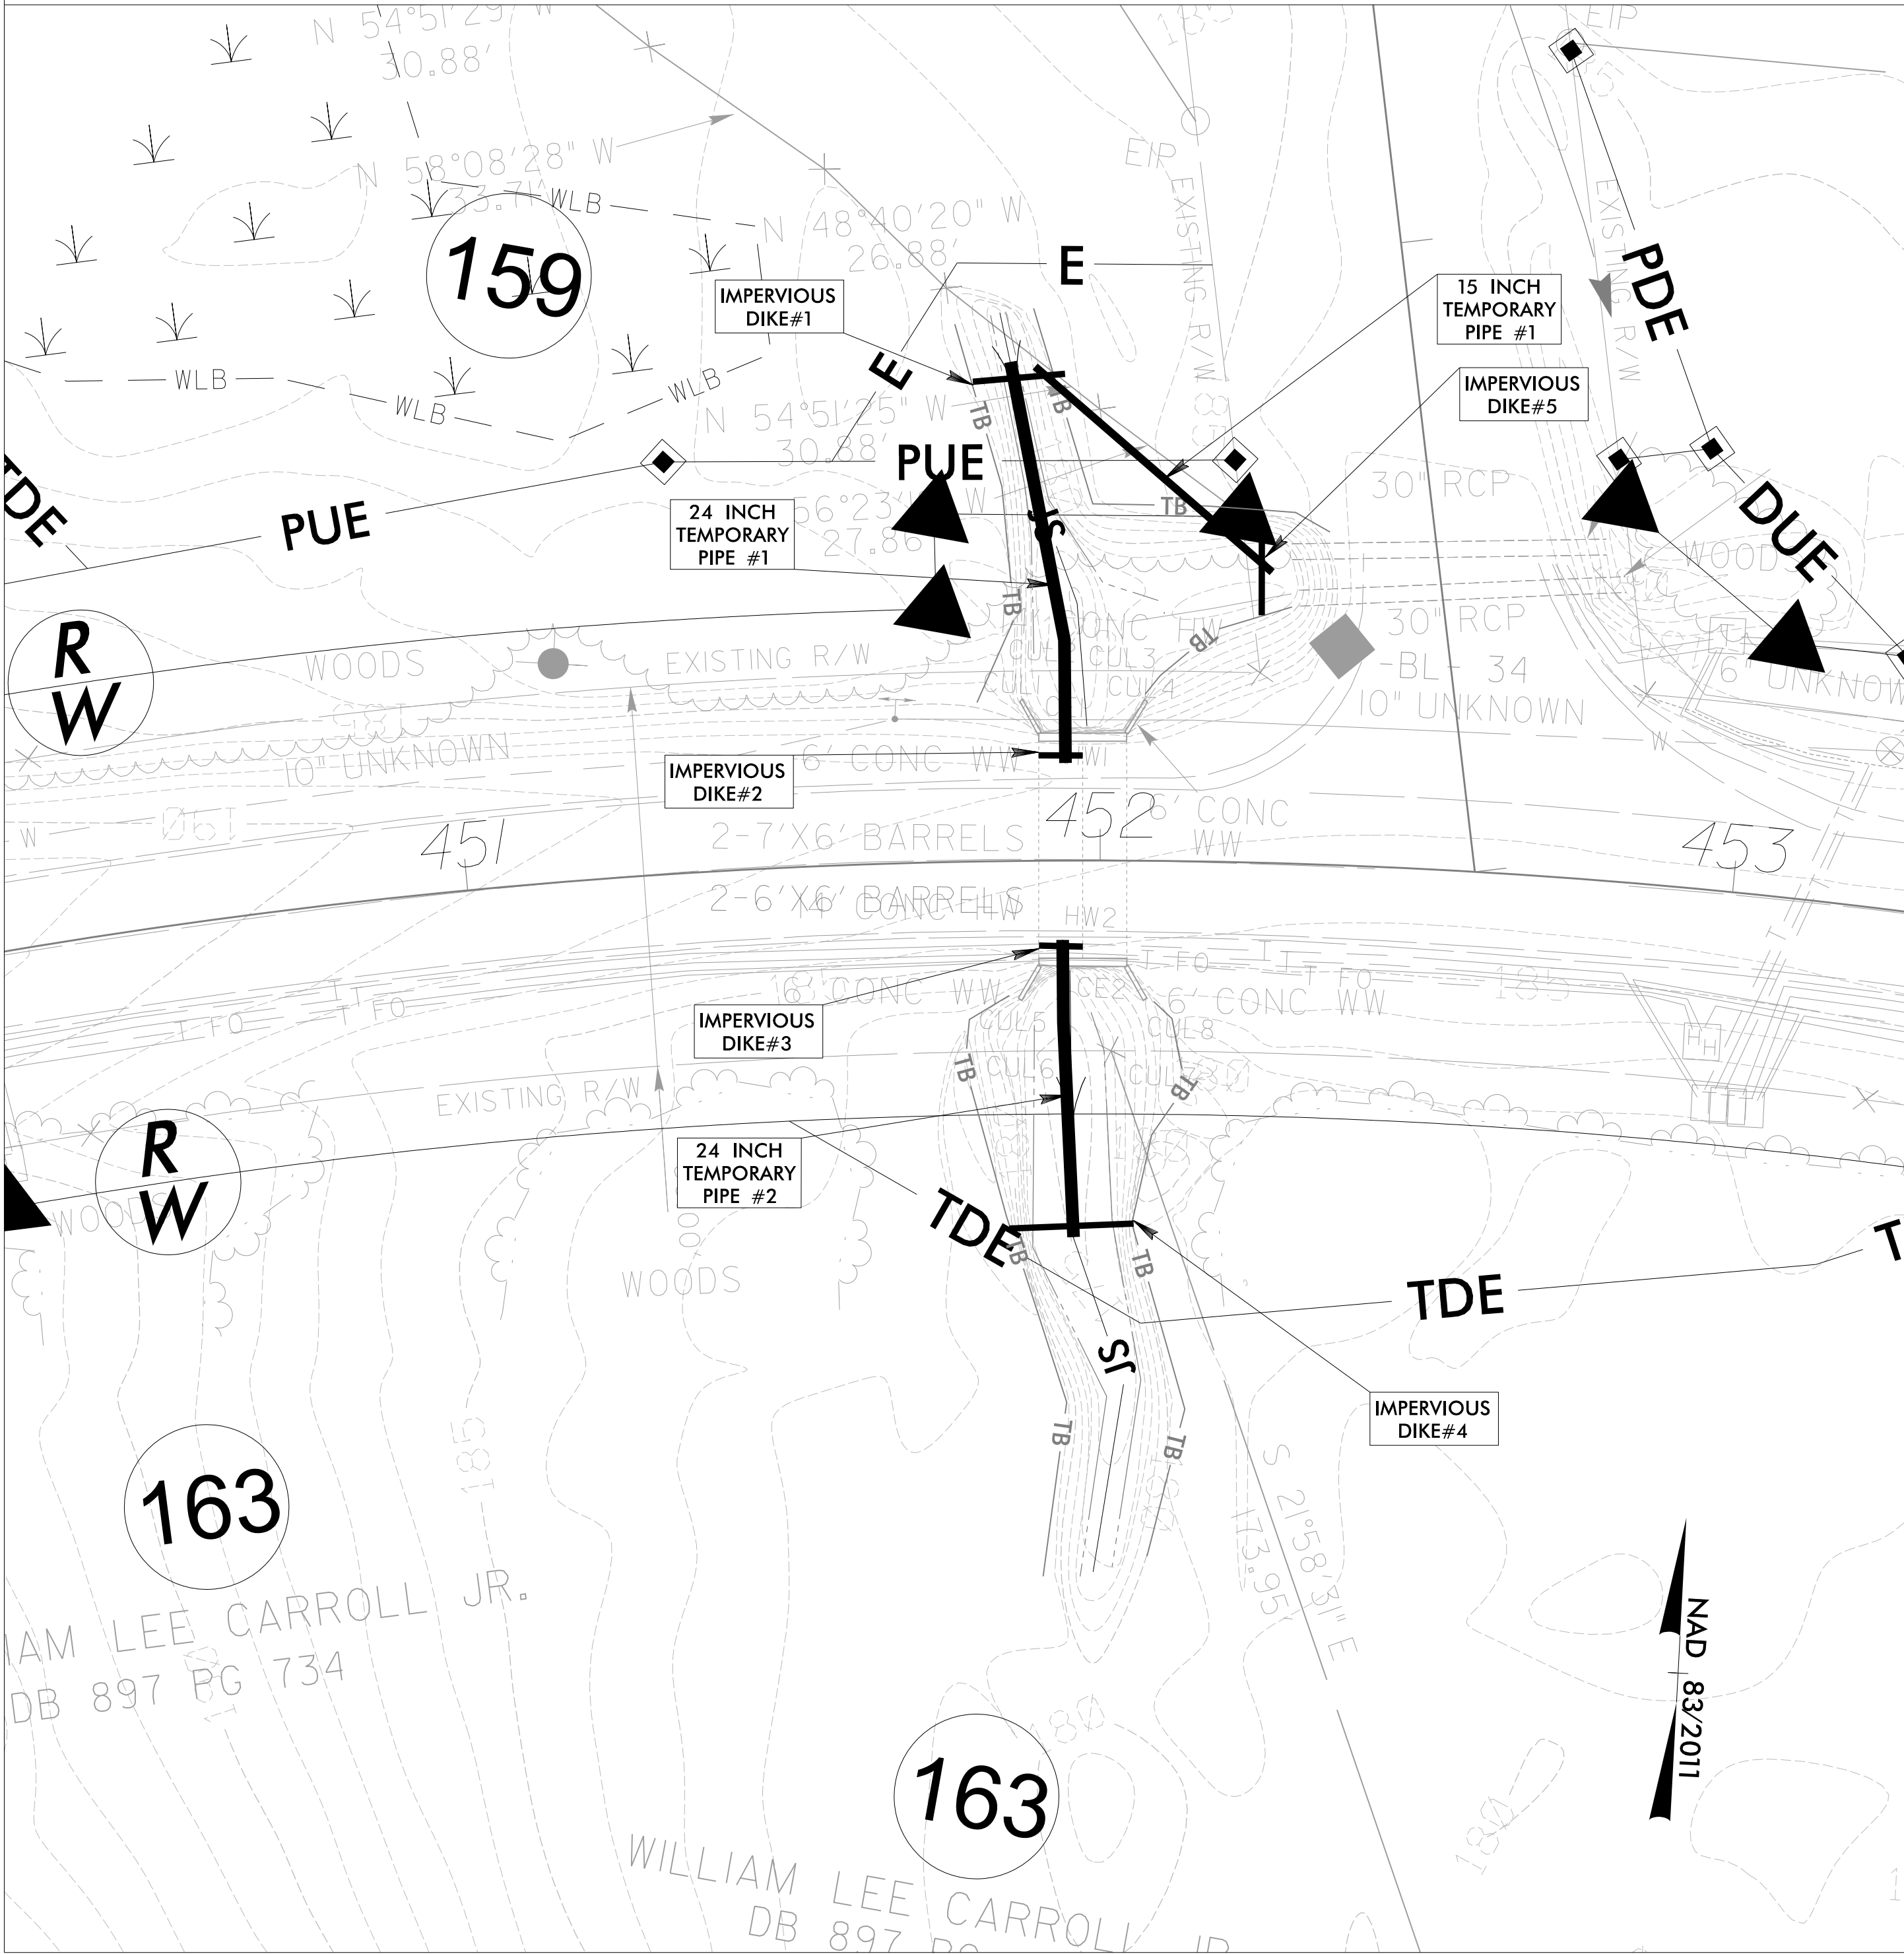

PHASE II

1. CONSTRUCT PROPOSED CULVERT EXTENSIONS, HEADWALLS, AND WINGWALLS.
2. INSTALL PROPOSED CLASS 'II' RIP-RAP AT CULVERT INLET AND OUTLET.
3. REMOVE IMPERVIOUS DIKES #1, #2, #3, #4, & #5, 24 INCH TEMPORARY PIPES #1 & #2, AND 15 INCH TEMPORARY PIPE #1.

