


CULVERT CONSTRUCTION SEQUENCE STA. 529+02 -L-

1"=20'

PROJECT REFERENCE NO.	SHEET NO.
R-5739	EC-41A/CONST.41
RW SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

PHASE I

1. INSTALL IMPERVIOUS DIKES #1, #2, #3, & #4 AND 15 INCH TEMPORARY PIPES #1 & #2.
2. DEWATER CONSTRUCTION AREA INTO SKIMMER BASINS #41.1, #41.2, & 41.3 AND SPECIAL STILLING BASIN(S) AS REQUIRED.
3. REMOVE EXISTING HEADWALLS AND WINGWALLS.

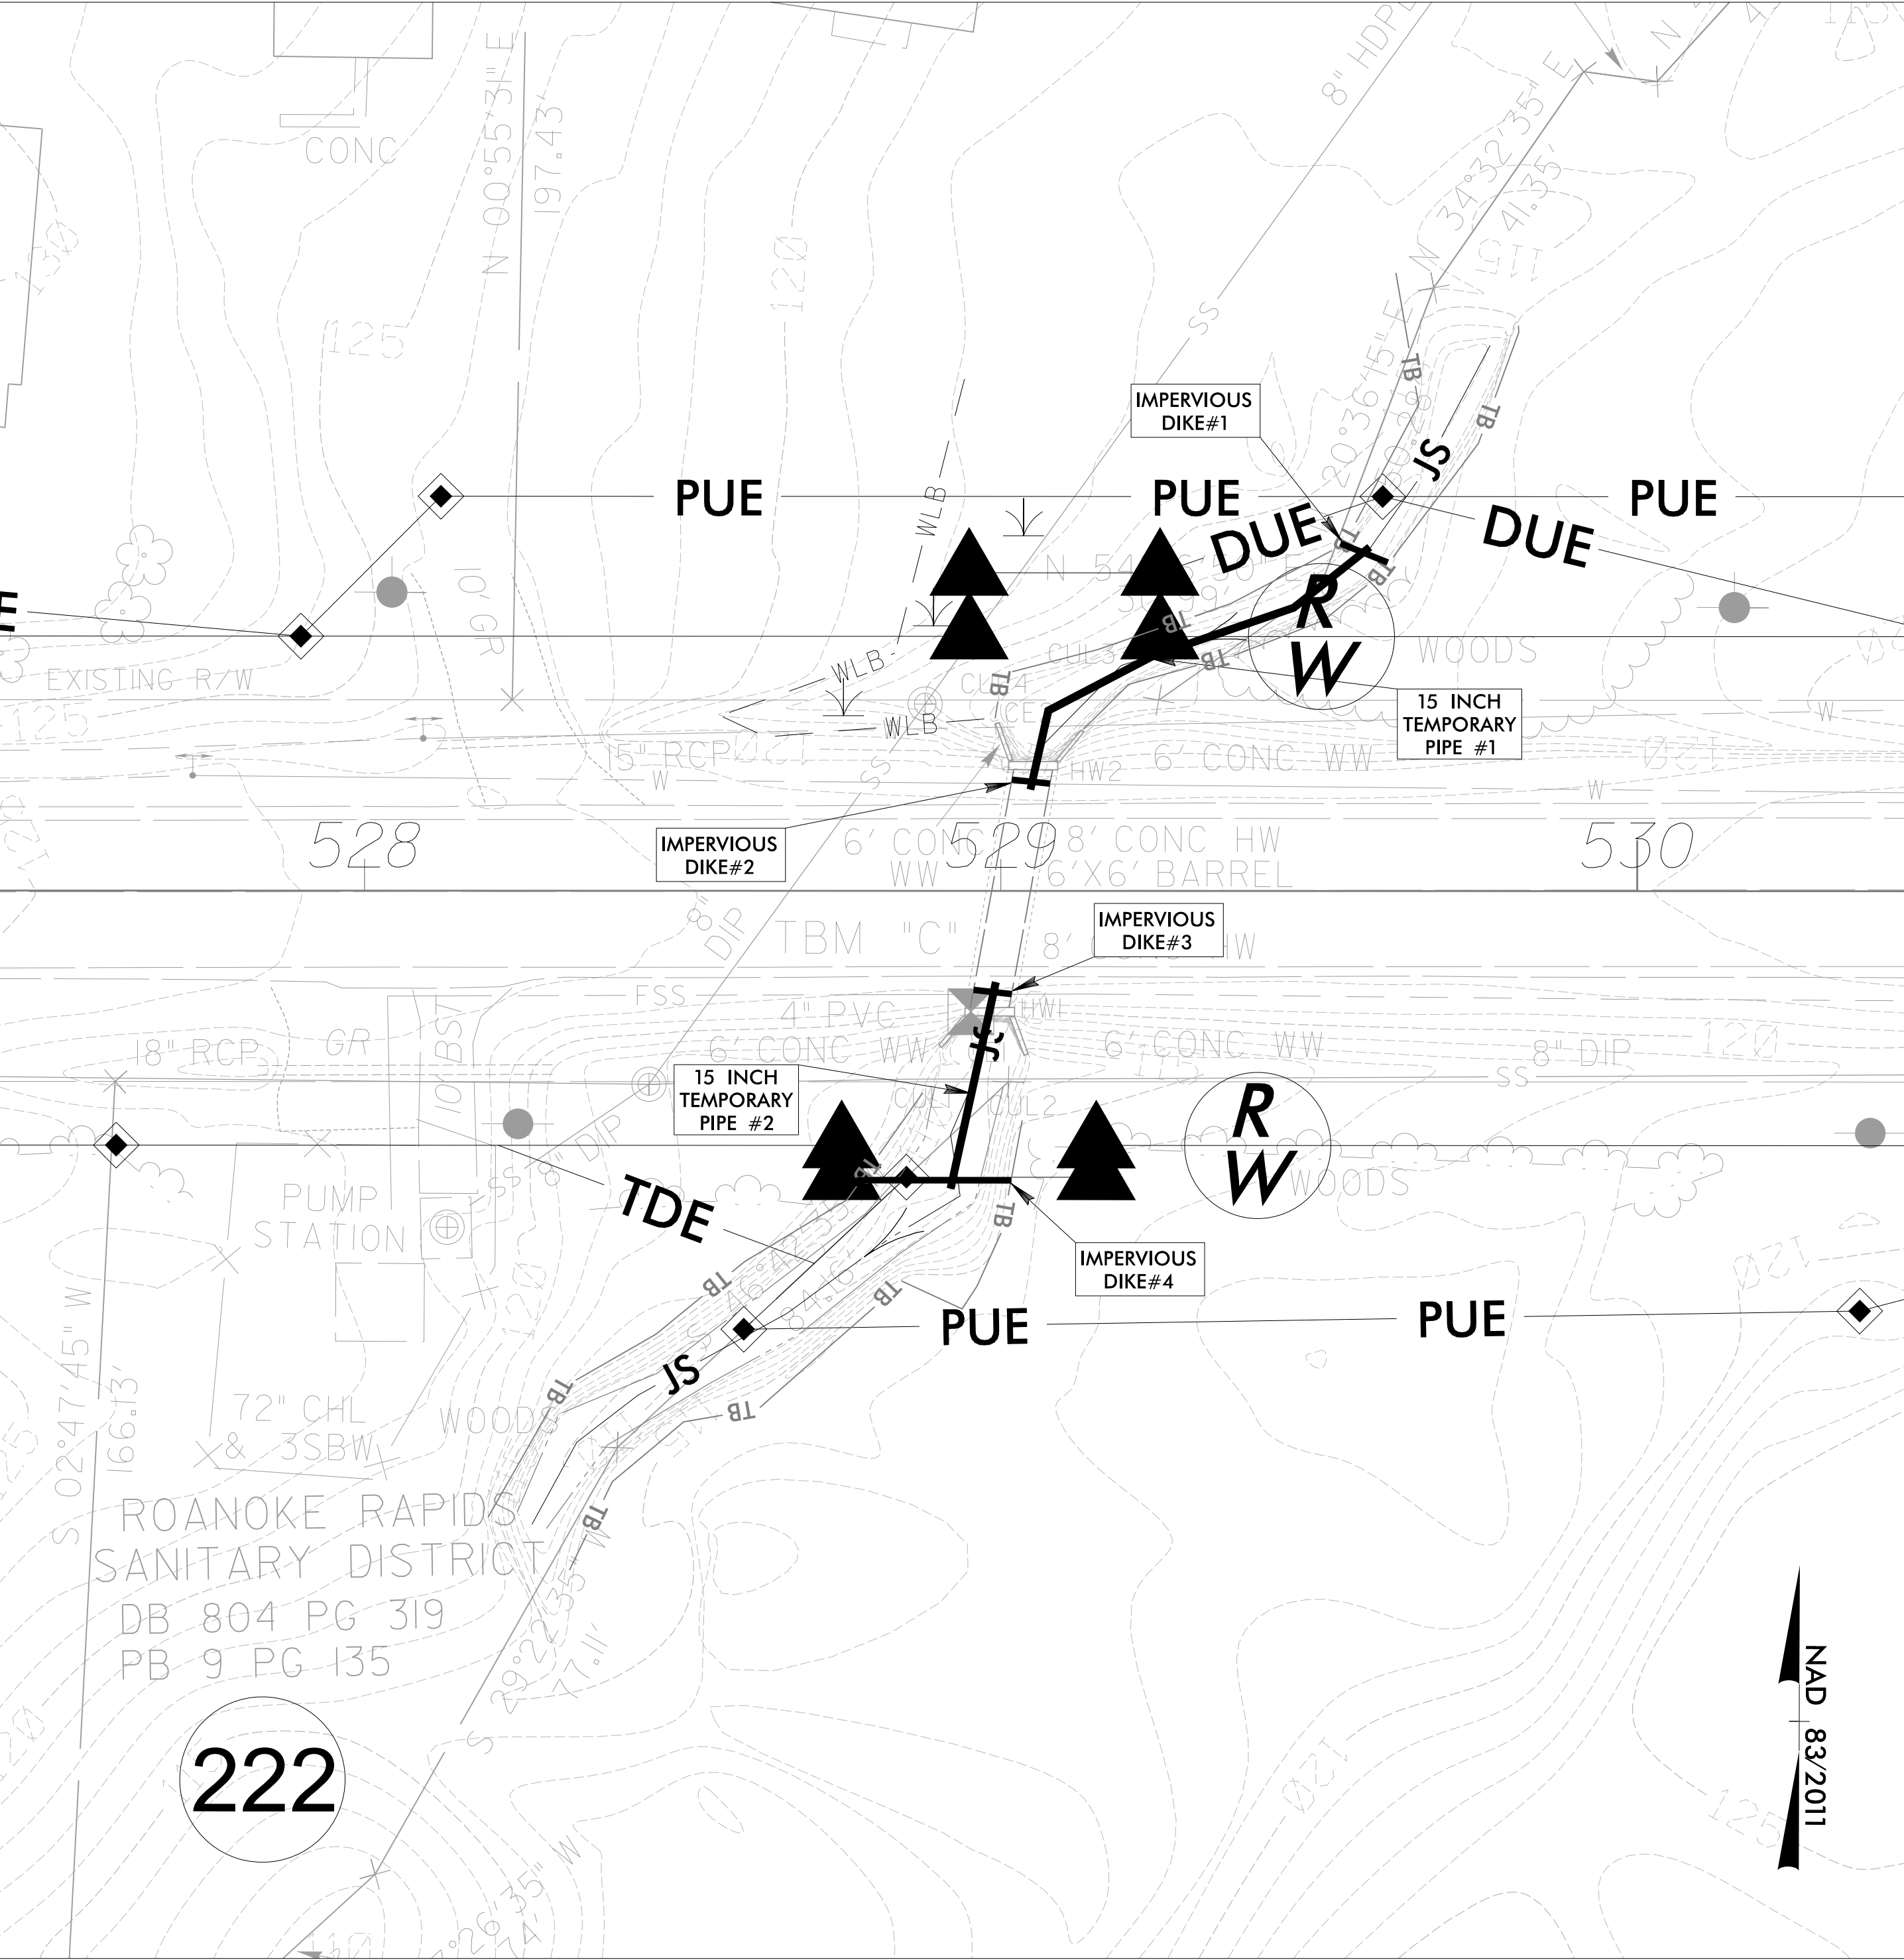

PHASE II

1. CONSTRUCT PROPOSED CULVERT EXTENSIONS, HEADWALLS, AND WINGWALLS.
2. INSTALL PROPOSED CLASS 'II' RIP-RAP AT CULVERT INLET AND OUTLET.
3. REMOVE IMPERVIOUS DIKES #1, #2, #3, & #4, AND 15 INCH TEMPORARY PIPES #1 & #2.

