


PROJECT REFERENCE NO.		SHEET NO.
U-5760		EC-5B/CONST.5
ROADWAY DESIGN ENGINEER		HYDRAULICS ENGINEER

CULVERT CONSTRUCTION SEQUENCE STA. 22 + 76 –L-58 + 36 –Y1–

PHASE I

- 1.) UTILIZE SPECIAL STILLING BASIN(S) DURING CONSTRUCTION AS NEEDED TO DEWATER WORK SITE. (TYP.)
- 2.) CONSTRUCT IMPERVIOUS DIKES 1 AND 2.
- 3.) INSTALL TEMPORARY 36 INCH PIPE THROUGH IMPERVIOUS DIKES TO DIVERT JS INTO TEMPORARY PIPE.

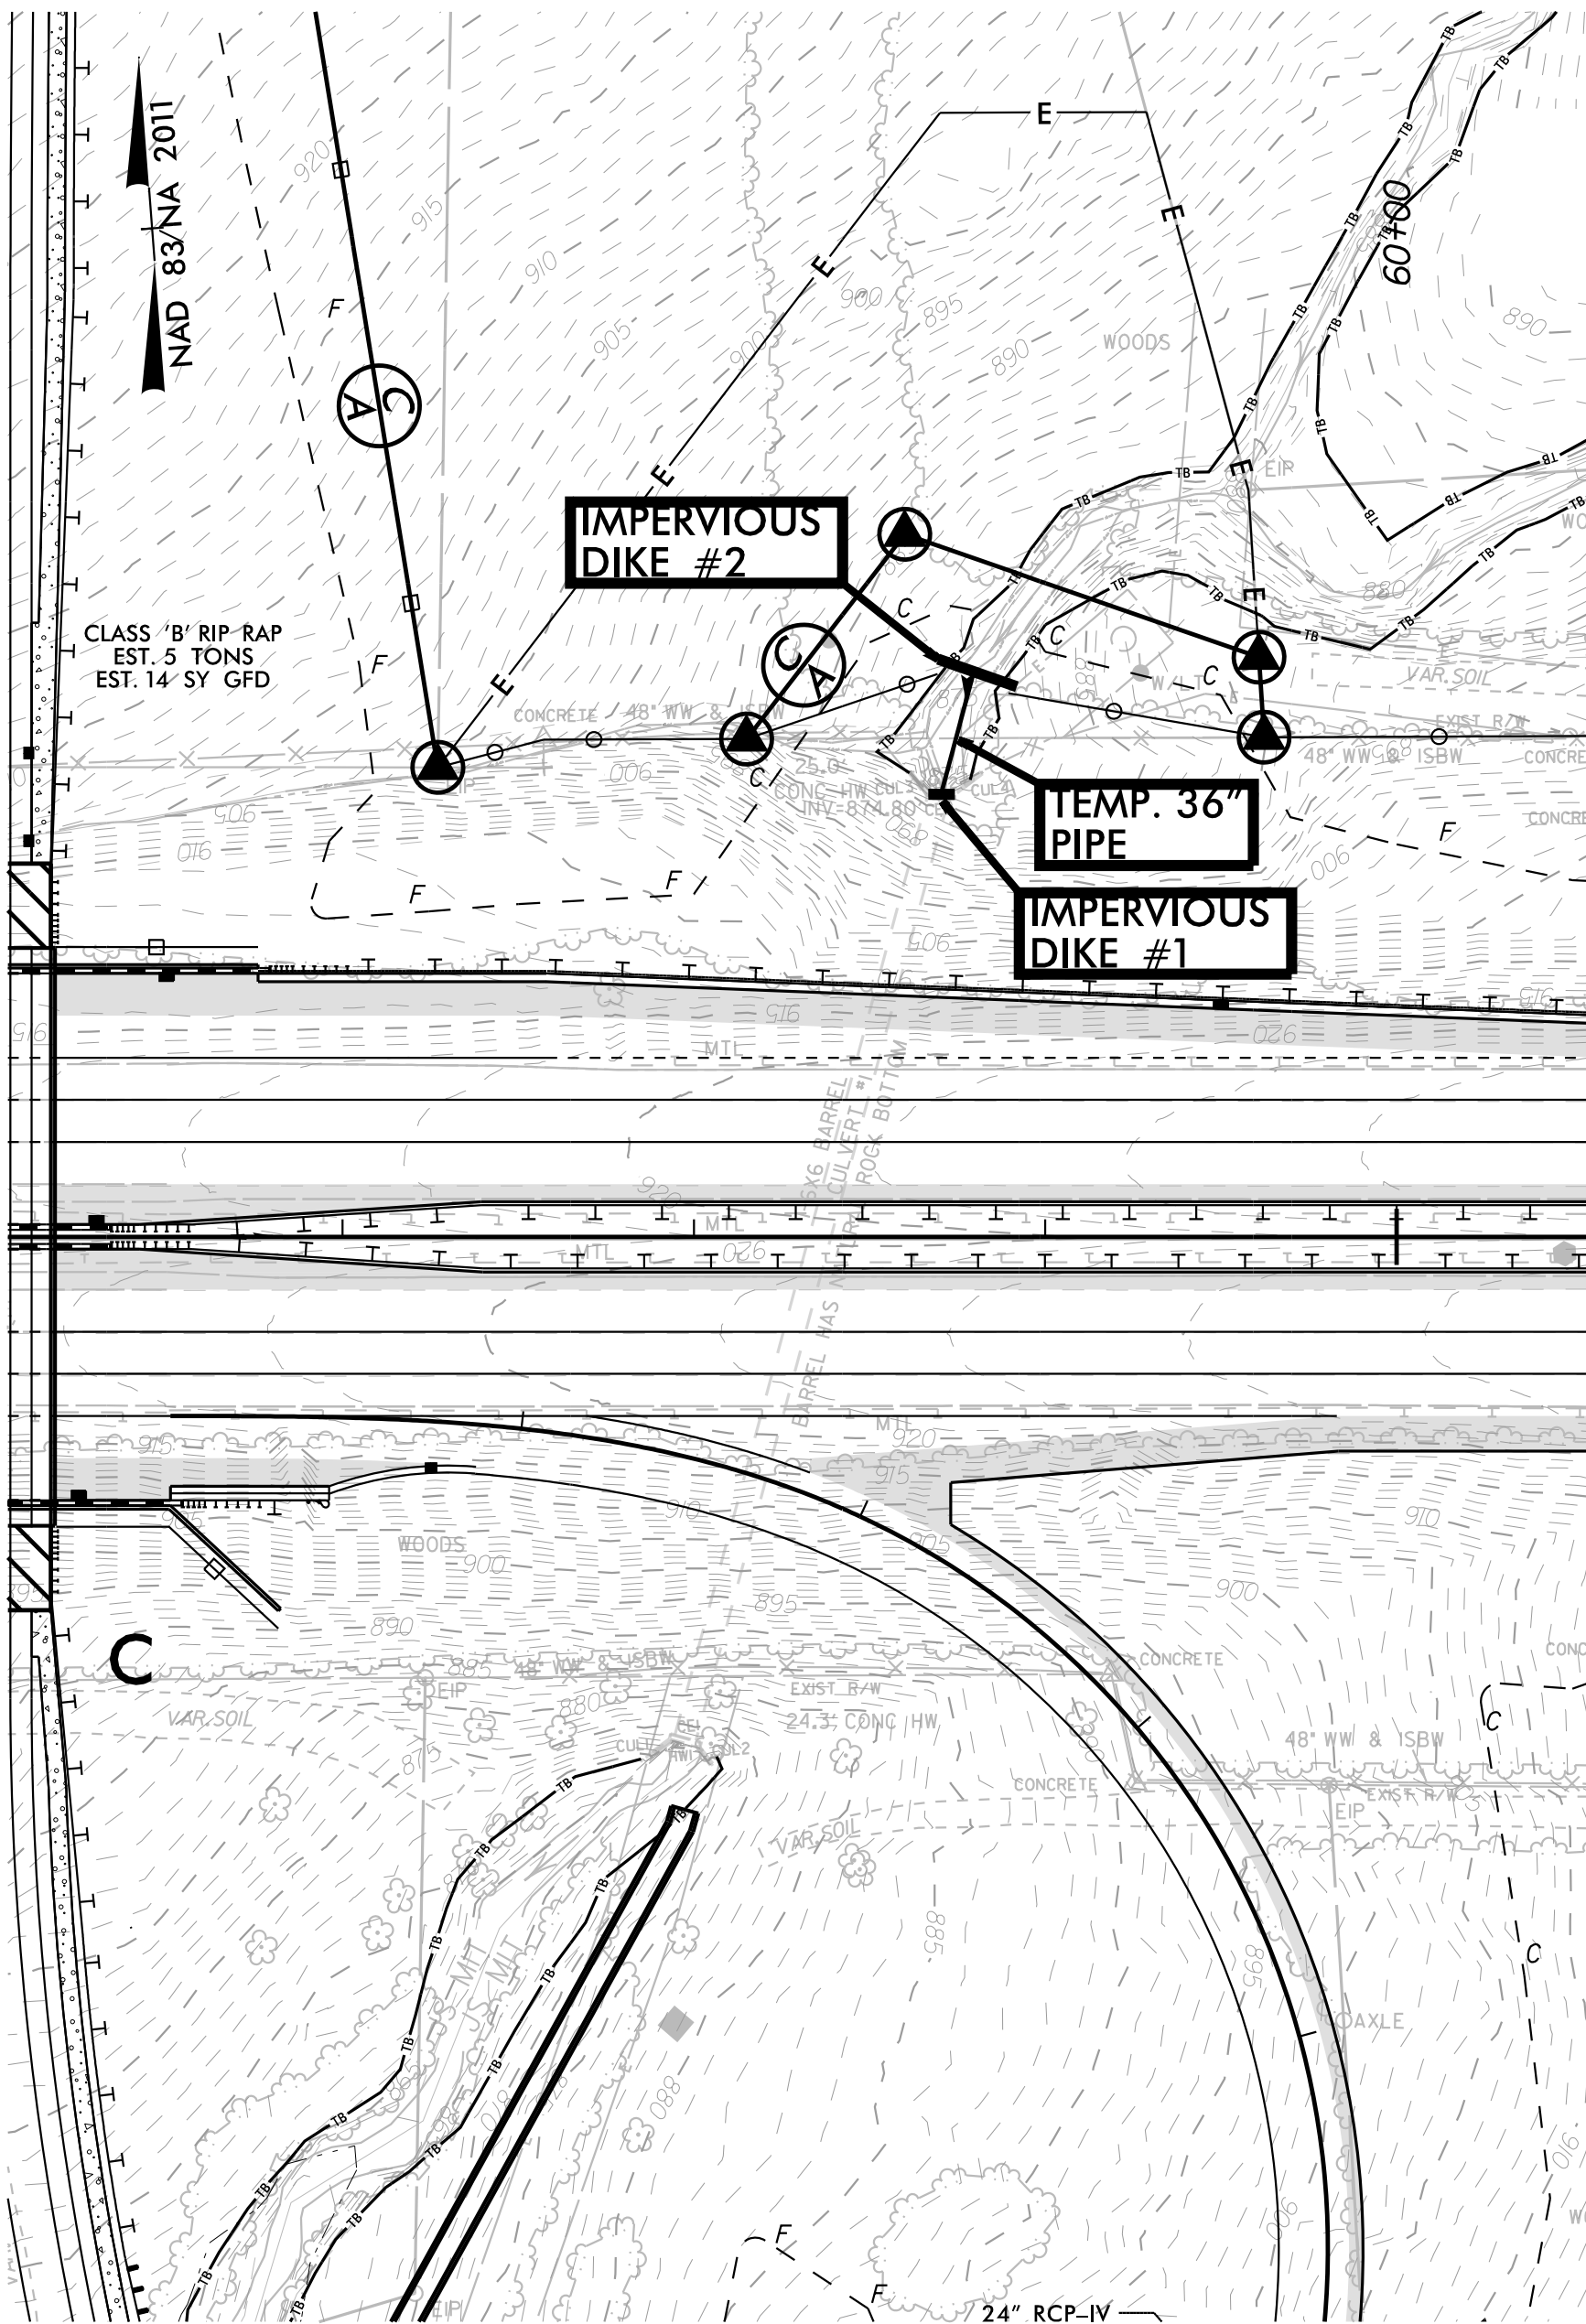

PHASE II

- 1.) CONSTRUCT PROPOSED 6'X7' RCBC CULVERT AND INLET IMPROVEMENTS.
- 2.) REMOVE IMPERVIOUS DIKES 1 AND 2 AND REMOVE TEMPORARY PIPE.
- 3.) REMOVE SPECIAL STILLING BASIN.
- 4.) STABILIZE DISTURBED AREA AND REMOVE ALL EROSION AND SEDIMENT CONTROL DEVICES AS DIRECTED.
- 5.) FINISH ROADWAY AND DRAINAGE CONSTRUCTION.

