


CULVERT CONSTRUCTION SEQUENCE STA. 43+26 -L-

STAGE 1 (TMP PHASE V STEP 1)

1. UTILIZE SPECIAL STILLING BASIN(S) AS NEEDED THROUGHOUT CULVERT CONSTRUCTION.
2. INSTALL IMPERVIOUS DIKES A & B TO DIVERT WATER THROUGH BARREL 2 OF THE EXISTING CULVERT.
3. INSTALL PORTABLE CONCRETE BARRIER AND SHIFT TRAFFIC TO NORTH BOUND LANES.
4. INSTALL TEMPORARY SHORING AND REMOVE A PORTION OF BARREL 1 OF THE EXISTING CULVERT UNDERNEATH THE SOUTH BOUND LANES.
5. DEWATER PROPOSED CULVERT CONSTRUCTION AREA.
6. CONSTRUCT A PORTION OF PROPOSED LOW FLOW BARREL CULVERT, LEAVING THE NORTH BOUND LANES OPEN TO TRAFFIC.

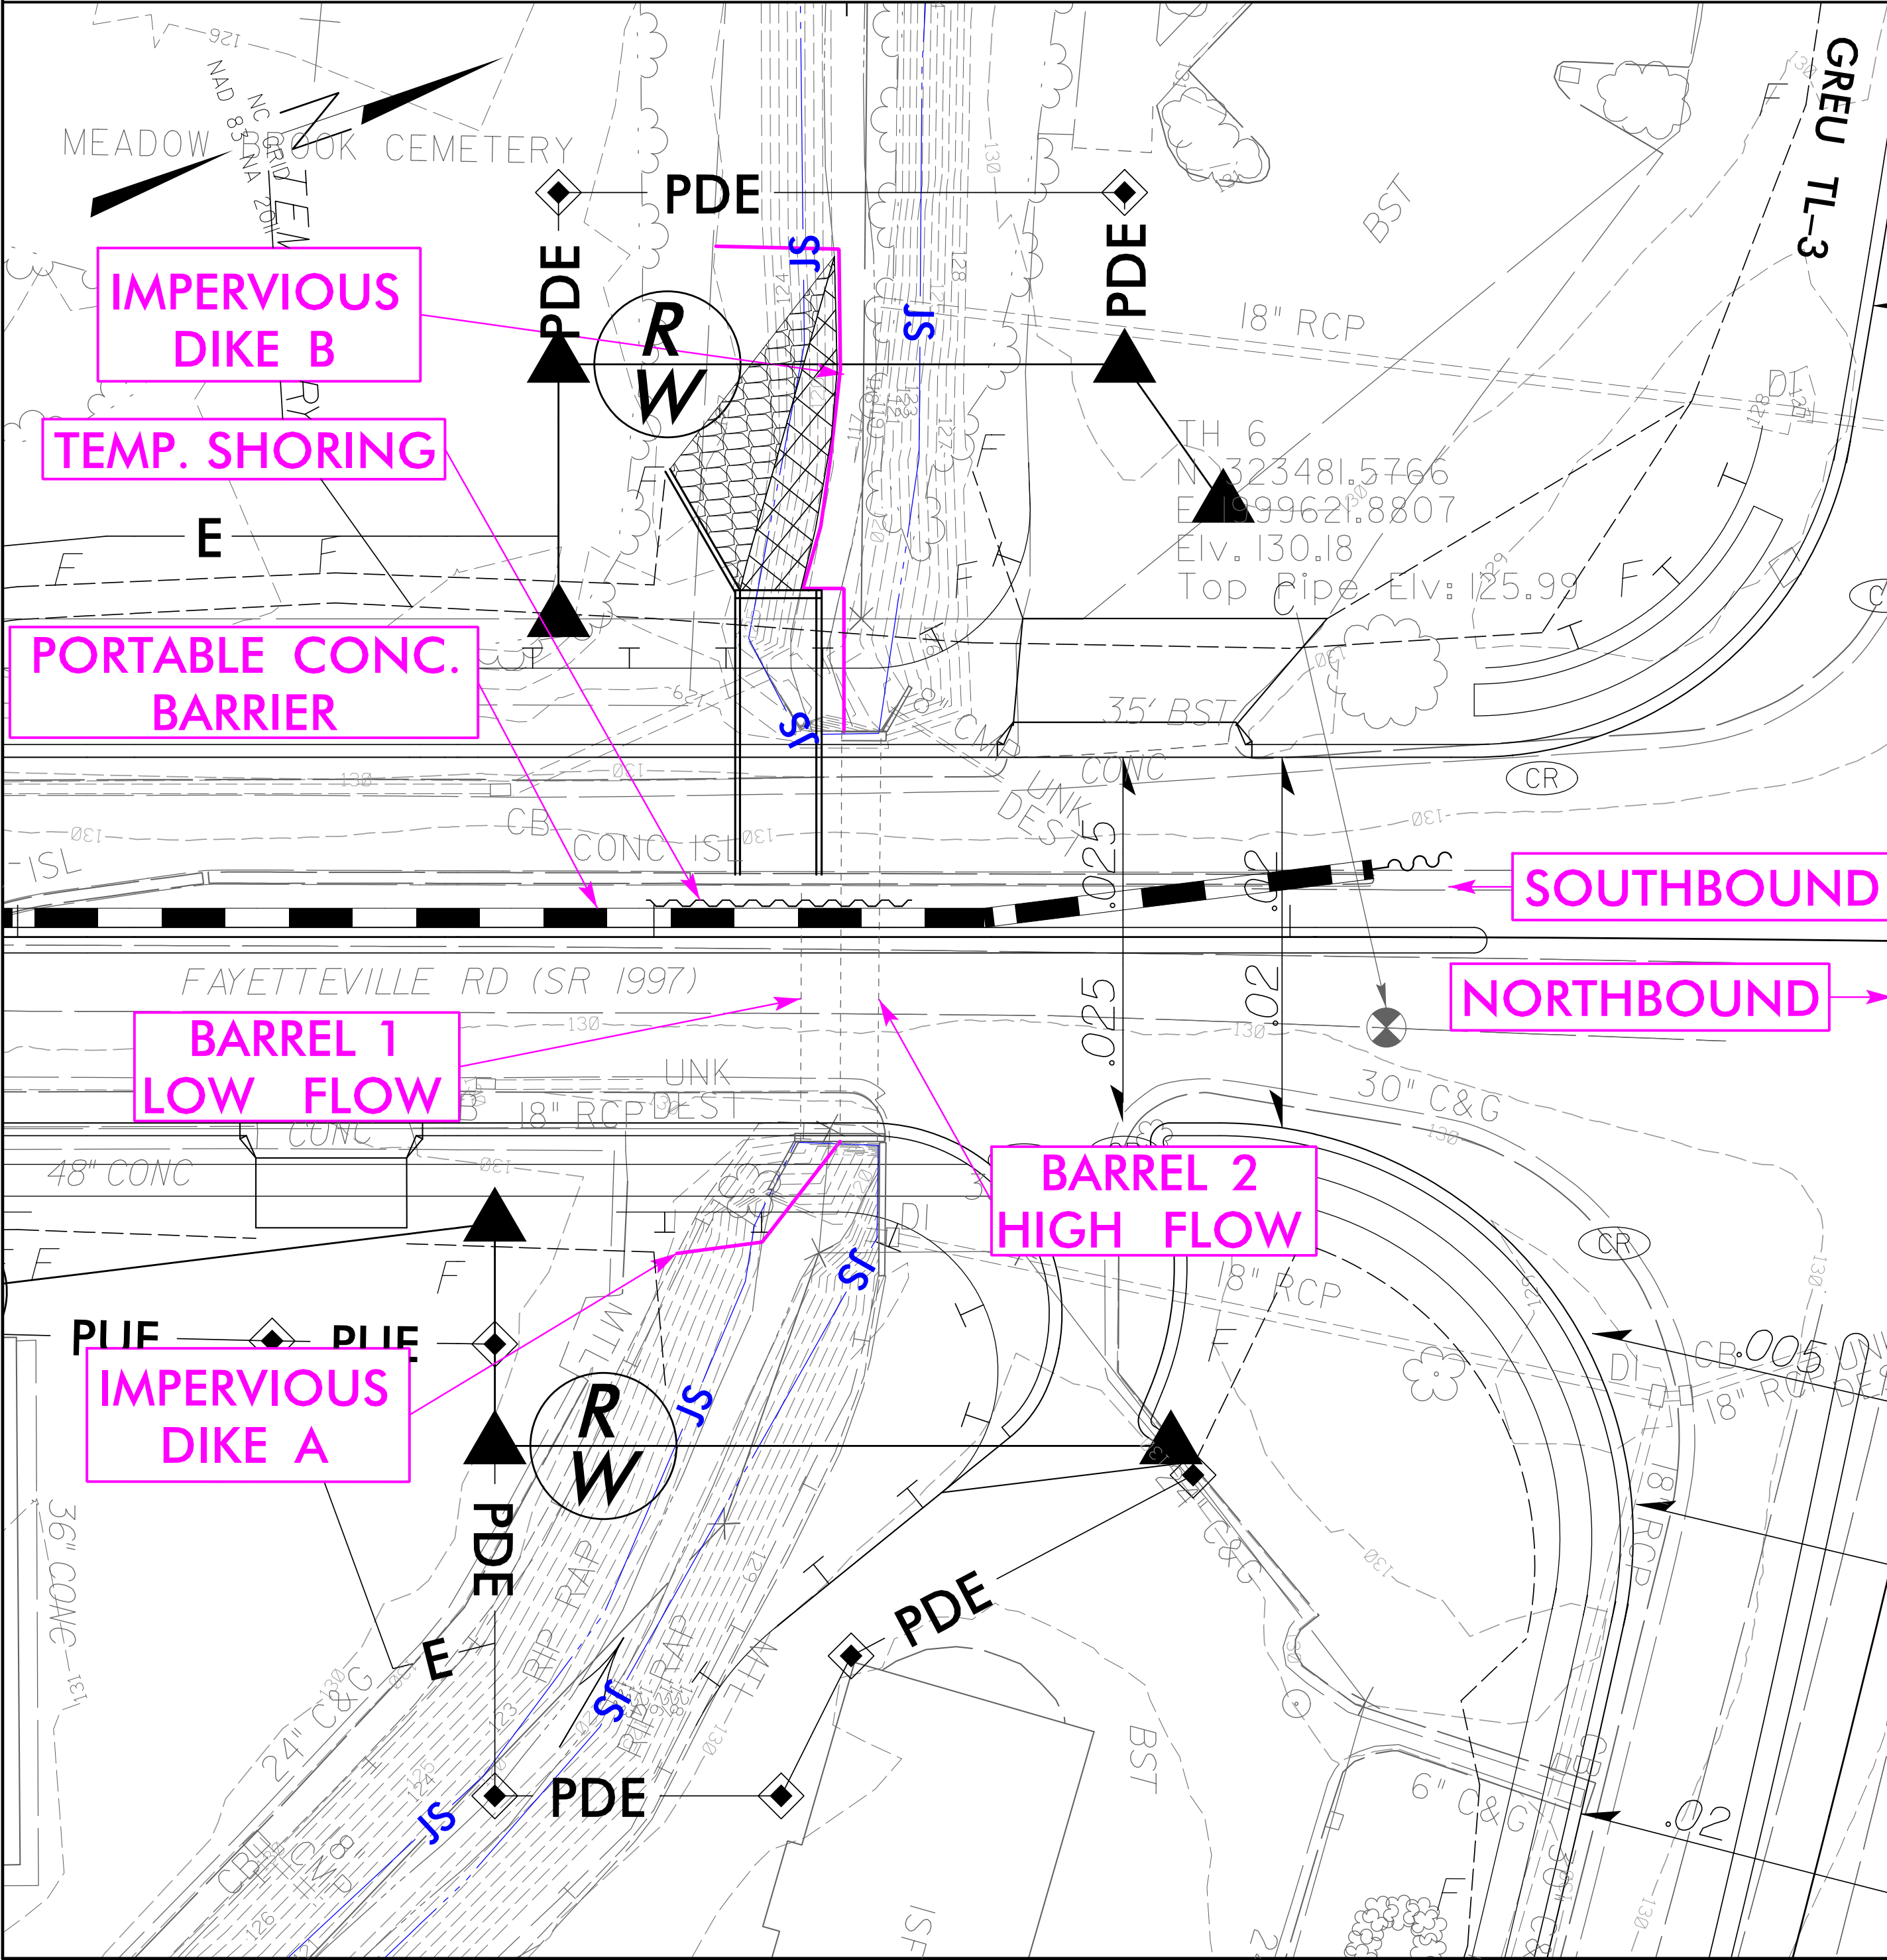

STAGE 2 (TMP PHASE V STEP 1)

7. REMOVE IMPERVIOUS DIKES A AND B AND INSTALL IMPERVIOUS DIKES C, D, AND E. DIVERT FLOW TO EXISTING CULVERT BARREL 1 AND CONSTRUCTED PROPOSED LOW FLOW CULVERT BARREL.
8. REMOVE A PORTION OF EXISTING CULVERT BARREL 2 UNDER SOUTHBOUND LANES.
9. EXCAVATE ANY ACCUMULATED SILT AND DEWATER PROPOSED CULVERT CONSTRUCTION AREA.
10. CONSTRUCT A PORTION OF PROPOSED HIGH FLOW CULVERT BARREL, LEAVING THE NORTH BOUND LANES OPEN TO TRAFFIC.

