


CULVERT CONSTRUCTION SEQUENCE STA. 43+26 -L-

STAGE 3 (TMP PHASE VI STEP 4)

11. REMOVE IMPERVIOUS DIKES C, D, AND E. INSTALL IMPERVIOUS DIKES F, G, AND H TO DIVERT FLOW TO EXISTING CULVERT BARREL 2 AND PARTIALLY INSTALLED HIGH FLOW BARREL OF PROPOSED CULVERT.
12. INSTALL PORTABLE CONCRETE BARRIER, SHORING, TEMPORARY PAVEMENT AND SHIFT TRAFFIC TO SOUTH BOUND LANES.
13. EXCAVATE ANY ACCUMULATED SILT AND REMOVE REMAINING PORTION OF EXISTING CULVERT BARREL 1.
14. DEWATER PROPOSED CULVERT CONSTRUCTION AREA.
15. CONSTRUCT REMAINING PORTION OF PROPOSED LOW FLOW CULVERT BARREL LEAVING THE SOUTH BOUND LANES OPEN TO TRAFFIC.

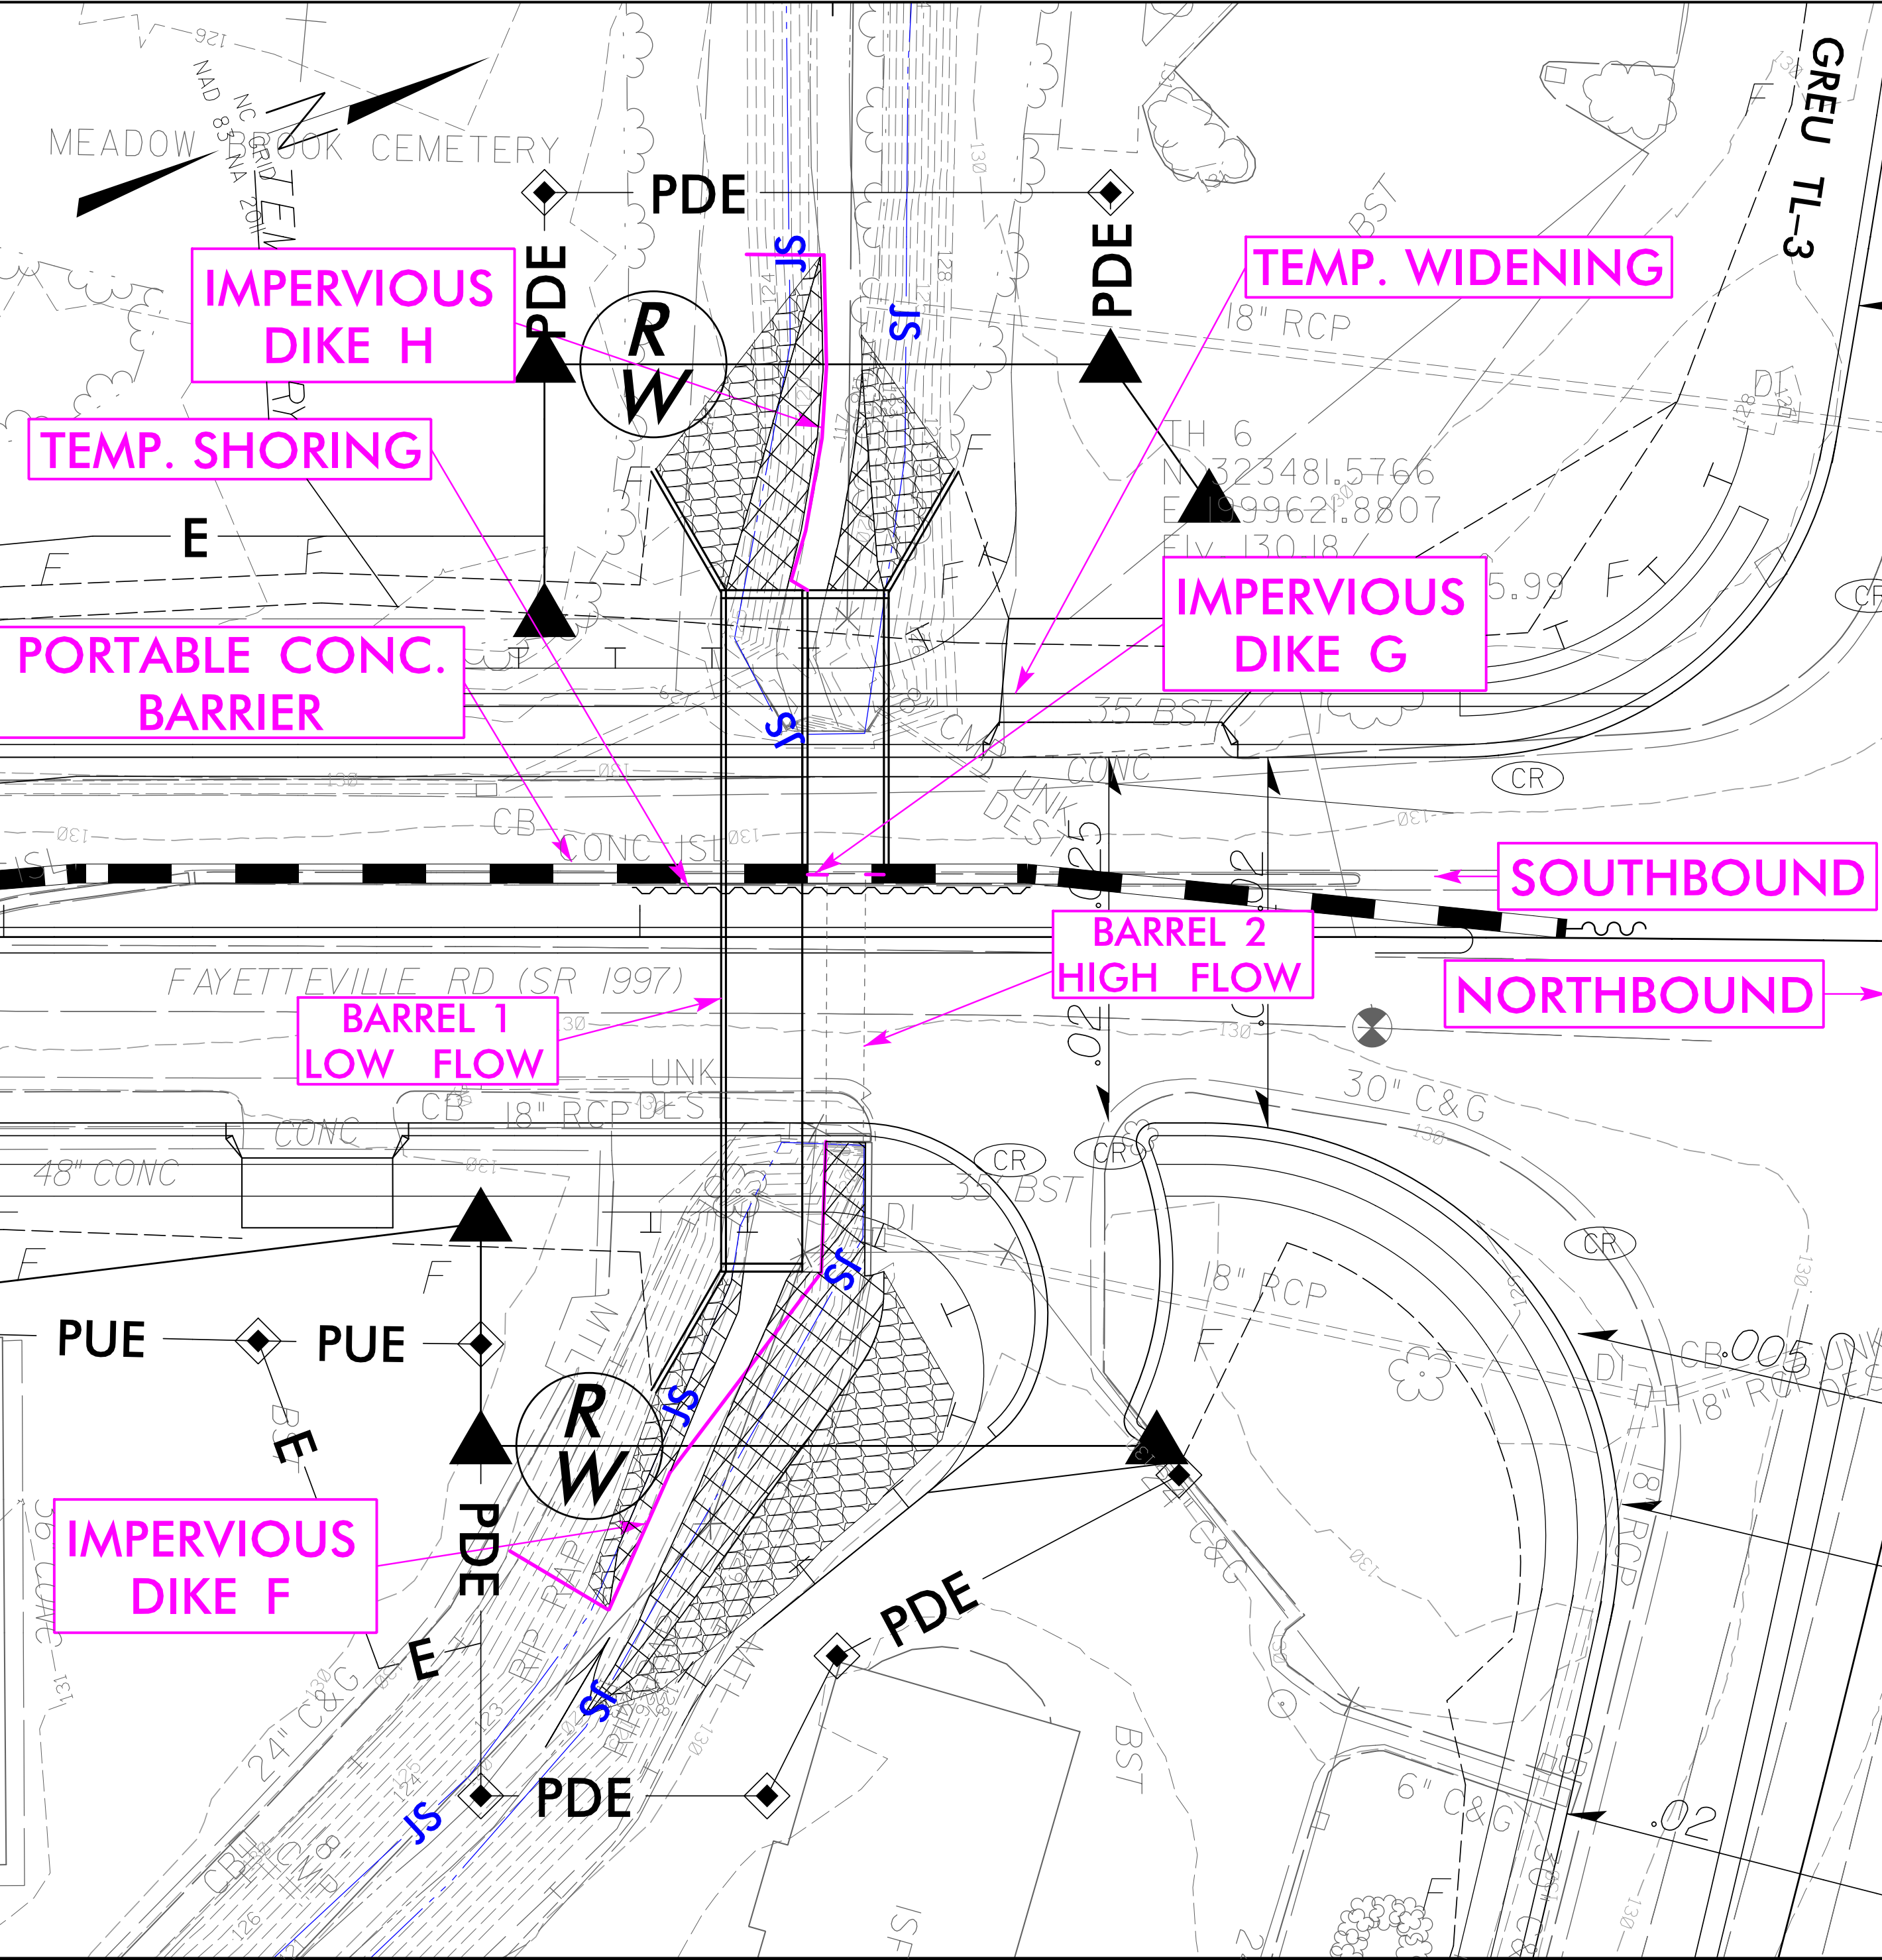

STAGE 4 (TMP PHASE VI STEP 4)

16. REMOVE IMPERVIOUS DIKES F, G, AND H AND INSTALL IMPERVIOUS DIKES I AND J. DIVERT FLOW TO COMPLETED PROPOSED CULVERT LOW FLOW BARREL.
17. EXCAVATE ANY ACCUMULATED SILT AND DEWATER PROPOSED CULVERT CONSTRUCTION AREA.
18. CONSTRUCT REMAINING PORTION OF PROPOSED HIGH FLOW BARREL TO COMPLETE CULVERT.

