


CULVERT CONSTRUCTION SEQUENCE STA. 68+62 -L-

STAGE 1 (TMP PHASE IV STEP 1)

1. UTILIZE SPECIAL STILLING BASIN(S) AS NEEDED THROUGHOUT CULVERT CONSTRUCTION.
2. INSTALL IMPERVIOUS DIKE A AND DEWATER LEFT WINGWALL/HEADWALL AND BOX 0801 CONSTRUCTION AREA.
3. CONSTRUCT DOWNSTREAM LEFT WINGWALL AND HEADWALL. INSTALL BOX 0801.
4. CONSTRUCT DOWNSTREAM TEMPORARY CHANNEL CHANGE WITH LINER.
5. INSTALL IMPERVIOUS DIKES 1 AND 2. CONSTRUCT UPSTREAM TEMPORARY CHANNEL CHANGE WITH LINER.

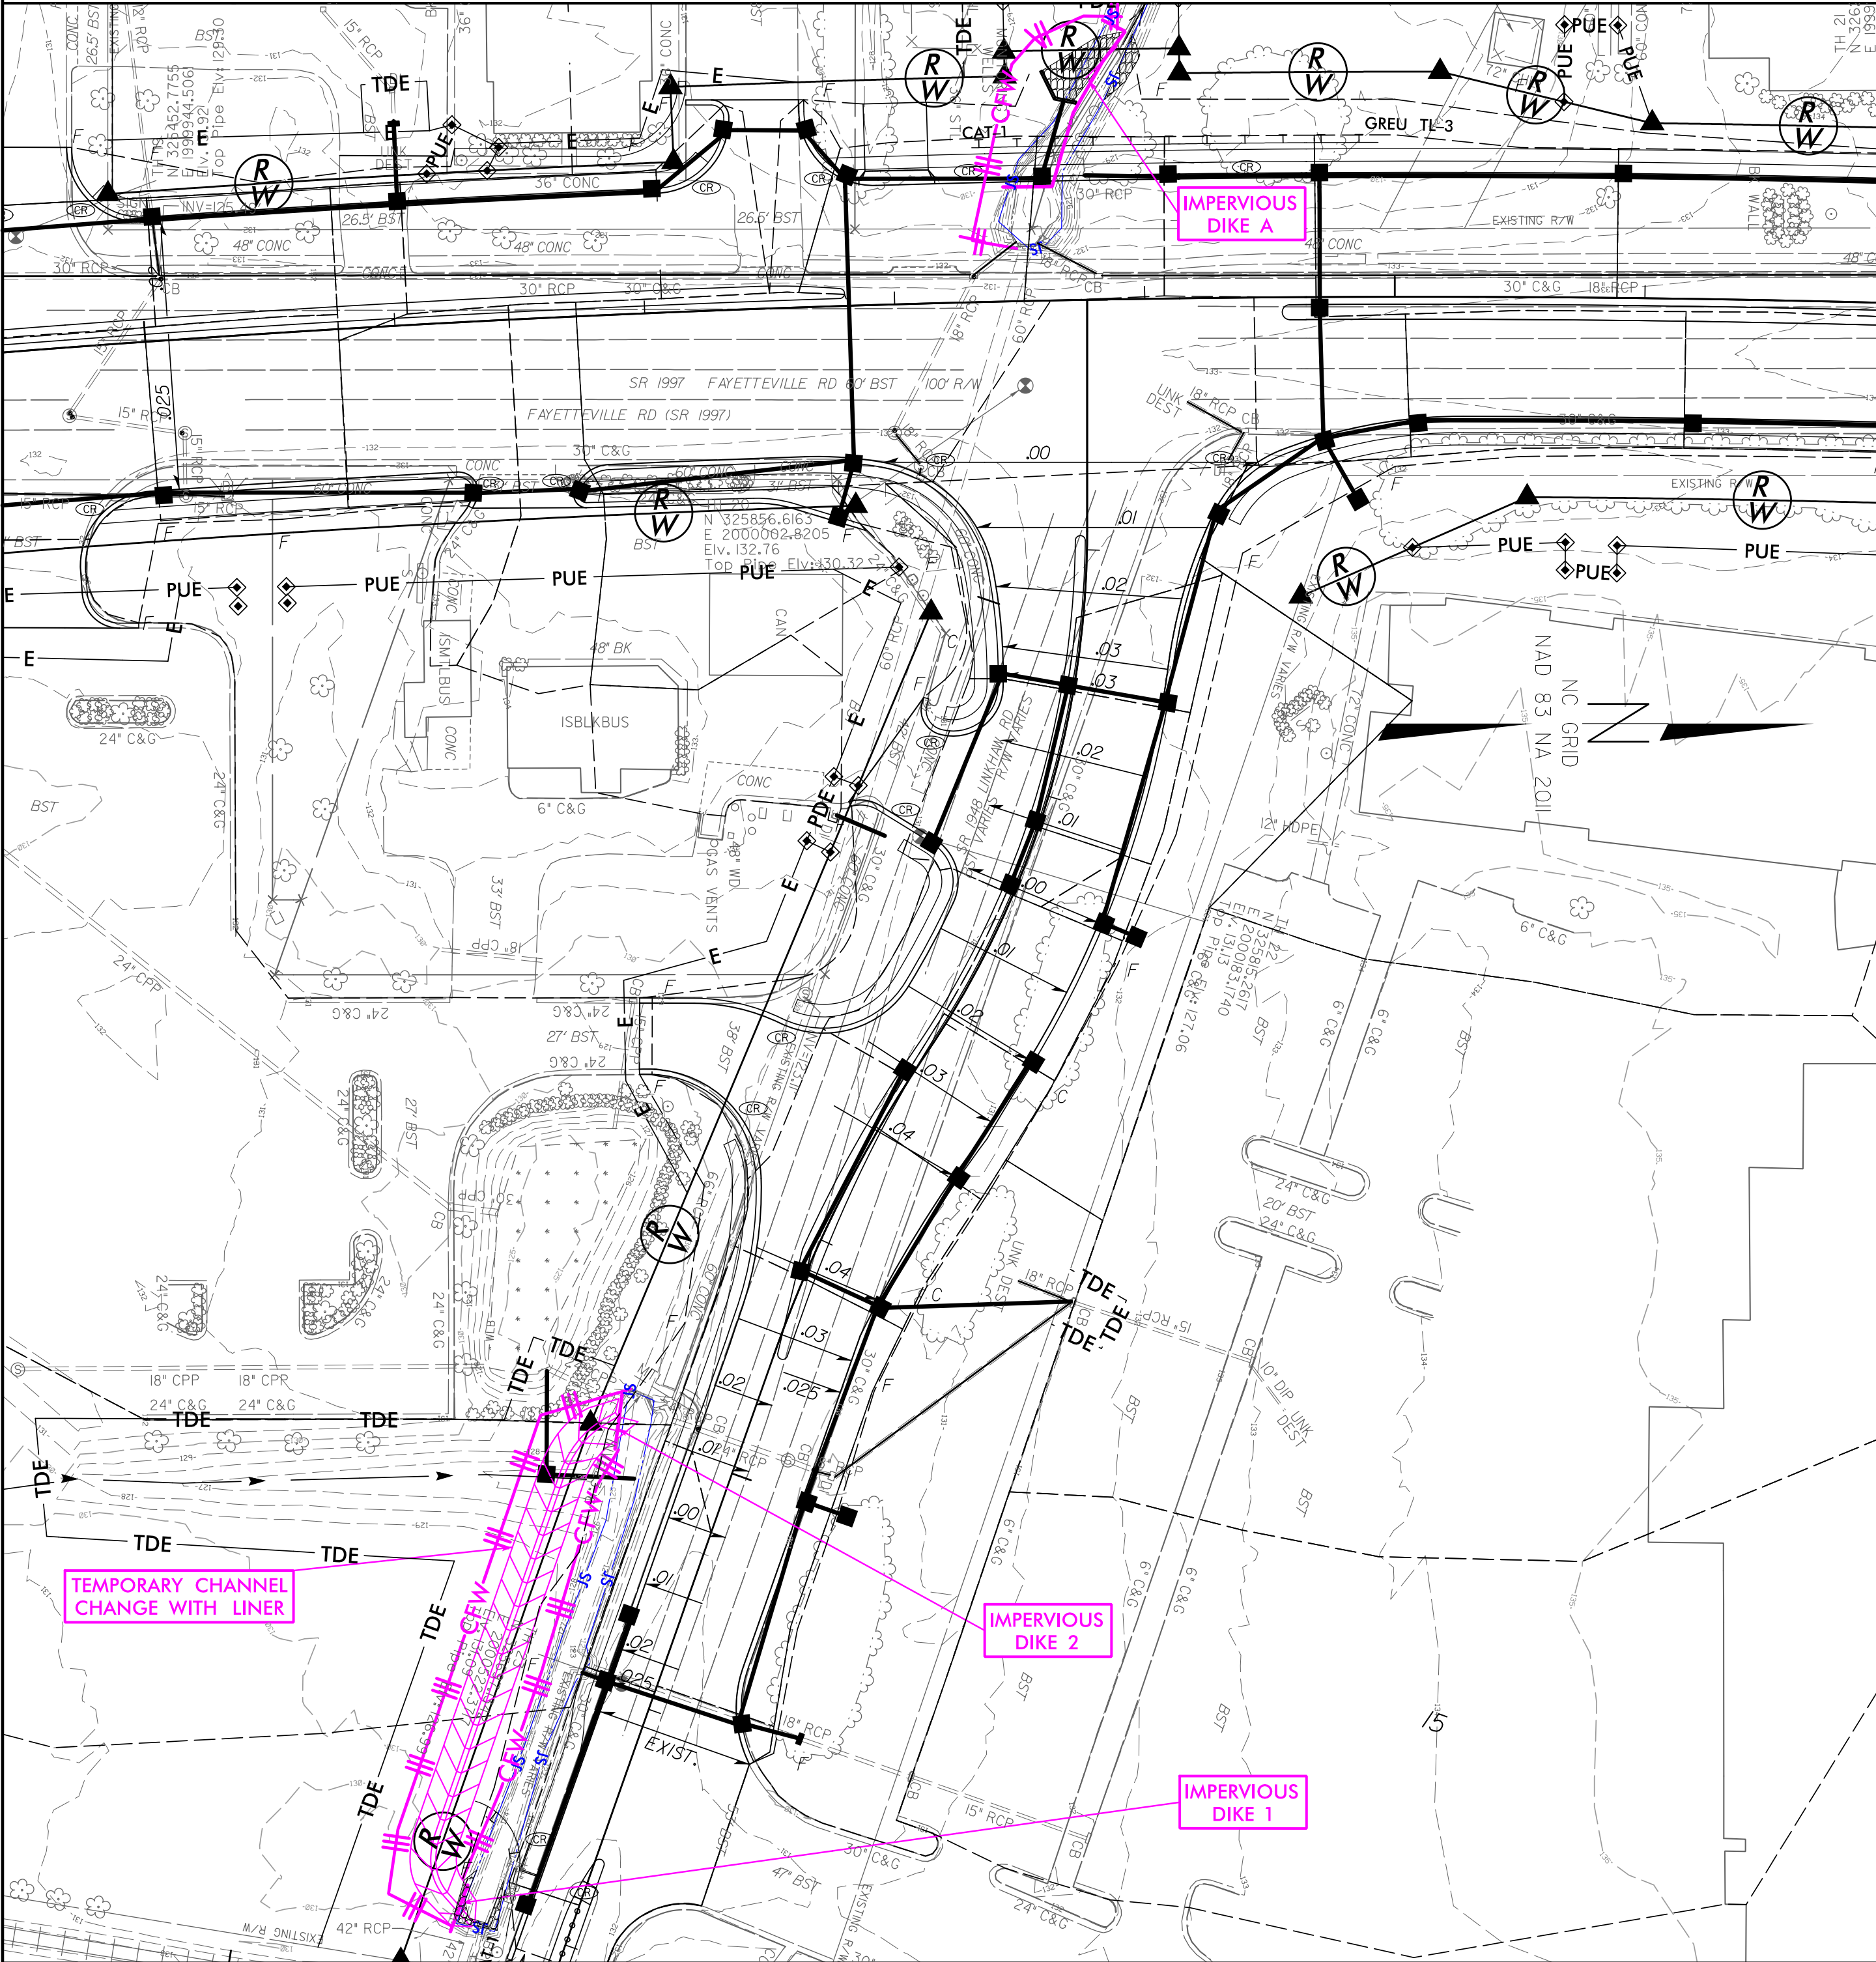

STAGE 2 (TMP PHASE IV STEP 1)

1. INSTALL IMPERVIOUS DIKE B AND 3 AND PUMP AROUND OPERATION TO DEWATER WORK AREA.
2. REMOVE IMPERVIOUS DIKE A. INSTALL 42 INCH TEMPORARY PIPE TO BOX 0801 WITH CONCRETE COLLAR.

