


CULVERT CONSTRUCTION SEQUENCE STA. 20+80 -Y2-

STAGE 5 (TMP PHASE VI STEP 1)

- 20. SHIFT TRAFFIC TO CONSTRUCTED LANES, REMOVE TEMPORARY PAVEMENT, AND REMOVE TEMP. 108" CSP AT BARREL 1.
- 21. COMPLETE WINGWALL ON UPSTREAM END OF PROPOSED CULVERT BARREL 1.
- 22. EXCAVATE ANY ACCUMULATED SILT AND DEWATER BEFORE REMOVAL OF IMPERVIOUS DIKES.
- 23. REMOVE IMPERVIOUS DIKES J AND K, ALLOWING NORMAL FLOW THROUGH THE PROPOSED BARREL 1.

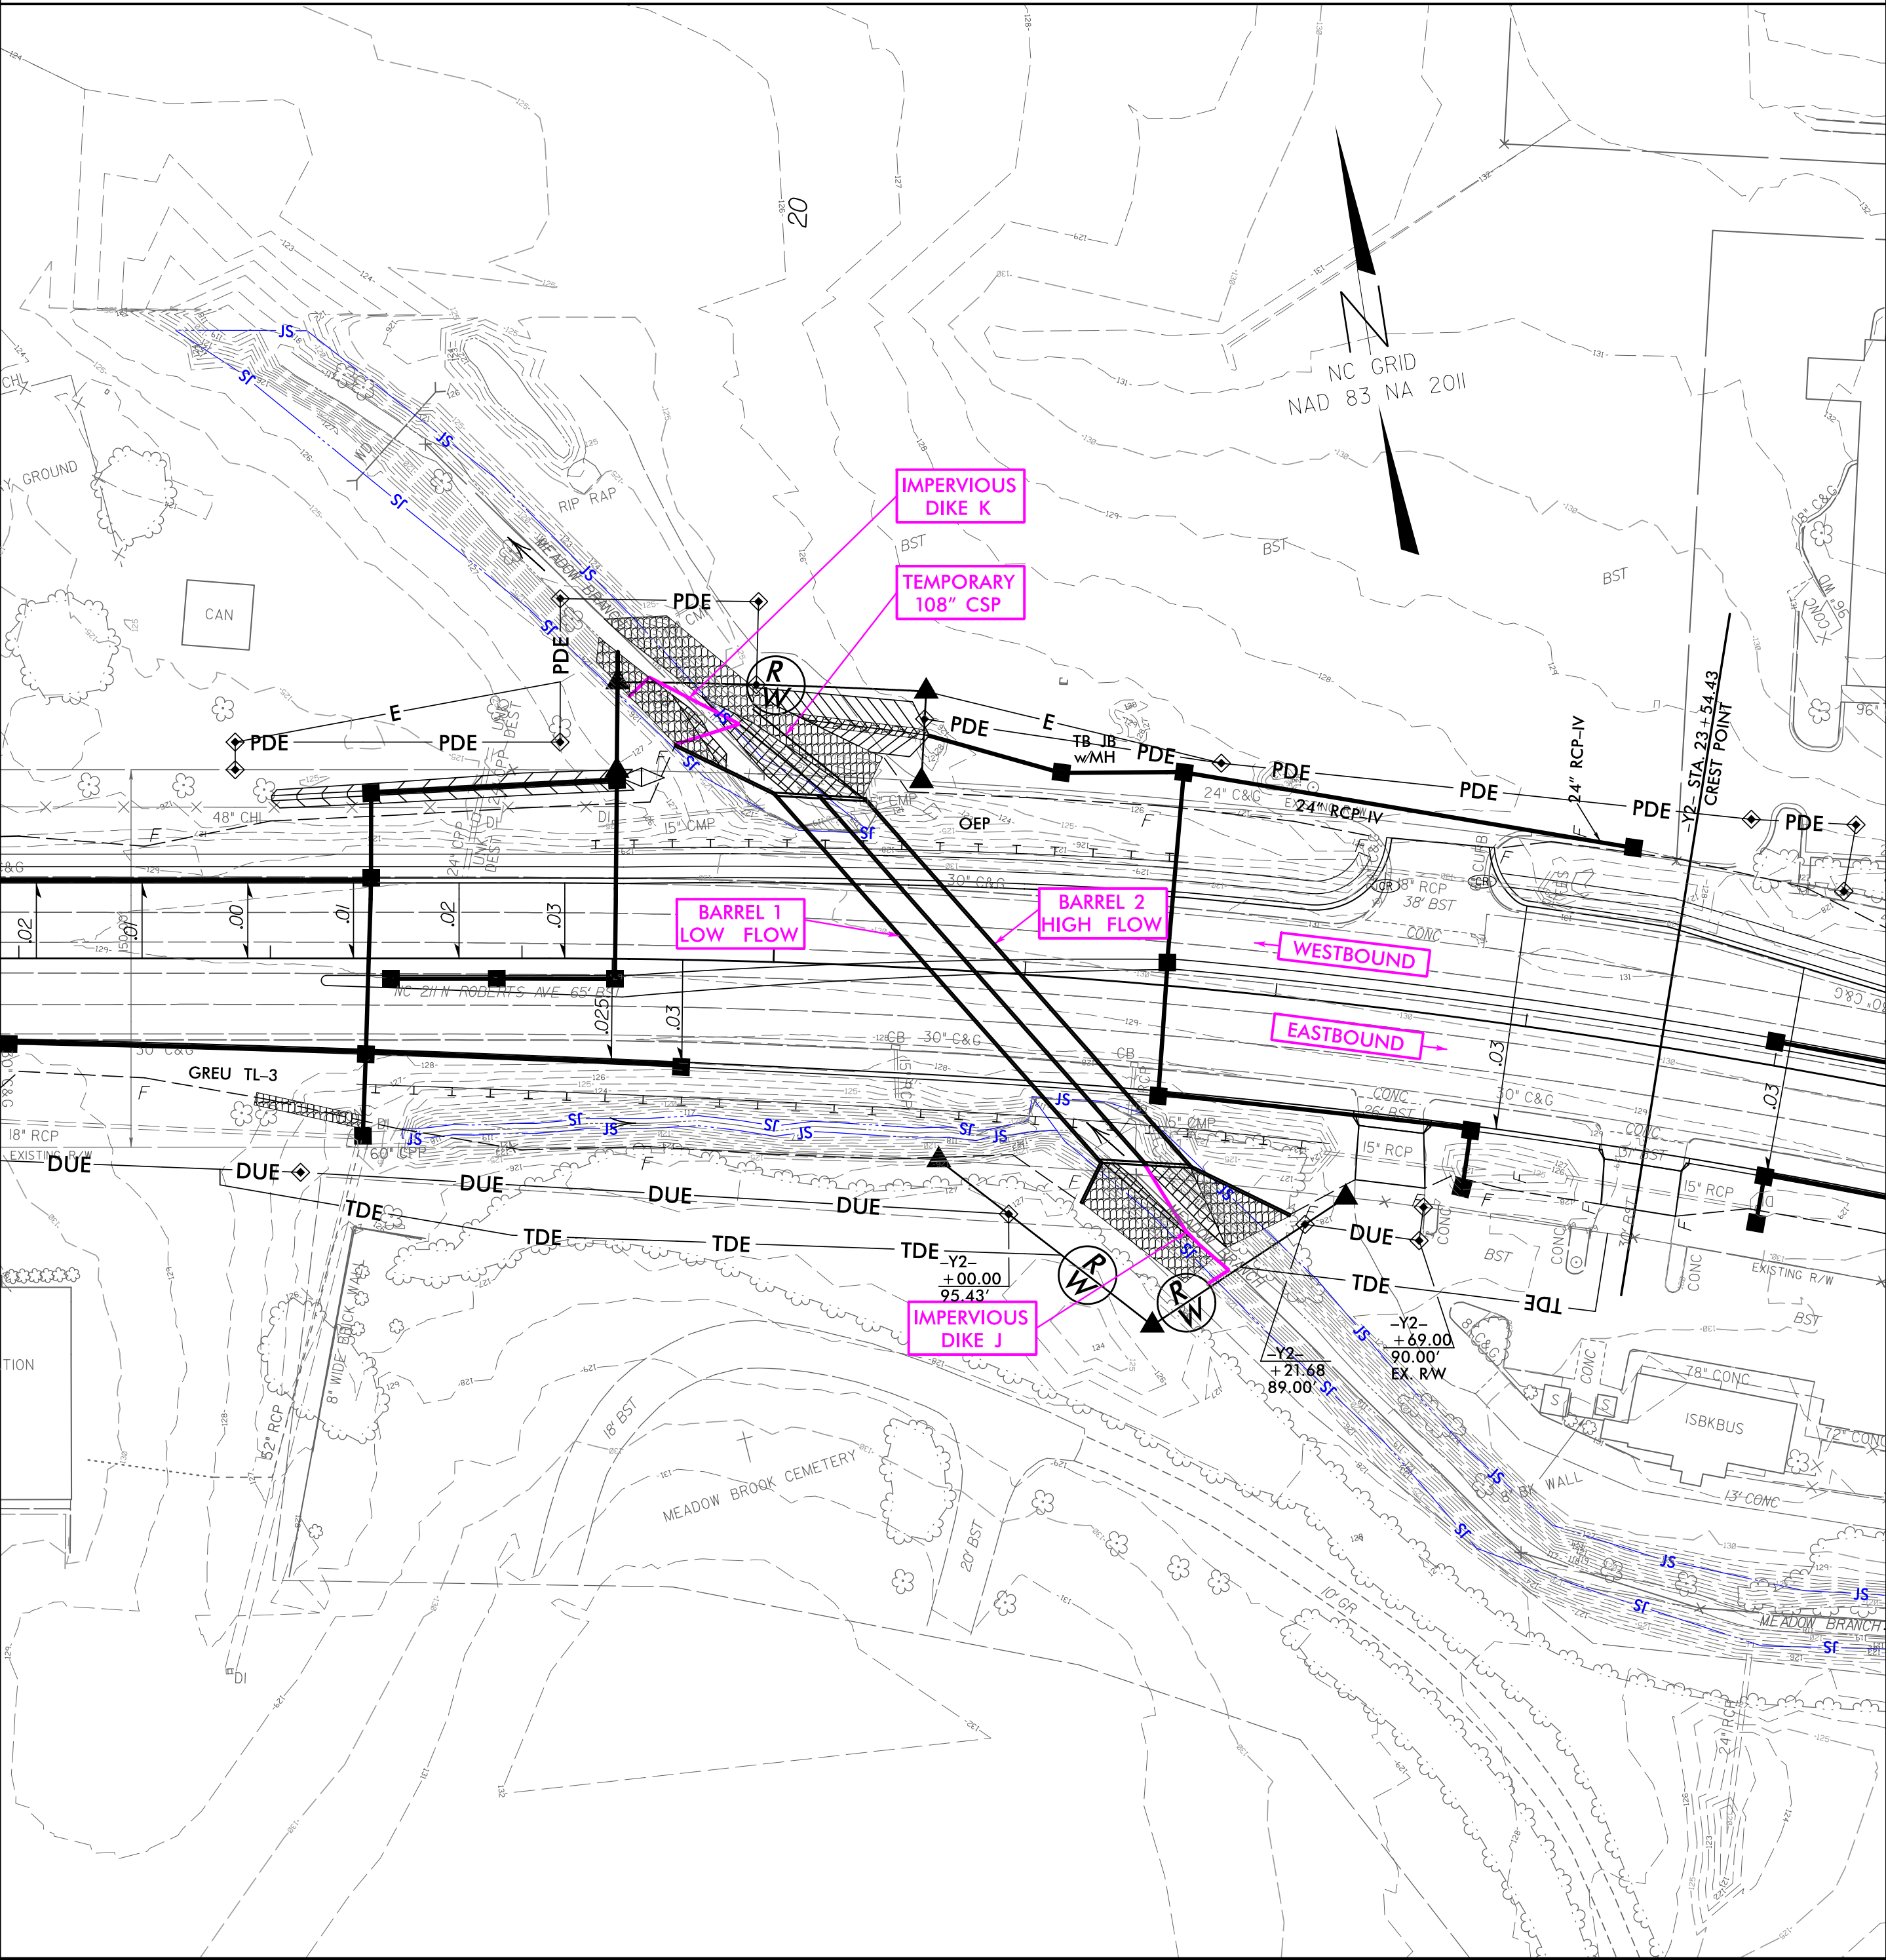

STAGE 6 (TMP PHASE VI STEP 1)

- 24. INSTALL IMPERVIOUS DIKES L AND M TO MAINTAIN FLOW THROUGH PROPOSED CULVERT BARREL 1.
- 25. COMPLETE WINGWALLS ON UPSTREAM END OF PROPOSED CULVERT BARREL 2.
- 26. EXCAVATE ANY ACCUMULATED SILT AND DEWATER BEFORE REMOVAL OF IMPERVIOUS DIKES.
- 27. REMOVE IMPERVIOUS DIKES L AND M ALLOWING NORMAL FLOW THROUGH PROPOSED BARRELS 1 AND 2.
- 28. COMPLETE CHANNEL IMPROVEMENTS AND RIP RAP EMBANKMENTS ON UPSTREAM AND DOWNSTREAM ENDS OF CULVERT.
- 29. REMOVE ANY REMAINING SPECIAL STILLING BASINS, STABILIZE DISTURBED AREA, AND COMPLETE ROADWAY.

