

PHASING

PROJ. REFERENCE NO.	SHEET NO.
15BPR.124.3	TMP-3A

BRIDGE #911084

NOTE: WORK ON BRIDGES #911083 AND #911084 MUST NOT BE DONE CONCURRENTLY. PHASES I AND II ARE INTERCHANGEABLE.

PHASE I

STEP 1
INSTALL AND COVER ALL NECESSARY DETOUR ROUTE SIGNS. SEE TMP-7C.

STEP 2
USING RSD 1101.02, SHEET 3 OF 14, AND TMP-7C, UNCOVER ALL DETOUR ROUTE SIGNS. USING RSD 1101.02, SHEET 3 OF 14, AND TMP-7 THRU TMP-7B, CLOSE NC 98 EAST AND PLACE TRAFFIC ONTO PROPOSED DETOUR SHOWN ON TMP-7C.

STEP 3
WITH TRAFFIC ON THE DETOUR(S) AND THE BRIDGE CLOSED, CONDUCT THE FOLLOWING AWAY FROM TRAFFIC:

- PARTIALLY REMOVE TOP OF BRIDGE DECK CONCRETE BY SCARIFICATION AND SHOUTBLASTING METHODS
- APPLY DECK SEALANT TO PREPARED TOP OF BRIDGE DECK
- REMOVE EXISTING JOINT MATERIAL AND INSTALL FOAM JOINTS
- REPLACE EXISTING JOINT GLAND OF EXPANSION JOINT SEALS
- CLEAN AND EXPOXY COAT EXISTING PRESTRESSED CONCRETE GIRDER ENDS
- REMOVE DEBRIS FROM TOP OF EXISTING END BENT AND BENT CAPS AND APPLY EPOXY COATING

STEP 4
INSTALL FINAL PAVEMENT MARKINGS.

STEP 5
COVER ALL DETOUR ROUTE SIGNS AND REOPEN NC 98 EAST.

STEP 6
REPEAT STEPS 2 THRU 5 AS NECESSARY UNTIL BRIDGE DECK WORK IS COMPLETE.

PHASE II

STEP 1
INSTALL AND COVER ALL NECESSARY DETOUR ROUTE SIGNS. SEE TMP-7G.

STEP 2
USING RSD 1101.02, SHEET 3 OF 14, AND TMP-7G, UNCOVER ALL DETOUR ROUTE SIGNS. USING RSD 1101.02, SHEET 3 OF 14, AND TMP-7D THRU TMP-7F, CLOSE NC 98 WEST AND PLACE TRAFFIC ONTO PROPOSED DETOUR SHOWN ON TMP-7G.

STEP 3
WITH TRAFFIC ON THE DETOUR(S) AND THE BRIDGE CLOSED, CONDUCT THE FOLLOWING AWAY FROM TRAFFIC:

- PARTIALLY REMOVE TOP OF BRIDGE DECK CONCRETE BY SCARIFICATION AND SHOUTBLASTING METHODS
- APPLY DECK SEALANT TO PREPARED TOP OF BRIDGE DECK
- REMOVE EXISTING JOINT MATERIAL AND INSTALL FOAM JOINTS
- REPLACE EXISTING JOINT GLAND OF EXPANSION JOINT SEALS
- CLEAN AND EXPOXY COAT EXISTING PRESTRESSED CONCRETE GIRDER ENDS
- REMOVE DEBRIS FROM TOP OF EXISTING END BENT AND BENT CAPS AND APPLY EPOXY COATING

STEP 4
INSTALL FINAL PAVEMENT MARKINGS.


STEP 5
COVER ALL DETOUR ROUTE SIGNS AND REOPEN NC 98 WEST.

STEP 6
REPEAT STEPS 2 THRU 6 AS NECESSARY UNTIL BRIDGE DECK WORK IS COMPLETE.

6/8/2023
U:\Traffic\Transportation Management Plan\TCP\PLAN SHEETS\15BPR\124.3_TMP_03A_PHASING.dgn
angood




Stantec Consulting Services Inc.
801 Jones Franklin Road
Suite 300
Raleigh, NC 27606
Tel. 919.851.6866
Fax. 919.851.7024
www.stantec.com
License No. F-0672



6/8/2023

DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED

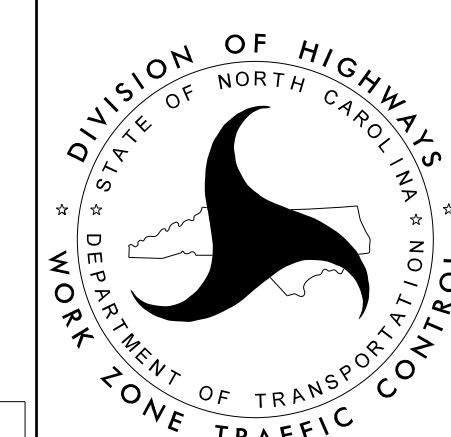

PHASING
