

AREA III



PROJ. REFERENCE NO.	SHEET NO.
R-2206C	TCP-15A

PHASE III (CONT.)

THE CONTRACTOR SHALL COMPLETE THE WORK REQUIRED OF PHASE III, STEPS 2 THRU 4 FROM 6:00 P.M. FRIDAY THRU 7:00 A.M. MONDAY. (SEE INTERMEDIATE CONTRACT TIME AND LIQUIDATED DAMAGES).

STEP 2. USING RSD NO. 1101.02 (SHEET 1 OF 7), PLACE ONE LANE, TWO-WAY TRAFFIC ONTO -Y14DET- EASTBOUND LANE (SEE SECTIONS D-D AND E-E). CONSTRUCT -Y14- TIE-IN (LEFT LANE) FROM STA. 12+20+/- TO STA. 12+70+/- AND FROM STA. 19+50+/- TO STA. 21+00+/-, UP TO BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE. PLACE TEMPORARY (PAINT) PAVEMENT MARKINGS AS MUCH AS POSSIBLE ON -Y14- (SEE PM-2 THRU 4). REFER TO RSD NOS. 1205.01, 1205.02, 1205.03, 1205.04, AND 1205.05 WHEN PLACING TEMPORARY (PAINT) PAVEMENT MARKINGS, SEE TCP-1 FOR TEMPORARY PAVEMENT MARKING SCHEDULE.



STEP 3. USING FLAGGERS, PLACE ONE LANE, TWO-WAY TRAFFIC ONTO -Y14- WESTBOUND LANE (SEE SECTIONS D-D AND E-E). CONSTRUCT -Y14- TIE-IN (RIGHT LANE) FROM STA. 12+20+/- TO STA. 12+70+/- AND FROM STA. 19+50+/- TO STA. 21+00+/-, UP TO BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE. PLACE REMAINING TEMPORARY (PAINT) PAVEMENT MARKINGS ON -Y14-.

STEP 4. OPEN -Y14- TO A 2-LANE, TWO-WAY TRAFFIC PATTERN.
INSTALL ALL BARRICADES AND DRUMS AS SHOWN ON THIS SHEET. MAINTAIN ACCESS TO ALL DRIVEWAYS WITHIN PROJECT LIMITS.

STEP 5. USING RSD NO. 1101.02 (SHEET 1 OF 7), CONSTRUCT -RPA- FROM STA. 15+31+/- TO STA. 15+53+/- AND -RPD- FROM STA. 14+96+/- TO STA. 15+20+/-, INCLUDING DRAINAGE, UP TO BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE.
CONSTRUCT -Y14- RIGHT TURN LANE AND PAVED SHOULDER FROM STA. 13+25+/- TO STA. 16+25+/-, UP TO BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE.
OBLITERATE REMAINING -Y14DET- PAVEMENT AND REMOVE TEMPORARY CAPS FOR GRATE INLETS (SEE ROADWAY PLANS).
USING TRENCHLESS CONSTRUCTION, INSTALL 1200mm RCP AT -Y14- STA. 20+03+/- (SEE ROADWAY PLANS).
CONTINUE CONSTRUCTION OF -L- LINE FROM FROM STA. 237+58+/- TO STA 238+19+/- UP TO PROPOSED GRADE LINE AND -L- LINE STRUCTURES (SEE STRUCTURE PLANS).

STEP 6. USING RSD NO. 1101.02 (SHEET 1 OF 7), PLACE FINAL PAVEMENT MARKINGS ON -Y14- FROM STA. 12+20+/- TO STA. 21+00+/- . REFER TO RSD NOS. 1205.01 AND 1205.02, 1205.03, 1205.04, 1205.05, 1250.01, AND 1251.01 WHEN PLACING FINAL (THERMO) PAVEMENT MARKINGS, SEE PM-2 THRU PM-4 FOR FINAL PAVEMENT MARKINGS. SEE PM-1 FOR FINAL PAVEMENT MARKING SCHEDULE.

PLACE ALL TYPE III BARRICADES AND DRUMS DEVICES TO BE LEFT IN PLACE AT COMPLETION OF PROJECT AS SHOWN ON PM-2 THRU PM-4.

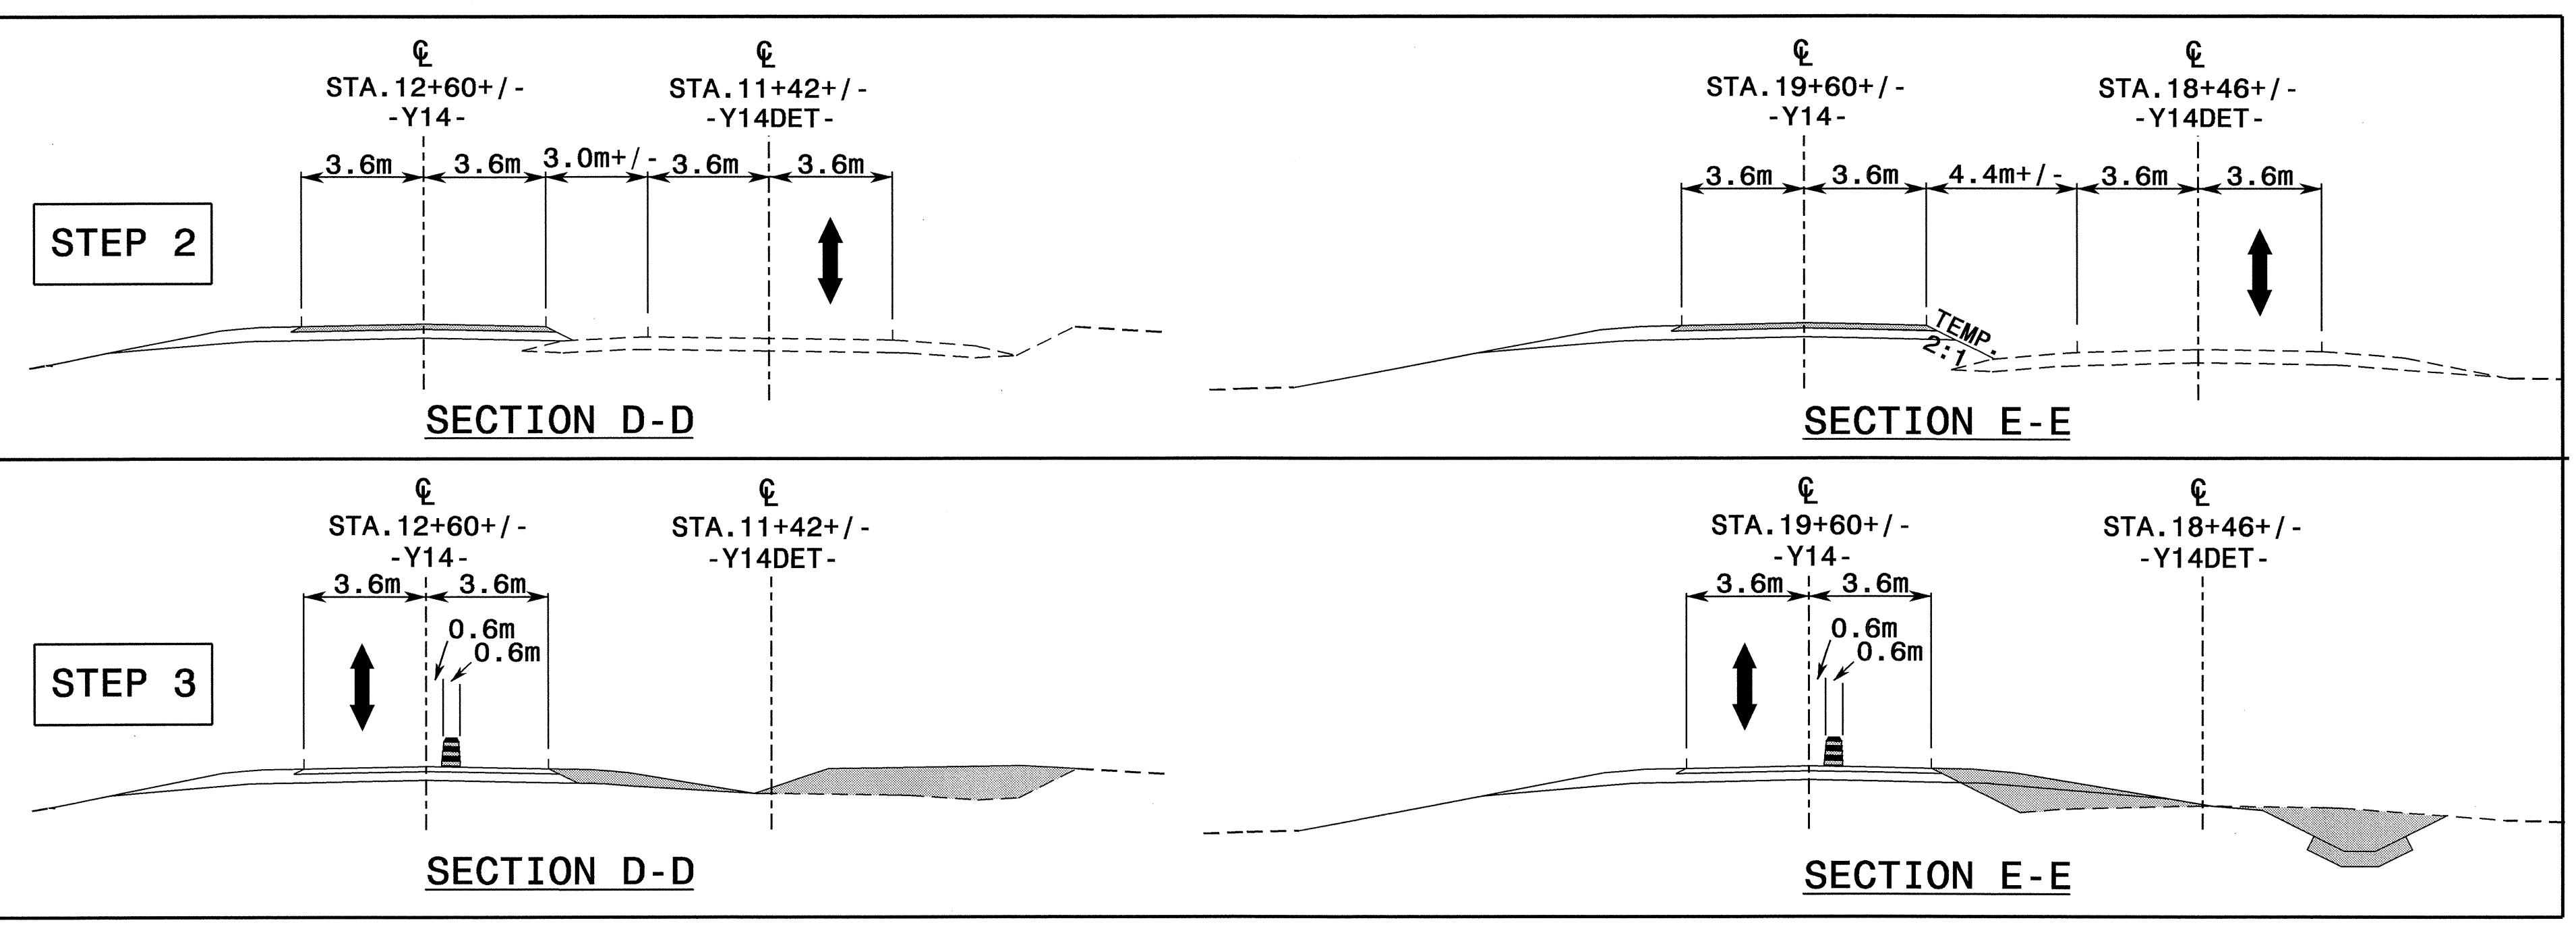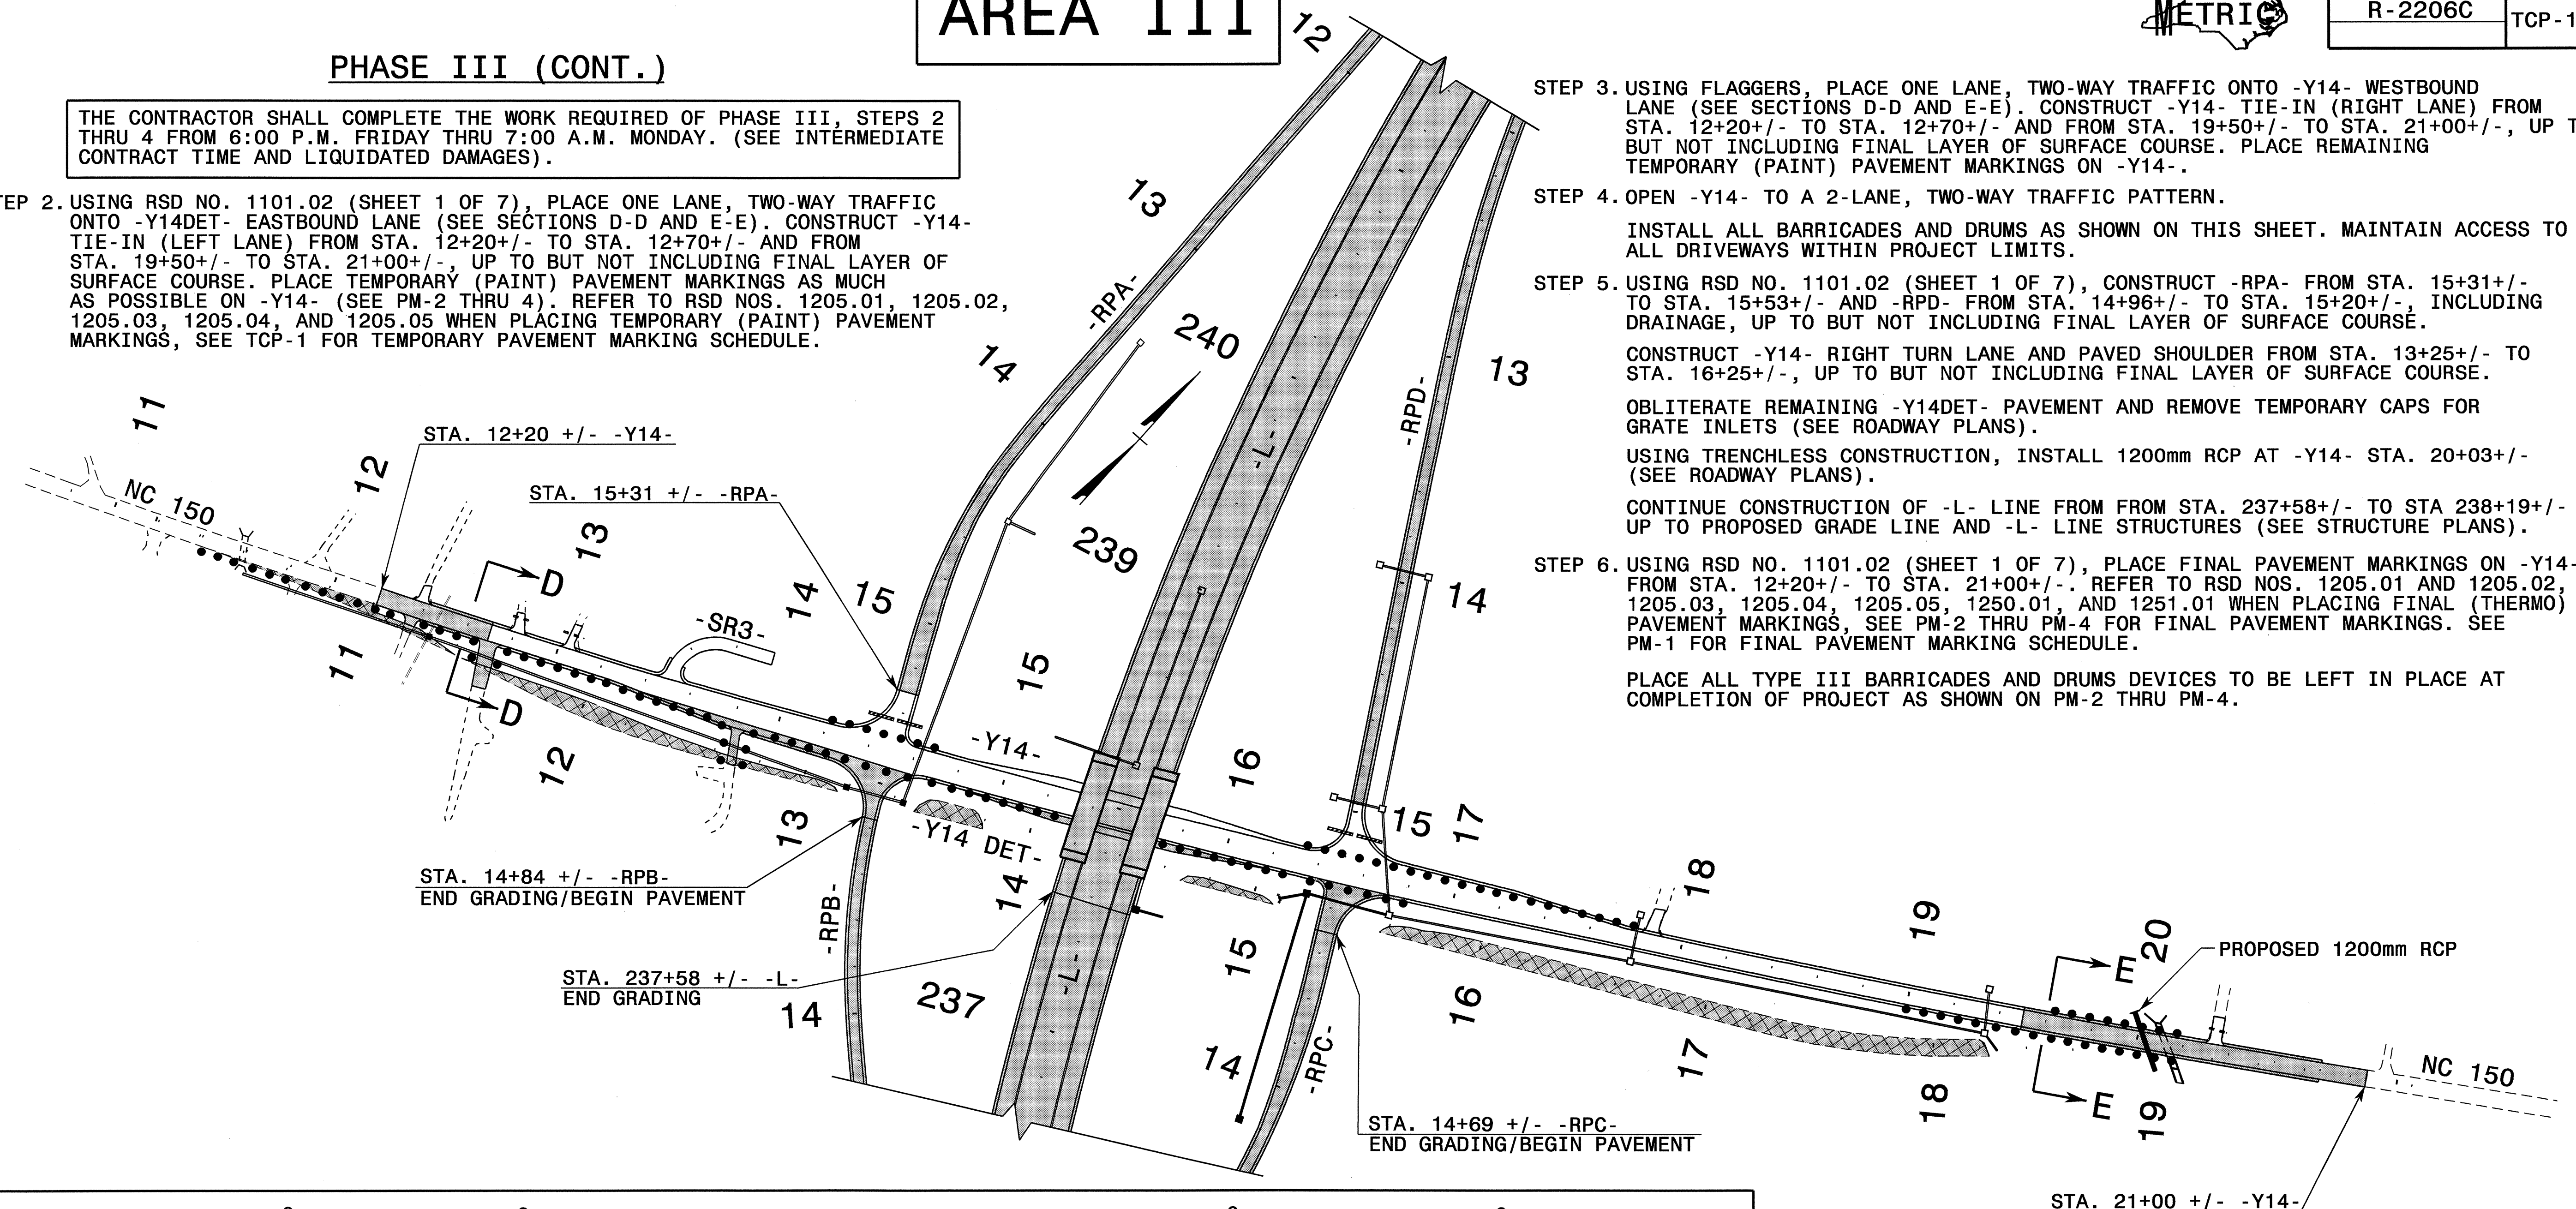

SEE TCP-16 AND RSD 1101.03 (SHEET 1 OF 9) FOR OFFSITE DETOUR AND SIGNING WHEN INSTALLING OVERHEAD BRIDGE GIRDERS OVER NC 150.

APPROVED:	DATE: 7/2/04	AREA 3 PHASE III (CONT.) DETAILS AND PHASING							
SEAL									
SCALE: 1:1500	DATE: 05-10-04	<table border="1"> <tr> <th colspan="2">REVISIONS</th> </tr> <tr> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> </tr> </table>		REVISIONS					
REVISIONS									
DWG. BY: SBC	DESIGN BY: SBC	REVIEWED BY: CLM							
			<small>CARD FILE</small>						

12-JUL-2004 13:26
 K:\TCP\AREA3\2206C.TC\AREA3_Tcp15A.dgn
 SCOOTERS AT TET206428
