

**STEP 8)** COMPLETE CONSTRUCTION OF US 29 OUTSIDE WIDENING FROM STEP 6.

USE RSD 1101.02 (SHEET 4 OF 14) FOR TEMPORARY LANE CLOSURES AND REMOVE OUTSIDE PCB ON US 29 AND PLACE DRUMS ALONG OUTSIDE SHOULDERS. (SEE TMP-15)

**SR 2817 (BARNES ST) STAGE 3 BRIDGE CONSTRUCTION**

**STEP 9)** USE RSD 1101.02 (SHEET 1 OF 14) AND FLAGGERS AS NEEDED FOR TEMPORARY LANE CLOSURES, INSTALL AND COVER TEMPORARY SIGNALS AT BOTH RAMP TERMINALS.

WORK AWAY FROM TRAFFIC OR BEHIND BARRIER TO PLACE TEMPORARY PAVEMENT MARKINGS (PAINT) AND MARKERS (RAISED) ON THE WESTBOUND LANE OF -L- ACCORDING TO THE FOLLOWING STATIONS: (SEE TMP-13 THRU TMP-14)

- L- STA. 32+31+/- TO STA. 33+83.5+/- WBL
- L- STA. 33+83.5+/- TO STA. 35+62.5+/- WBL
- L- STA. 35+62.5+/- TO STA. 38+17+/- WBL

**STEP 10)** USE RSD 1101.02 (SHEET 1 AND 4 OF 14) AND FLAGGERS AS NEEDED, COMPLETE TEMPORARY PAVEMENT MARKING (PAINT) AND MARKERS (RAISED) ACCORDING TO THE FOLLOWING STATIONS: (SEE TMP-13 THRU TMP-14)

- L- STA. 28+00+/- TO STA. 32+31 +/-
- L- STA. 38+17+/- TO STA. 42+00 +/-

PLACE DRUMS IN MEDIAN, UNCOVER AND ACTIVATE SIGNALS AND SHIFT TRAFFIC INTO TEMPORARY PATTERN.

SHIFT WESTBOUND TRAFFIC INTO NEW WESTBOUND LANE AND USE FLAGGERS TO STOP EASTBOUND TRAFFIC AND COMPLETE PAVEMENT MARKING FOR THE EASTBOUND LANE AND TO RESET PCB ALONG -L- ACCORDING TO THE FOLLOWING STATION: (SEE TMP-13 AND TMP-14).

- L- STA. 31+82+/- TO STA. 37+82 +/- LT

**STEP 11)** WORK BEHIND BARRIER TO CONSTRUCT STAGE 3 SIDEWALK AND RAIL ALONG WESTBOUND LANE OF THE PROPOSED BRIDGE AND -L- (SR 2817) AND RAMP CONSTRUCTION UP TO, BUT NOT INCLUDING THE FINAL LAYER OF SURFACE COURSE, ACCORDING TO THE FOLLOWING STATIONS: (SEE TMP-13 THRU TMP-14)

- L- STA. 31+60+/- TO STA. 38+37+/- LT

USE DETAIL ON TMP-2E TO CLOSE RAMPS AND DETOUR RAMP TRAFFIC TO THE NEXT INTERCHANGE AND CONSTRUCT RAMPS UP BUT NOT INCLUDING THE FINAL LAYER OF SURFACE COURSE ACCORDING TO THE FOLLOWING STATIONS:

- RPA- STA. 12+50+/- TO -RPA- STA. 13+51+/- LT

**STEP 12)** USE RSD 1101.02 (SHEETS 1 OF 14) AND FLAGGERS FOR TEMPORARY LANE CLOSURE AND REMOVE PCB ACROSS BRIDGE.

**PHASE IV**

**STEP 1)** USE RSD 1101.02 (SHEETS 3 AND 4 OF 14) FOR TEMPORARY LANE CLOSURES ON -L- (BARNES ST), -Y- (US 29), AND RAMPS TO CONSTRUCT MONOLITHIC ISLANDS AND PLACE THE FINAL LAYER OF SURFACE COURSE. USE RSD 1205.01, 1205.02, 1205.04, 1205.05, 1205.08, 1205.09, 1205.12, 1250.01, AND 1253.01 TO PLACE FINAL PAVEMENT MARKING (THERMOPLASTIC AND POLYUREA) AND MARKERS (SNOWPLOWABLE AND RAISED) IN FINAL PATTERN ACCORDING TO THE FOLLOWING STATIONS: (SEE TMP-12 THRU TMP-15 AND PAVEMENT MARKING PLANS)

- L- STA. 16+00 +/- TO STA. 42+00 +/-
- Y- STA. 15+00+/- TO STA. 26+00+/-
- Y1- STA. 11+00+/- TO STA. 12+19+/-
- RPA- STA. 12+50 +/- TO STA. 13+51 +/-
- RPB- STA. 15+00 +/- TO STA. 16+31 +/-
- RPC- STA. 12+20 +/- TO STA. 13+61 +/-
- RPD- STA. 11+70 +/- TO STA. 13+75 +/-

AND COVER TEMPORARY PAVEMENT MARKINGS WITH 12" BLACK MARKING LINES (SEE LOCAL NOTES) AND PLACE FINAL PAVEMENT MARKING (POLYUREA) AND MARKERS (SNOWPLOWABLE) BACK INTO ORIGINAL PATTERN ACCORDING TO THE FOLLOWING STATIONS:


- Y- STA. 10+50 +/- TO STA. 15+00 +/- NBL
- Y- STA. 11+50 +/- TO STA. 15+00 +/- SBL
- Y- STA. 26+00 +/- TO STA. 29+50 +/- NBL
- Y- STA. 26+00 +/- TO STA. 33+00 +/- SBL

COVER ANY TEMPORARY PAVEMENT MARKINGS ON -L- (SR 2817) THAT EXTEND BEYOND THE FINAL PAVING LIMITS WITH 12" BLACK PAVEMENT MARKING LINES (SEE LOCAL NOTES) OR REMOVE MARKINGS AS DIRECTED BY THE ENGINEER. PLACE FINAL PAVEMENT MARKINGS (POLYUREA) IN THE ORIGINAL PATTERN.


REMOVE ALL REMAINING TRAFFIC CONTROL SIGNS AND DEVICES AND OPEN PROJECT FULLY TO TRAFFIC.

2/15/2023 BR0041.TC\_TMP\_03B\_Phasing.dgn jon.ar.chambault


**AECOM**  
 NC Firm License No.: F-0342  
 5438 Wade Park Boulevard  
 Suite 200 Raleigh, NC 27607  
 Phone: 919-461-1100

APPROVED:   
 DATE: 2/15/2023

SEAL



**DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED**

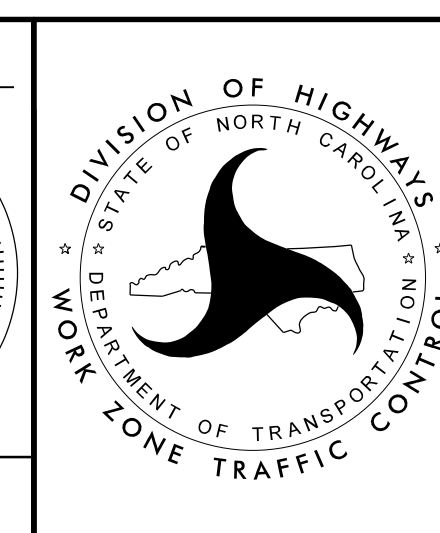

PROJECT PHASING
