


CLOSE THE MEDIAN OPENING/ TURN LANE AS NEEDED TO COMPLETE THE DRAINAGE AND ROADWAY CONSTRUCTION. PROTECT THE EXCAVATION FOR DRAINAGE CONSTRUCTION WITH TEMPORARY PORTABLE CONCRETE BARRIER W/ DRAINAGE SLOTS.

CLOSE THE MEDIAN OPENING/ TURN LANE AS NEEDED TO COMPLETE THE DRAINAGE AND ROADWAY CONSTRUCTION.

DO NOT CLOSE THE ADJACENT UPSTREAM/ DOWNSTREAM MEDIAN OPENINGS/ TURN LANES AT THE SAME TIME.

DO NOT CLOSE THE ADJACENT UPSTREAM/ DOWNSTREAM MEDIAN OPENINGS/ TURN LANES AT THE SAME TIME.

DELINEATE PROPOSED MEDIAN WITH SKINNY DRUMS AND TEMPORARY PAVEMENT MARKINGS TO IMPLEMENT FINAL LANE CONFIGURATION. IN ACCORDANCE WITH THE TIME RESTRICTIONS ON TMP-2, CLOSE THE INSIDE TRAVEL LANES ON -L- (US 421) AS NEEDED TO CONSTRUCT THE MEDIAN OF -L-. SEE RSD 1101.02, SHEET 3 OF 14 FOR DETAIL.

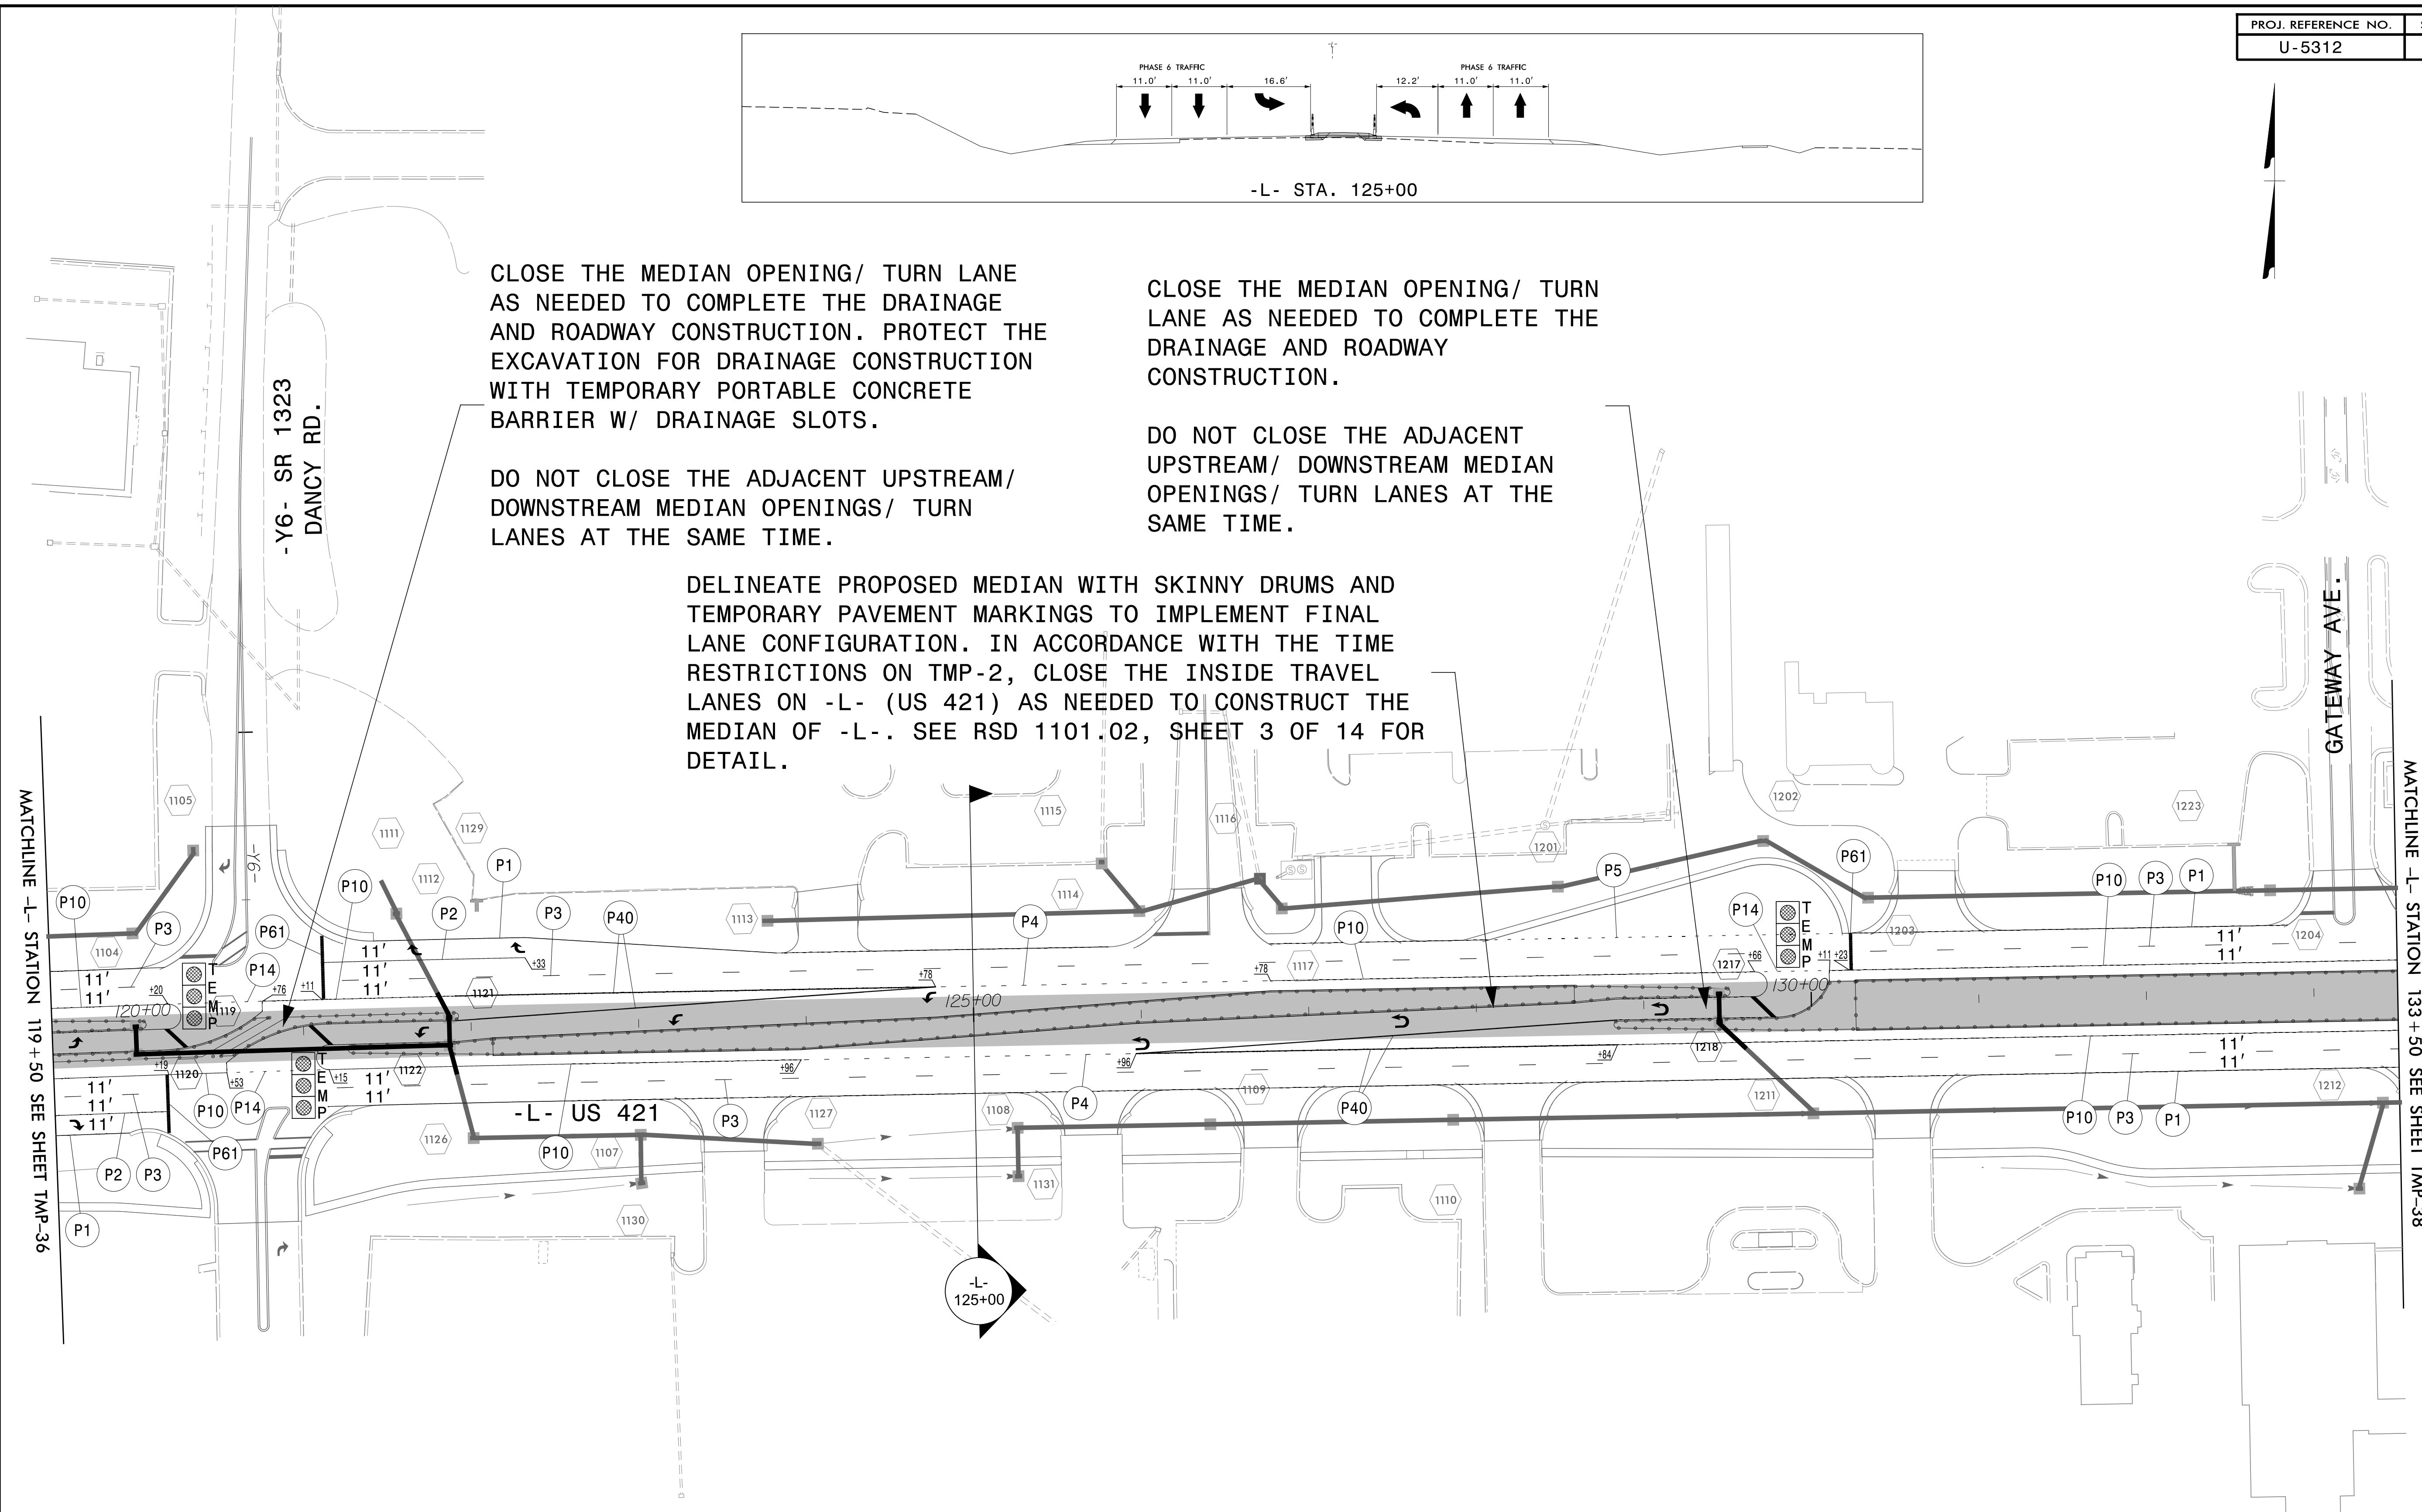

MATCHLINE -L- STATION 119 + 50 SEE SHEET TMP-36


MATCHLINE -L- STATION 133 + 50 SEE SHEET TMP-38

NOTE: INSTALL TEMPORARY PAINT PAVEMENT MARKINGS IN ACCORDANCE WITH FINAL PAVEMENT MARKING PLANS UNLESS SPECIFIED OTHERWISE.

APPROVED: _____
 DATE: _____

8/10/2023

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED



PHASE 6 DETAIL

8/9/2023
 R:\TrafficControl\CP\U5312_fc_tmp37.dgn
 User:jtowndsend
