



INCOMPLETE PLANS
DO NOT USE FOR R/W ACQUISITION
PRELIMINARY PLANS
DO NOT USE FOR CONSTRUCTION

SOIL TEST RESULTS															
SAMPLE NO.	OFFSET	STATION	DEPTH INTERVAL	AASHTO CLASS.	LL	PI	% BY WEIGHT				% PASSING (SIEVES)			% MOISTURE	% ORGANIC
							C.SAND	F.SAND	SILT	CLAY	10	40	200		
S-12	8.5M RT	22+00	0.70-0.80	A-7-5(50)	83	45	3.6	5.6	16.5	74.3	99	97	91		
S-12A	8.5M RT	22+00	1.10-1.20	A-7-5(22)	60	22	6.4	19.5	40.0	34.1	100	96	81		
S-53	5M RT	22+60	0.50-0.80	A-7-5(50)	85	51	8.1	8.1	17.2	66.7	99	92	85		
S-13	9.5M RT	23+00	0.70-0.80	A-7-5(30)	70	27	6.2	10.2	41.4	42.2	100	96	87		
S-13A	9.5M RT	23+00	2.40-2.50	A-7-5(9)	52	19	28.5	22.3	29.1	20.1	100	79	56		
S-14	7.5M LT	24+20	0.50-0.60	A-4(0)	20	3	28.7	29.3	21.9	20.1	90	73	42		
S-14A	7.5M LT	24+20	1.20-1.30	A-7-6(11)	41	16	12.0	21.9	42.0	24.1	99	93	71		
S-14B	7.5M LT	24+20	1.40-1.50	A-2-4(0)	26	8	42.8	24.3	24.9	8.0	95	64	35		

PI = 21+54.000
EL = 265.407 m
VC = 64 m
K = 57

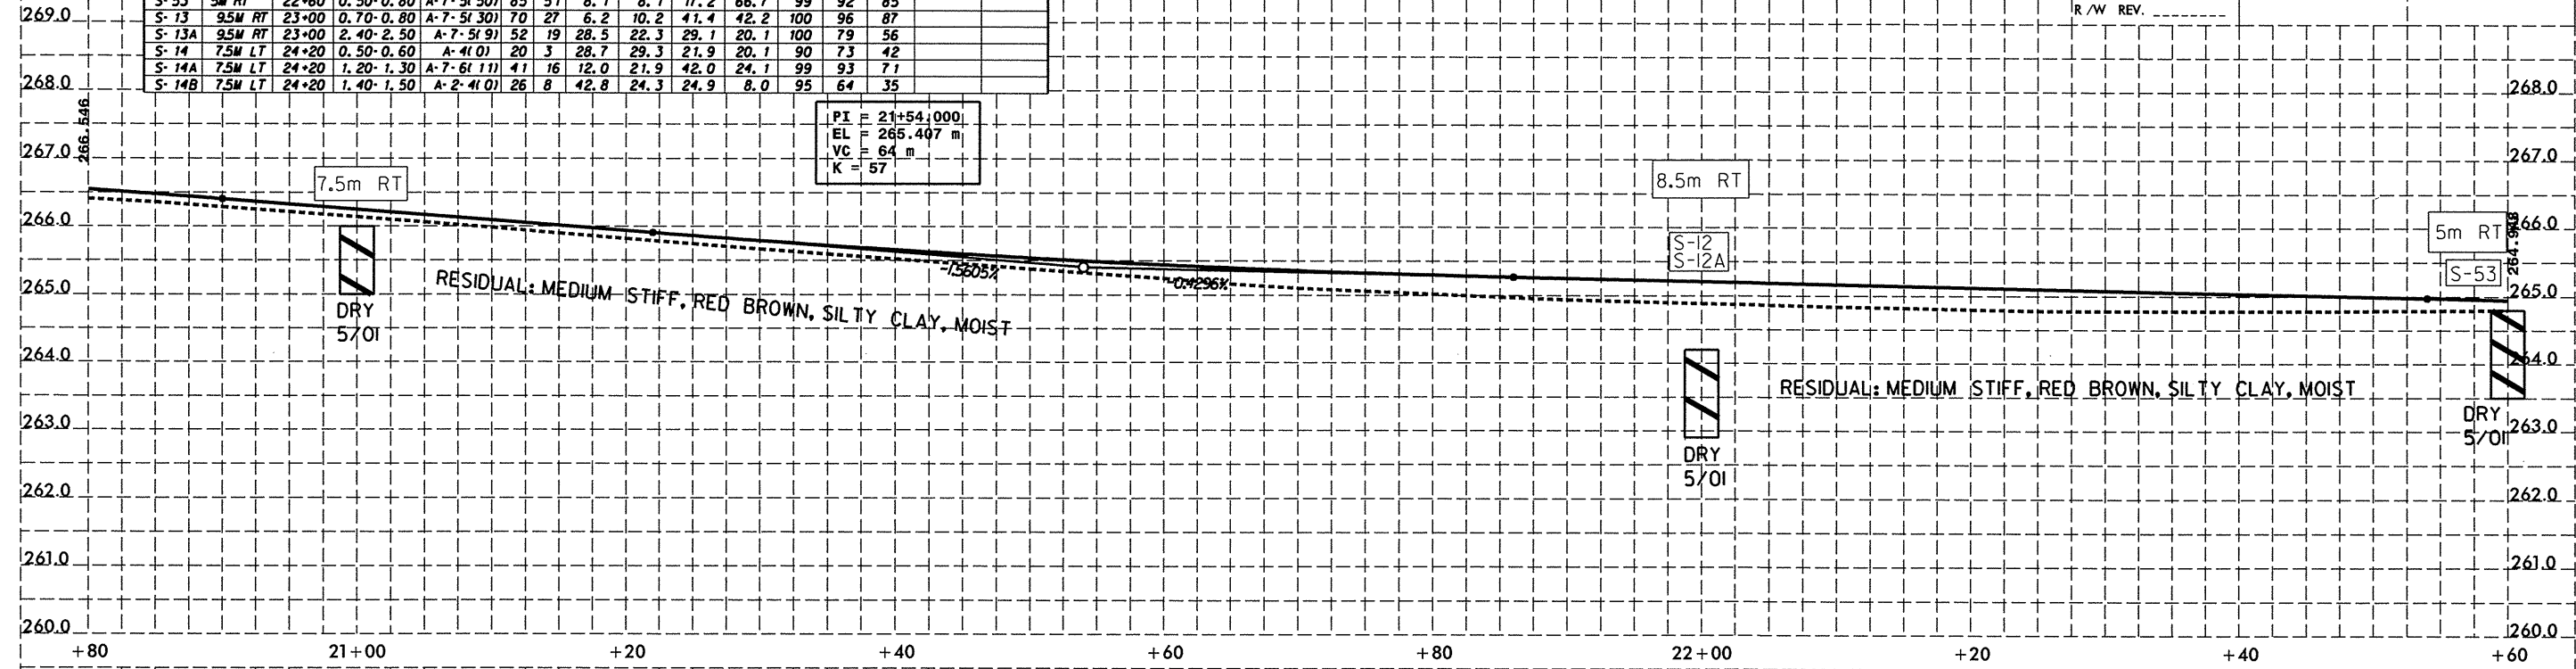

PI = 22+96.000
EL = 264.797 m
VC = 84 m
K = 46

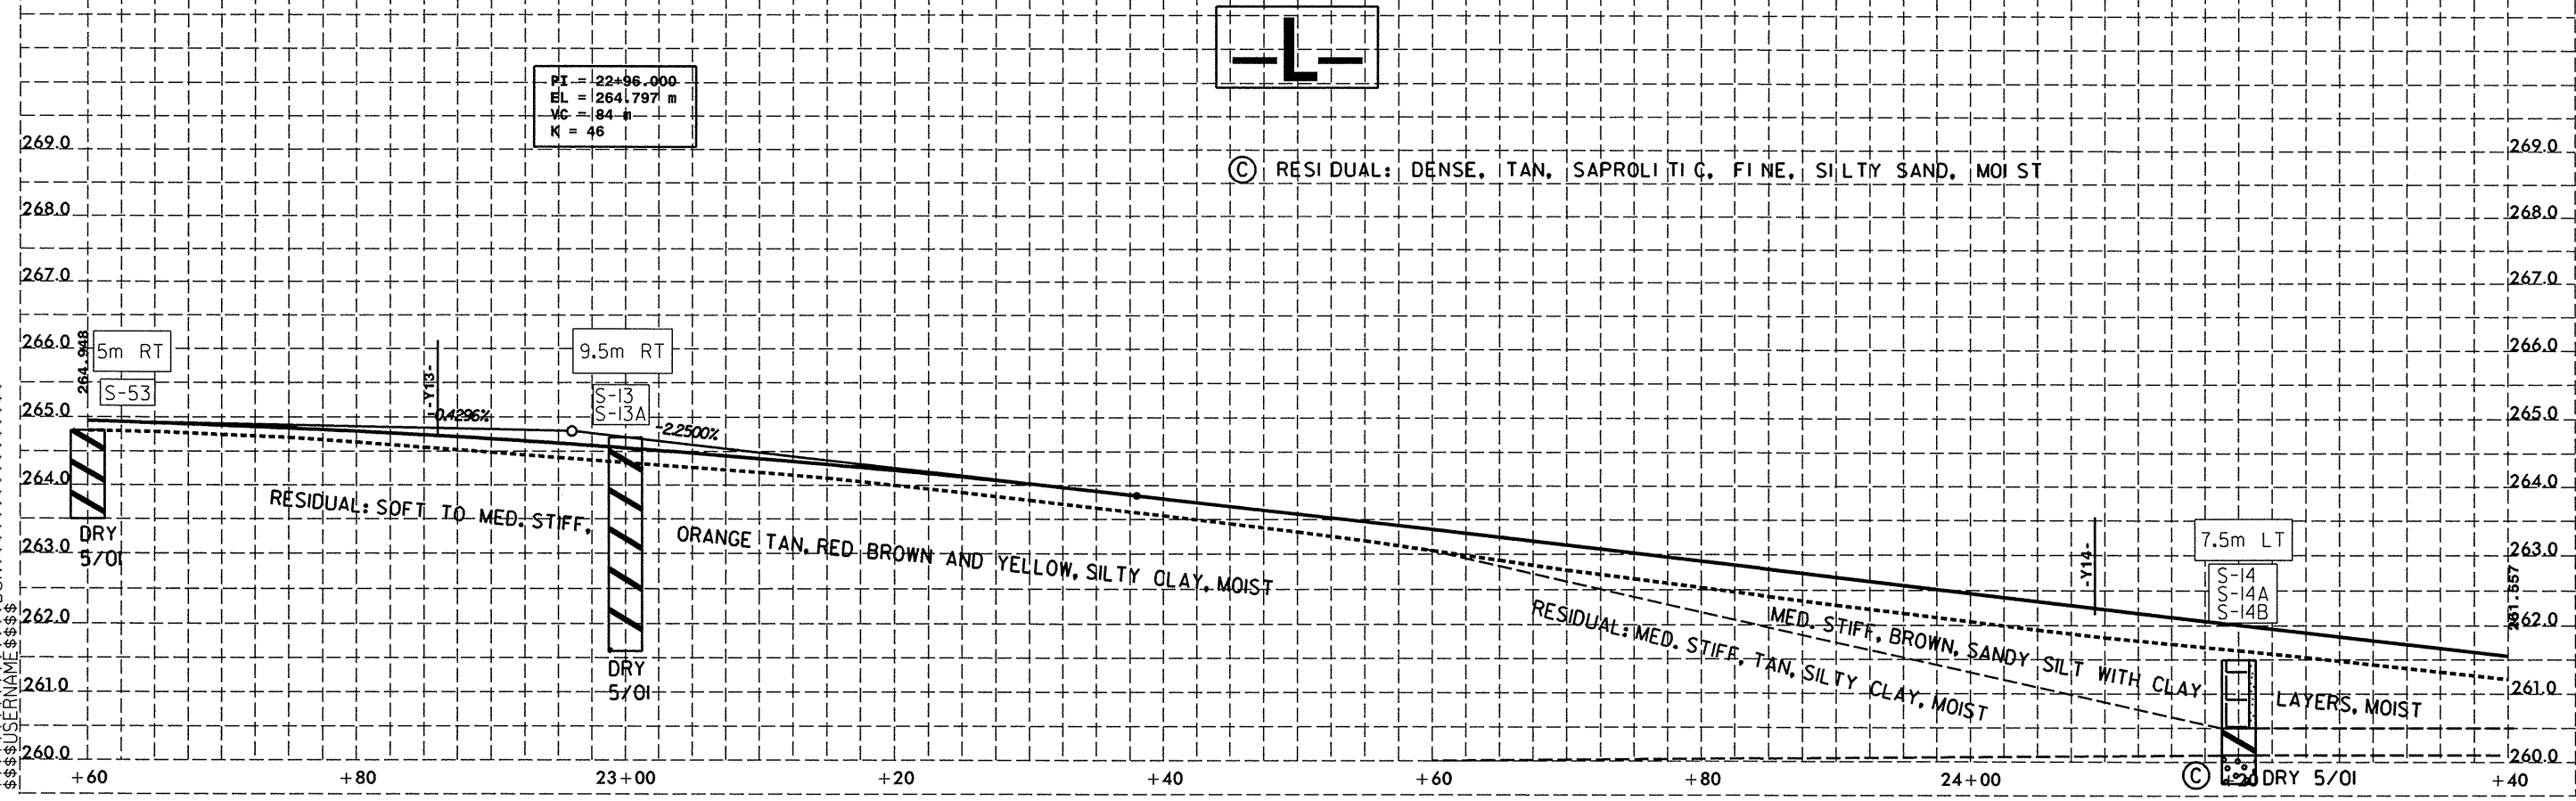

SYSTEM TIME: 08/01/2001 10:00:00
DGN: 08/01/2001 10:00:00
PLN: 08/01/2001 10:00:00
PLOT: 08/01/2001 10:00:00
