


PROJ. REFERENCE NO.	SHEET NO.
B-3857	TCP-4

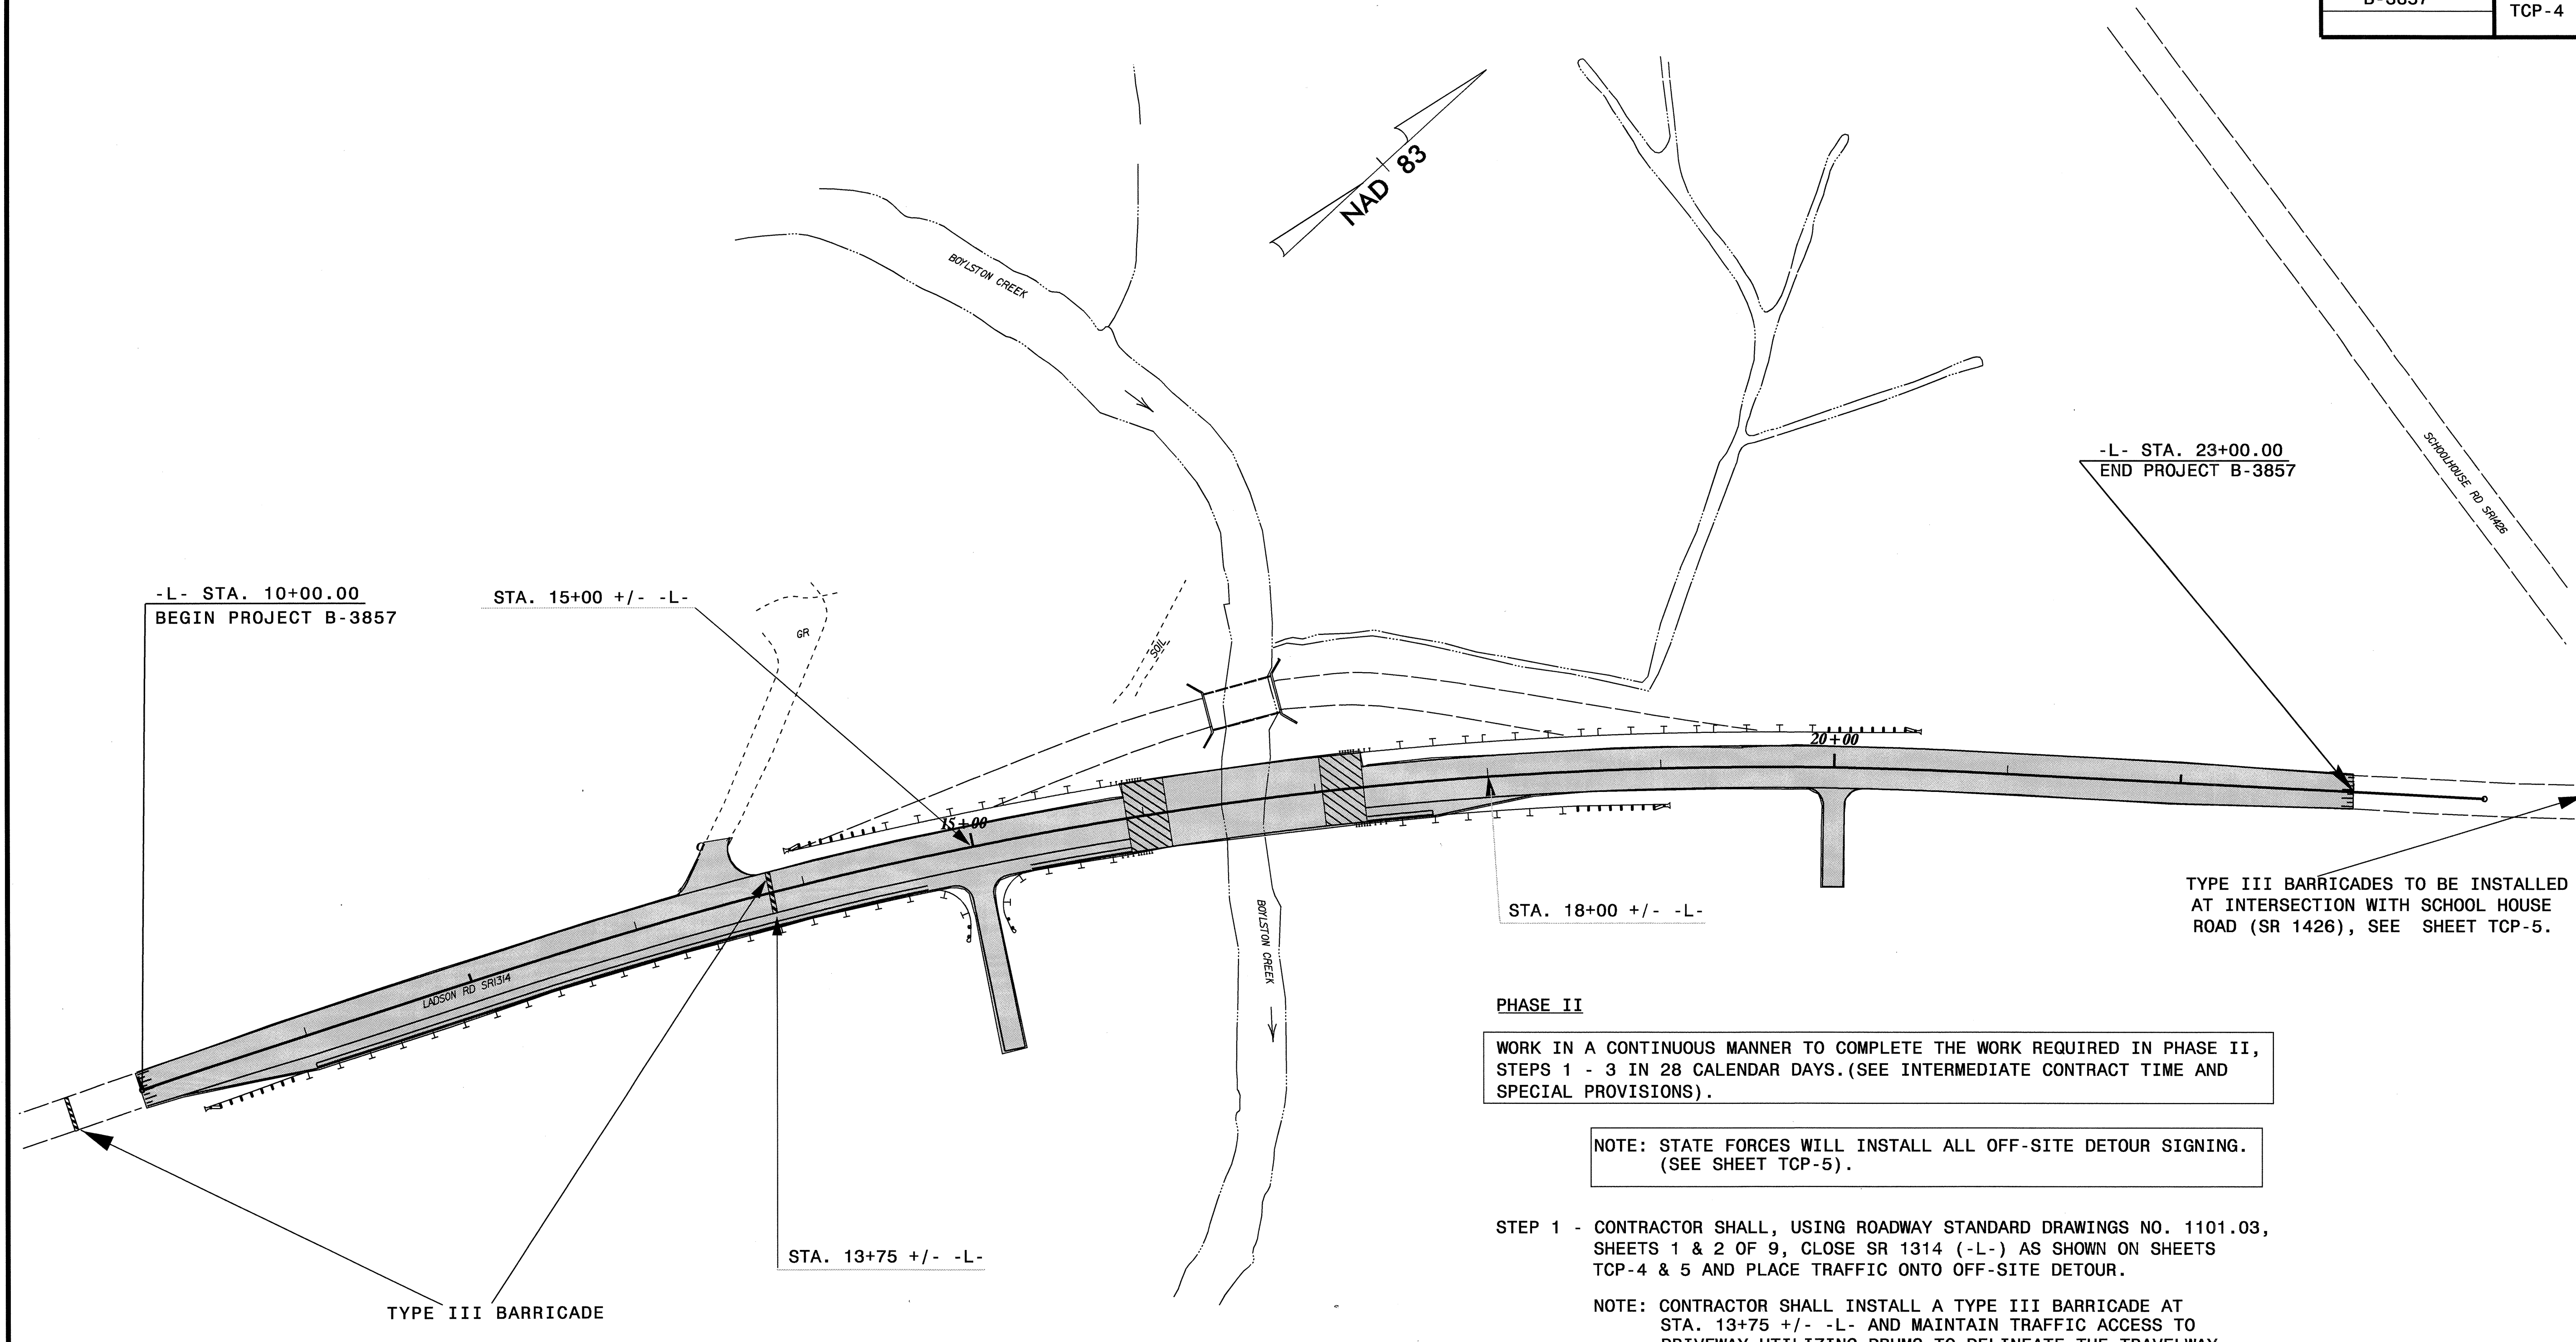

-L- STA. 10+00.00  
BEGIN PROJECT B-3857

STA. 15+00 +/- -L-

-L- STA. 23+00.00  
END PROJECT B-3857

STA. 18+00 +/- -L-

STA. 13+75 +/- -L-

TYPE III BARRICADES TO BE INSTALLED  
AT INTERSECTION WITH SCHOOL HOUSE  
ROAD (SR 1426), SEE SHEET TCP-5.

TYPE III BARRICADE

**PHASE II**

WORK IN A CONTINUOUS MANNER TO COMPLETE THE WORK REQUIRED IN PHASE II, STEPS 1 - 3 IN 28 CALENDAR DAYS. (SEE INTERMEDIATE CONTRACT TIME AND SPECIAL PROVISIONS).

NOTE: STATE FORCES WILL INSTALL ALL OFF-SITE DETOUR SIGNING. (SEE SHEET TCP-5).

STEP 1 - CONTRACTOR SHALL, USING ROADWAY STANDARD DRAWINGS NO. 1101.03, SHEETS 1 & 2 OF 9, CLOSE SR 1314 (-L-) AS SHOWN ON SHEETS TCP-4 & 5 AND PLACE TRAFFIC ONTO OFF-SITE DETOUR.

NOTE: CONTRACTOR SHALL INSTALL A TYPE III BARRICADE AT STA. 13+75 +/- -L- AND MAINTAIN TRAFFIC ACCESS TO DRIVEWAY UTILIZING DRUMS TO DELINEATE THE TRAVELWAY.

STEP 2 - CONSTRUCT THE REMAINDER OF PROPOSED SR 1314 (-L-) UP TO, BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE. (SEE CONSTRUCTION PLANS).

- PLACE INTERMEDIATE PAVEMENT MARKINGS (PAINT), ON PROPOSED SR 1314 (-L-) FROM STA. 10+00 +/- -L- TO STA. 23+00 +/- -L-. (SEE SHEET TCP-6).

STEP 3 - OPEN PROPOSED SR 1314 (-L-) TO THE FINAL TRAFFIC PATTERN (SEE SHEET TCP-6).

20-JUN-2005 07:11  
\\nets-ccfso\538574\tcp\top\b3857-rc-top4.dgn  
mwashaya AT TC0224168

APPROVED:	DATE: 6/5/05	<b>PHASE II</b>	
	SCALE: NONE		REVISIONS
	DATE: 06-05		
	DWG. BY: MW		
	DESIGN BY: MW		
REVIEWED BY: JWG			
