

WORK ZONE TRAFFIC CONTROL GENERAL REQUIREMENTS

LANE CLOSURE RESTRICTIONS

CHANGES MAY BE REQUIRED WHEN PHYSICAL DIMENSIONS IN THE DETAIL DRAWINGS, STANDARD DETAILS, AND ROADWAY DETAILS ARE NOT ATTAINABLE TO MEET FIELD CONDITIONS OR RESULT IN DUPLICATE OR UNDESIRED OVERLAPPING OF DEVICES. MODIFICATION MAY INCLUDE: MOVING, SUPPLEMENTING, COVERING, OR REMOVAL OF DEVICES AS DIRECTED BY THE ENGINEER.

THE FOLLOWING GENERAL NOTES APPLY AT ALL TIMES FOR THE DURATION OF THE CONSTRUCTION PROJECT EXCEPT WHEN OTHERWISE NOTED IN THE PLAN OR DIRECTED BY THE ENGINEER.

TIME RESTRICTIONS (SEE SPECIAL PROVISION, INTERMEDIATE CONTRACT TIME, AND LIQUIDATED DAMAGES)

A) DO NOT CLOSE OR NARROW TRAVEL LANES AS FOLLOWS:

ROAD NAME	DAY AND TIME RESTRICTIONS
I-95 RAMPS & LOOPS	MONDAY THROUGH THURSDAY FROM 6:00 AM TO 7:00 PM AND FRIDAY 6:00 AM TO SUNDAY 9:00 PM

B) DO NOT CLOSE OR NARROW TRAVEL LANES DURING HOLIDAYS AND SPECIAL EVENTS AS FOLLOWS:

- | ROAD NAME | DAY AND TIME RESTRICTIONS |
|---------------------|---------------------------|
| I-95, RAMPS & LOOPS | HOLIDAY |
1. FOR ANY UNEXPECTED OCCURRENCE THAT CREATES UNUSUALLY HIGH TRAFFIC VOLUMES, AS DIRECTED BY THE ENGINEER.
 2. FOR NEW YEAR'S, BETWEEN THE HOURS OF 6:00 AM DECEMBER 31ST AND 9:00 P.M. JANUARY 2ND. IF NEW YEAR'S DAY IS ON A FRIDAY, SATURDAY, SUNDAY, OR MONDAY THEN UNTIL 9:00 P.M. THE FOLLOWING TUESDAY.
 3. FOR EASTER, BETWEEN THE HOURS OF 6:00 AM THURSDAY AND 9:00 P.M. MONDAY.
 4. FOR MEMORIAL DAY, BETWEEN THE HOURS OF 6:00 AM FRIDAY AND 9:00 P.M. TUESDAY.
 5. FOR INDEPENDENCE DAY, BETWEEN THE HOURS OF 6:00 AM THE DAY BEFORE INDEPENDENCE DAY AND 9:00 P.M. THE DAY AFTER INDEPENDENCE DAY.

IF INDEPENDENCE DAY IS ON A FRIDAY, SATURDAY, SUNDAY, OR MONDAY THEN BETWEEN THE HOURS OF 6:00 AM THE THURSDAY BEFORE INDEPENDENCE DAY AND 9:00 P.M. THE TUESDAY AFTER INDEPENDENCE DAY.
 6. FOR LABOR DAY, BETWEEN THE HOURS OF 6:00 AM FRIDAY AND 9:00 P.M. TUESDAY.
 7. FOR THANKSGIVING DAY, BETWEEN THE HOURS OF 6:00 AM TUESDAY TO 9:00 P.M. MONDAY.
 8. FOR CHRISTMAS, BETWEEN THE HOURS OF 6:00 AM THE FRIDAY BEFORE THE WEEK OF CHRISTMAS DAY AND 9:00 P.M. THE FOLLOWING TUESDAY AFTER THE WEEK OF CHRISTMAS.
 9. FOR THE DAYTONA 500, BETWEEN THE HOURS OF 6:00 AM THE DAY OF THE EVENT AND 9:00 P.M. THE DAY AFTER THE EVENT.
 10. FOR THE MYRTLE BEACH BIKE WEEK, BETWEEN THE HOURS OF 6:00 A.M. THE THURSDAY BEFORE THE WEEKEND OF THE MYRTLE BEACH BIKE WEEK AND 6:00 A.M. THE MONDAY AFTER THE WEEKEND OF THE MYRTLE BEACH BIKE WEEK.

C) DO NOT CLOSE RAMPS/LOOPS AS FOLLOWS:

ROAD NAME	DAY AND TIME RESTRICTIONS
I-95 RAMPS/LOOPS	MONDAY THROUGH THURSDAY FROM 6:00 A.M. TO 9:00 P.M. AND FRIDAY 6:00 A.M. TO SUNDAY 9:00 P.M.

D) DO NOT CONDUCT ANY HAULING OPERATIONS AGAINST THE FLOW OF TRAFFIC OF AN OPEN TRAVELWAY UNLESS THE HAULING OPERATION IS PROTECTED BY BARRIER OR GUARDRAIL OR AS DIRECTED BY THE ENGINEER.

WORK ZONE SIGNING:

(A) INSTALLATION

IF THERE IS A PERIOD OF CONSTRUCTION INACTIVITY LONGER THAN 14 CALENDAR DAYS, REMOVE OR COVER ADVANCE/GENERAL WARNING WORK ZONE SIGNS. UNCOVER ADVANCE/GENERAL WARNING WORK ZONE SIGNS NO MORE THAN 7 CALENDAR DAYS BEFORE WORK RESUMES. ALL OTHER OPERATIONS MAY BE SUSPENDED UPON FAILURE TO COMPLY WITH THE ABOVE REQUIREMENTS. SUCH SUSPENDED OPERATIONS WOULD NOT BE RESUMED UNTIL THE ABOVE REQUIREMENTS ARE FULFILLED.

(B) SIGN REMOVAL

ALL STATIONARY WORK ZONE SIGNS SHALL BE REMOVED ONCE THE PROJECT IS SUBSTANTIALLY COMPLETE. THE PROJECT IS SUBSTANTIALLY COMPLETE WHEN THE RESURFACING OPERATIONS ARE COMPLETED AND THE SHOULDERS ARE BROUGHT UP TO THE SAME ELEVATION AS THE PROPOSED PAVEMENT AND WHEN PAVEMENT MARKINGS ARE INSTALLED. THE PAVEMENT MARKING DOESN'T HAVE TO BE THE FINAL MARKING MATERIAL TO BE CONSIDERED SUBSTANTIALLY COMPLETE. ANY REMAINING PUNCH LIST ITEMS ARE TO BE COMPLETED WITH PORTABLE WORK ZONE SIGNING.

(C) LANE CLOSURE WORK ZONE SIGNS

INSTALL ANY REQUIRED LANE CLOSURE SIGNING NEEDED DURING THE LIFE OF THE PROJECT IN ACCORDANCE WITH THE STANDARD DRAWING NO. 1101.02, 1101.11, AND 1110.02 OF THE 2012 ROADWAY STANDARD DRAWINGS.

(D) RAMP/LOOP CLOSURE SIGNS

NOTIFY THE ENGINEER FOURTEEN (14) CALENDAR DAYS PRIOR TO RAMP/LOOP CLOSURE. PROVIDE SIGNING AND DEVICES REQUIRED TO CLOSE THE RAMP/LOOP ACCORDING TO THE ROADWAY STANDARD DRAWINGS AND TRAFFIC CONTROL PLANS AND PROVIDE SIGNING REQUIRED FOR THE OFF-SITE DETOUR ROUTE AS SHOWN IN THE TRAFFIC CONTROL PLANS. COVER OR REMOVE ALL SIGNS AND DEVICES REQUIRED TO CLOSE THE RAMP/LOOP AND ALL SIGNS REQUIRED FOR THE OFF-SITE DETOUR WHEN THE DETOUR IS NOT IN OPERATION. ENSURE ALL NECESSARY SIGNING IS IN PLACE PRIOR TO ALTERING ANY TRAFFIC PATTERN.

PAVEMENT MARKING AND MARKERS:

DESCRIPTION

TEMPORARY PAVEMENT MARKINGS SHALL BE INSTALLED IN ACCORDANCE WITH STANDARD DRAWINGS 1205.01 THROUGH 1205.13 OF THE 2012 ROADWAY STANDARD DRAWINGS AND SECTION 1205 OF THE 2012 STANDARD SPECIFICATIONS.

(A) MARKERS

REMOVE EXISTING SNOWPLOWABLE PAVEMENT MARKERS IN PREPARATION FOR PAVING. REPAIR ANY PAVEMENT DAMAGE DUE TO EXISTING PAVEMENT MARKER REMOVAL PRIOR TO THE END OF THE WORK DAY. DISPOSE OF EXISTING PAVEMENT MARKERS AS DIRECTED BY THE ENGINEER. NO DIRECT PAYMENT WILL BE MADE FOR THIS WORK AS IT WILL BE INCIDENTAL TO THE PAVING OPERATION.

INSTALL PERMANENT PAVEMENT MARKERS WITHIN 60 CALENDAR DAYS AFTER COMPLETING THE RESURFACING. PAVEMENT MARKERS SHALL BE INSTALLED IN ACCORDANCE WITH STANDARD DRAWING 1205.12 AND STANDARD DRAWINGS 1250.01 THROUGH 1253.01 OF THE 2012 ROADWAY STANDARD DRAWINGS AND SECTIONS 1250 THROUGH 1253 OF THE 2012 STANDARD SPECIFICATIONS.

(B) MARKING AND MARKERS

FOR TEMPORARY PAVEMENT MARKING USE RSD 1205.01, 1205.02, 1205.03, 1205.06, 1205.08, 1205.12, 1205.13.

FOR TEMPORARY RAISED PAVEMENT MARKERS USE RSD 1250.01 AND 1251.01.

TEMPORARY TRAFFIC CONTROL (TTC):

MAINTAIN TRAFFIC IN ACCORDANCE WITH DIVISIONS 10, 11, AND 12 OF THE 2012 STANDARD SPECIFICATIONS AND THE FOLLOWING PROVISIONS:

INSTALL WORK ZONE ADVANCE WARNING SIGNS IN ACCORDANCE WITH THE DETAIL DRAWING PROVIDED IN THESE PLANS PRIOR TO BEGINNING ANY OTHER WORK.

WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING ON THE SHOULDER ADJACENT TO AND WITHIN 10 FEET OF OPEN TRAVEL LANE, CLOSE THE NEAREST OPEN TRAVEL LANE USING STANDARD DRAWING NO. 1101.02 OF THE 2012 ROADWAY STANDARD DRAWINGS. WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING WITHIN A LANE OF TRAVEL OF AN UNDIVIDED OR DIVIDED FACILITY, CLOSE THE LANE ACCORDING TO THE TRAFFIC CONTROL PLANS, 2012 ROADWAY STANDARD DRAWINGS OR AS DIRECTED BY THE ENGINEER. CONDUCT THE WORK SO THAT ALL PERSONNEL AND/OR EQUIPMENT REMAIN WITHIN THE CLOSED TRAVEL LANE.

WHEN UTILIZING A SLOW-MOVING OPERATION FOR SUCH ITEMS AS PAVEMENT MARKING AND MARKER PLACEMENT, AS A MINIMUM THE SLOW MOVING OPERATION CARAVAN SHALL CONSIST OF THE VEHICLES AND DEVICES SHOWN ON THE MOVING OPERATION CARAVAN DETAILS ACCORDING TO ROADWAY STANDARD DRAWING NO. 1101.02, SHEET 13 OF THE 2012 ROADWAY STANDARD DRAWINGS. TRAFFIC CONES MAY BE USED WHEN NECESSARY TO PROVIDE ADDITIONAL PROTECTION OF WET PAVEMENT MARKINGS. BALLAST ALL TRAFFIC CONES SO THEY WILL NOT BE BLOWN OVER BY TRAFFIC.

CONSTRUCTION OPERATIONS:

1. CONTRACTOR SHALL MILL AND PAVE LANES IN AN ORDER SUCH THAT WATER SHALL NOT ACCUMULATE.
2. CONTRACTOR SHALL MILL AND PAVE BACK ASPHALT SURFACE COURSE AND PLACE TEMPORARY PAVEMENT MARKINGS AND TEMPORARY MARKERS BY THE END OF EACH WORK DAY. REMOVE LANE CLOSURE AND REOPEN TO EXISTING TRAFFIC PATTERN BY THE END OF EACH WORK PERIOD. (SEE INTERMEDIATE CONTRACT TIME FOR ALLOWABLE LANE CLOSURE TIMES).
3. REMOVE/REPLACE ANY CONFLICTING OR DAMAGED PAVEMENT MARKINGS AND MARKERS BY THE END OF EACH DAY'S OPERATION.
4. OPERATE EQUIPMENT AND CONDUCT OPERATIONS IN THE SAME DIRECTION AS THE FLOW OF TRAFFIC. MAINTAIN VEHICULAR ACCESS IN ACCORDANCE WITH ARTICLE 1101-05 OF THE 2012 STANDARD SPECIFICATIONS.
5. DO NOT INSTALL MORE THAN 2 MILES OF LANE CLOSURE ON I-95, MEASURED FROM THE BEGINNING OF THE MERGE TAPER TO THE END OF THE LANE CLOSURE, AND DO NOT INSTALL ANY MORE THAN ONE PER DIRECTION.

4/5/2016 4:57:31 PM L:\Transportation\TR13.017.00 NCDOT 2012 Traffic LSA\TR13.017.00 I-5731\TMP-1A.dgn


SEPI
ENGINEERING & CONSTRUCTION

1025 Wade Avenue
Raleigh, NC 27605
Tel: 919-789-9977
Fax: 919-789-9591
License: C-2197

APPROVED: *Steve Miller*
DATE: 4/5/2016

SEAL

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED

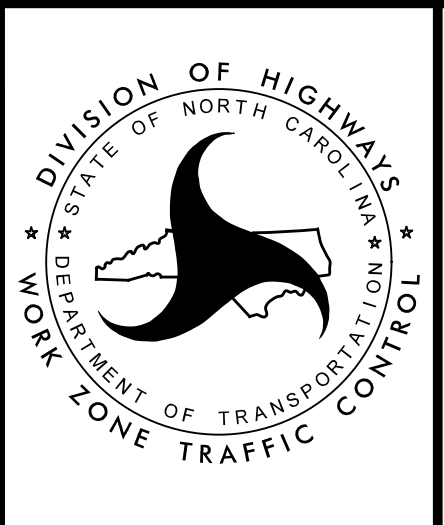

TRANSPORTATION OPERATIONS PLAN
