

PROJECT REFERENCE NO.	SHEET NO.
I-5878	TMP-4E

DOCUMENT NOT CONSIDERED FINAL  
UNLESS ALL SIGNATURES COMPLETED

**Michael Baker**  
INTERNATIONAL


**ICT**  
CONSTRUCT -SR18- JACKSON RD STA. 14+00± TO 25+35± UNDER CLOSURE. SEE INTERMEDIATE CONTRACT TIMES.

**TEMPORARY SHORING LEGEND**  
 1-4 QUANTITY = 378.0 SQFT  
 TEMPORARY SHORING FROM -LREV- STA. 1002+00, 21.0' LT TO -LREV- STA. 1002+35, 21.0' LT  
 LENGTH = 35.00 FT  
 AVERAGE HEIGHT = 10.8 FT  
 MAXIMUM HEIGHT = 14.5 FT  
 (SEE SHEET TMP-2G1 FOR TEMPORARY SHORING NOTES)

**TEMPORARY SHORING LEGEND**  
 1-5 QUANTITY = 835.7 SQFT  
 TEMPORARY SHORING FROM -LREV- STA. 1003+39, 18.0' LT TO -LREV- STA. 1004+00, 18.0' LT  
 LENGTH = 61.00 FT  
 AVERAGE HEIGHT = 13.7 FT  
 MAXIMUM HEIGHT = 20.4 FT  
 (SEE SHEET TMP-2G1 FOR TEMPORARY SHORING NOTES)

**TEMPORARY SHORING LEGEND**  
 1-7 QUANTITY = 1864.8 SQFT  
 TEMPORARY SHORING FROM -LREV- STA. 1003+28, 10.0' LT TO -LREV- STA. 1004+00, 10.0' LT  
 LENGTH = 72.00 FT  
 AVERAGE HEIGHT = 25.9 FT  
 MAXIMUM HEIGHT = 27.9 FT  
 (SEE SHEET TMP-2G1 FOR TEMPORARY SHORING NOTES)

**TEMPORARY SHORING LEGEND**  
 1-6 QUANTITY = 1113.4 SQFT  
 TEMPORARY SHORING FROM -LREV- STA. 1002+00, 13.0' LT TO -LREV- STA. 1002+38, 13.0' LT  
 LENGTH = 38.00 FT  
 AVERAGE HEIGHT = 29.3 FT  
 MAXIMUM HEIGHT = 31.3 FT  
 (SEE SHEET TMP-2G1 FOR TEMPORARY SHORING NOTES)

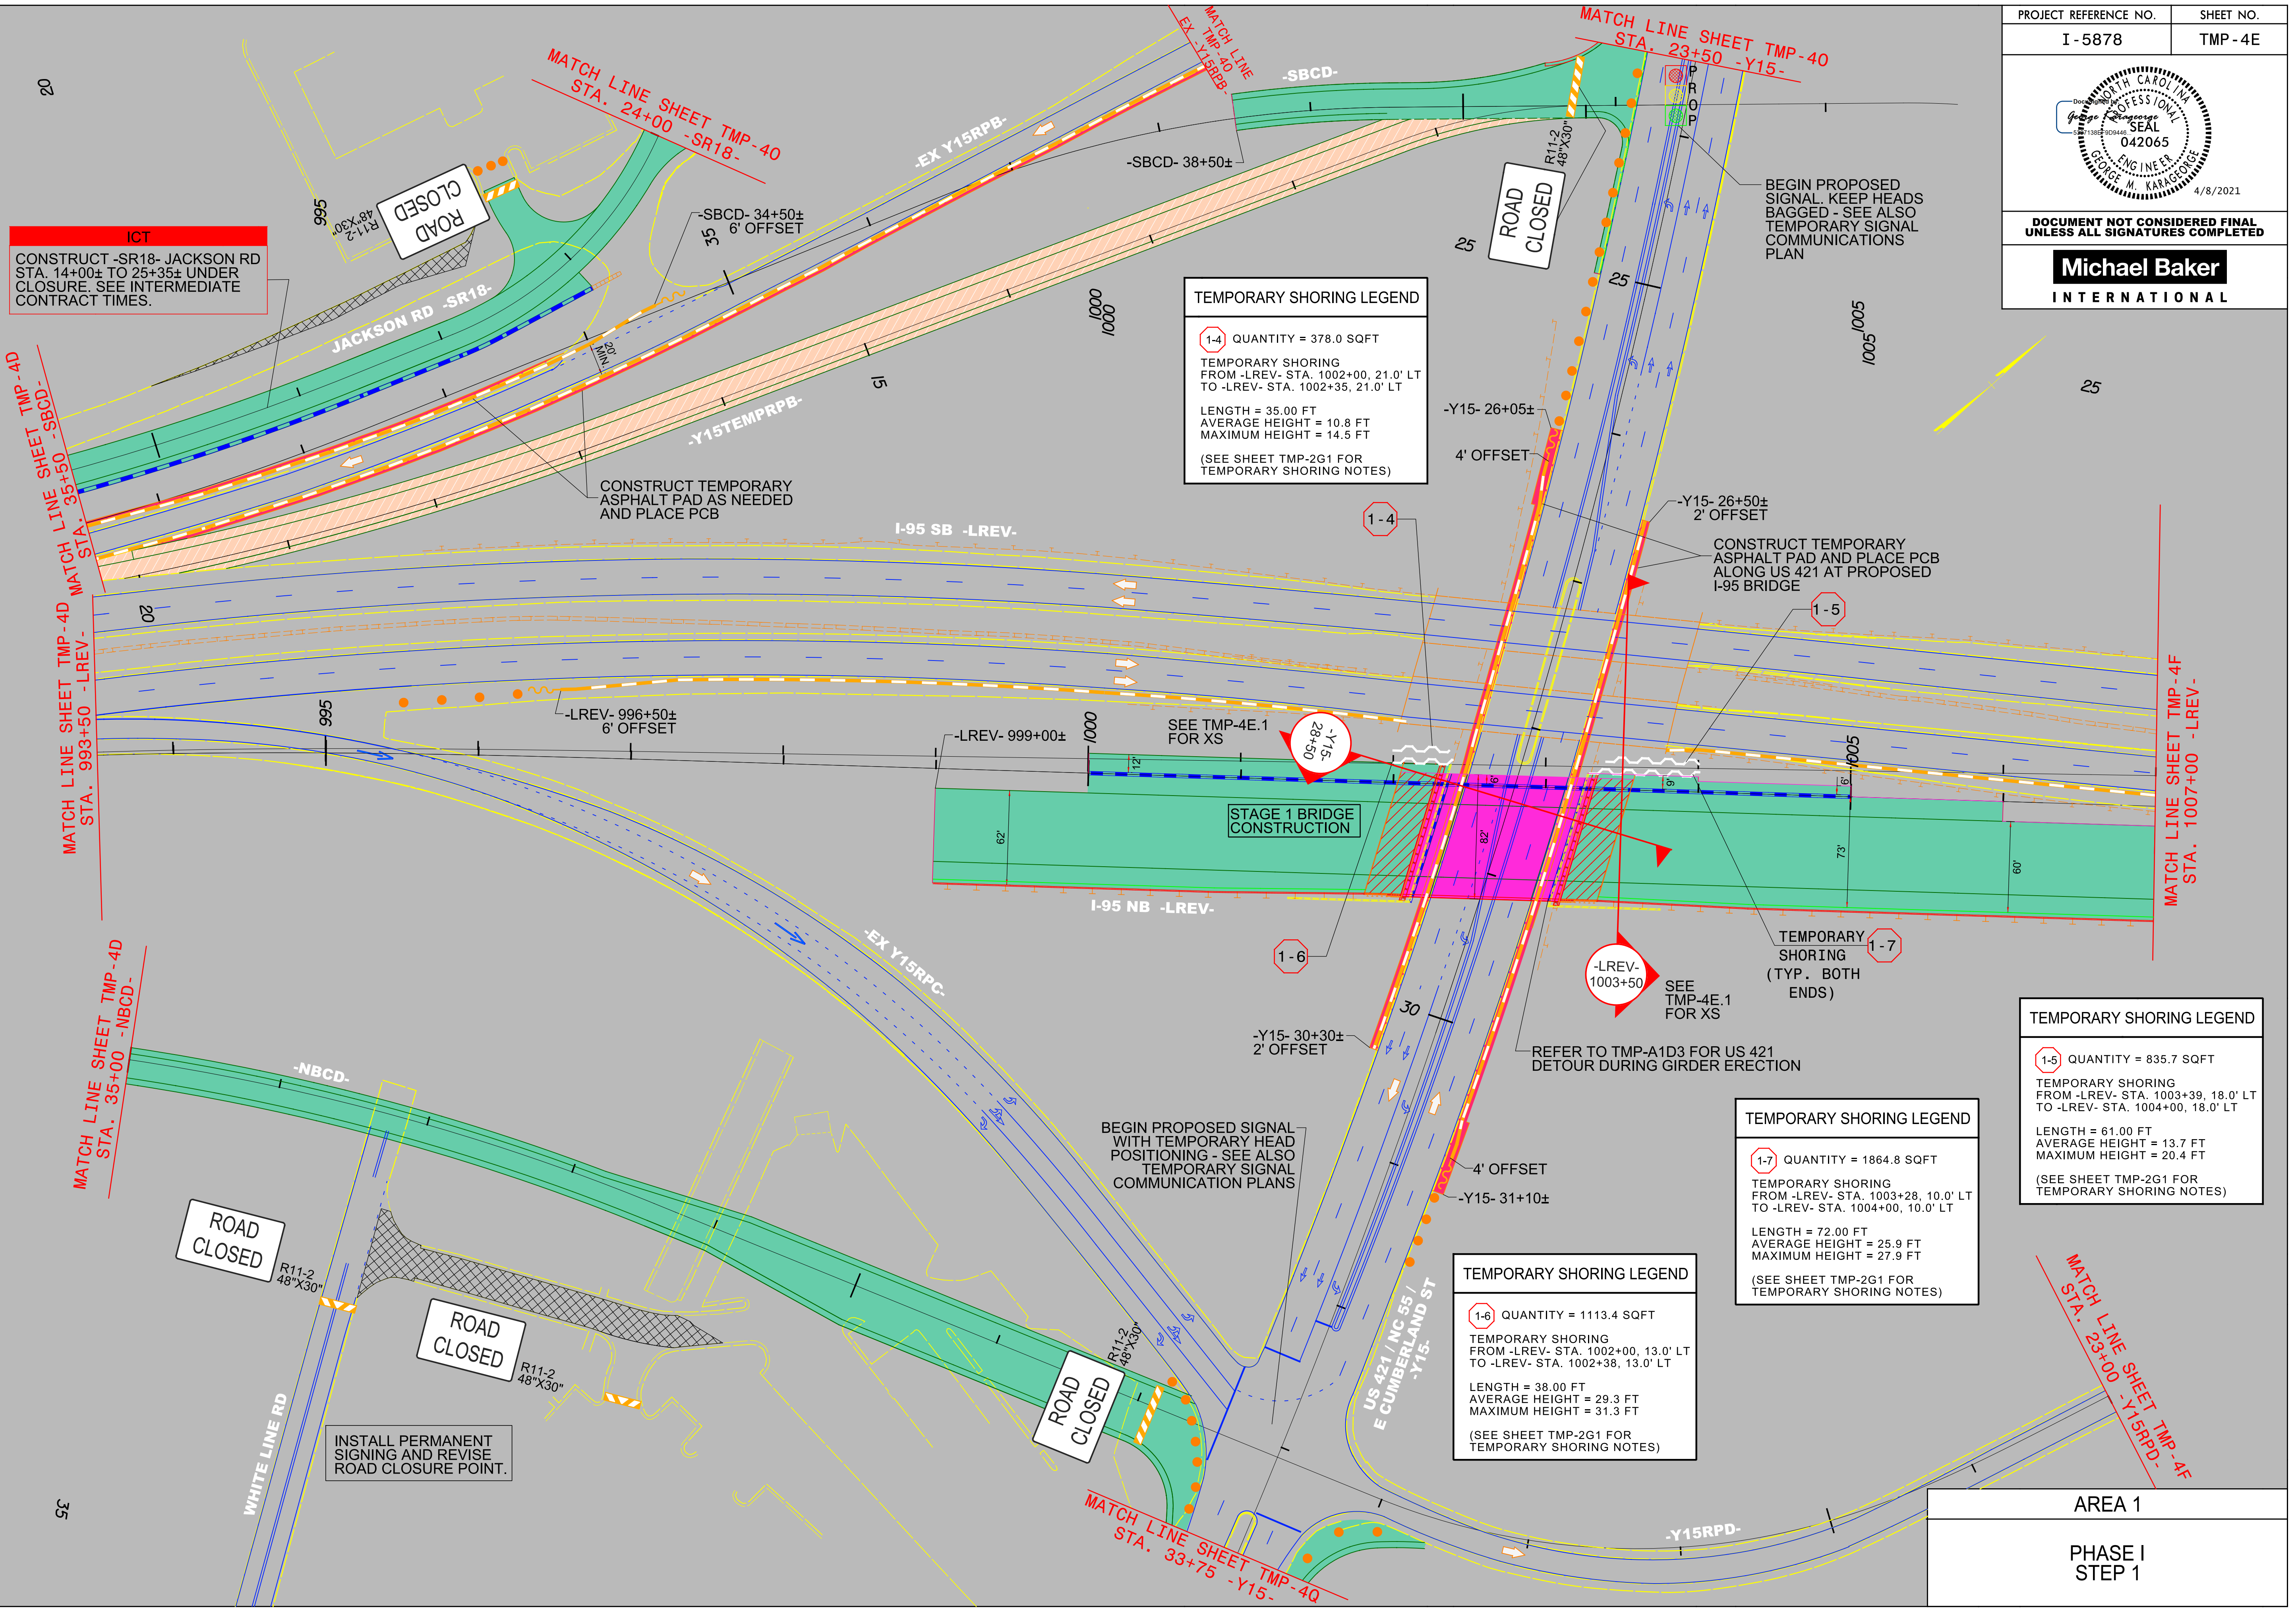

4/1/2021 R:\Tireg\file\Transportation Management\PLAN SHEETS\I-5878\I-5878E\01STEP\_01.dgn Carolin@owings

**AREA 1**  
**PHASE I**  
**STEP 1**
