


- (X) 73' SHOP CURVED TEMPORARY GUARDRAIL WITH B-77 ANCHOR TO PCB AND TEMP AT-1
- (Y) 73' SHOP CURVED TEMPORARY GUARDRAIL WITH B-77 ANCHOR TO PCB AND TEMP AT-1

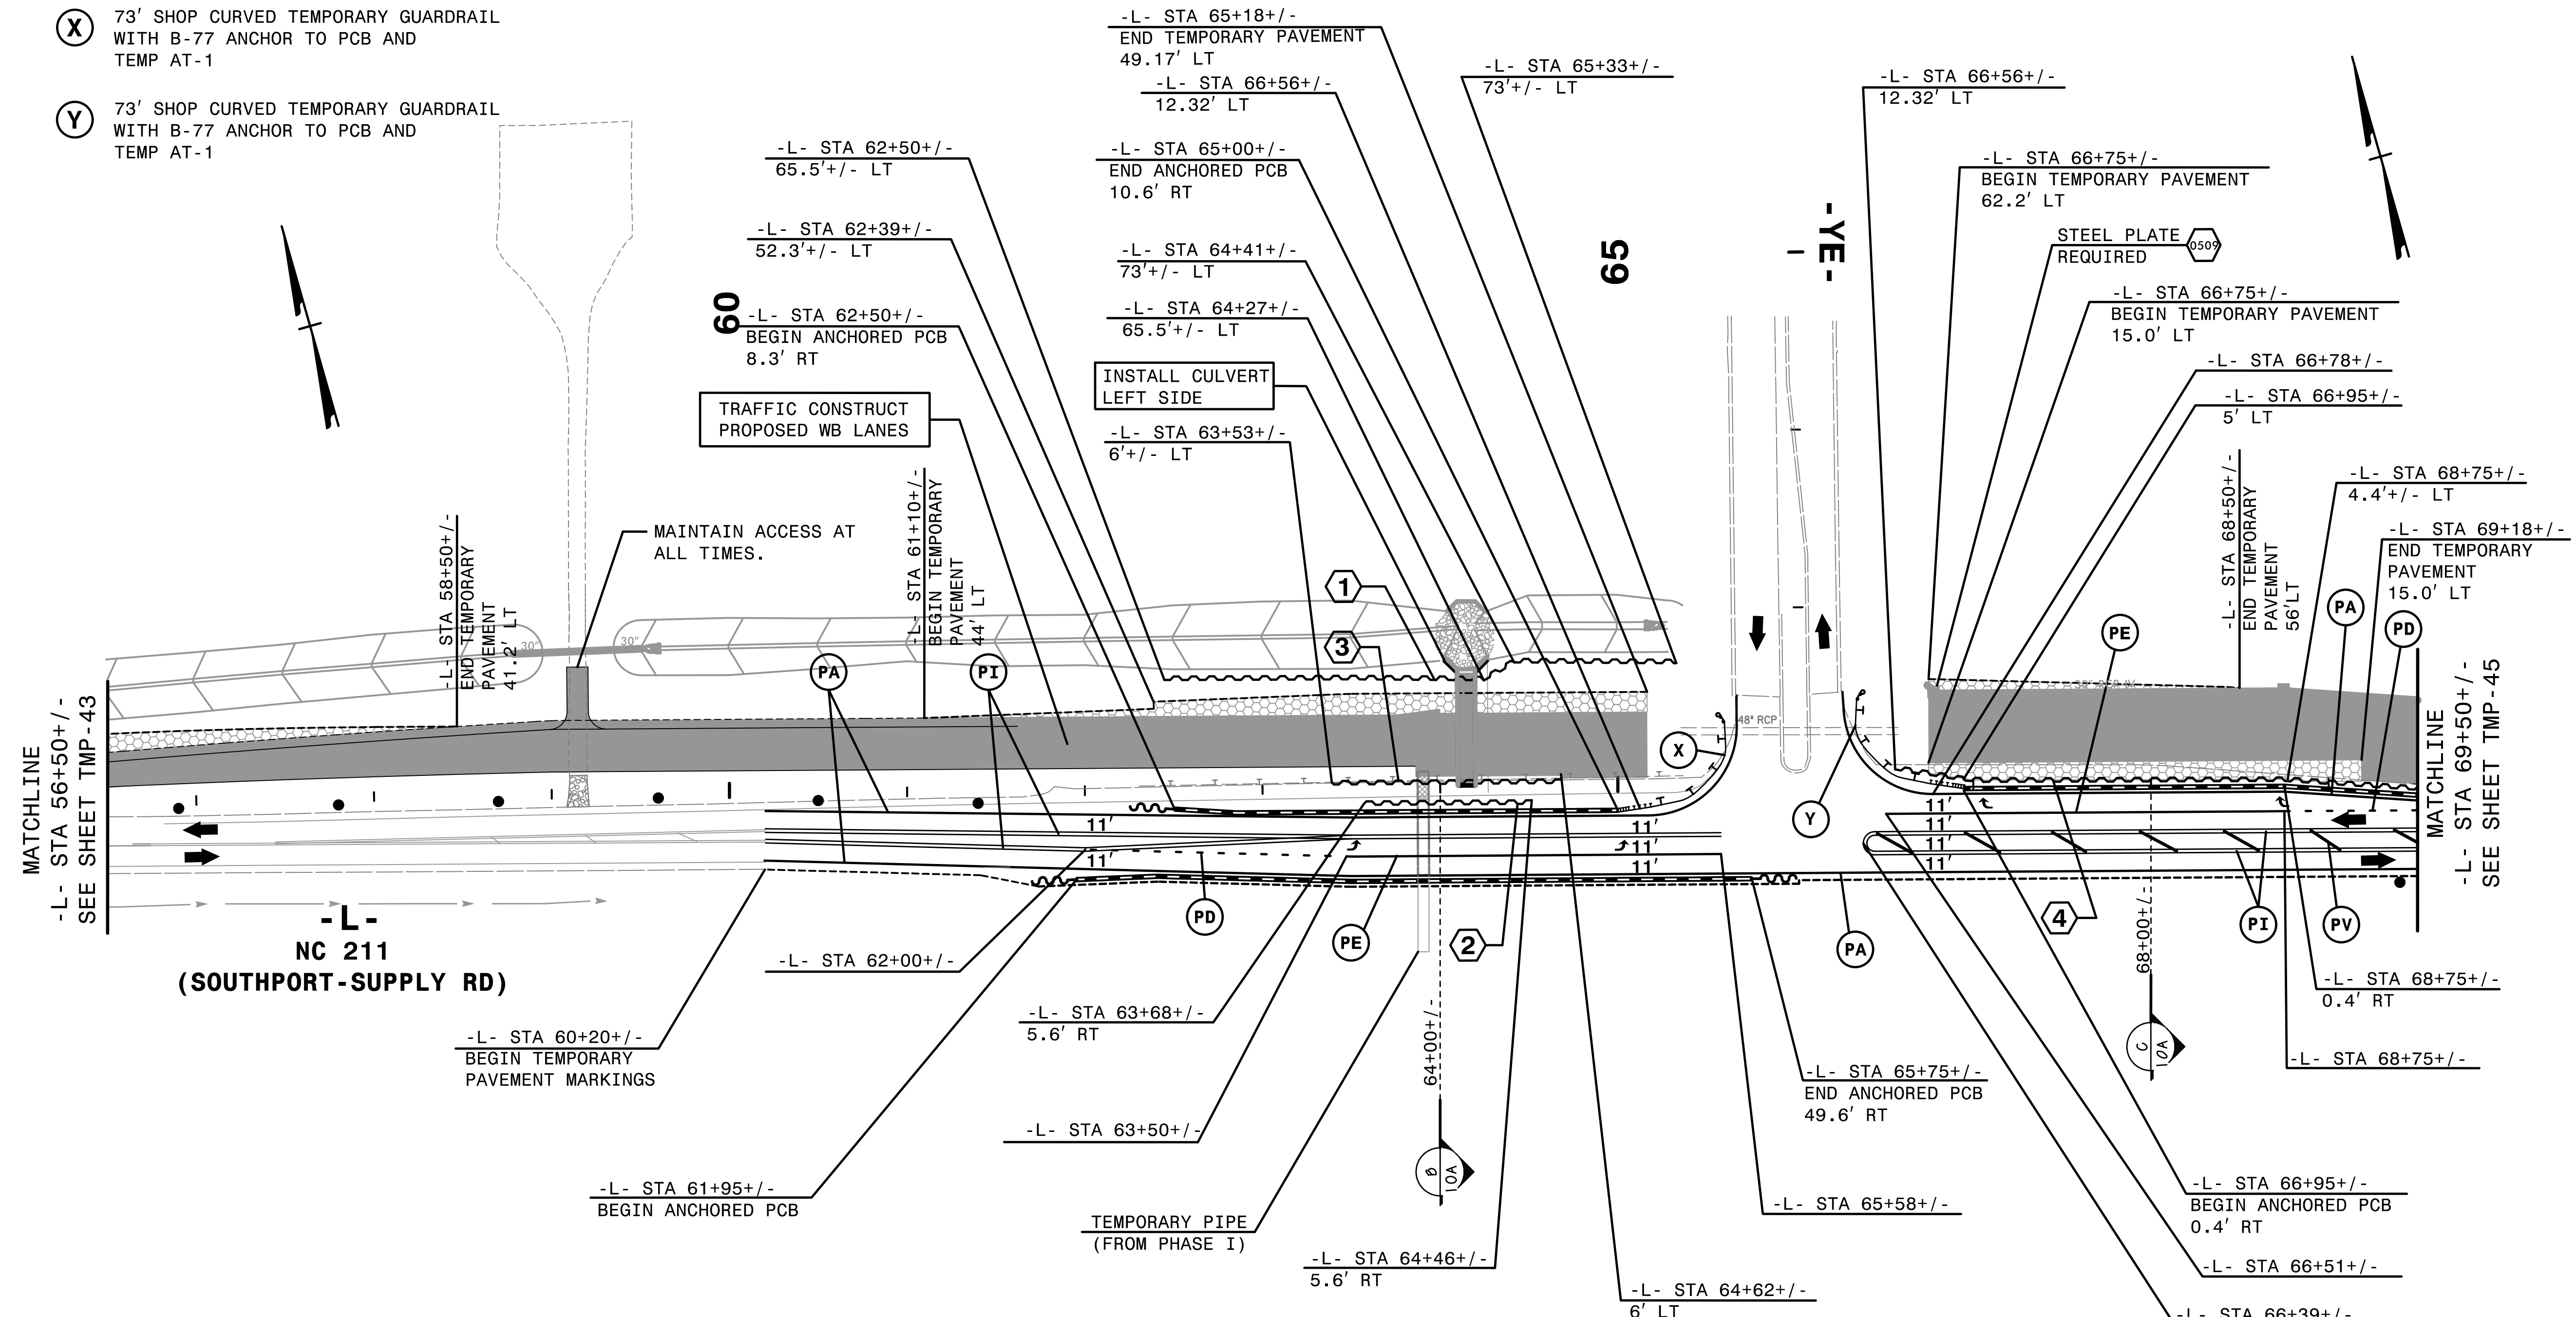

NOTE: DRAINAGE INFO SHOWN IS ONLY FOR CONTRACTOR CONSIDERATION. CONTRACTOR SHOULD VERIFY THAT PONDING OF WATER WILL NOT OCCUR IN THE TRAVEL LANES.

SEE CULVERT PHASING ON 5A/CONST.5

1 EST QUANTITY = 701.5 SF
 TEMPORARY SHORING
 FROM -L- STA 62+50+/-, 65.5'+/- LT,
 TO -L- STA 64+27+/-, 65.5'+/- LT AND
 FROM -L- STA 64+27+/-, 65.5'+/- LT,
 TO -L- STA 64+41+/-, 73'+/- LT AND
 FROM -L- STA 64+41+/-, 73'+/- LT,
 TO -L- STA 65+33+/-, 73'+/- LT

2 EST QUANTITY = 400 SF
 TEMPORARY SHORING
 FROM -L- STA 63+68+/-, 5.6'+/- RT,
 TO -L- STA 64+46+/-, 5.6'+/- RT


3 EST QUANTITY = 885 SF
 TEMPORARY SHORING
 FROM -L- STA 63+53+/-, 6'+/- LT,
 TO -L- STA 64+62+/-, 6'+/- LT

4 EST QUANTITY = 2118 SF
 TEMPORARY SHORING
 FROM -L- STA 66+56+/-, 12.32'+/- LT,
 TO -L- STA 67+00+/-, 5'+/- LT AND
 FROM -L- STA 67+00+/-, 5'+/- LT,
 TO -L- STA 68+75+/-, 4.4'+/- LT AND
 FROM -L- STA 68+75+/-, 4.4'+/- LT,
 TO -L- STA 70+13+/-, 5.67'+/- RT


REMOVE CONFLICTING PAVEMENT MARKING.

4:56:21PM \\TCF\5021\TC\pld2a.dgn

(SEE SHEET TMP-2G FOR TEMPORARY SHORING NOTES)



APPROVED: *Helen Shyu*
 DATE: 11/10/2021
 SEAL
 PROFESSIONAL ENGINEER
 HELLEN SHYU
 042517



TRANSPORTATION MANAGEMENT PLAN
 PHASE IA
 DETAIL

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED
