



**This electronic collection of documents is provided
for the convenience of the user
and is Not a Certified Document –**

**The documents contained herein were originally issued
and sealed by the individuals whose names and license
numbers appear on each page, on the dates appearing
with their signature on that page.**

**This file or an individual page
shall not be considered a certified document.**

STATE OF NORTH CAROLINA
DIVISION OF HIGHWAYS

TRANSPORTATION MANAGEMENT PLAN
NORTHAMPTON AND HERTFORD COUNTIES

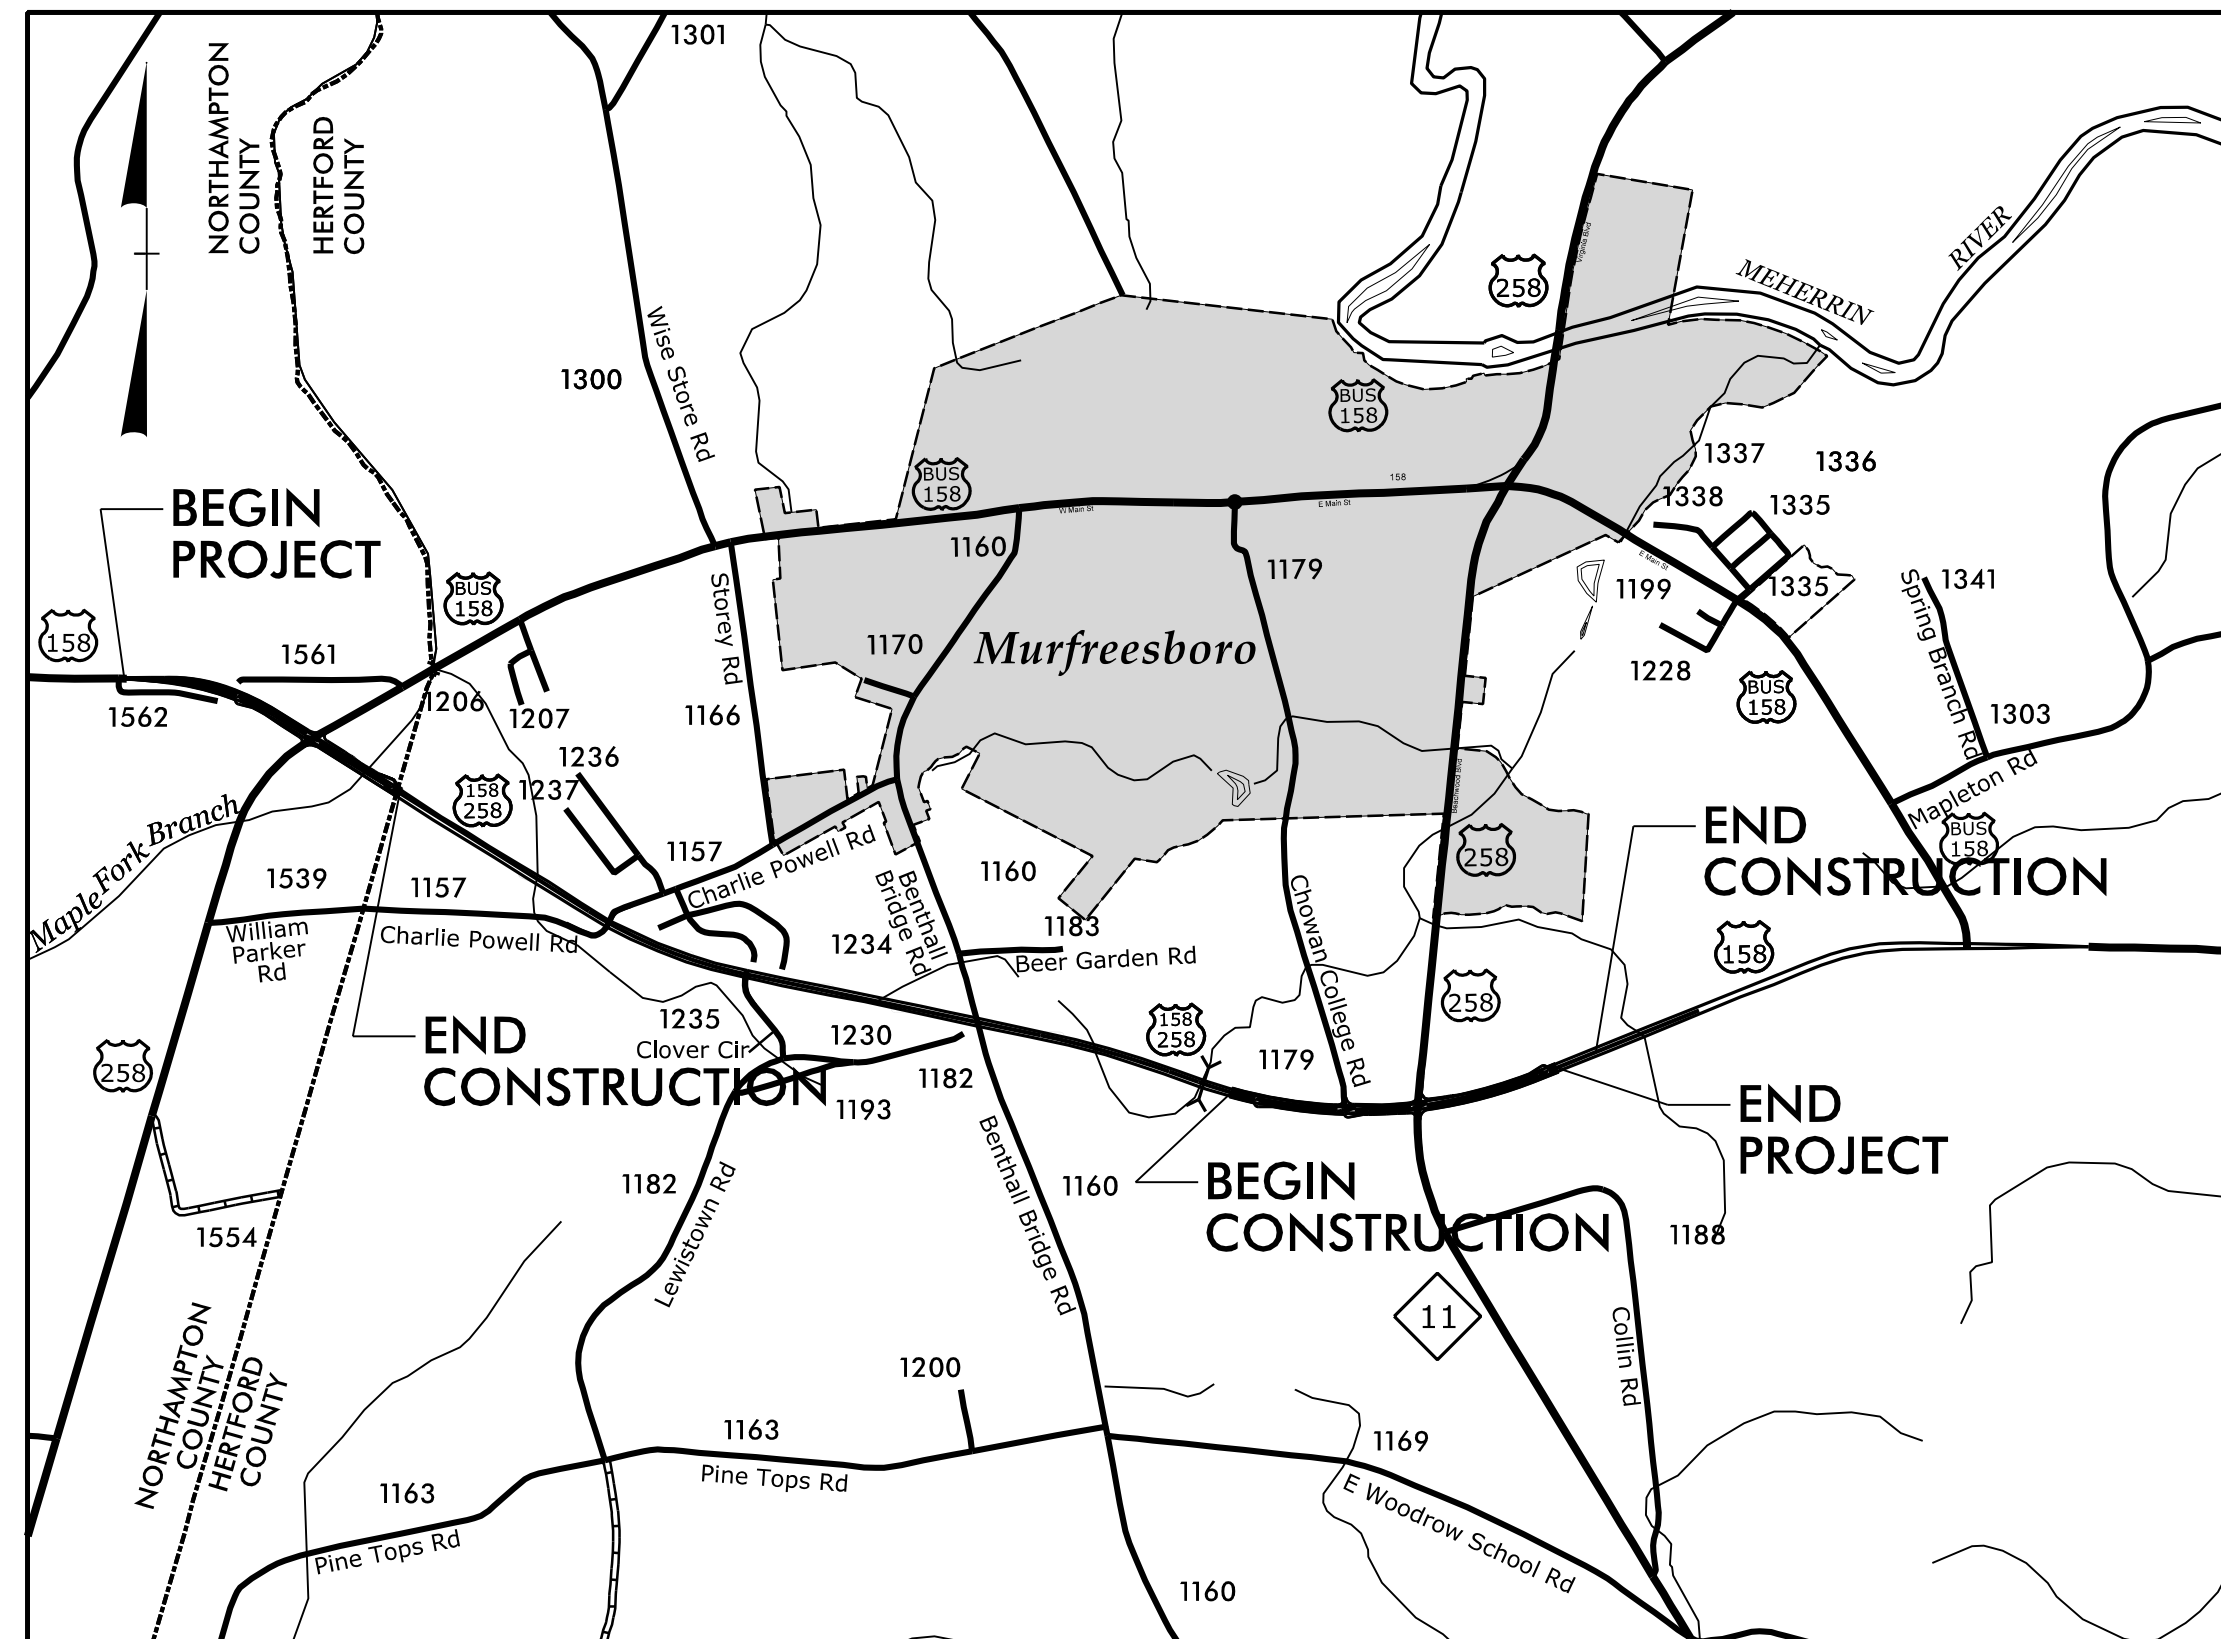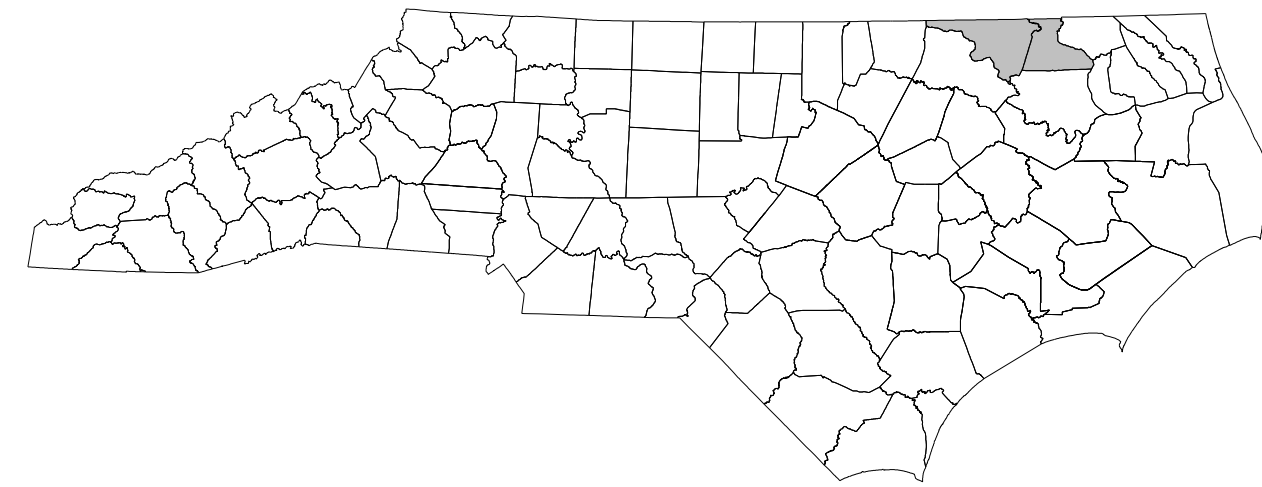

INDEX OF SHEETS


SHEET NO.	TITLE
TMP-1	TITLE SHEET, VICINITY MAP, AND INDEX OF SHEETS
TMP-1A	LIST OF APPLICABLE ROADWAY STANDARD DRAWINGS, AND LEGEND
TMP-2 AND 2A	GENERAL NOTES
TMP-3	MANAGEMENT STRATEGIES AND TRAFFIC CONTROL PHASING
TMP-4 THRU 10	TEMPORARY TRAFFIC CONTROL PHASE I DETAILS
TMP-11 THRU 23	TEMPORARY TRAFFIC CONTROL PHASE II DETAILS

SHEET NO.
TMP-1

W-5701B


TIP PROJECT:

**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**

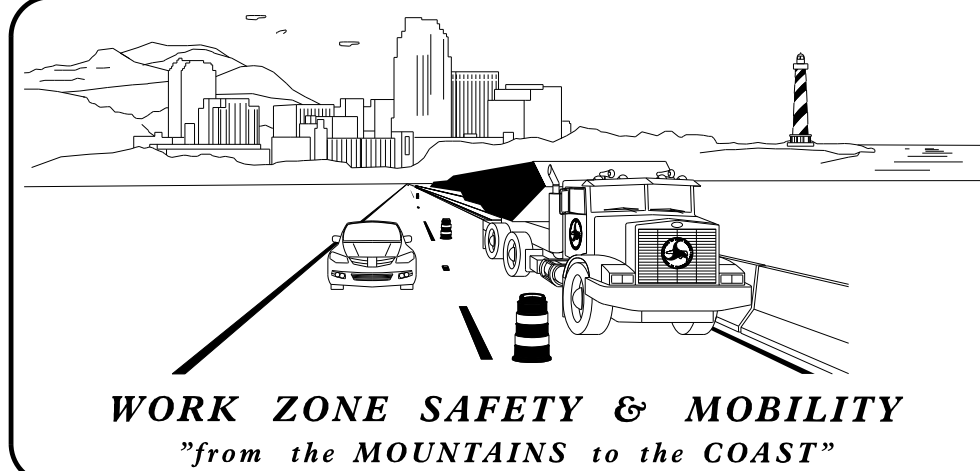


PLANS PREPARED BY:
KEVIN BISBY, P.E.
TECHNICAL MANAGER
W. PORTER ERICKSON-JONES, E.I.
PROJECT ENGINEER

NC DOT CONTACTS:
JOHN ABEL
PROJECT ENGINEER

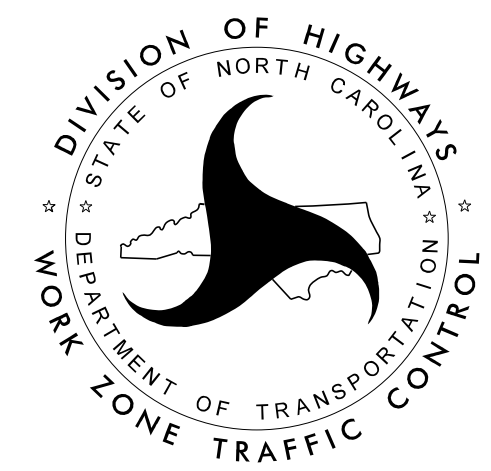

RK&K
P: (919) 878-9560
8601 Six Forks Road, Forum 1, Suite 700
Raleigh, North Carolina 27615-3960
NC License No. F-0112
www.rk.com
Responsive People | Creative Solutions

APPROVED: *Kevin Bisby*
DATE: 1/9/2023



SEAL

1/9/2023
W5701B-TMP_PSH01.dgn
KBISBY










ROADWAY STANDARD DRAWINGS

THE FOLLOWING ROADWAY STANDARDS AS SHOWN IN "ROADWAY STANDARD DRAWINGS" - N.C. DEPARTMENT OF TRANSPORTATION - RALEIGH, N.C., DATED JANUARY 2018 ARE APPLICABLE TO THIS PROJECT AND BY REFERENCE HEREBY ARE CONSIDERED A PART OF THESE PLANS:




STD. NO.	TITLE
1101.01	WORK ZONE ADVANCE WARNING SIGNS
1101.02	TEMPORARY LANE CLOSURES
1101.04	TEMPORARY SHOULDER CLOSURES
1101.05	WORK ZONE VEHICLE ACCESSES
1101.11	TRAFFIC CONTROL DESIGN TABLES
1110.01	STATIONARY WORK ZONE SIGNS
1110.02	PORTABLE WORK ZONE SIGNS
1115.01	FLASHING ARROW BOARDS
1130.01	DRUM
1135.01	CONES
1145.01	BARRICADES
1150.01	FLAGGING DEVICES
1165.01	WORK VEHICLE LIGHTING SYSTEMS AND TMA DELINEATION
1205.01	PAVEMENT MARKINGS - LINE TYPES AND OFFSETS
1205.02	PAVEMENT MARKINGS - TWO-LANE AND MULTI-LANE ROADWAYS
1205.04	PAVEMENT MARKINGS - INTERSECTIONS
1205.05	PAVEMENT MARKINGS - TURN LANES
1205.08	PAVEMENT MARKINGS - SYMBOLS AND WORD MESSAGES
1205.09	PAVEMENT MARKINGS - PAINTED ISLANDS
1205.13	PAVEMENT MARKINGS - LANE REDUCTIONS
1205.15	PAVEMENT MARKINGS - SUPERSTREETS
1250.01	RAISED PAVEMENT MARKERS - INSTALLATION SPACING
1251.01	RAISED PAVEMENT MARKERS - PERMANENT AND TEMPORARY
1261.01	GUARDRAIL AND BARRIER DELINEATORS - INSTALLATION SPACING
1261.02	GUARDRAIL AND BARRIER DELINEATORS - TYPES AND MOUNTING
1262.01	GUARDRAIL END DELINEATION

LEGEND

GENERAL

-  DIRECTION OF TRAFFIC FLOW
-  DIRECTION OF PEDESTRIAN TRAFFIC FLOW
-  EXIST. PVMT.
-  NORTH ARROW
-  PROPOSED PVMT.
-  TEMP. SHORING (LOCATION PURPOSES ONLY)
-  WORK AREA
-  REMOVAL
-  ONGOING CONSTRUCTION

















SIGNALS

-  EXISTING
-  PROPOSED
-  TEMPORARY



PAVEMENT MARKINGS

-  EXISTING LINES
-  TEMPORARY LINES


TRAFFIC CONTROL DEVICES

-  BARRICADE (TYPE III)
-  CONE
-  DRUM
-  SKINNY DRUM
-  TUBULAR MARKER
-  TEMPORARY CRASH CUSHION
-  FLASHING ARROW BOARD
-  FLAGGER
-  LAW ENFORCEMENT
-  TRUCK MOUNTED ATTENUATOR (TMA)
-  CHANGEABLE MESSAGE SIGN
-  PORTABLE CONCRETE BARRIER
-  PORTABLE CONCRETE BARRIER (EXISTING)
-  SHORING
-  PORTABLE CONCRETE BARRIER (SECTION VIEW)
-  DRUM (SECTION VIEW)

TEMPORARY PAVEMENT MARKING SCHEDULE



PAINT			
Symbol	Description	Symbol	Description
P20	WHITE EDGELINE (6")	P34	2 FT. - 6 FT./SP YELLOW MINISKIP (6")
P23	3 FT. - 9 FT./SP WHITE MINISKIP (6")	P50	WHITE GORELINE (12")
P24	2 FT. - 6 FT./SP WHITE MINISKIP (6")	P51	WHITE DIAGONAL (12")
P30	YELLOW EDGELINE (6")	P61	WHITE STOPBAR (24")
PAINT SYMBOLS		TEMPORARY RAISED PAVEMENT MARKERS	
Symbol	Description	Symbol	Description
	LEFT TURN ARROW	MI	TEMPORARY RAISED, CRYSTAL/RED
	U-TURN ARROW		

1/9/2023
W5701B-TMP_PSH01A.dgn
KBISBY

APPROVED: 
DESIGNED BY: Kevin Bish, BDO082628912472

DATE: 1/9/2023

SEAL

ROADWAY STANDARD DRAWINGS & LEGEND

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED

GENERAL NOTES

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-2

RK
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rk.com
 Responsive People | Creative Solutions

CHANGES MAY BE REQUIRED WHEN PHYSICAL DIMENSIONS IN THE DETAIL DRAWINGS, STANDARD DETAILS, AND ROADWAY DETAILS ARE NOT ATTAINABLE TO MEET FIELD CONDITIONS OR RESULT IN DUPLICATE OR UNDESIRABLE OVERLAPPING OF DEVICES. MODIFICATION MAY INCLUDE: MOVING, COVERING, OR REMOVAL OF DEVICES AS DIRECTED BY THE ENGINEER.

THE FOLLOWING GENERAL NOTES APPLY AT ALL TIMES FOR THE DURATION OF THE CONSTRUCTION PROJECT EXCEPT WHEN OTHERWISE NOTED IN THE PLAN OR DIRECTED BY THE ENGINEER.

TIME RESTRICTIONS

A) DO NOT CLOSE OR NARROW TRAVEL LANES AS FOLLOWS:

ROAD NAME
 US 158, US 258, NC 11 AND CHOWAN COLLEGE RD

DAY AND TIME RESTRICTIONS

MONDAY-FRIDAY FROM THIRTY (30) MINUTES BEFORE SUNSET TO THIRTY (30) MINUTES AFTER SUNRISE THE FOLLOWING DAY.

SATURDAY FROM THIRTY (30) MINUTES BEFORE SUNSET TO THIRTY (30) MINUTES AFTER SUNRISE THE FOLLOWING MONDAY.

B) DO NOT CLOSE OR NARROW TRAVEL LANES DURING HOLIDAYS AND SPECIAL EVENTS AS FOLLOWS:

ROAD NAME
 US 158, US 258, NC 11 AND CHOWAN COLLEGE RD

HOLIDAY

1. FOR ANY UNEXPECTED OCCURRENCE THAT CREATES UNUSUALLY HIGH TRAFFIC VOLUMES, AS DIRECTED BY THE ENGINEER.
2. FOR NEW YEAR'S, BETWEEN THE HOURS OF 6:00 AM DECEMBER 31ST TO 6:00 PM JANUARY 2ND. IF NEW YEAR'S DAY IS ON A FRIDAY, SATURDAY, SUNDAY, OR MONDAY THEN UNTIL 6:00 PM THE FOLLOWING TUESDAY.
3. FOR EASTER, BETWEEN THE HOURS OF 6:00 AM THURSDAY AND 6:00 PM MONDAY.
4. FOR MEMORIAL DAY, BETWEEN THE HOURS OF 6:00 AM FRIDAY TO 6:00 PM TUESDAY.
5. FOR INDEPENDENCE DAY, BETWEEN THE HOURS OF 6:00 AM THE DAY BEFORE INDEPENDENCE DAY AND 6:00 PM THE DAY AFTER INDEPENDENCE DAY.

IF INDEPENDENCE DAY IS ON A FRIDAY, SATURDAY, SUNDAY, OR MONDAY THEN BETWEEN THE HOURS OF 6:00 AM THE THURSDAY BEFORE INDEPENDENCE DAY AND 6:00 PM THE TUESDAY AFTER INDEPENDENCE DAY.




6. FOR LABOR DAY, BETWEEN THE HOURS OF 6:00 AM FRIDAY AND 6:00 PM TUESDAY.
7. FOR THANKSGIVING DAY, BETWEEN THE HOURS OF 6:00 AM TUESDAY TO 6:00 PM MONDAY.
8. FOR CHRISTMAS, BETWEEN THE HOURS OF 6:00 AM THE FRIDAY BEFORE THE WEEK OF CHRISTMAS DAY AND 6:00 PM THE FOLLOWING TUESDAY AFTER THE WEEK OF CHRISTMAS.

LANE AND SHOULDER CLOSURE REQUIREMENTS

- C) REMOVE LANE CLOSURE DEVICES FROM THE LANE WHEN WORK IS NOT BEING PERFORMED BEHIND THE LANE CLOSURE OR WHEN A LANE CLOSURE IS NO LONGER NEEDED OR AS DIRECTED BY THE ENGINEER.
- D) WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING WITHIN 15 FT OF AN OPEN TRAVEL LANE, CLOSE THE NEAREST OPEN SHOULDER USING ROADWAY STANDARD DRAWING NO. 1101.04 UNLESS THE WORK AREA IS PROTECTED BY BARRIER OR GUARDRAIL OR A LANE CLOSURE IS INSTALLED.
- E) WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING ON THE SHOULDER ADJACENT TO AN UNDIVIDED FACILITY AND WITHIN 5 FT OF AN OPEN TRAVEL LANE, CLOSE THE NEAREST OPEN TRAVEL LANE USING ROADWAY STANDARD DRAWING NO. 1101.02 UNLESS THE WORK AREA IS PROTECTED BY BARRIER OR GUARDRAIL.

 WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING ON THE SHOULDER ADJACENT TO A DIVIDED FACILITY AND WITHIN 10 FT OF AN OPEN TRAVEL LANE, CLOSE THE NEAREST OPEN TRAVEL LANE USING ROADWAY STANDARD DRAWING NO. 1101.02 UNLESS THE WORK AREA IS PROTECTED BY BARRIER OR GUARDRAIL.
- F) WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING WITHIN A LANE OF TRAVEL OF AN UNDIVIDED OR DIVIDED FACILITY, CLOSE THE LANE ACCORDING TO THE TRAFFIC CONTROL PLANS, ROADWAY STANDARD DRAWINGS, OR AS DIRECTED BY THE ENGINEER. CONDUCT THE WORK SO THAT ALL PERSONNEL AND/OR EQUIPMENT REMAIN WITHIN THE CLOSED TRAVEL LANE.
- G) DO NOT WORK SIMULTANEOUSLY WITHIN 15 FT ON BOTH SIDES OF AN OPEN TRAVELWAY, RAMP, OR LOOP WITHIN THE SAME LOCATION UNLESS PROTECTED WITH GUARDRAIL OR BARRIER.
- H) DO NOT INSTALL MORE THAN ONE LANE CLOSURES IN ANY ONE DIRECTION ON US 158.

1/9/2023 W5701B-TMP_PSH02.dgn kbisby

APPROVED:  DATE: 1/9/2023 SEAL 		TRANSPORTATION OPERATIONS PLAN GENERALNOTES
DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED		

GENERAL NOTES

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-2A

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

PAVEMENT EDGE DROP OFF REQUIREMENTS

- I) BACKFILL AT A 6:1 SLOPE UP TO THE EDGE AND ELEVATION OF EXISTING PAVEMENT IN AREAS ADJACENT TO AN OPENED TRAVEL LANE THAT HAS AN EDGE OF PAVEMENT DROP-OFF AS FOLLOWS:

 BACKFILL DROP-OFFS THAT EXCEED 2 INCHES ON ROADWAYS WITH POSTED SPEED LIMITS OF 45 MPH OR GREATER.

 BACKFILL DROP-OFFS THAT EXCEED 3 INCHES ON ROADWAYS WITH POSTED SPEED LIMITS LESS THAN 45 MPH.

 BACKFILL WITH SUITABLE COMPACTED MATERIAL, AS APPROVED BY THE ENGINEER, AT NO EXPENSE TO THE DEPARTMENT.
- J) DO NOT EXCEED A DIFFERENCE OF 2 INCHES IN ELEVATION BETWEEN OPEN LANES OF TRAFFIC FOR NOMINAL LIFTS OF 1.5 INCHES. INSTALL ADVANCE WARNING "UNEVEN LANES" SIGNS (W8-11) (LENGTH) IN ADVANCE AND A MINIMUM OF EVERY HALF MILE THROUGHOUT THE UNEVEN AREA.

TRAFFIC PATTERN ALTERATIONS

- K) NOTIFY THE ENGINEER THIRTY (30) CALENDAR DAYS PRIOR TO ANY TRAFFIC PATTERN ALTERATION.

SIGNING

- L) INSTALL ADVANCE WORK ZONE WARNING SIGNS WHEN WORK IS WITHIN 40 FT FROM THE EDGE OF TRAVEL LANE AND NO MORE THAN THREE (3) DAYS PRIOR TO THE BEGINNING OF CONSTRUCTION.
- M) ENSURE ALL NECESSARY SIGNING IS IN PLACE PRIOR TO ALTERING ANY TRAFFIC PATTERN.

TRAFFIC CONTROL DEVICES

- N) WHEN LANE CLOSURES ARE NOT IN EFFECT SPACE CHANNELIZING DEVICES IN WORK AREAS NO GREATER IN FEET THAN TWICE THE POSTED SPEED LIMIT (MPH) EXCEPT, 10 FT ON-CENTER IN RADII, AND 3 FT OFF THE EDGE OF AN OPEN TRAVELWAY. REFER TO STANDARD SPECIFICATIONS FOR ROADS AND STRUCTURES SECTIONS 1130 (DRUMS), 1135 (CONES) AND 1180 (SKINNY DRUMS) FOR ADDITIONAL REQUIREMENTS.
- O) PLACE TYPE III BARRICADES, WITH "ROAD CLOSED" SIGN R11-2 ATTACHED, OF SUFFICIENT LENGTH TO CLOSE ENTIRE ROADWAY.
- P) PLACE ADDITIONAL SETS OF THREE CHANNELIZING DEVICES (DRUMS) PERPENDICULAR TO THE EDGE OF TRAVELWAY ON 200 FT CENTERS WHEN UNOPENED LANES ARE CLOSED TO TRAFFIC.




PAVEMENT MARKINGS AND MARKERS

- Q) INSTALL TEMPORARY PAVEMENT MARKINGS AND TEMPORARY PAVEMENT MARKERS ON INTERIM LAYERS OF PAVEMENT AS FOLLOWS:

ROAD NAME	MARKING	MARKER
US 158, US 258, NC 11, CHOWAN COLLEGE RD	PAINT	TEMPORARY RAISED

- R) PLACE ONE APPLICATION OF PAINT FOR TEMPORARY TRAFFIC PATTERNS. PLACE A SECOND APPLICATION OF PAINT SIX (6) MONTHS AFTER THE INITIAL APPLICATION AND EVERY SIX MONTHS AS DIRECTED BY THE ENGINEER.
- S) TIE PROPOSED PAVEMENT MARKING LINES TO EXISTING PAVEMENT MARKING LINES.
- T) REMOVE/REPLACE ANY CONFLICTING/DAMAGED PAVEMENT MARKINGS AND MARKERS BY THE END OF EACH DAY'S OPERATION.

1/9/2023
W5701B_TMP_PSH02A.dgn
KBISBY

APPROVED:  DATE: 1/9/2023 SEAL			TRANSPORTATION OPERATIONS PLAN GENERALNOTES
DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED			



MANAGEMENT STRATEGIES

THE FOLLOWING LISTED WORK ZONE STRATEGIES ARE RECOMMENDED FOR INCLUSION WITHIN THIS TRANSPORTATION MANAGEMENT PLAN (TMP).

RECOMMENDED STRATEGIES:

TRAFFIC MANAGEMENT STRATEGIES:

- LANE SHIFTS OR CLOSURES
- SHOULDER CLOSURES
- ONE-LANE, TWO WAY OPERATION (FLAGGING)

TRAFFIC CONTROL PHASING

PHASE I

STEP 1:
USING RDWY STD 1101.01, ERECT WORK ZONE ADVANCE WARNING SIGNS ON -L- (US 158), -Y1- (US 258), -Y2- (US 158 BUS), -Y6- (CHOWAN COLLEGE RD), AND -Y7- (NC 11).

STEP 2:
USING RDWY STD 1101.02 CONSTRUCT THE PROPOSED WIDENING ON -L- (US 158) AND -Y7- (NC 11) UP TO THE EDGE AND ELEVATION OF EXISTING PAVEMENT WHILE MAINTAINING CURRENT TRAFFIC PATTERNS: (REFER TO TMP-4 THROUGH 10)

- -L- STA 29+15± TO STA 51+75±
- -L- STA 161+95± TO STA 198+00±

STEP 3:
USING RDWY STD 1101.02, CONSTRUCT MONOLITHIC ISLANDS IN THE MEDIAN AT THE U-TURN BULBS. (SEE TMP-4, 6, 7 AND 10).

PHASE II

STEP 1:
USING RDWY STD 1101.02, APPLY PAVEMENT MARKINGS AND OPEN U-TURN LANES TO TRAFFIC. CLOSE THE EXISTING US 158/US 258/US 158 BUS INTERSECTION MEDIAN OPENING, THE EXISTING US 158/CHOWAN COLLEGE RD INTERSECTION MEDIAN OPENING, AND THE US 158/NC 11 INTERSECTION MEDIAN OPENING TRAFFIC ONCE THE MEDIAN U-TURN INTERSECTIONS ARE OPEN TO TRAFFIC. REMOVE SIGNALS. (REFER TO TMP-11 THROUGH 17)

STEP 2:
USING RDWY STD 1101.02, CONSTRUCT LEFT-OVER MEDIAN ISLANDS ON -L- (US 158/258). (SEE TMP-12 AND 15)

USING RDWY STD 1101.02 CONSTRUCT PAVEMENT IN THE NORTHWEST AND SOUTHEAST QUADRANTS OF THE -L- (US 158)/-Y1- (US 258)/-Y2- (US 158 BUS) INTERSECTION TO THE EDGE AND ELEVATION OF THE EXISTING PAVEMENT. (SEE TMP-12)




STEP 3:
USING RDWY STD 1101.02, APPLY PAVEMENT MARKINGS AND OPEN INTERSECTION MEDIAN OPENINGS TO TRAFFIC. (REFER TO TMP-18 THROUGH 23)

STEP 4:
USING RDWY STD 1101.02, CONSTRUCT MONOLITHIC ISLANDS ON -Y1- US 258, -Y2- US 158 BUSINESS AND -Y7- US 258/NC 11. (SEE TMP-19 AND 22)

PHASE III




USING RDWY STD 1101.02, PAVE THE SURFACE COURSE, APPLY THE FINAL PAVEMENT MARKINGS, REMOVE TRAFFIC CONTROL DEVICES AND OPEN TO TRAFFIC IN THE FINAL PATTERN. (REFER TO THE FINAL PAVEMENT MARKING PLANS).

1/9/2023 W5701B-TMP_PSH03.dgn KB/sby

<p>APPROVED:  <small>DocuSigned by: Kevin Bly BDD082E28912472</small></p> <p>DATE: 1/9/2023</p> <p style="text-align: center;">SEAL</p>			<p>MANAGEMENT STRATEGIES</p> <p>TRAFFIC CONTROL PHASING</p>
<p>DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED</p>			

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-4

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

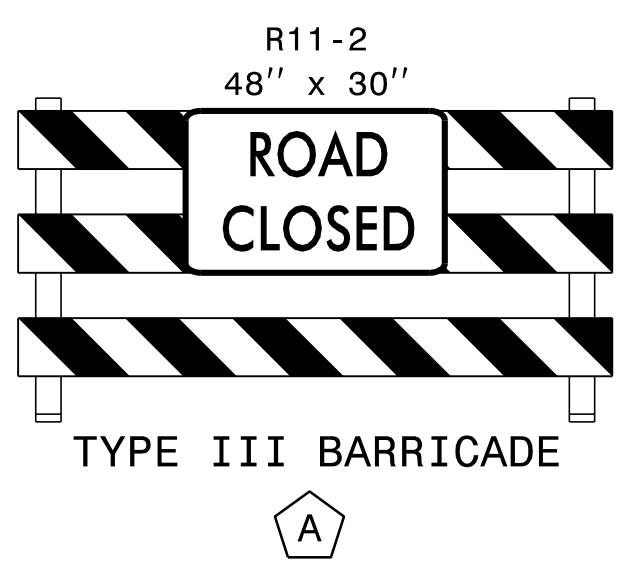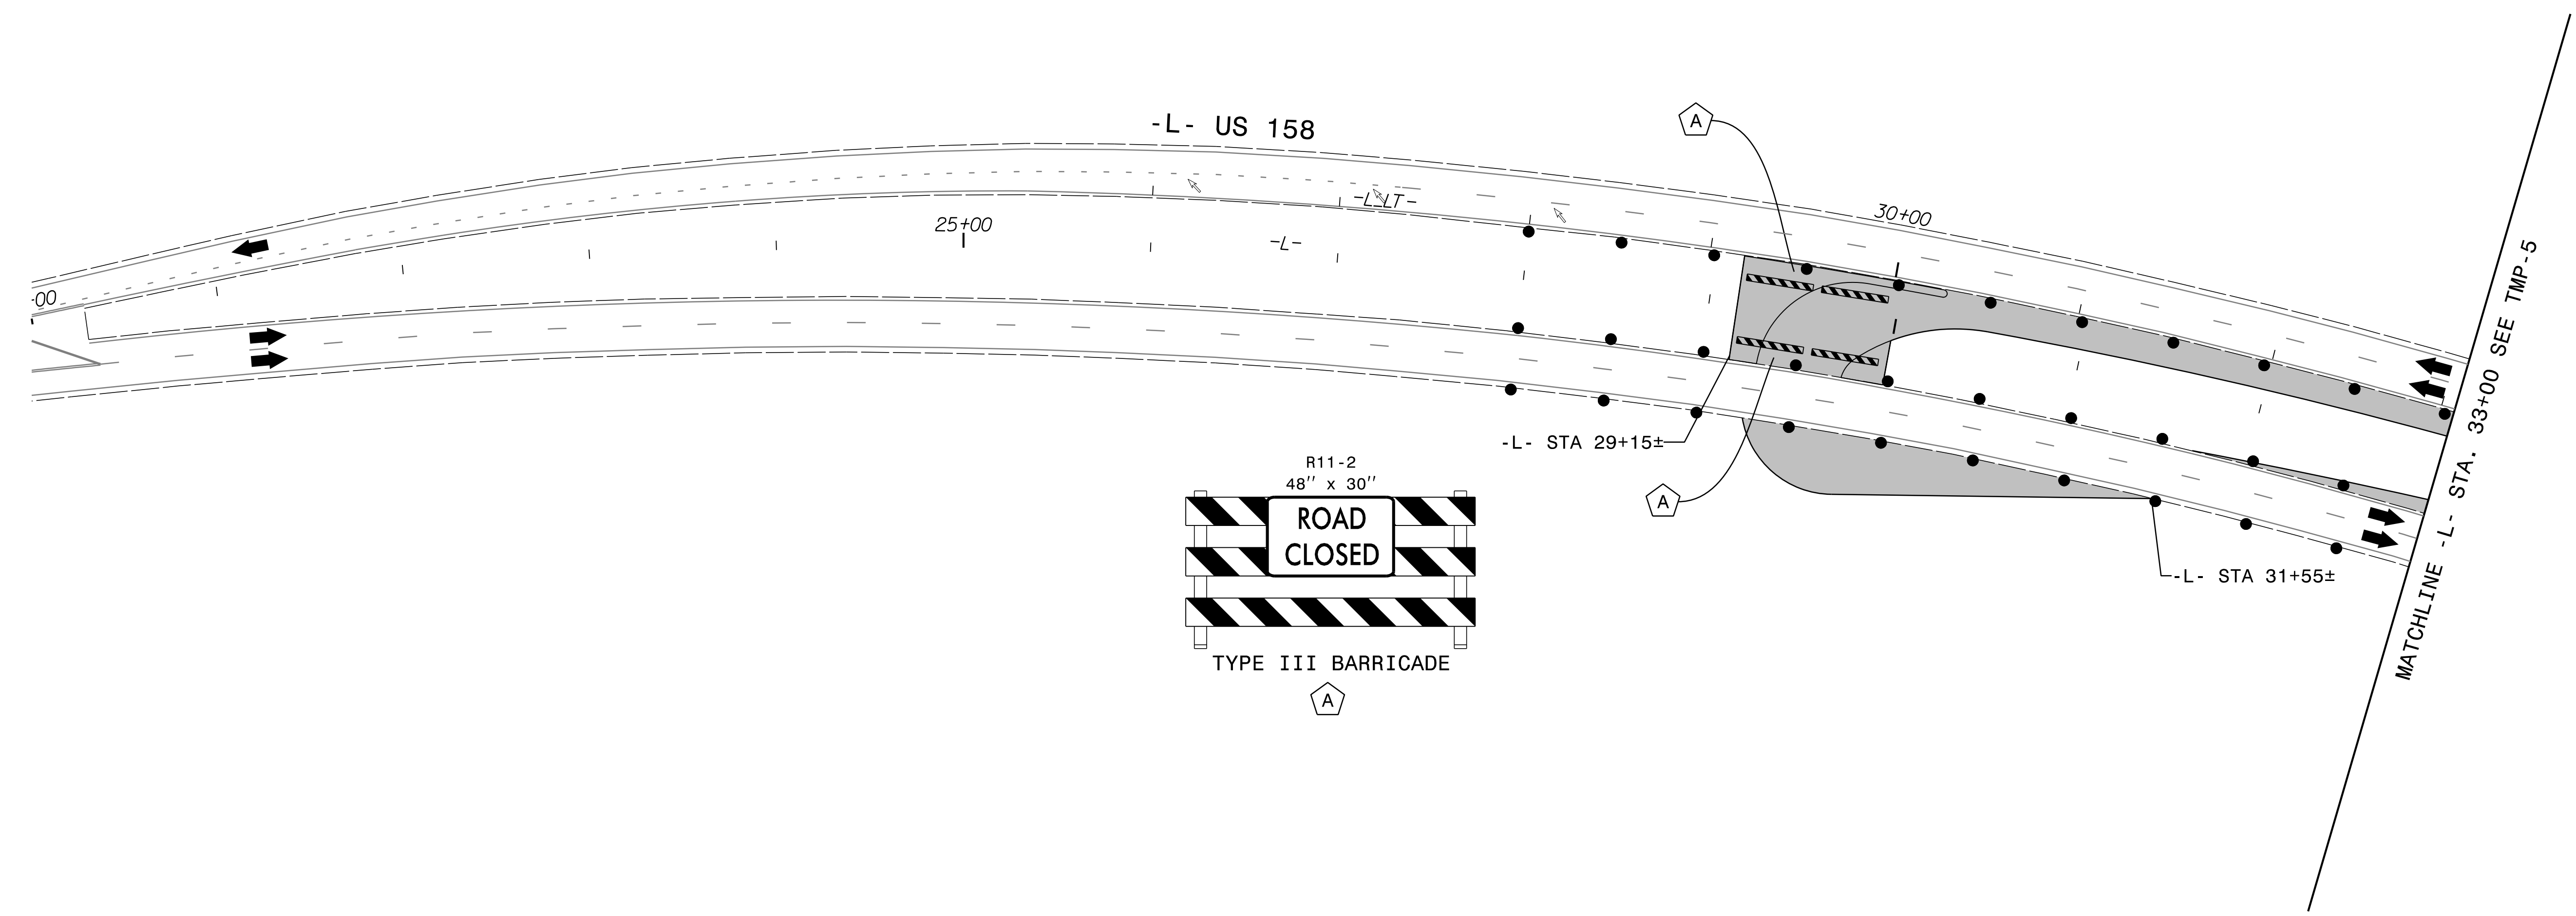


1/9/2023
W5701B-TMP_PSH04.dgn
KBISBY

APPROVED: *Kevin B. Bly*
800802628912472

DATE: 1/9/2023

SEAL



**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**

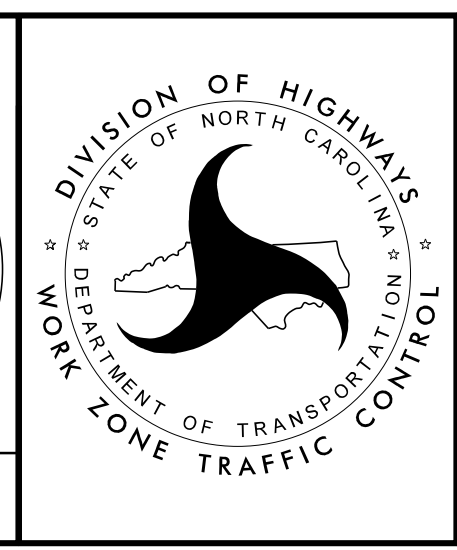


PHASE I - STEPS 2 AND 3

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-5

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

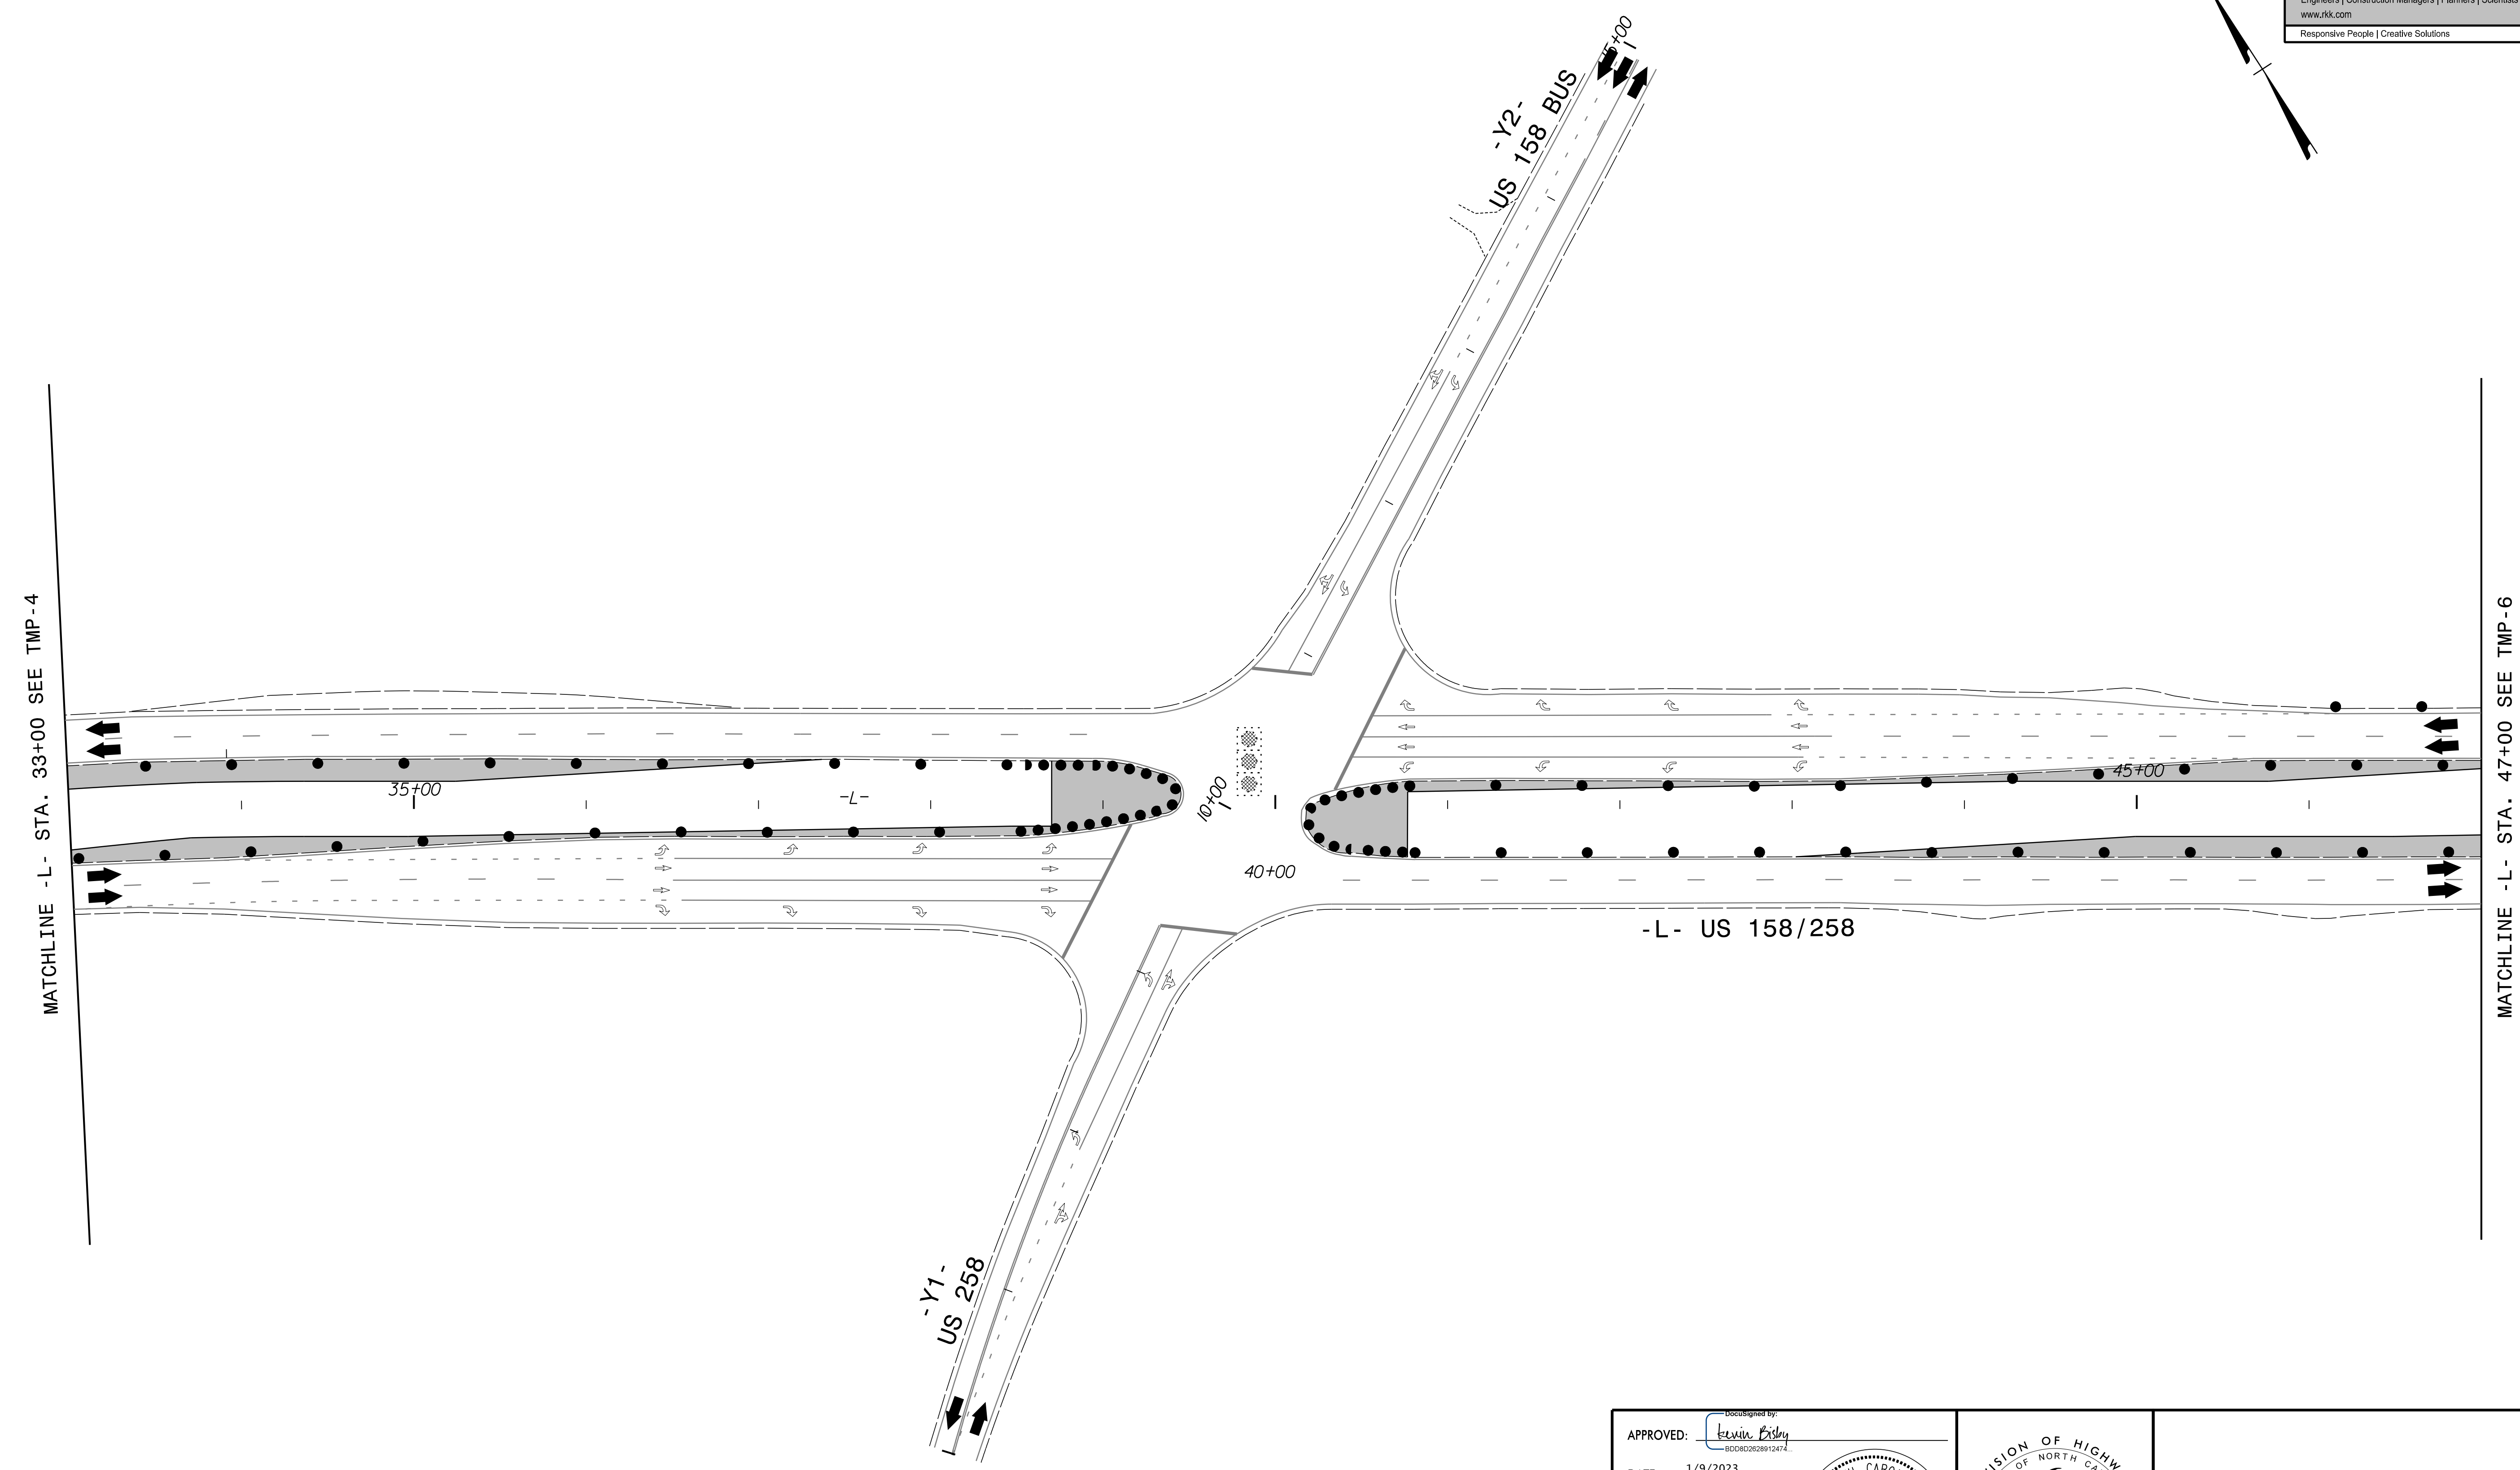


1/9/2023
 W5701B_TMP_PSH05.dgn
 KB/sby


APPROVED: 
800802628912472

DATE: 1/9/2023




SEAL




**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

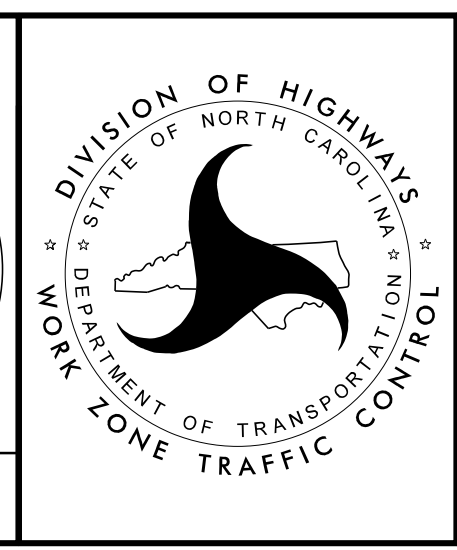

PHASE I - STEP 2

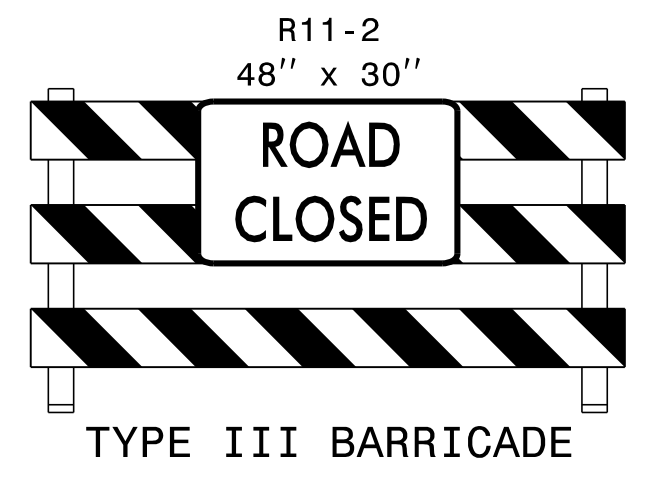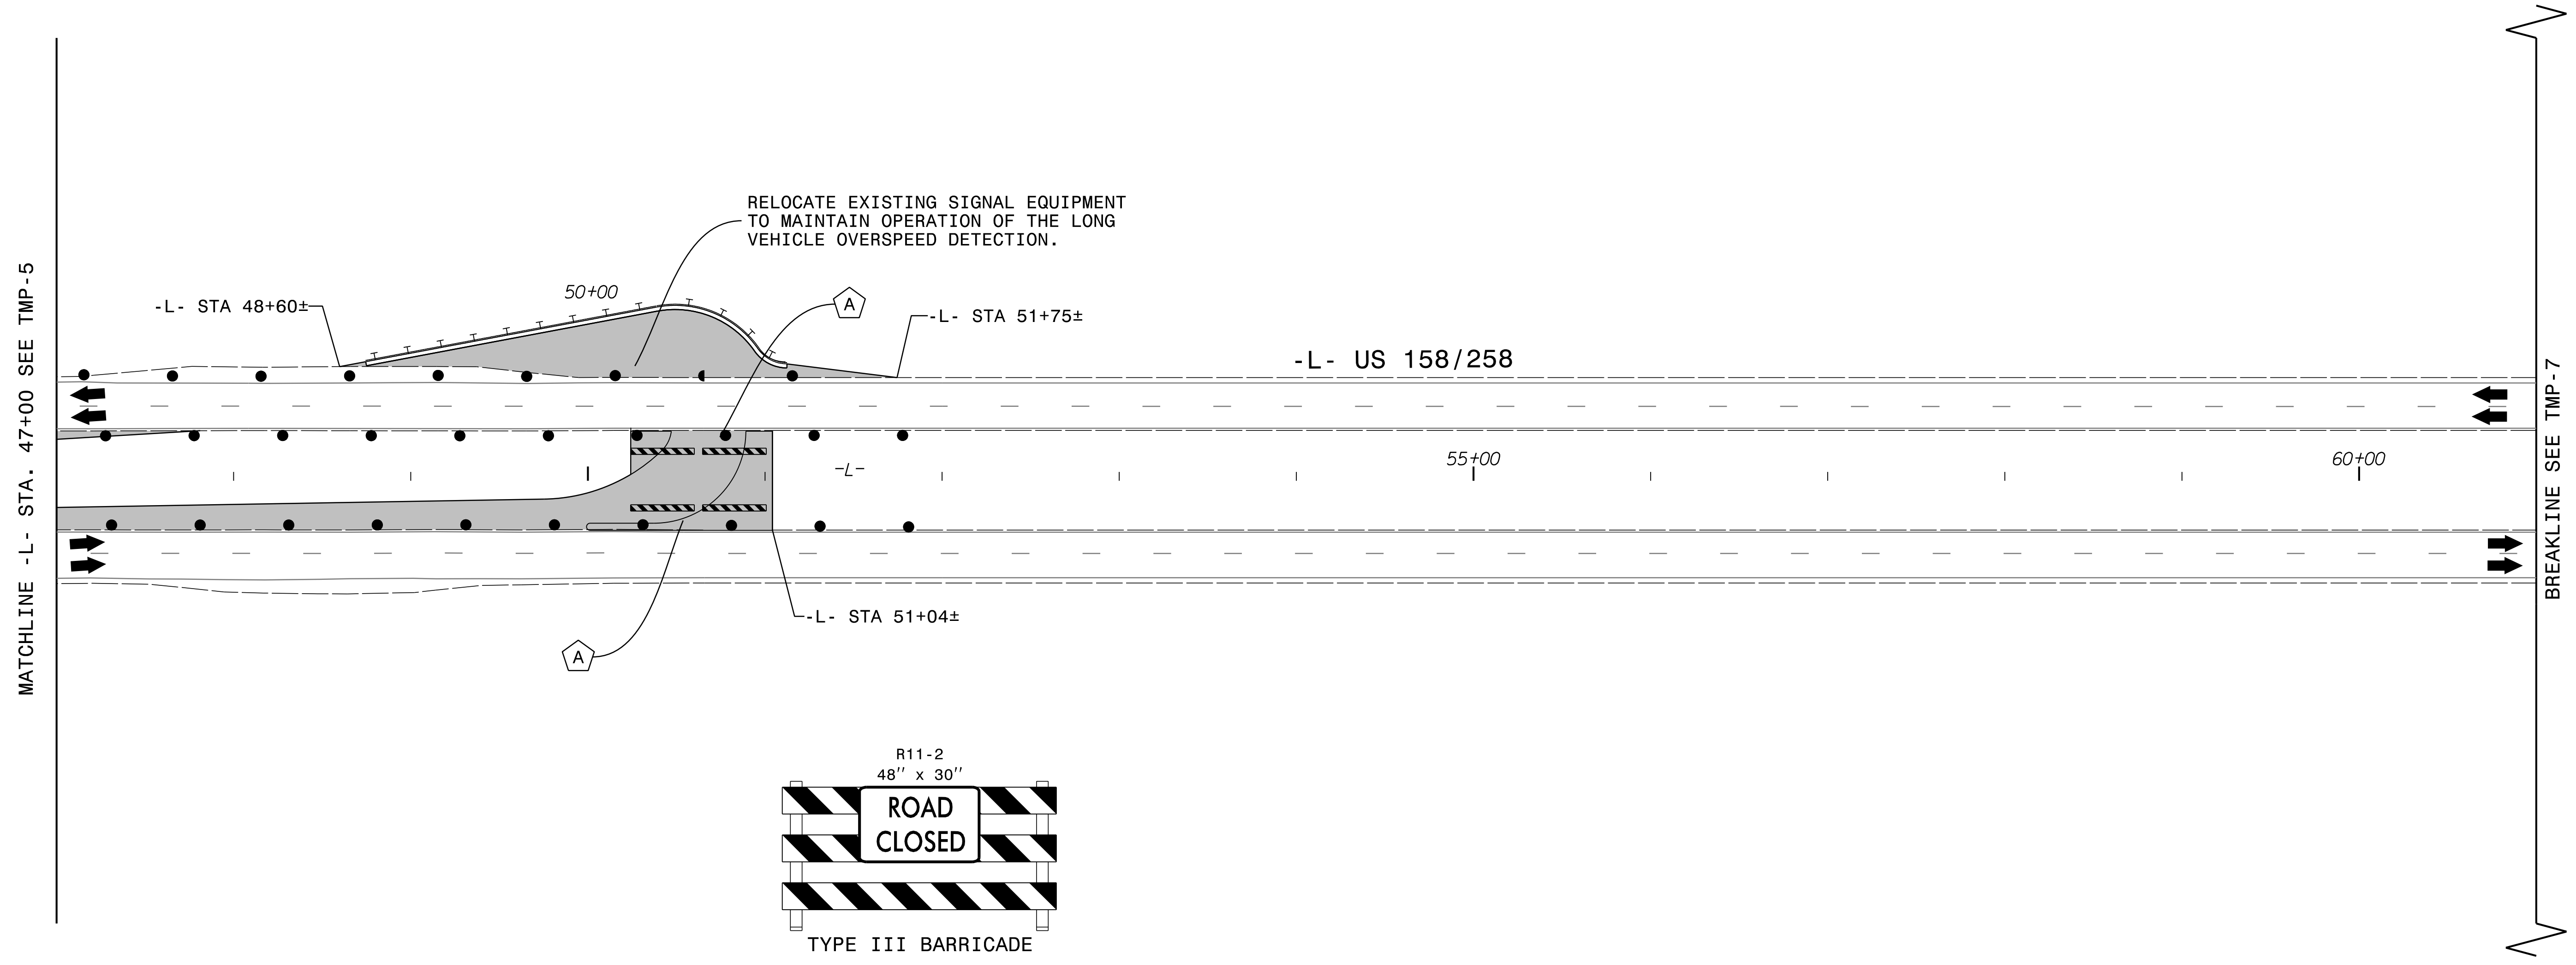


1/9/2023
 W5701B_TMP_PSH06.dgn
 KB/bsby

APPROVED: 
800802628912472



DATE: 1/9/2023

SEAL




PHASE I - STEPS 2 AND 3

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

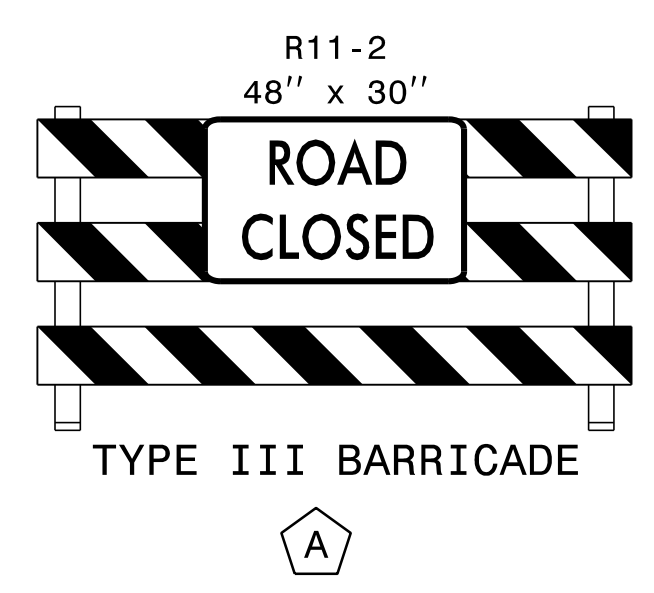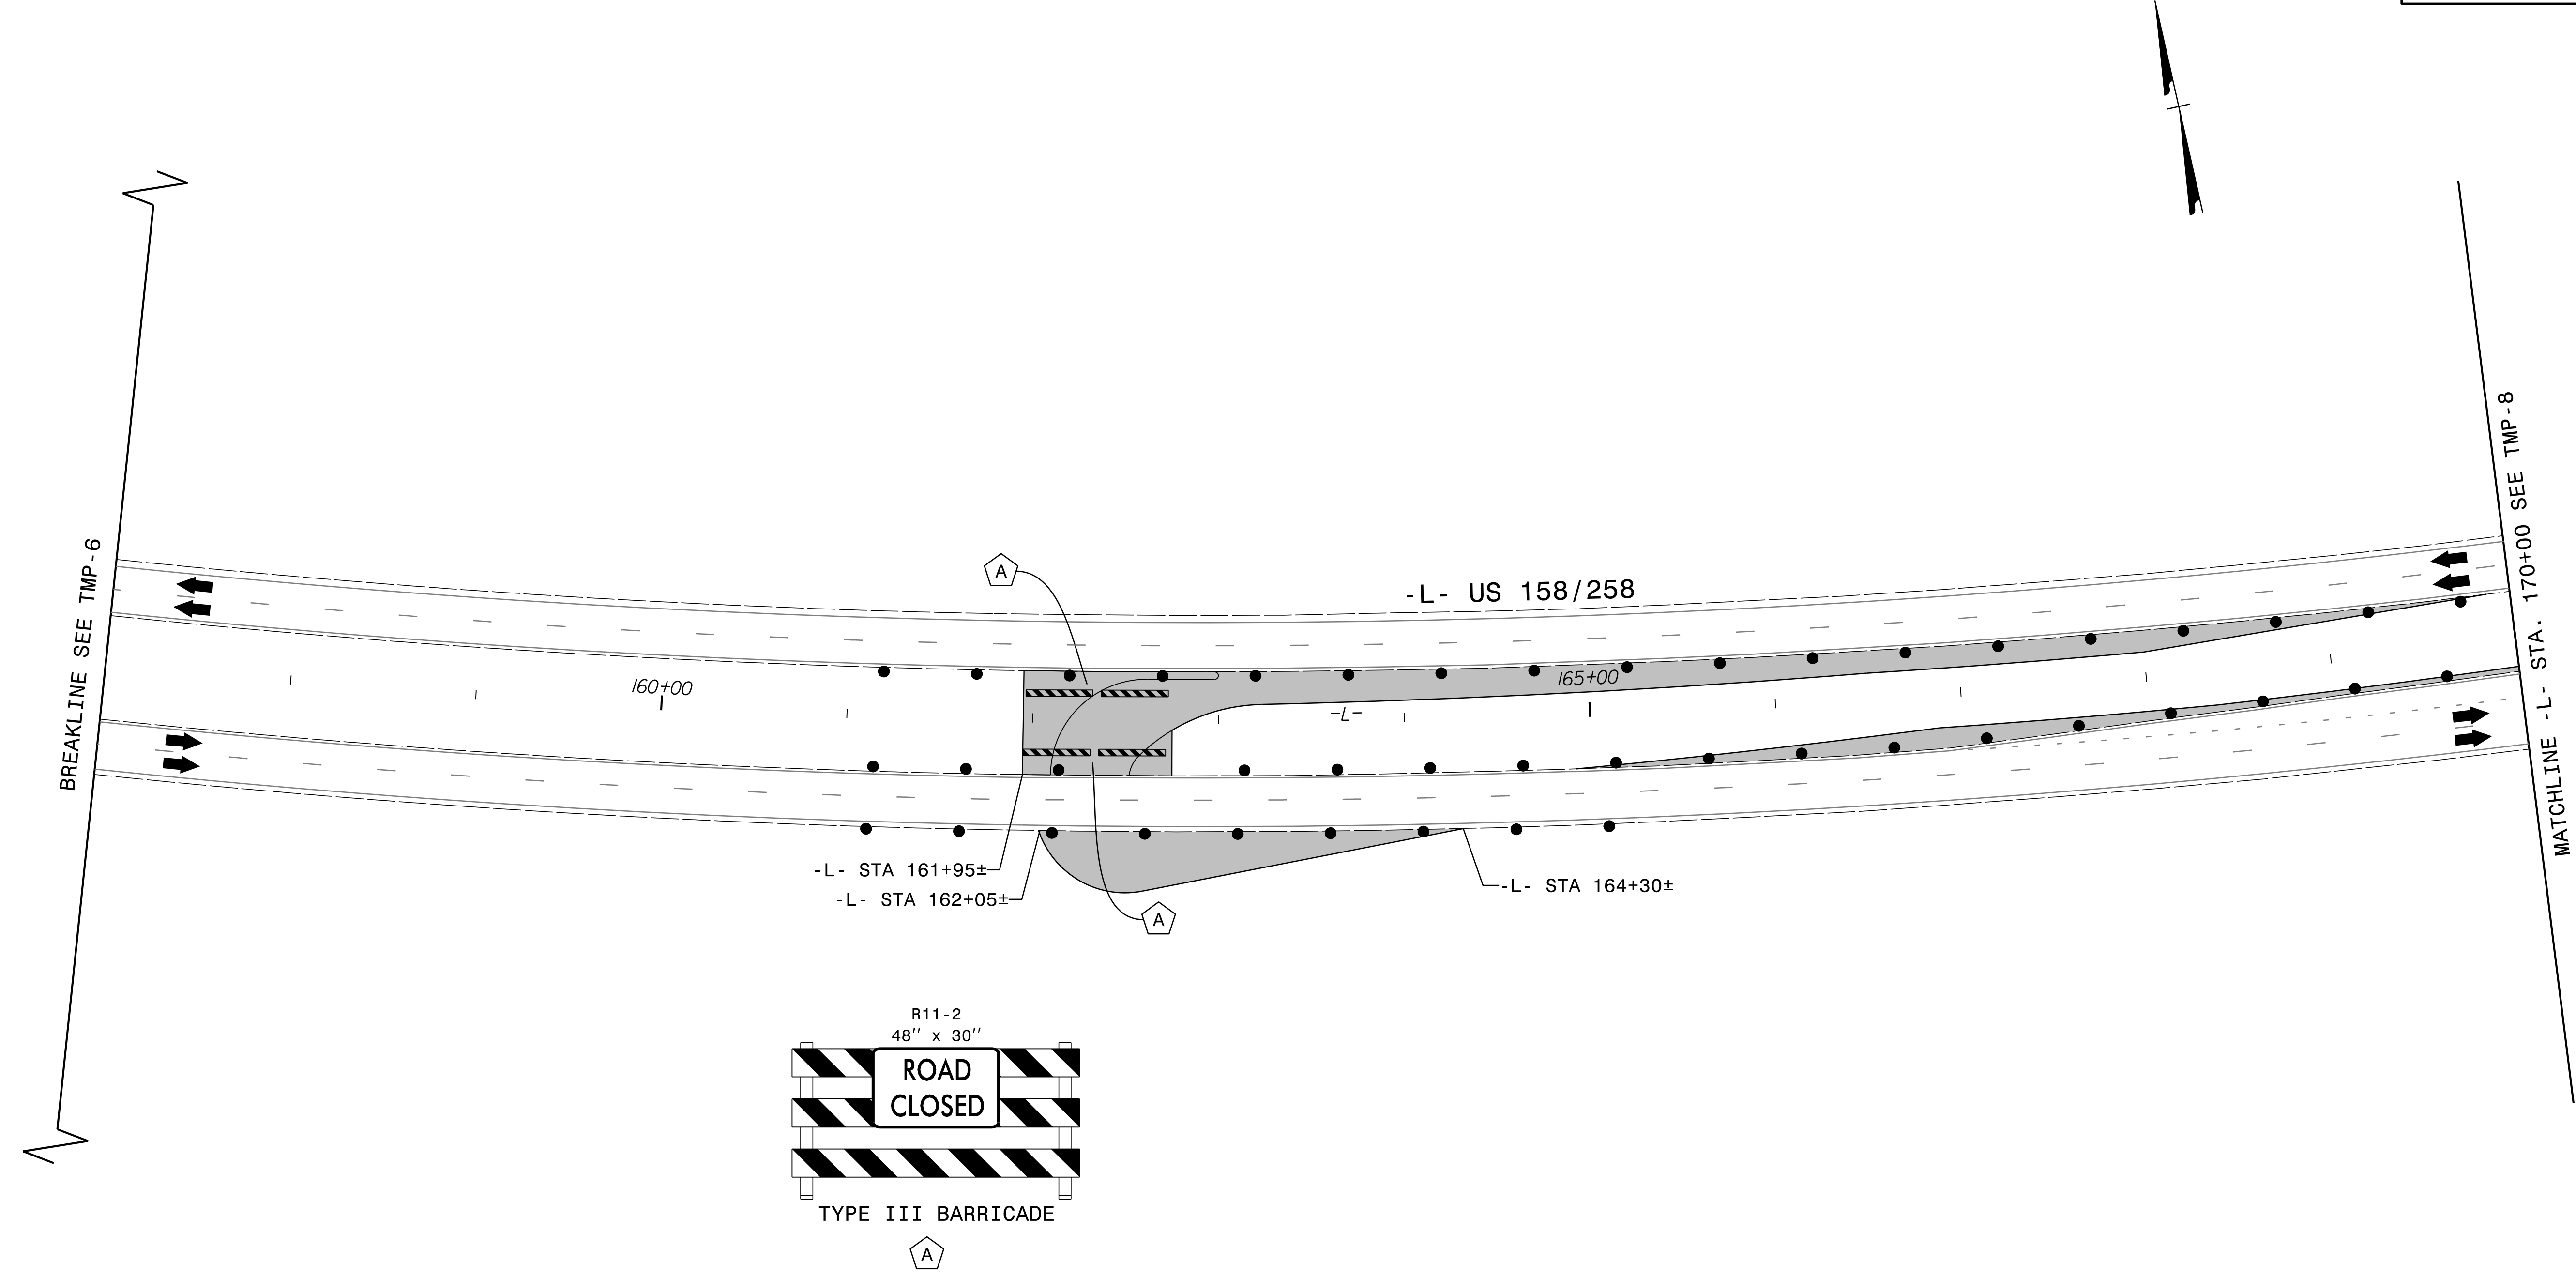


1/9/2023
 W5701B_TMP_PSH07.dgn
 KB/lsby

APPROVED: *Kevin Esley*
 DATE: 1/9/2023

SEAL


**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

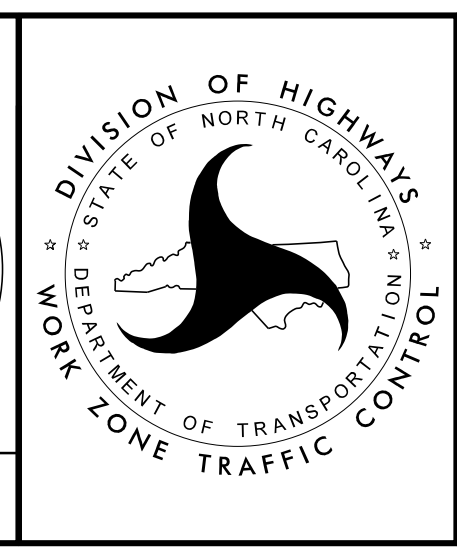

PHASE I - STEPS 2 AND 3

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-8

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

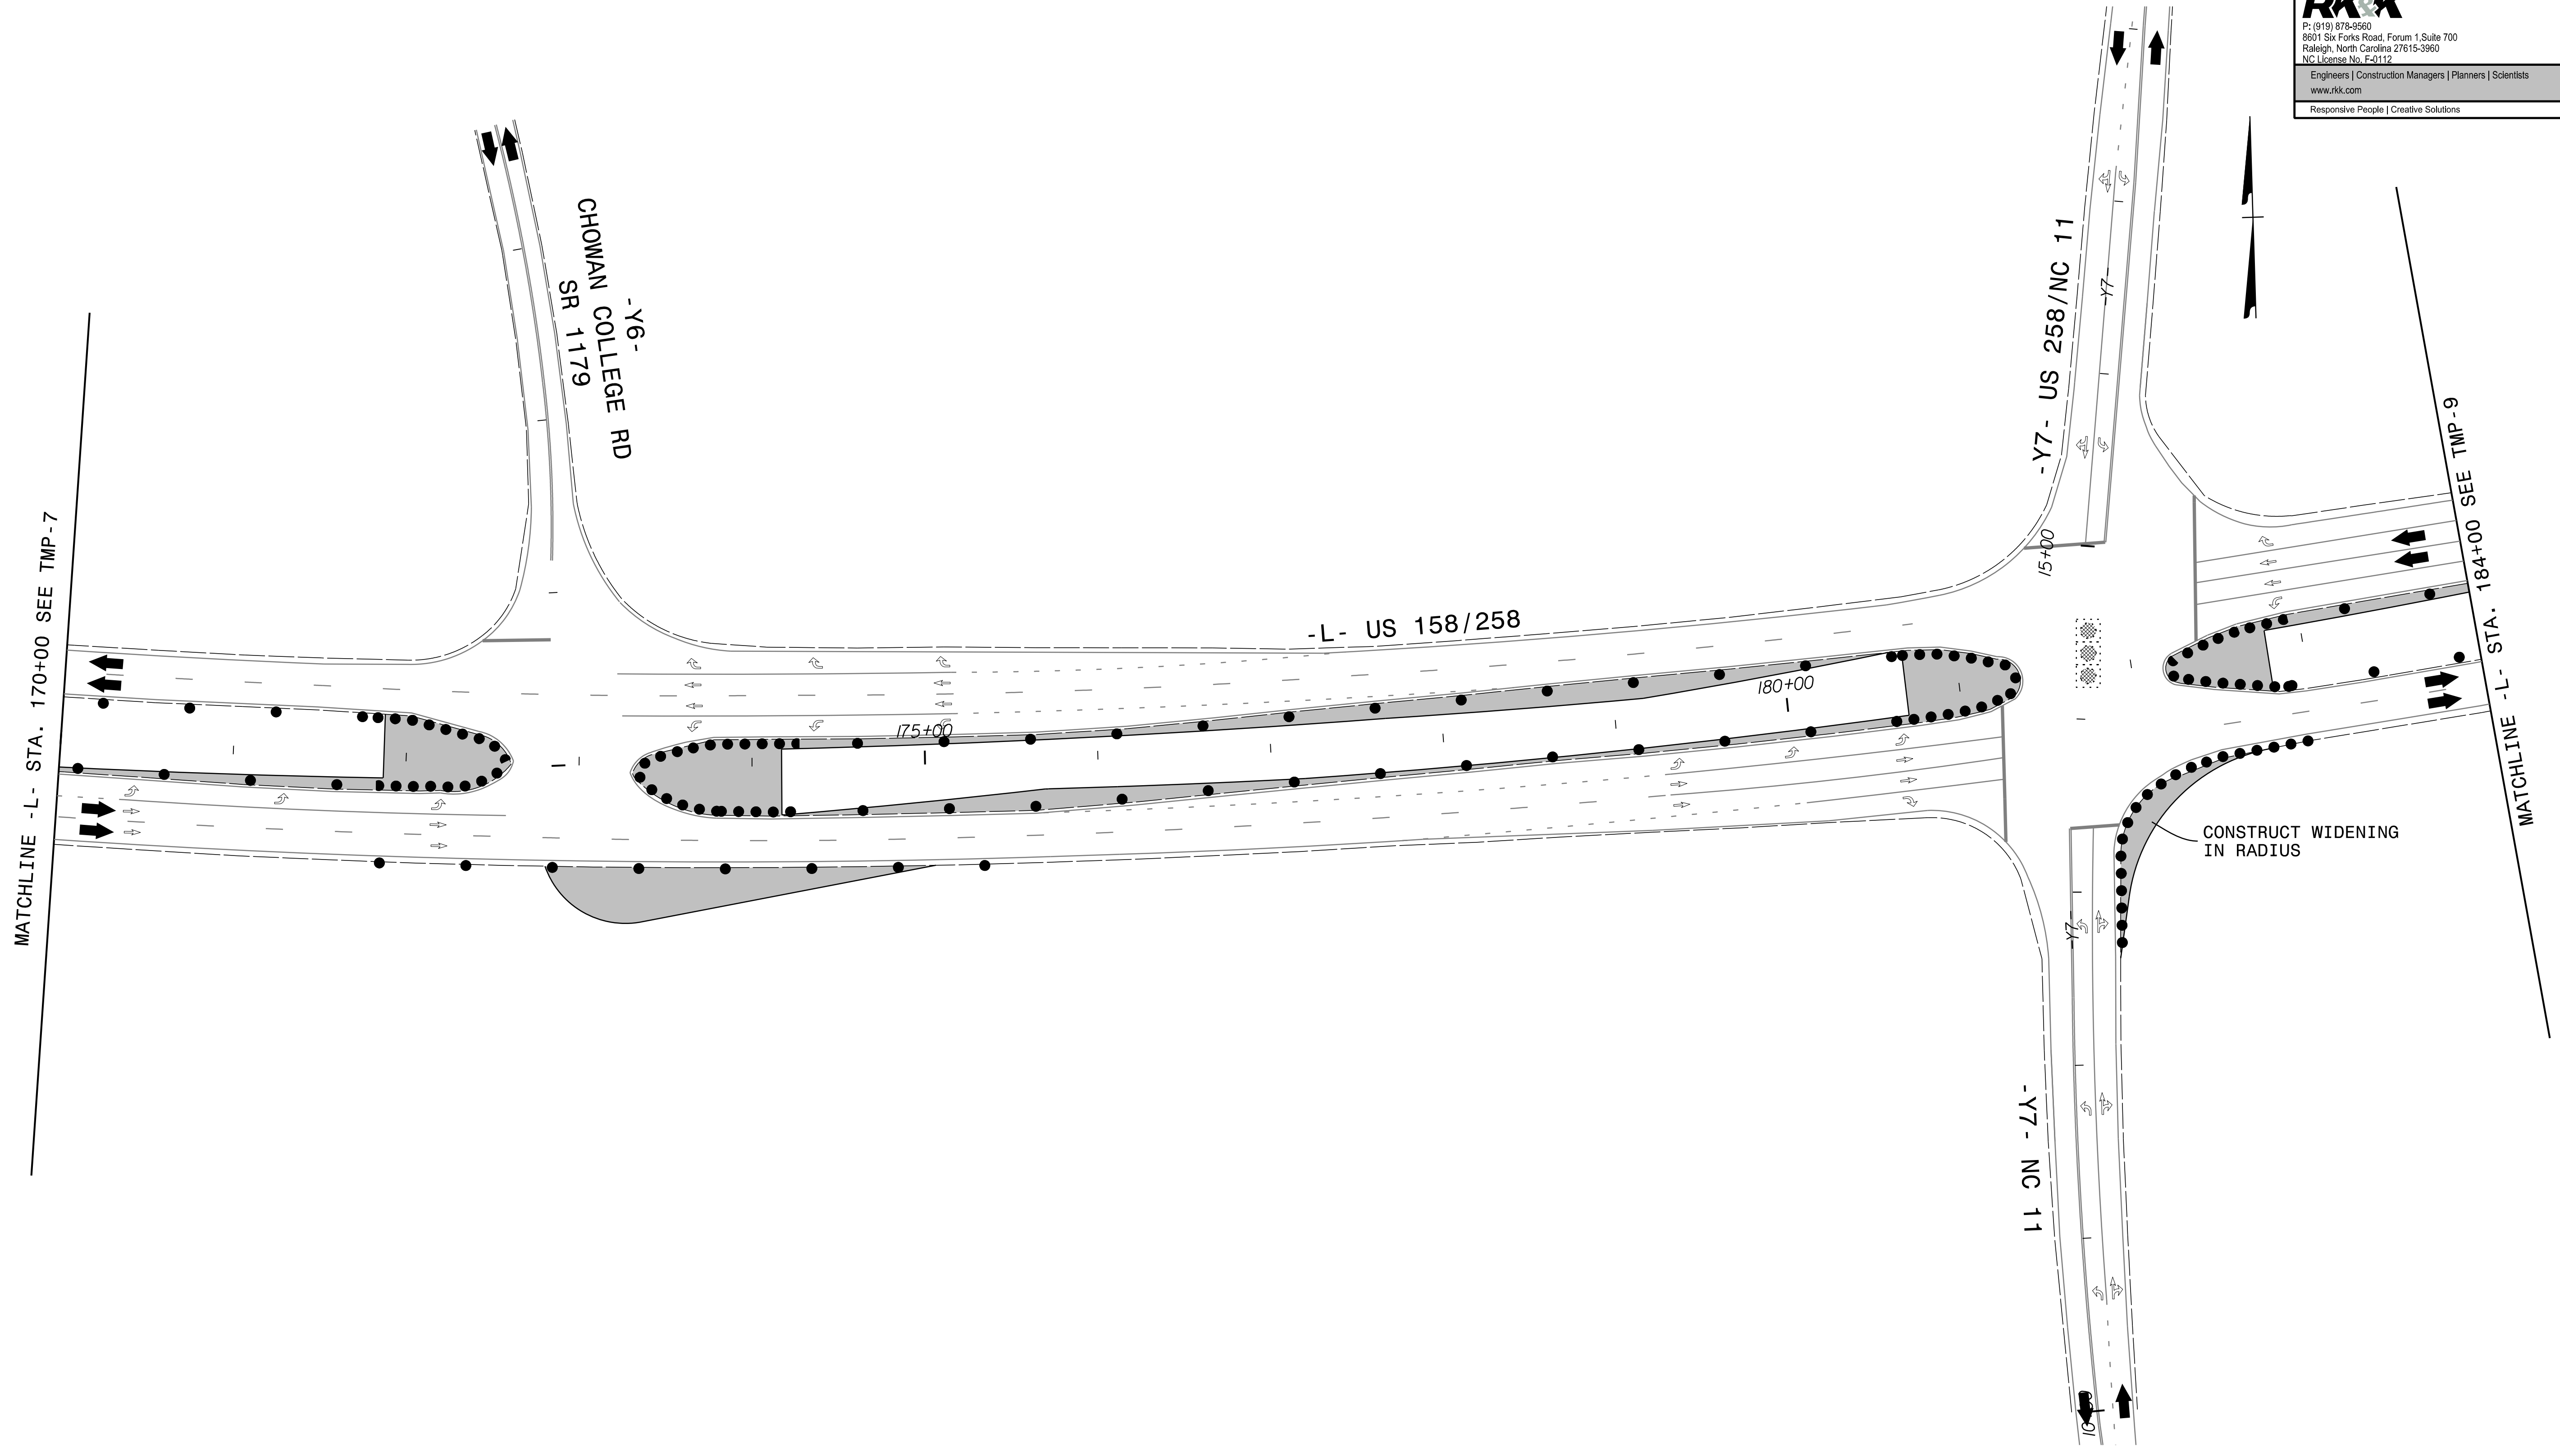


1/9/2023
 W5701B_TMP_PSH08.dgn
 KBISBY

APPROVED: *Kevin Bisy*
800802628912472

DATE: 1/9/2023

SEAL


**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

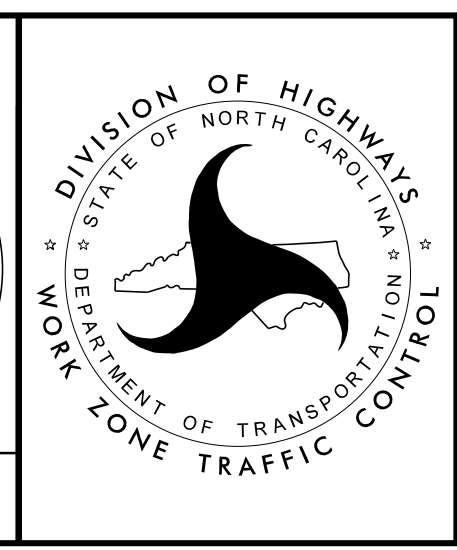

PHASE I - STEP 2

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-9

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

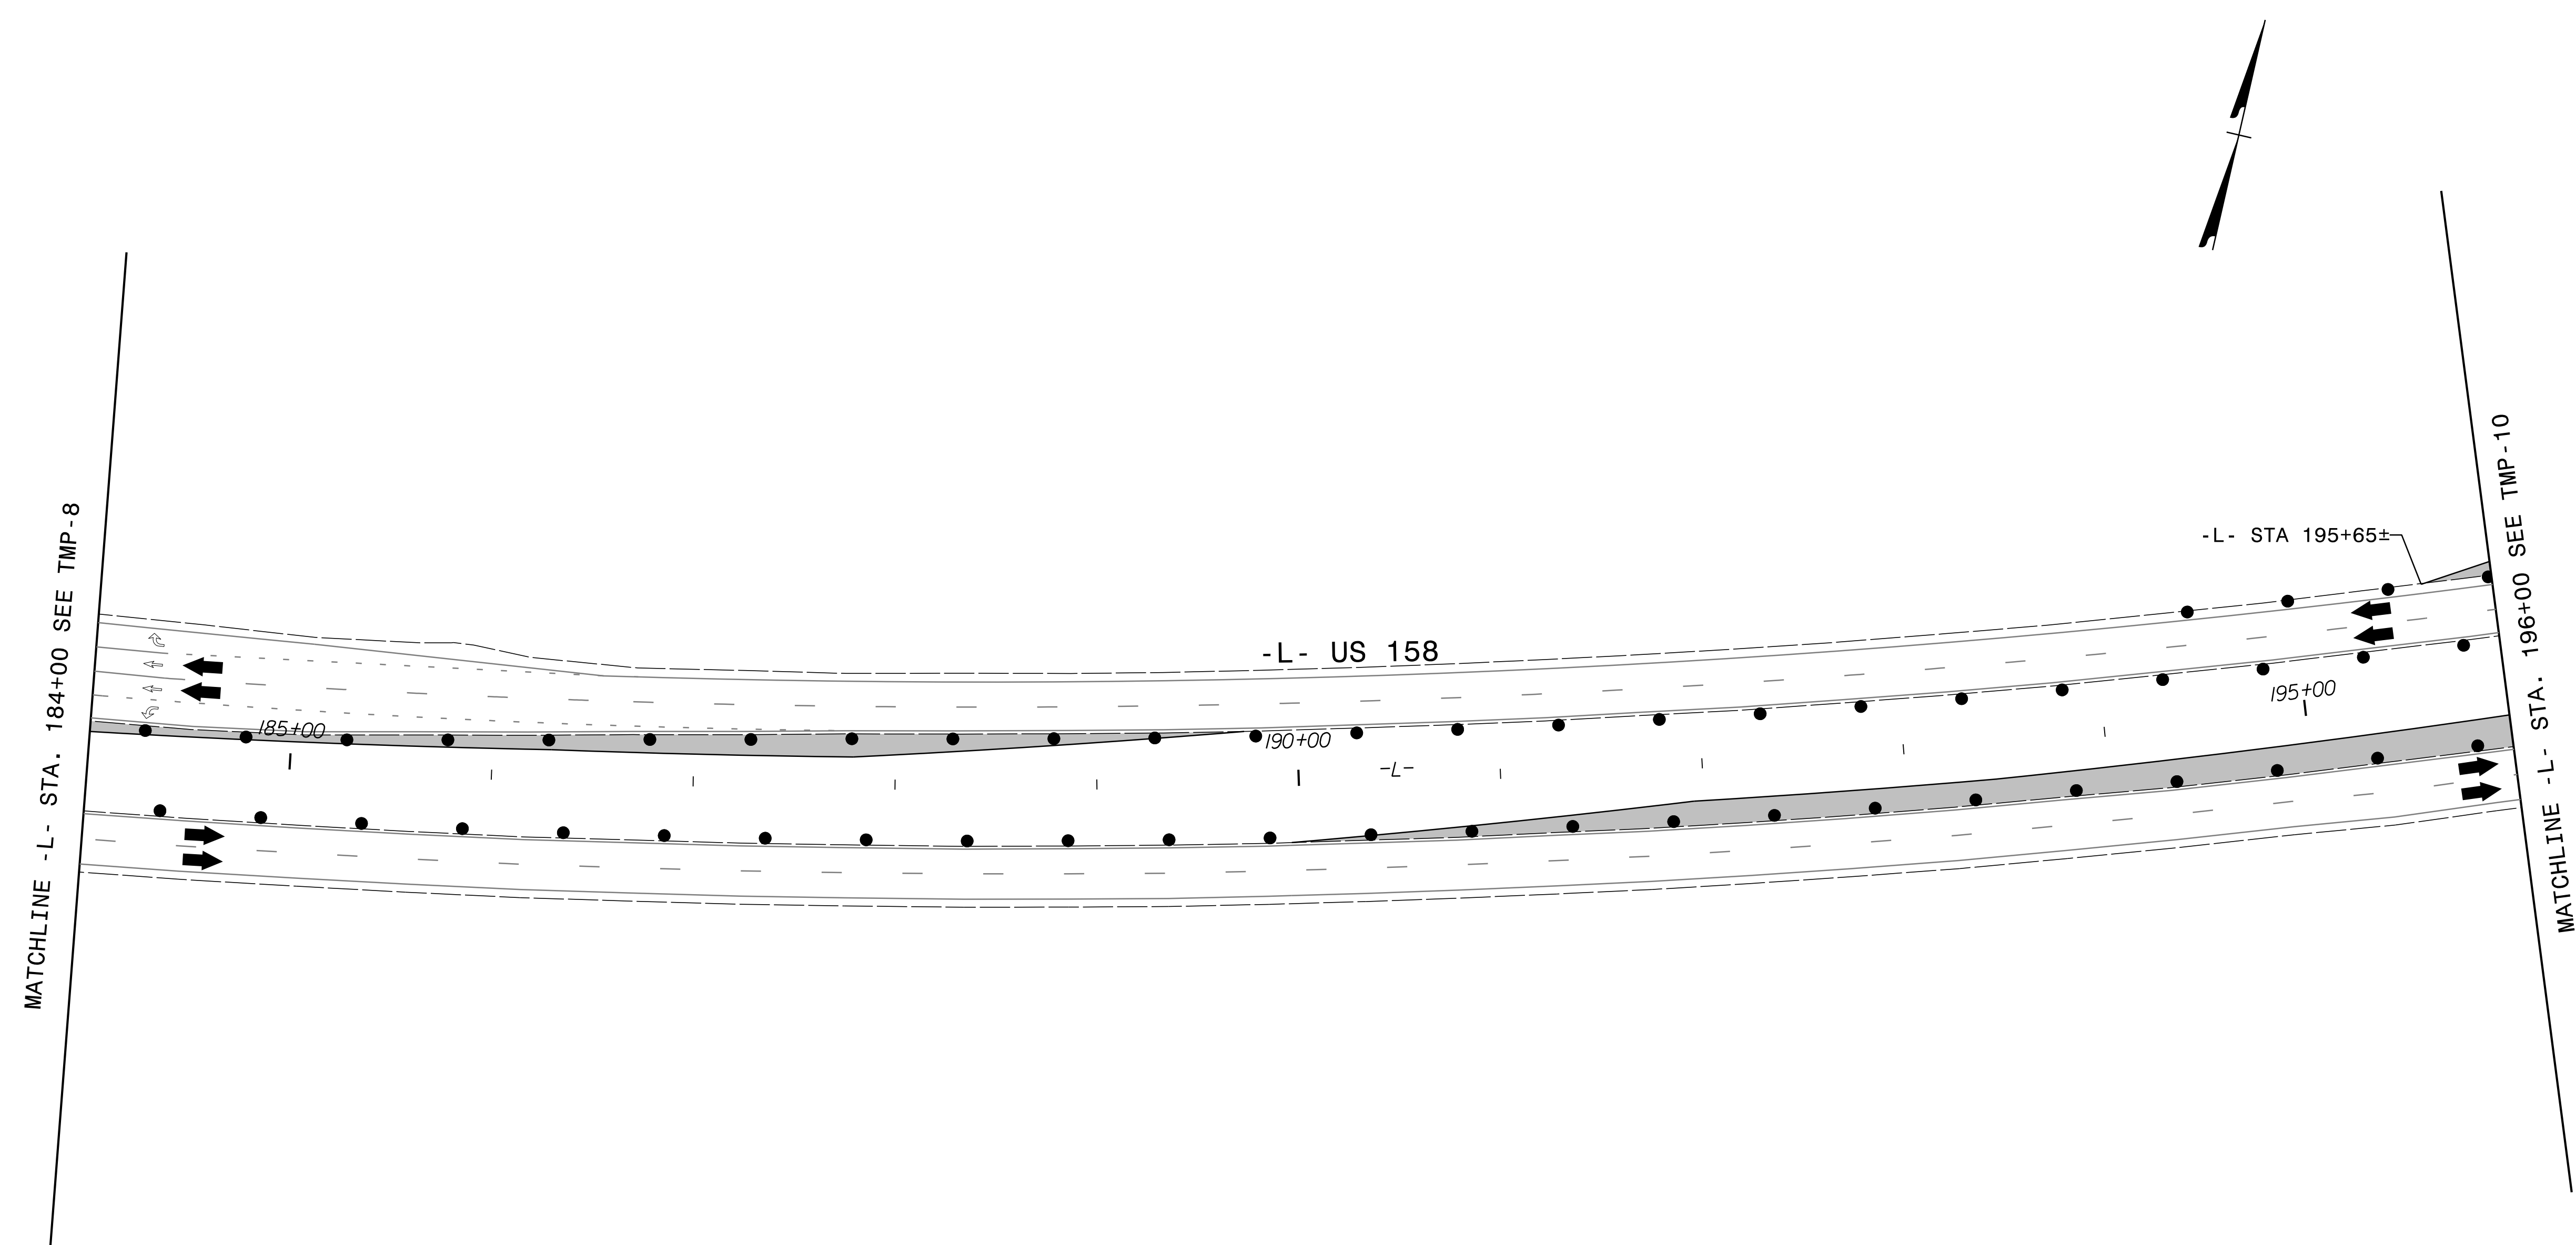

1/9/2023
 W5701B_TMP_PSH09.dgn
 KBISBY


APPROVED: *Kevin Bisy*
800802628912472

DATE: 1/9/2023

SEAL

NORTH CAROLINA PROFESSIONAL ENGINEER
 SEAL 21047
 KEVIN W. BISBY




DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED

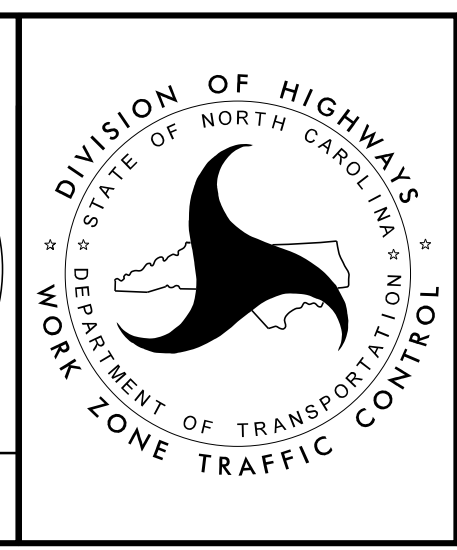


PHASE I - STEP 2

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-10

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

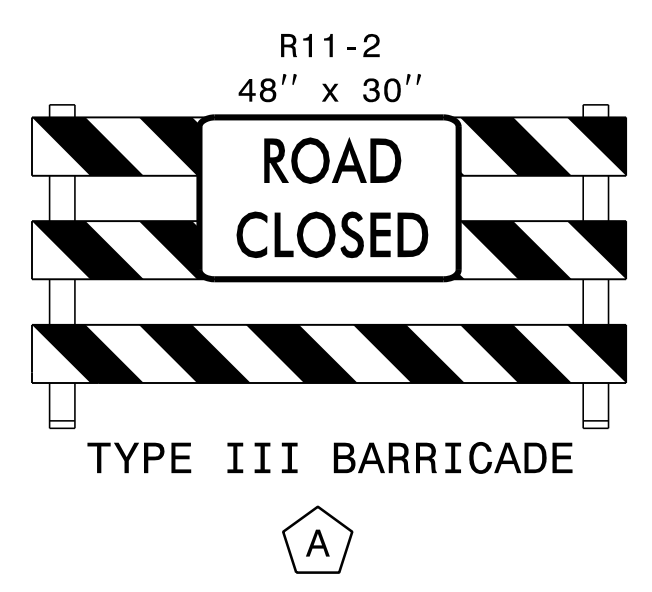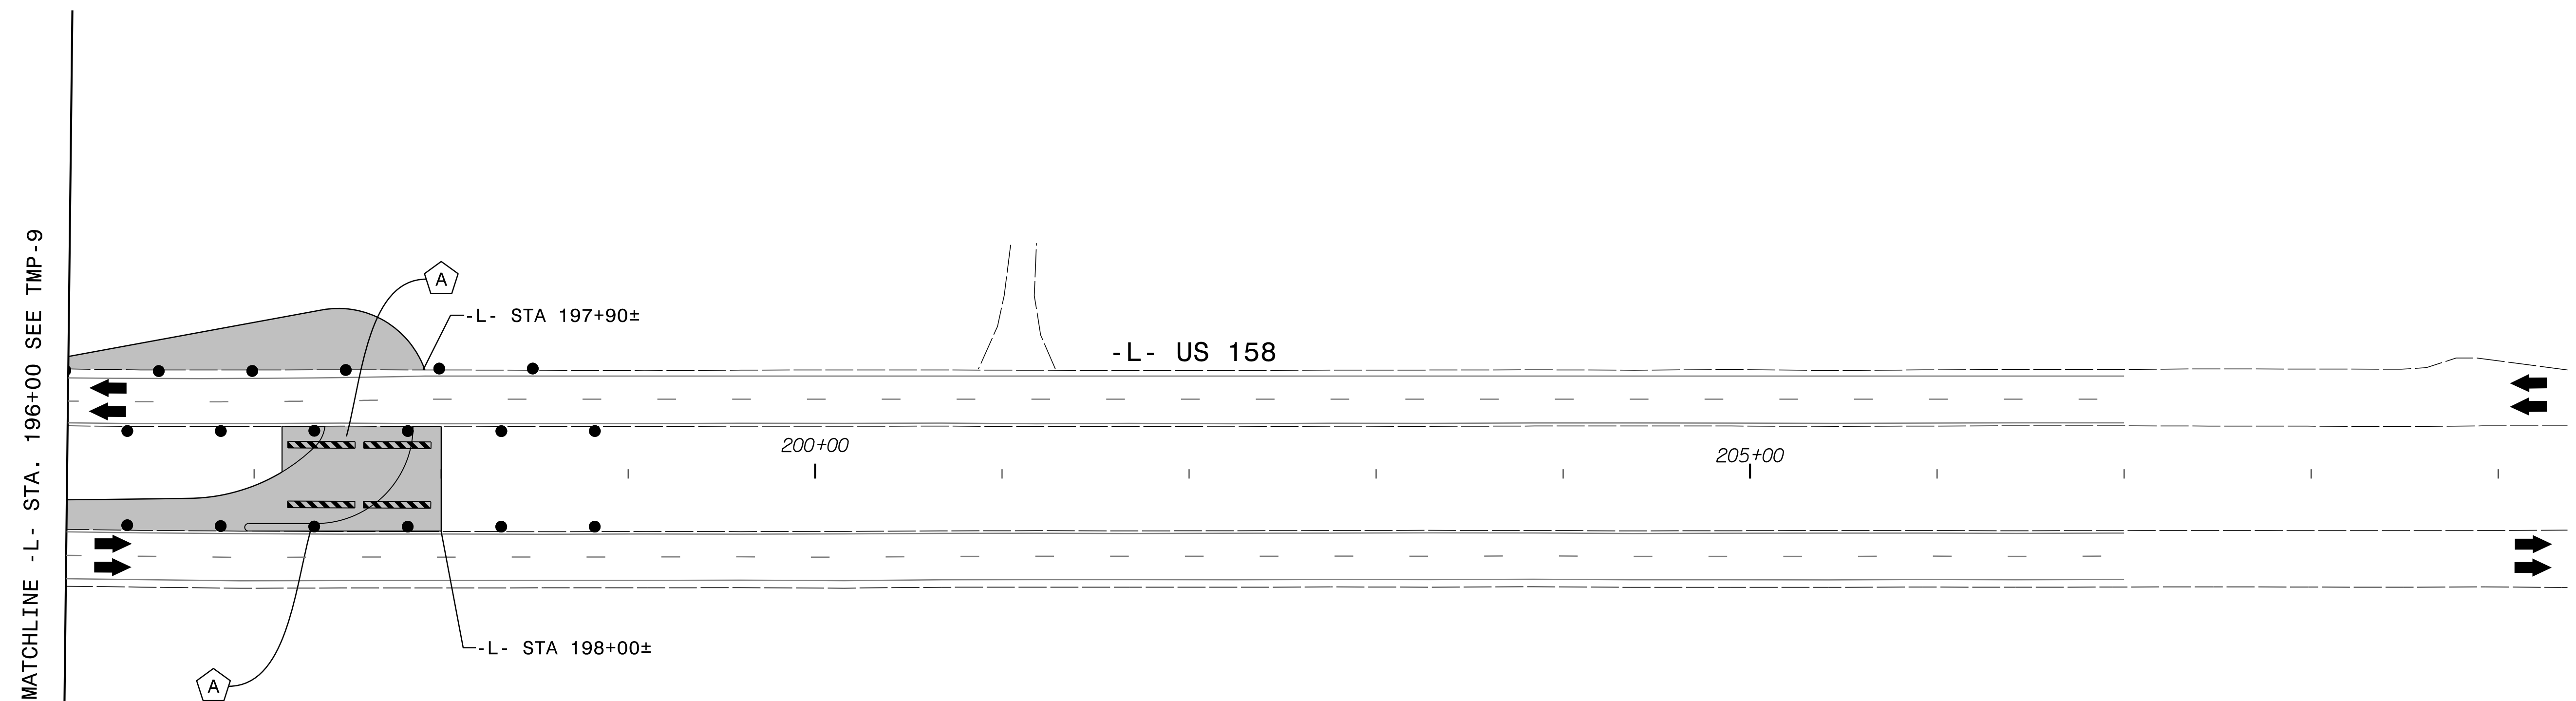



1/9/2023
 W5701B_TMP_PSH10.dgn
 KBISBY

APPROVED: 
800802628912472

DATE: 1/9/2023

SEAL


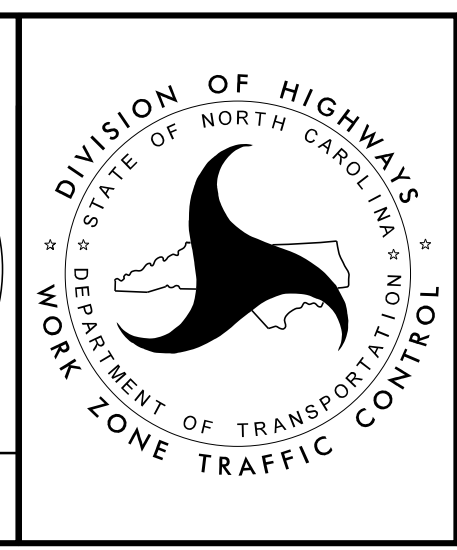



PHASE I - STEPS 2 AND 3

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-11

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

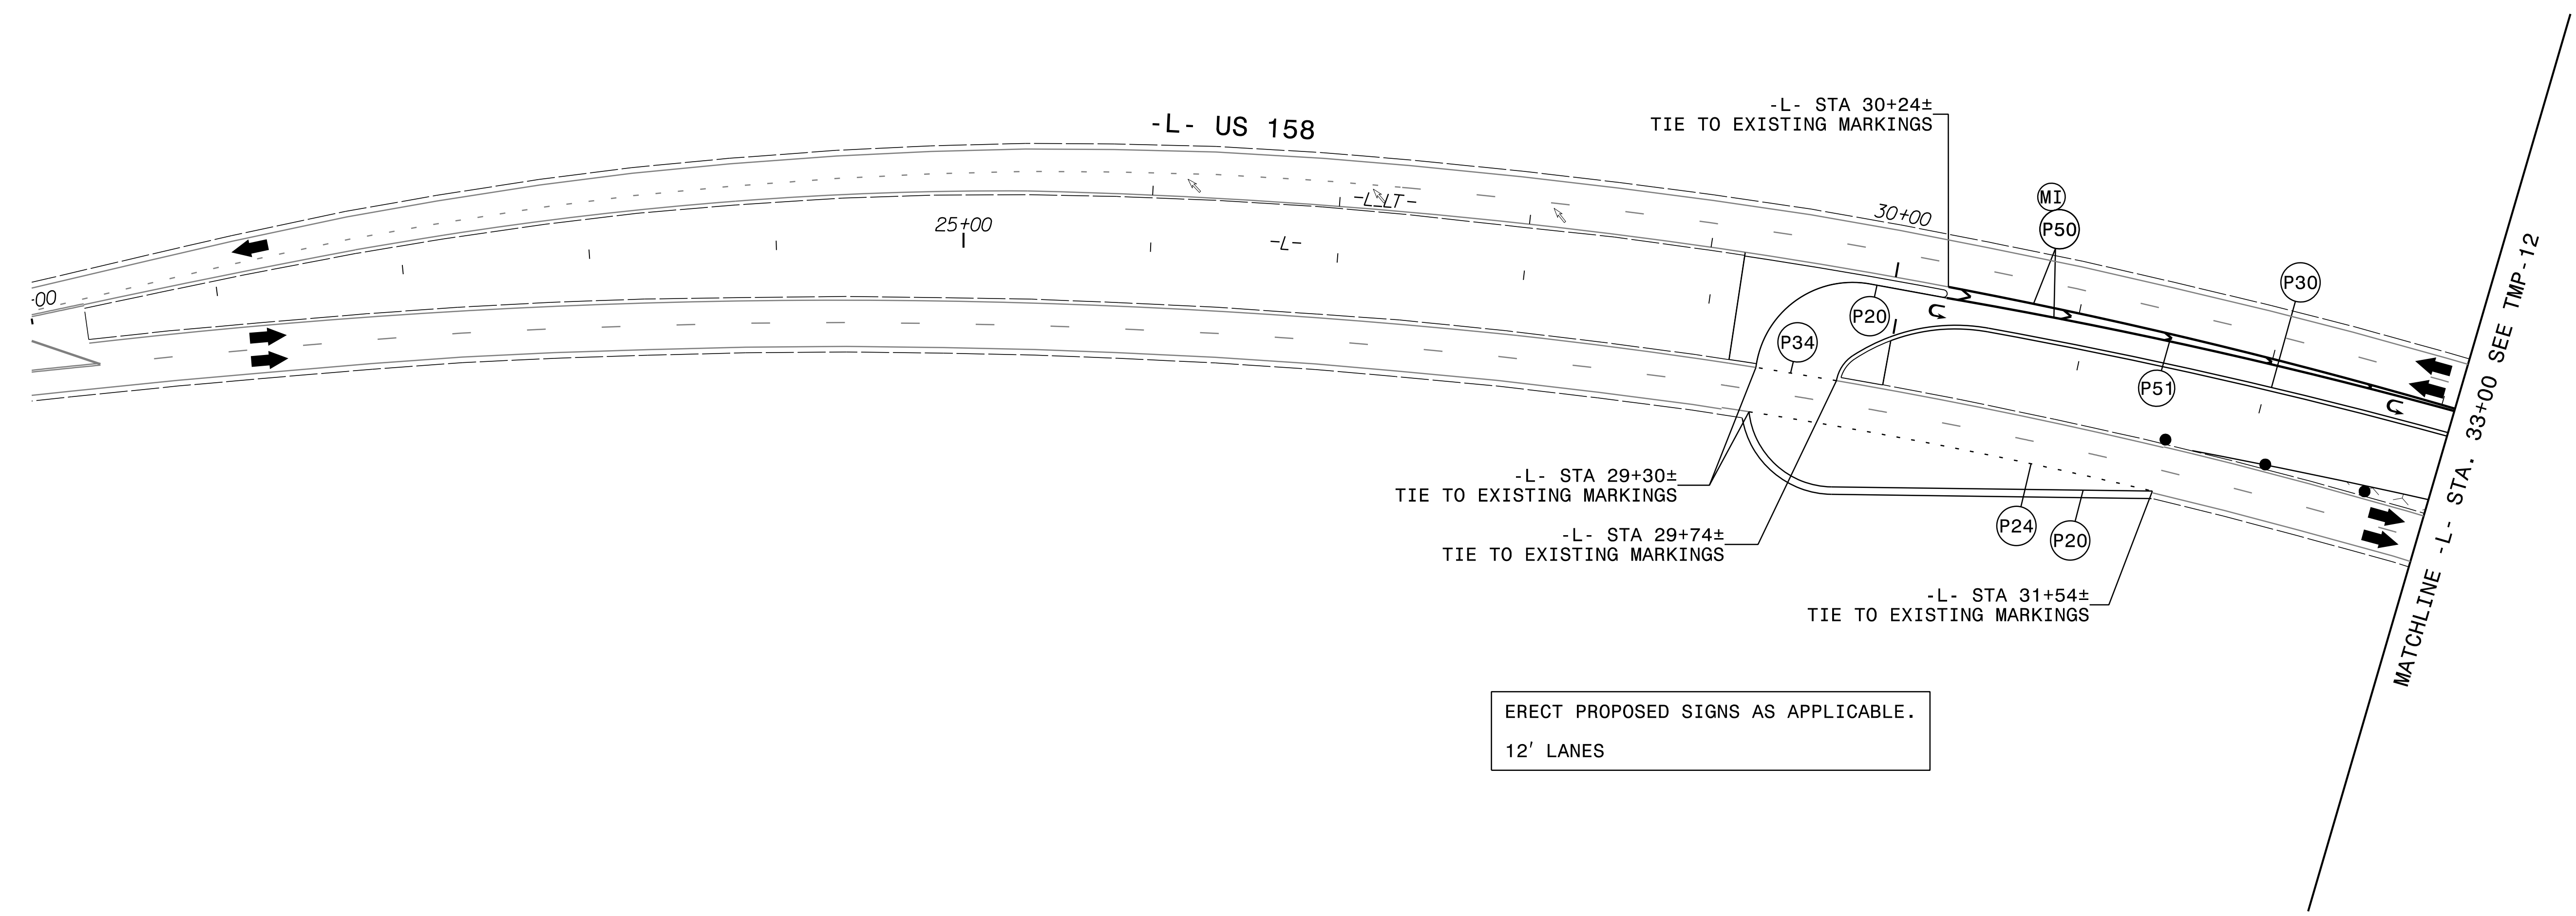

1/9/2023
 W5701B_TMP_PSHIL.dgn
 KBISBY

APPROVED: *Kevin W. Bly*
800802628912472




DATE: 1/9/2023

SEAL

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**



PHASE II - STEP 1

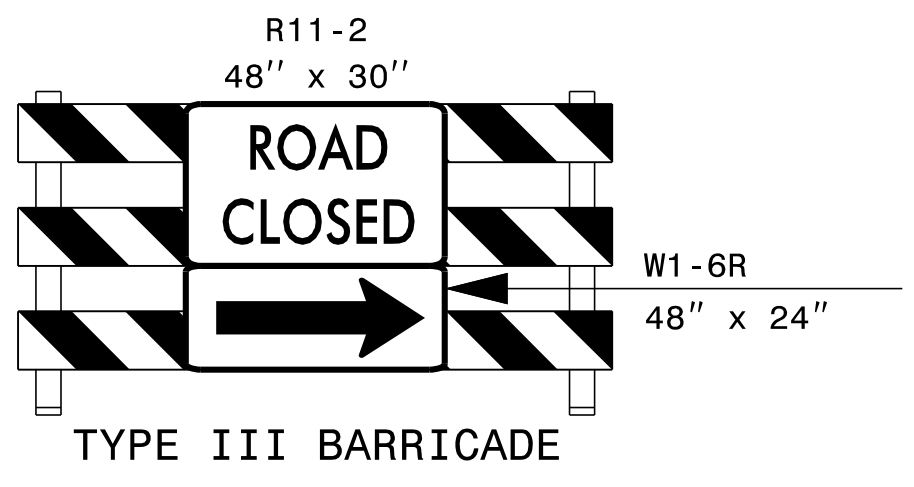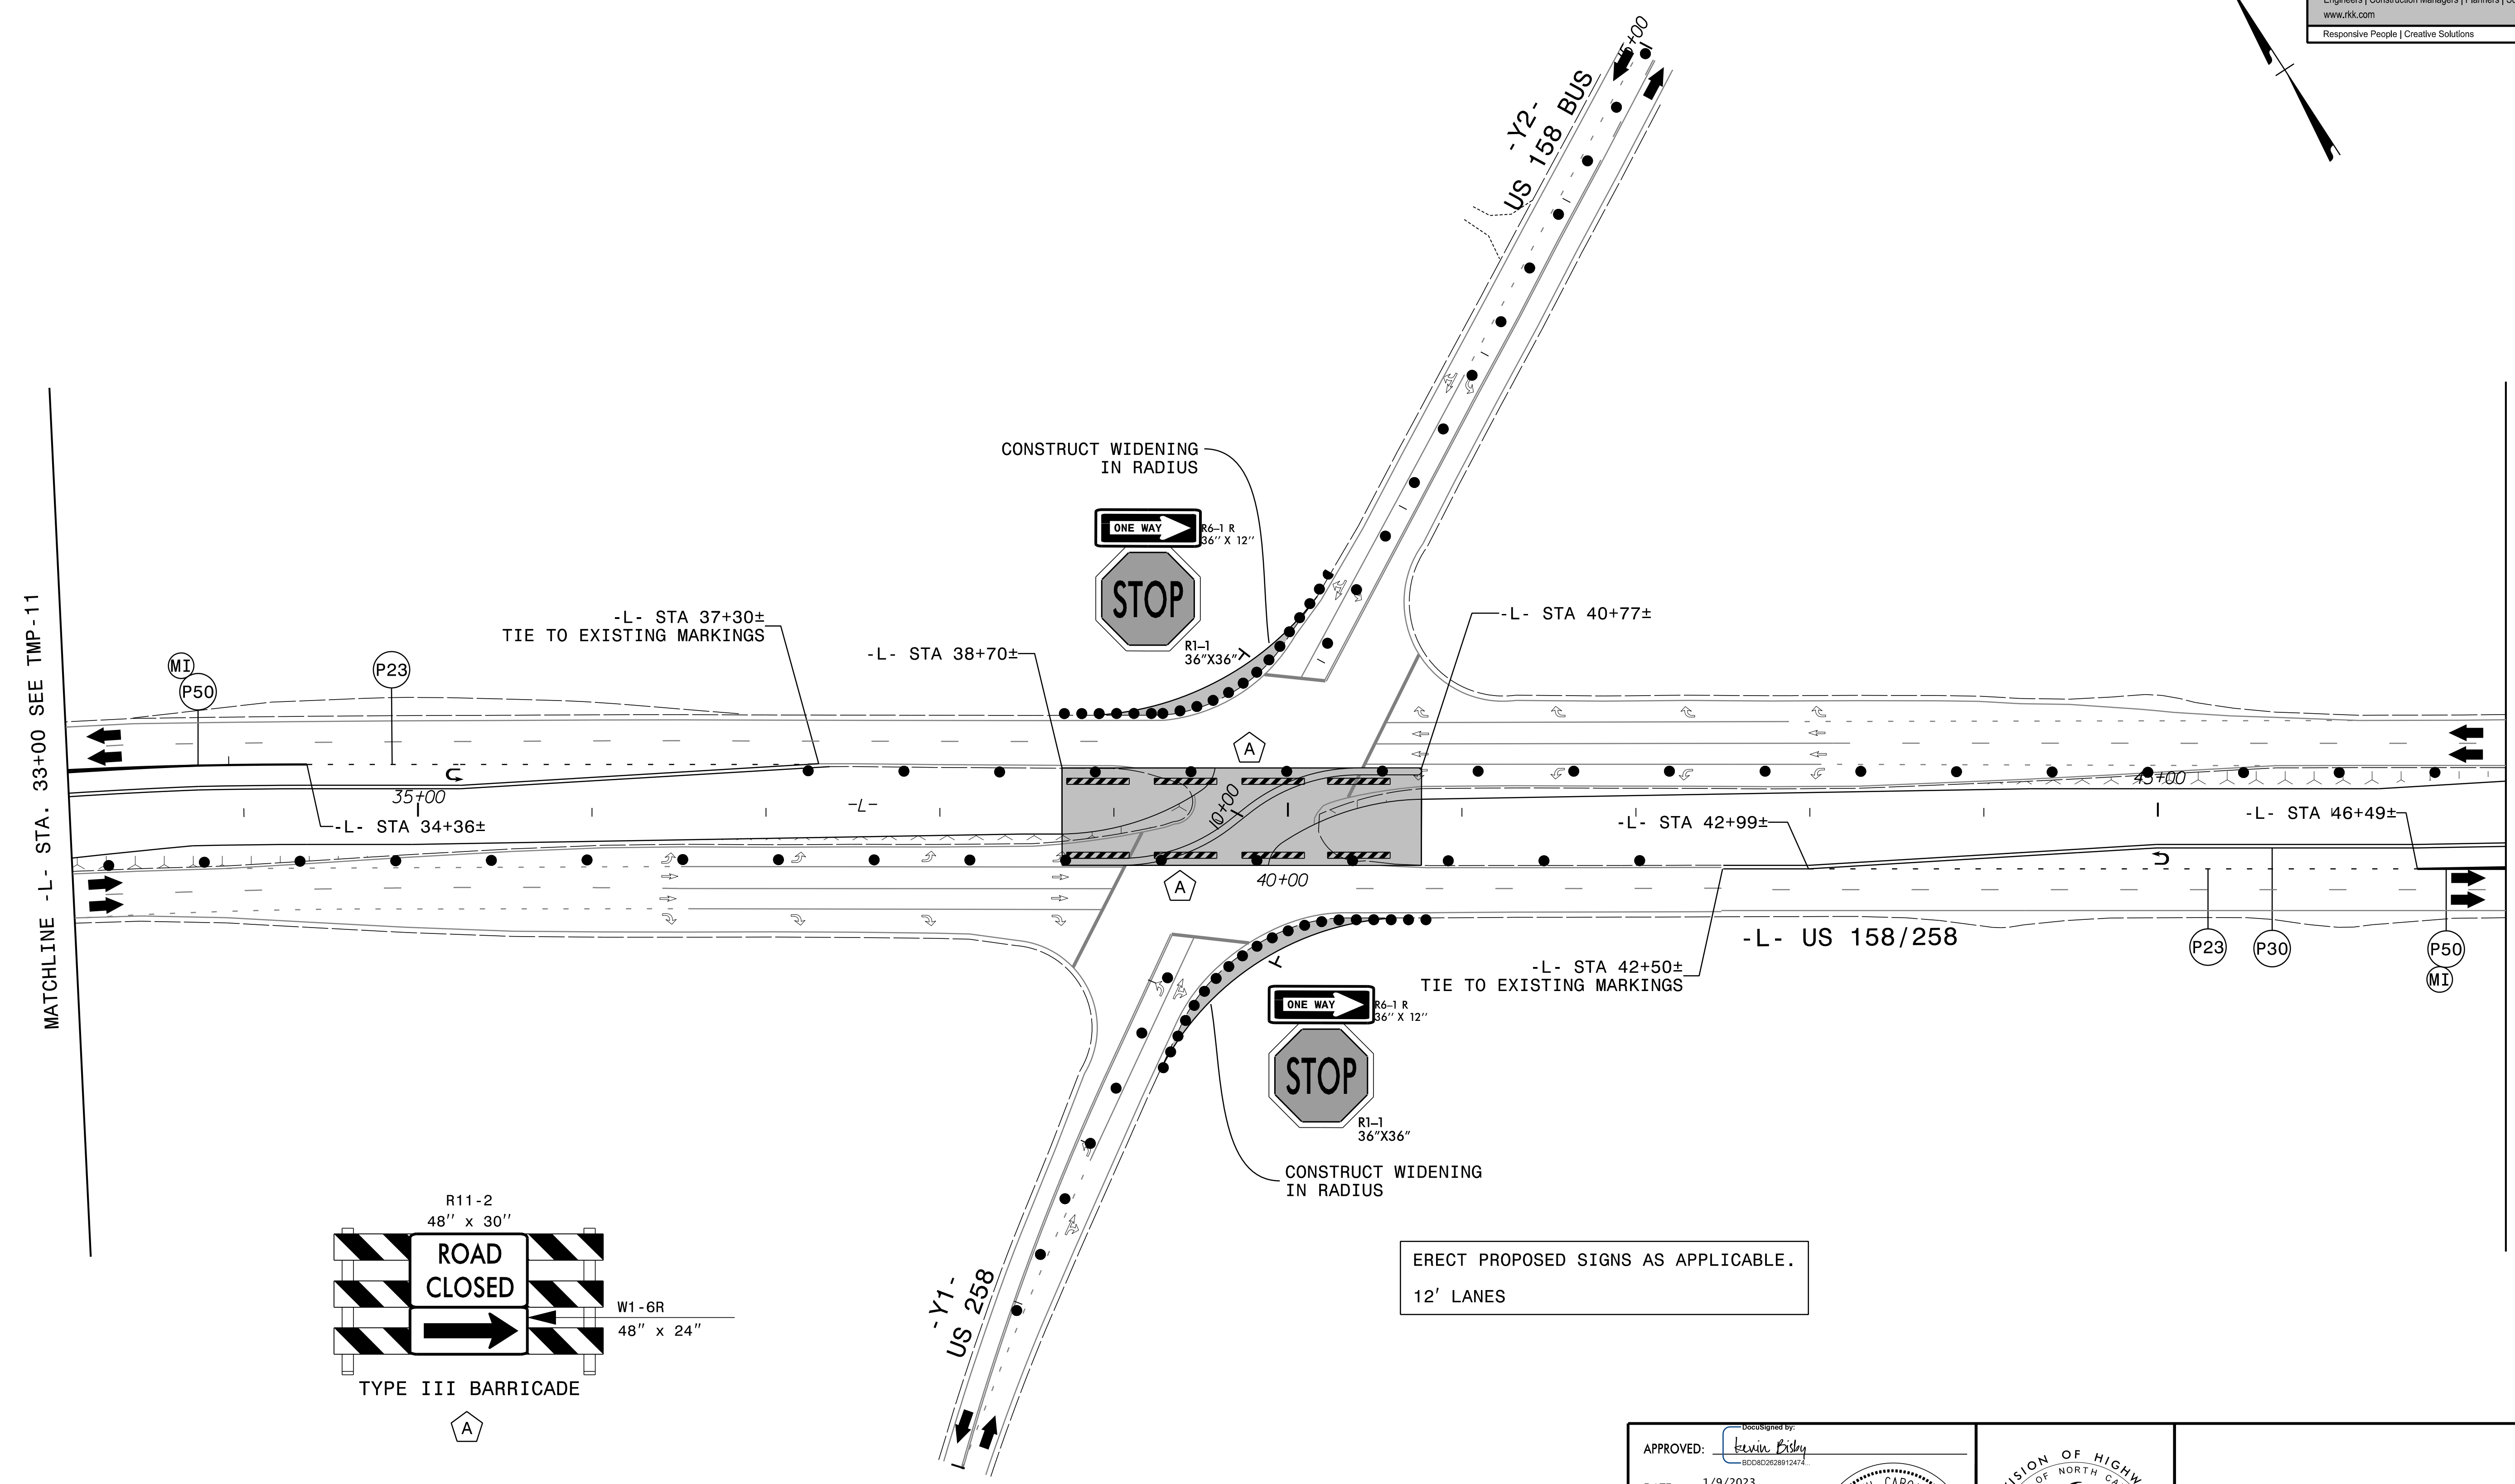

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES

1/9/2023
 W5701B-TMP_PSH12.dgn
 KB/bsb



APPROVED: *Kevin Esley*
 DATE: 1/9/2023

SEAL




PHASE II - STEPS 1 AND 2

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

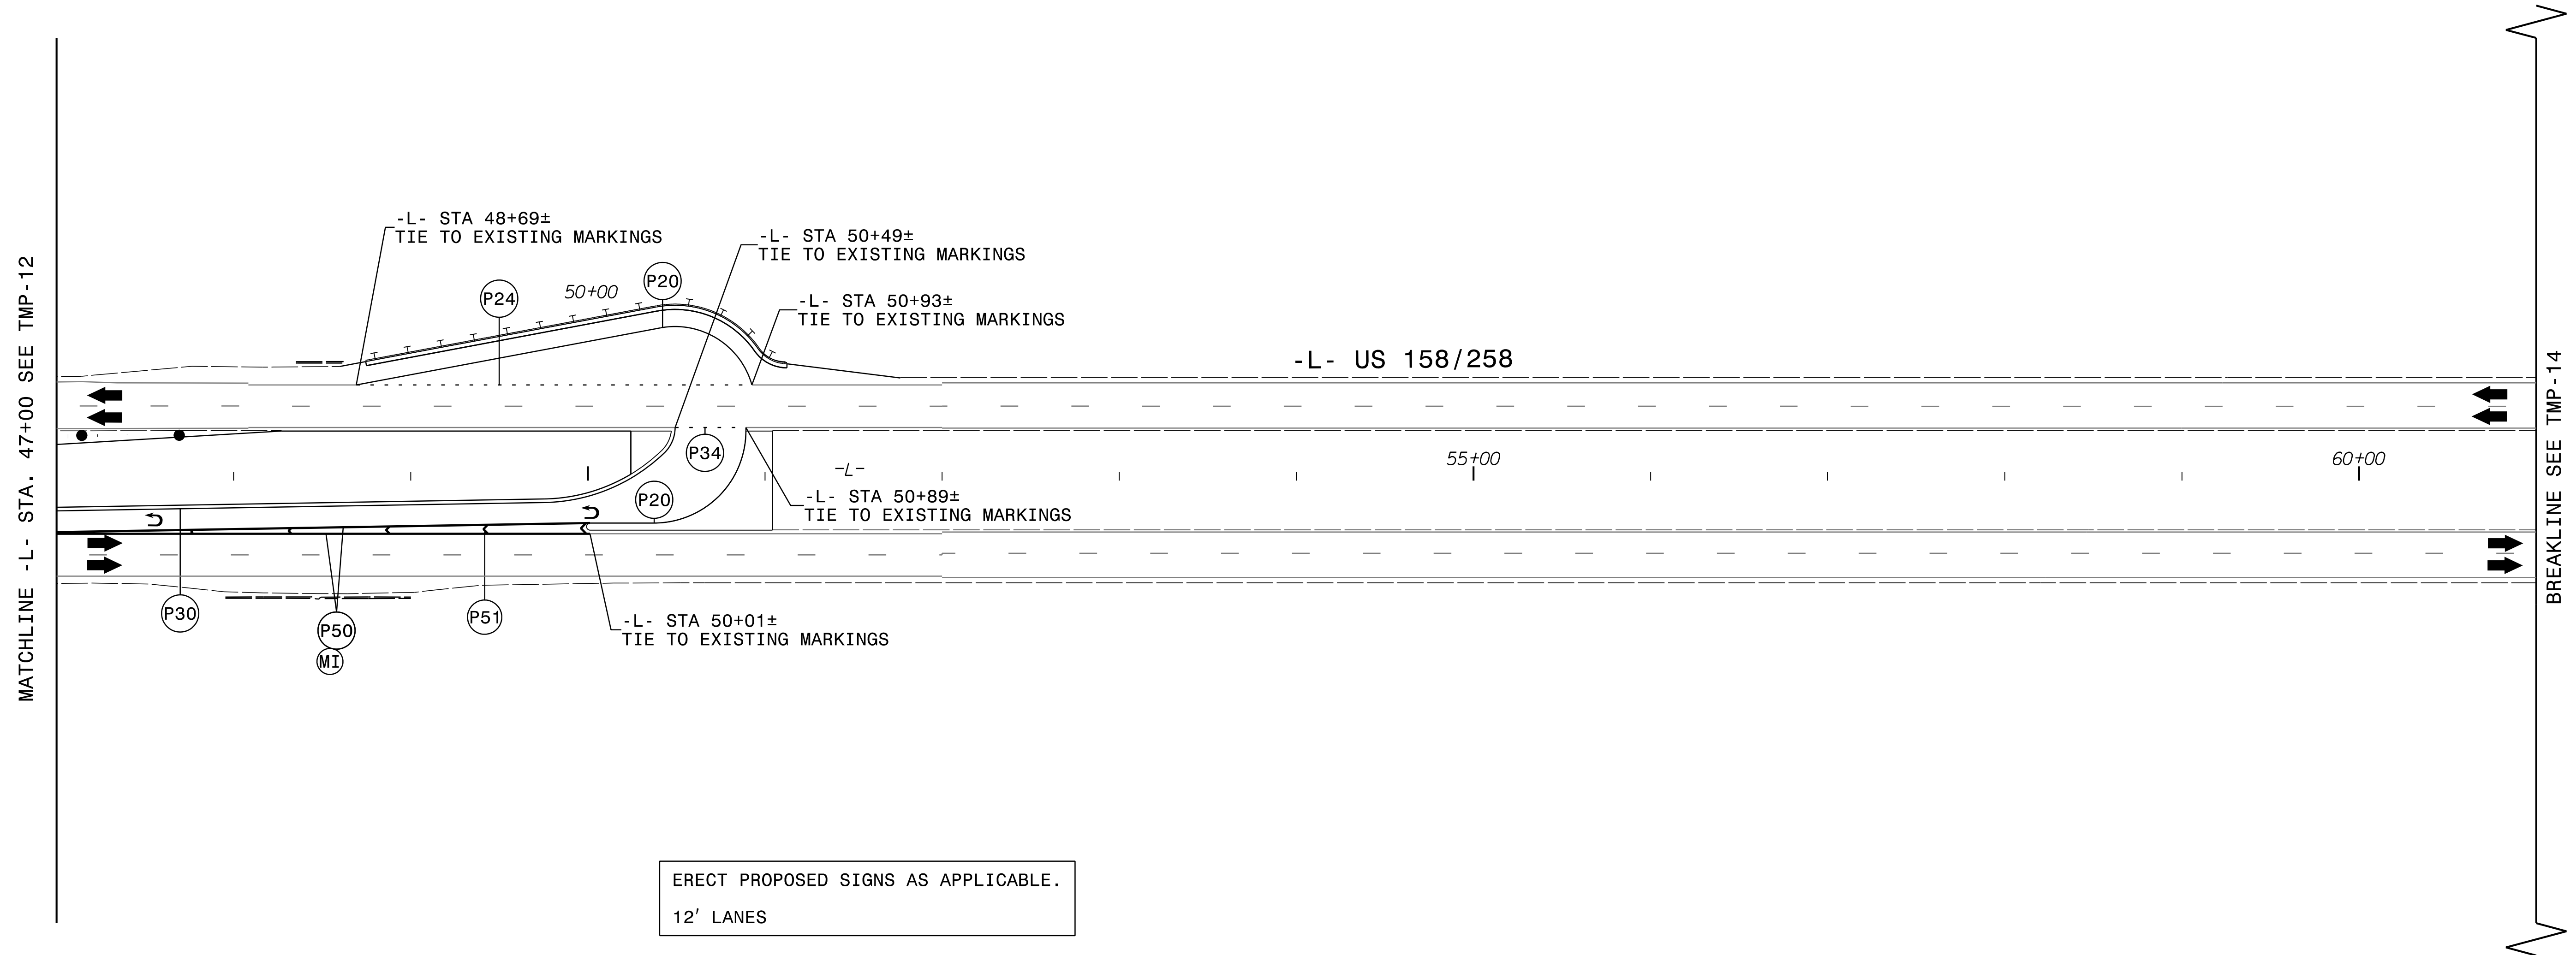



1/9/2023
 W5701B_TMP_PSH13.dgn
 KBISBY

APPROVED: 
800802628912472


DATE: 1/9/2023

SEAL

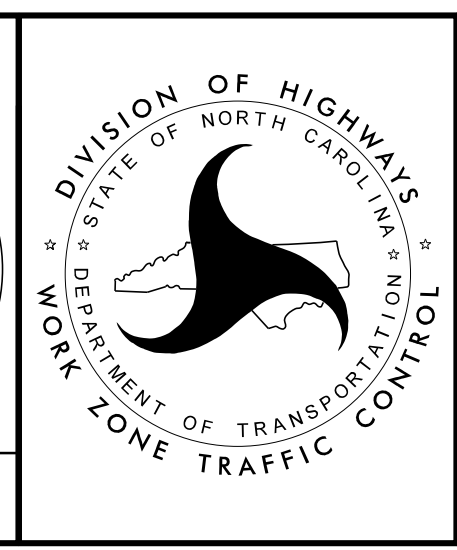PHASE II - STEP 1

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

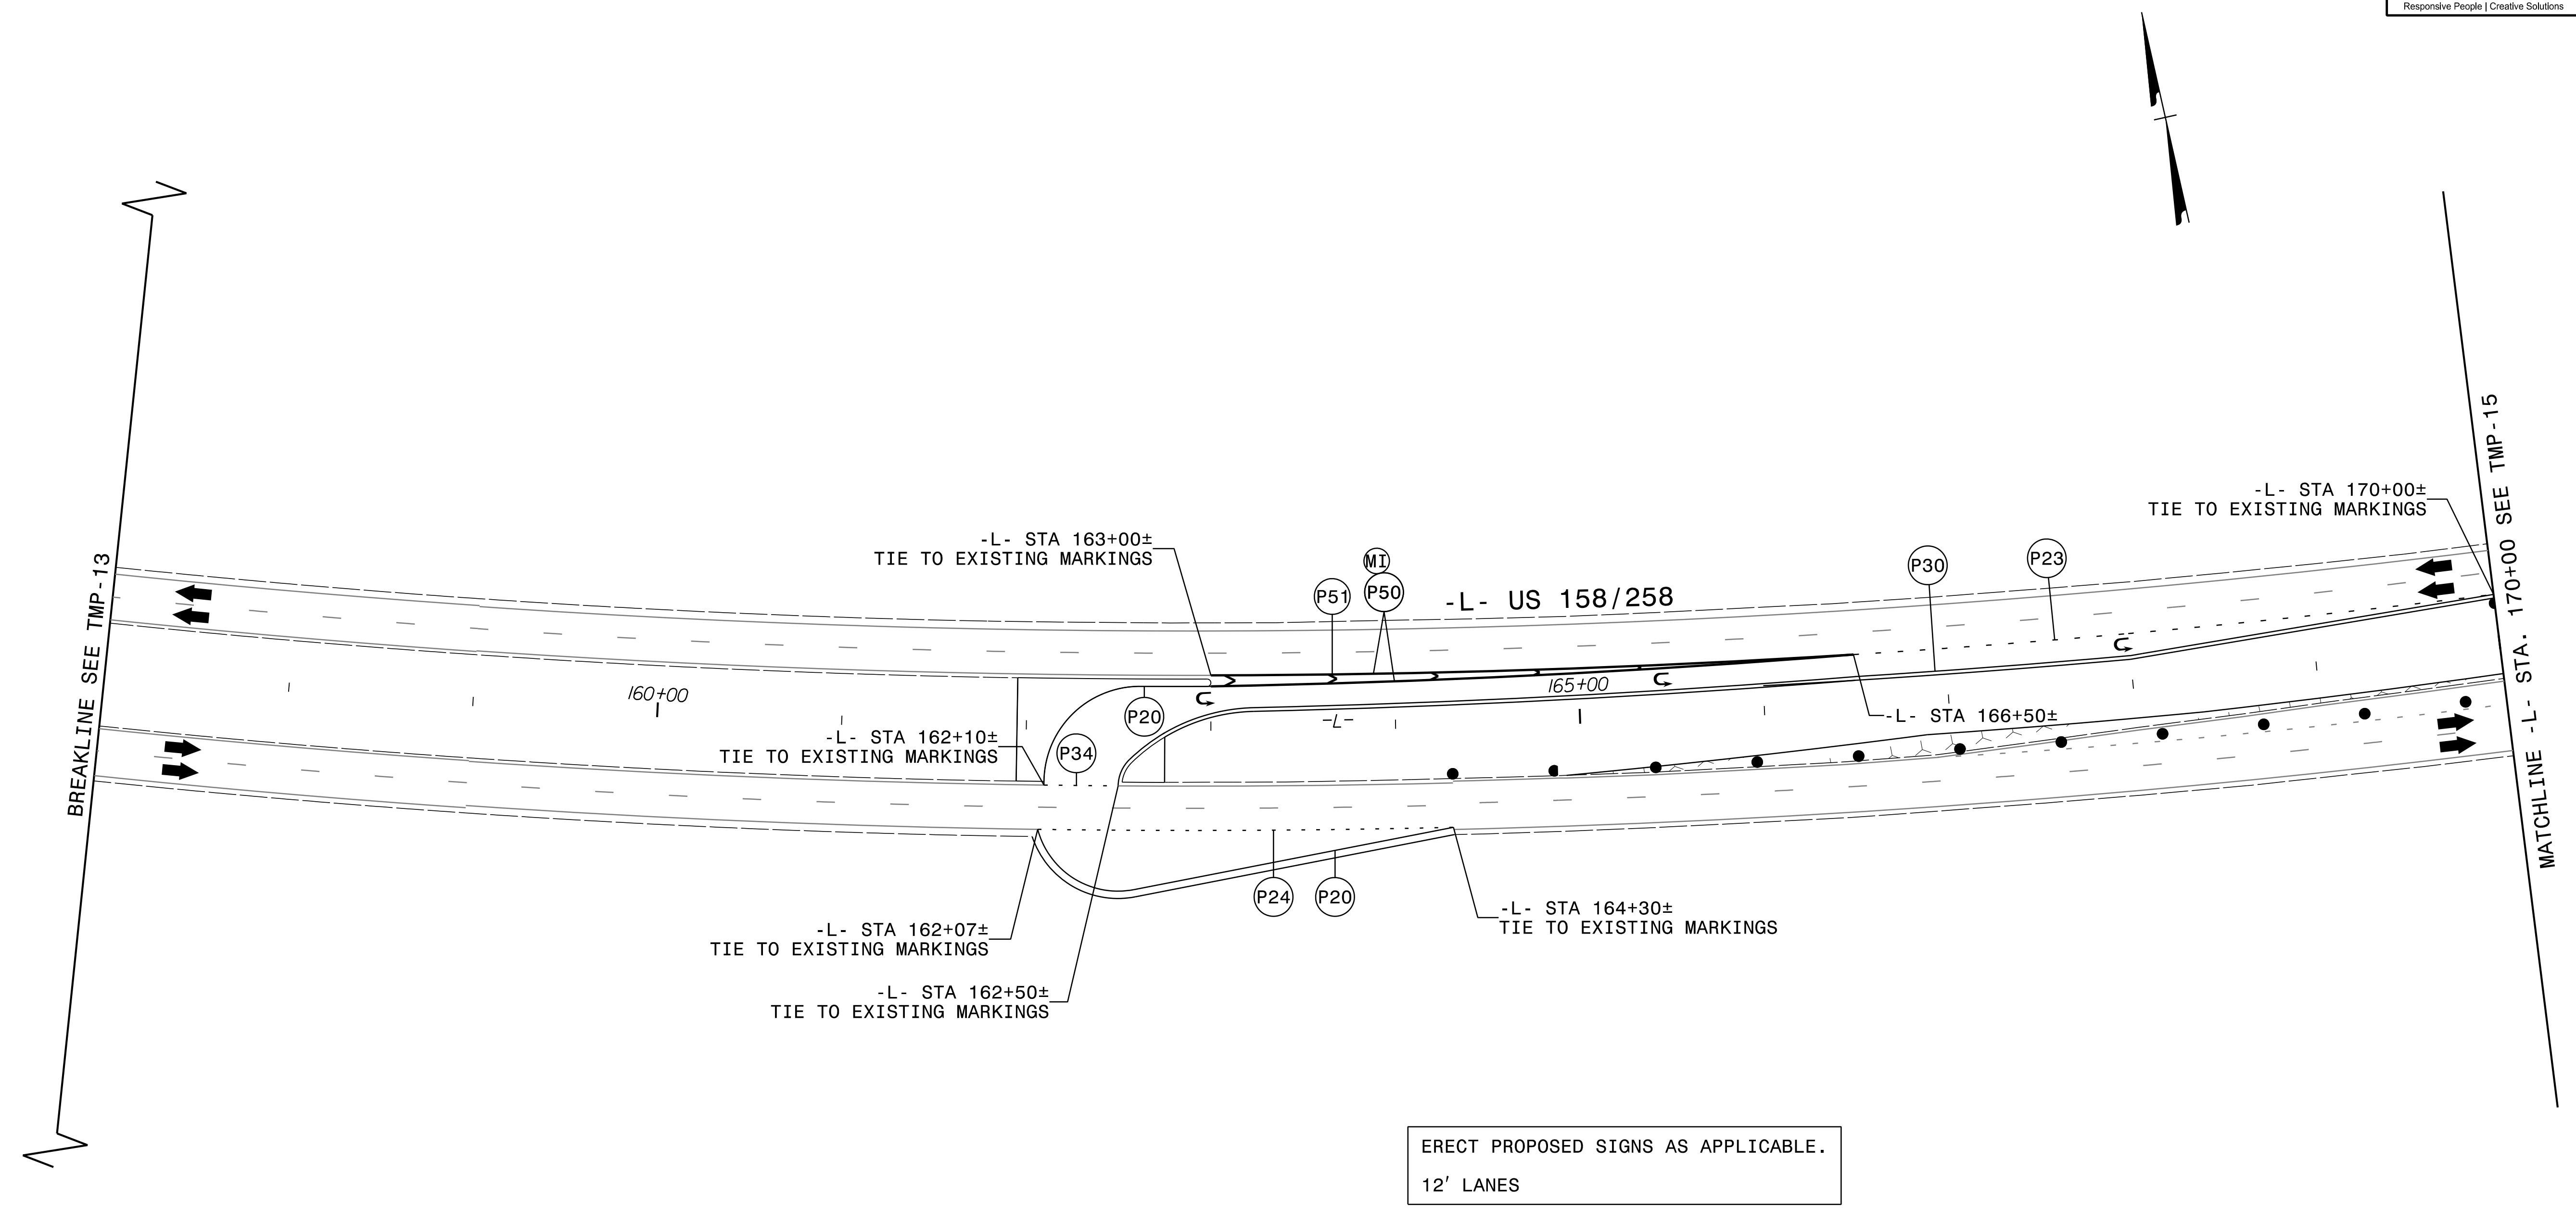

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES


1/9/2023
 W5701B-TMP_PSH14.dgn
 KB/lsby

APPROVED: *Kevin Bishy*
800802628912472


DATE: 1/9/2023

SEAL

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**



PHASE II - STEP 1

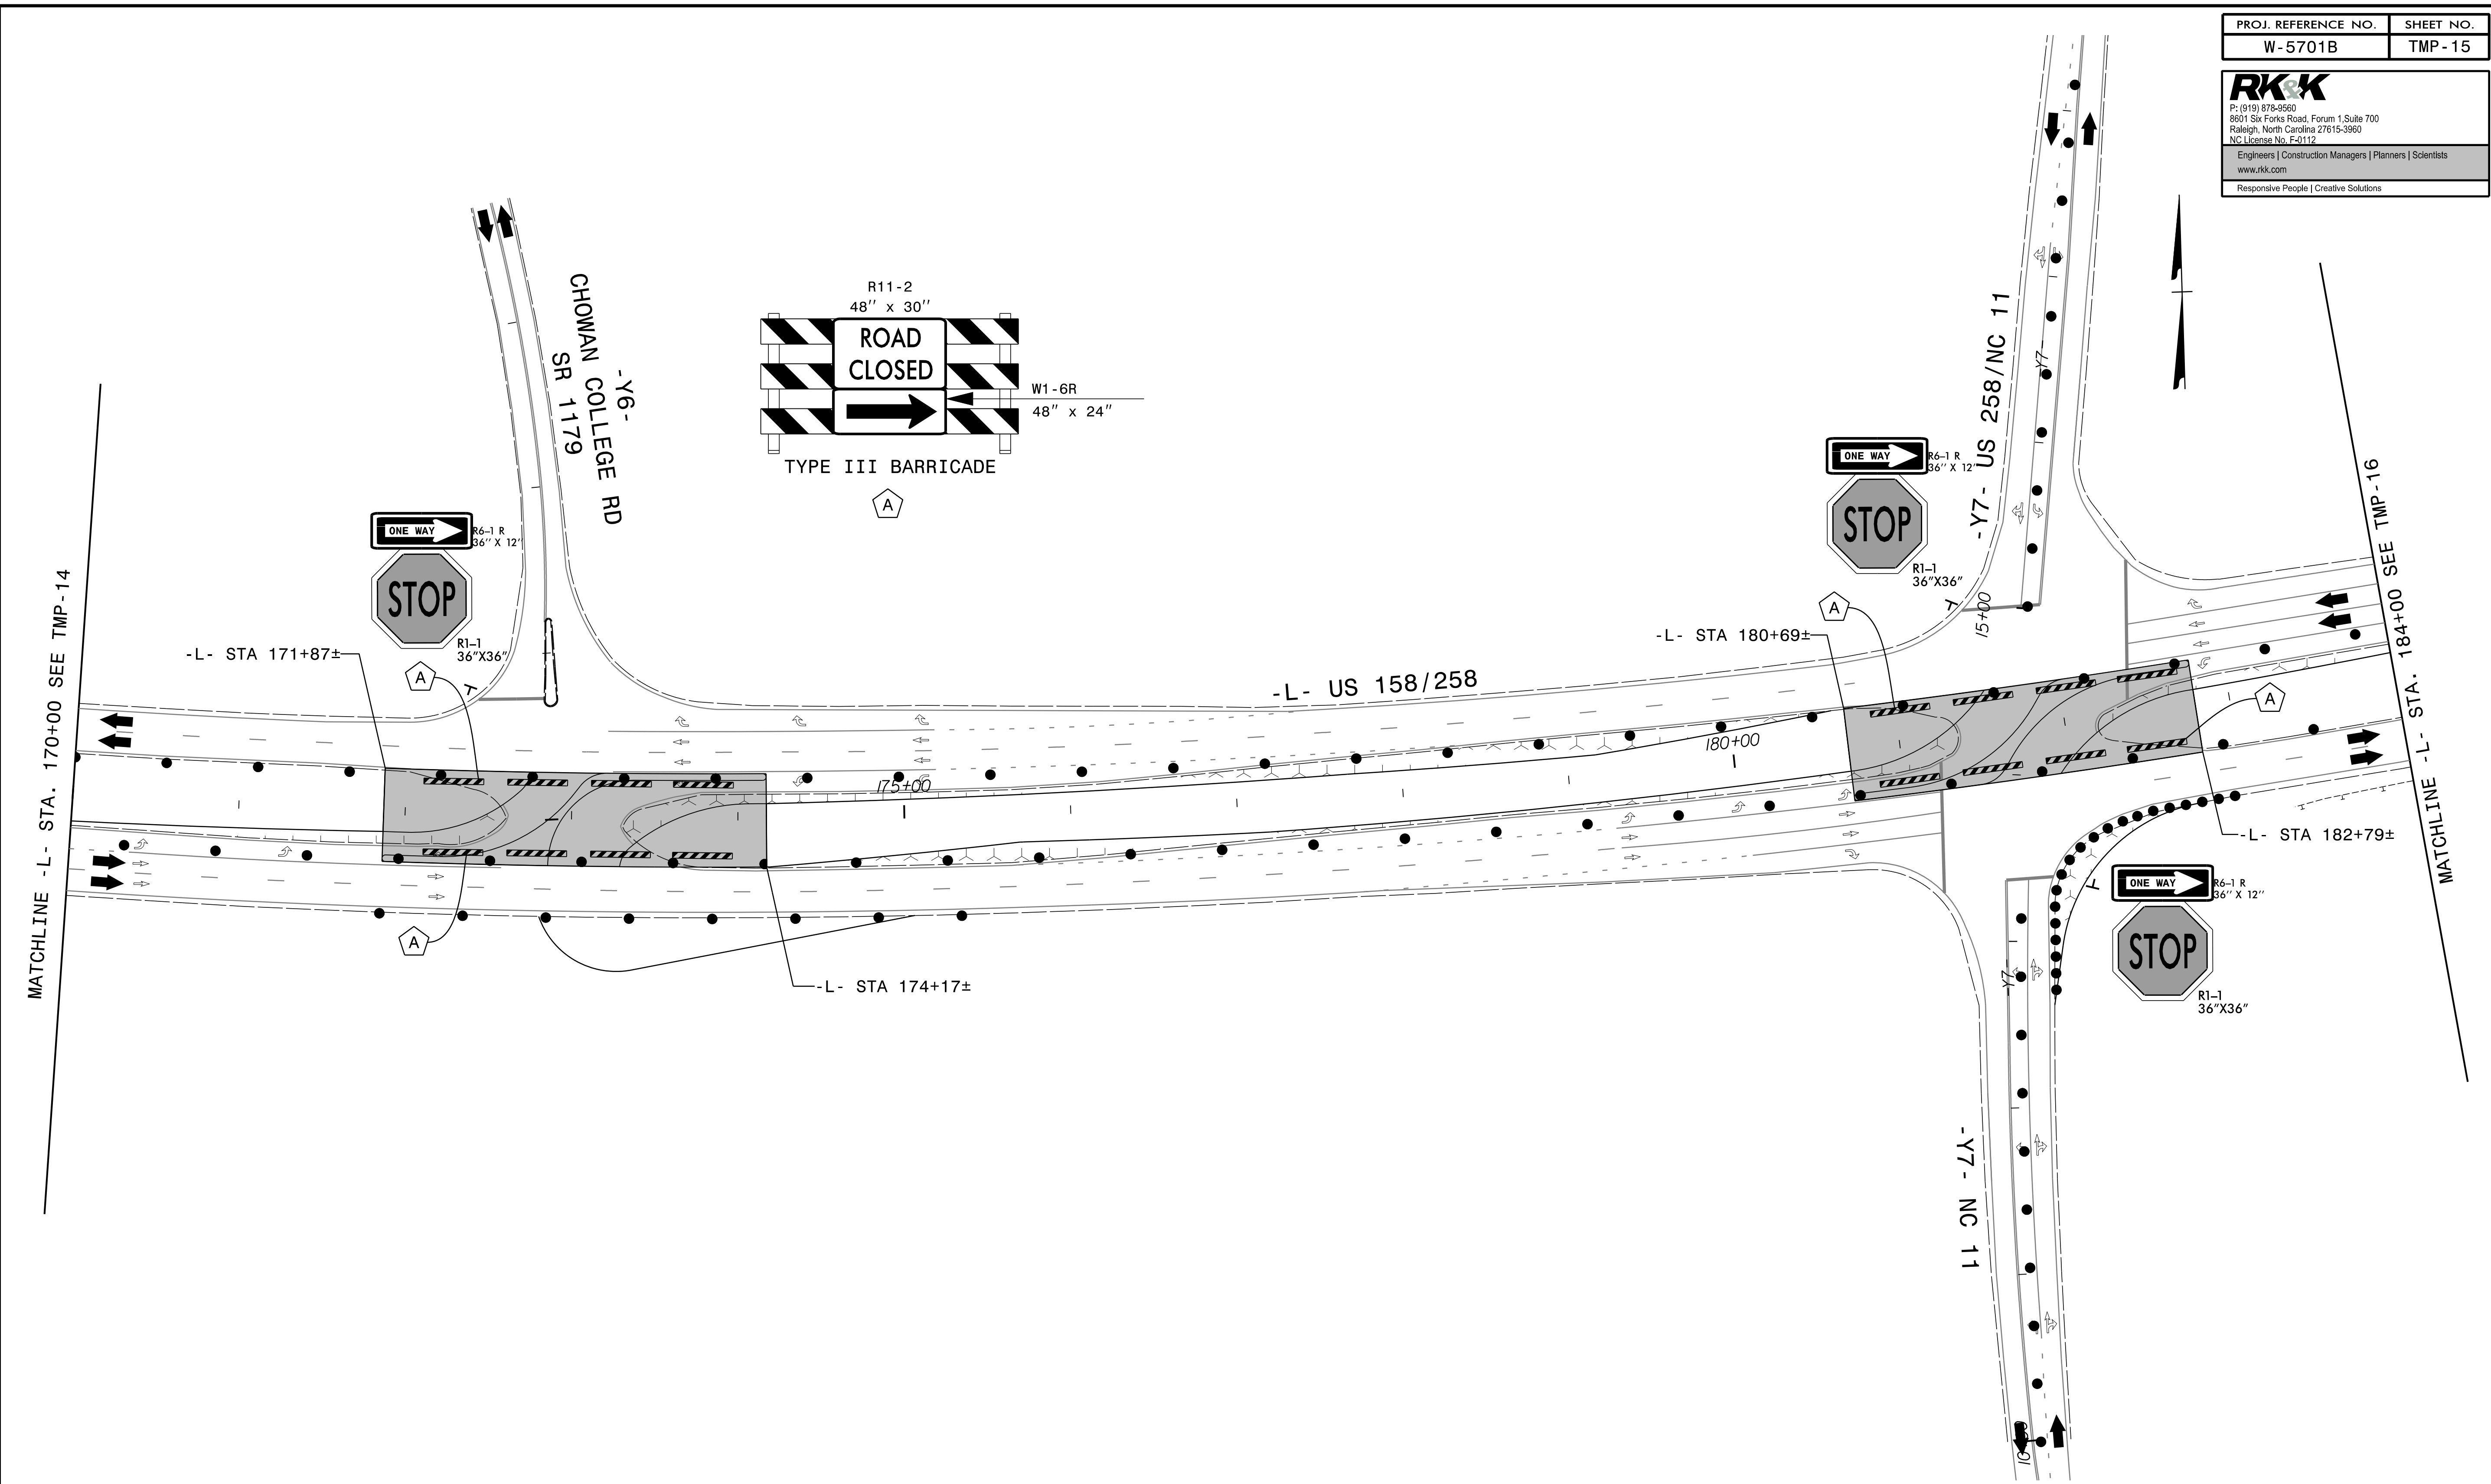


1/9/2023
 W5701B_TMP_PSH15.dgn
 KB/bsby

APPROVED: *Kevin B. Sibley*
800802628912472


DATE: 1/9/2023

SEAL

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

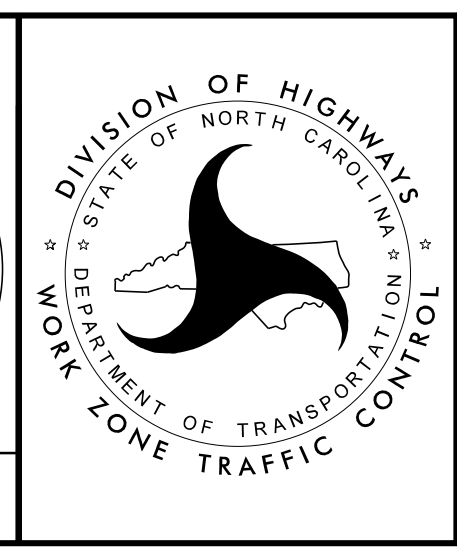

PHASE II - STEPS 1 AND 2

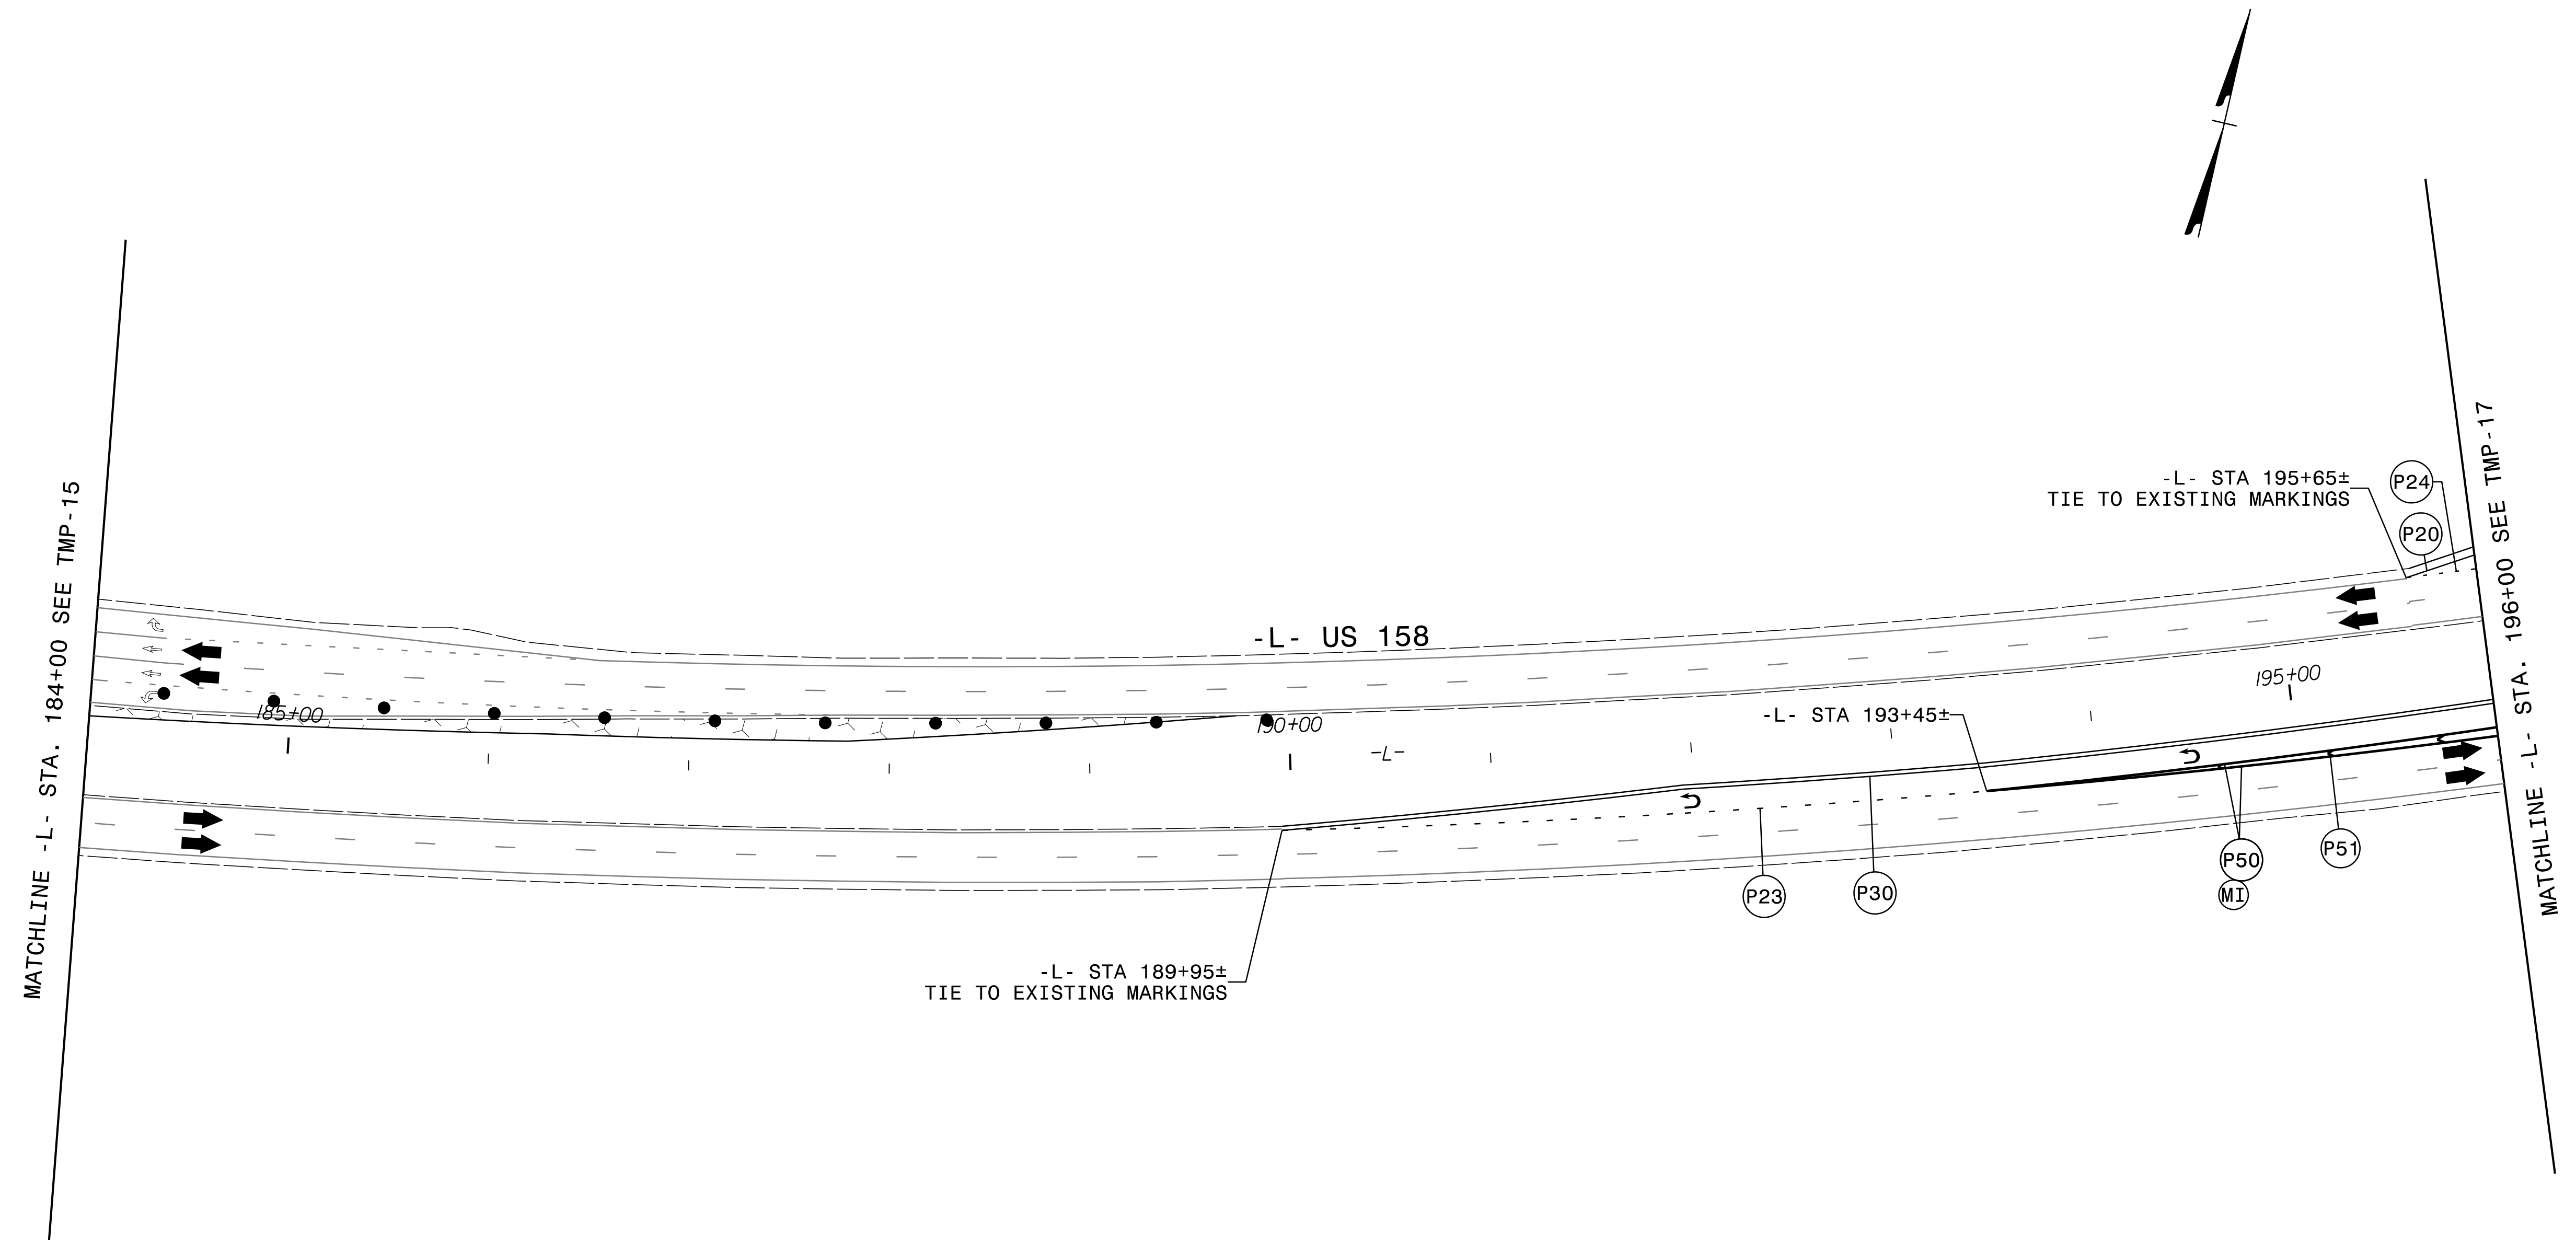

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES


1/9/2023
 W5701B_TMP_PSH16.dgn
 KB/bsby

APPROVED: *Kevin Esley*
BD0802628912472

DATE: 1/9/2023

SEAL



**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

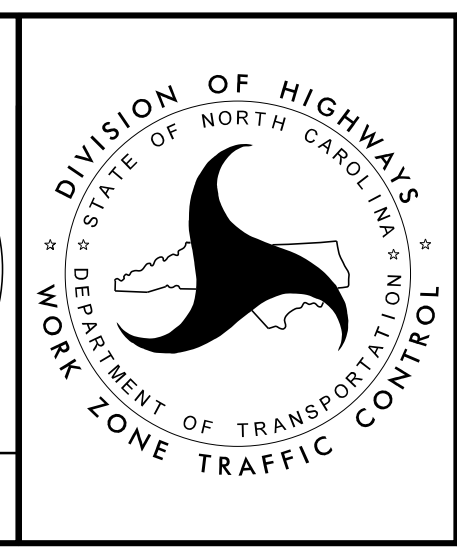




PHASE II - STEP 1

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-17

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

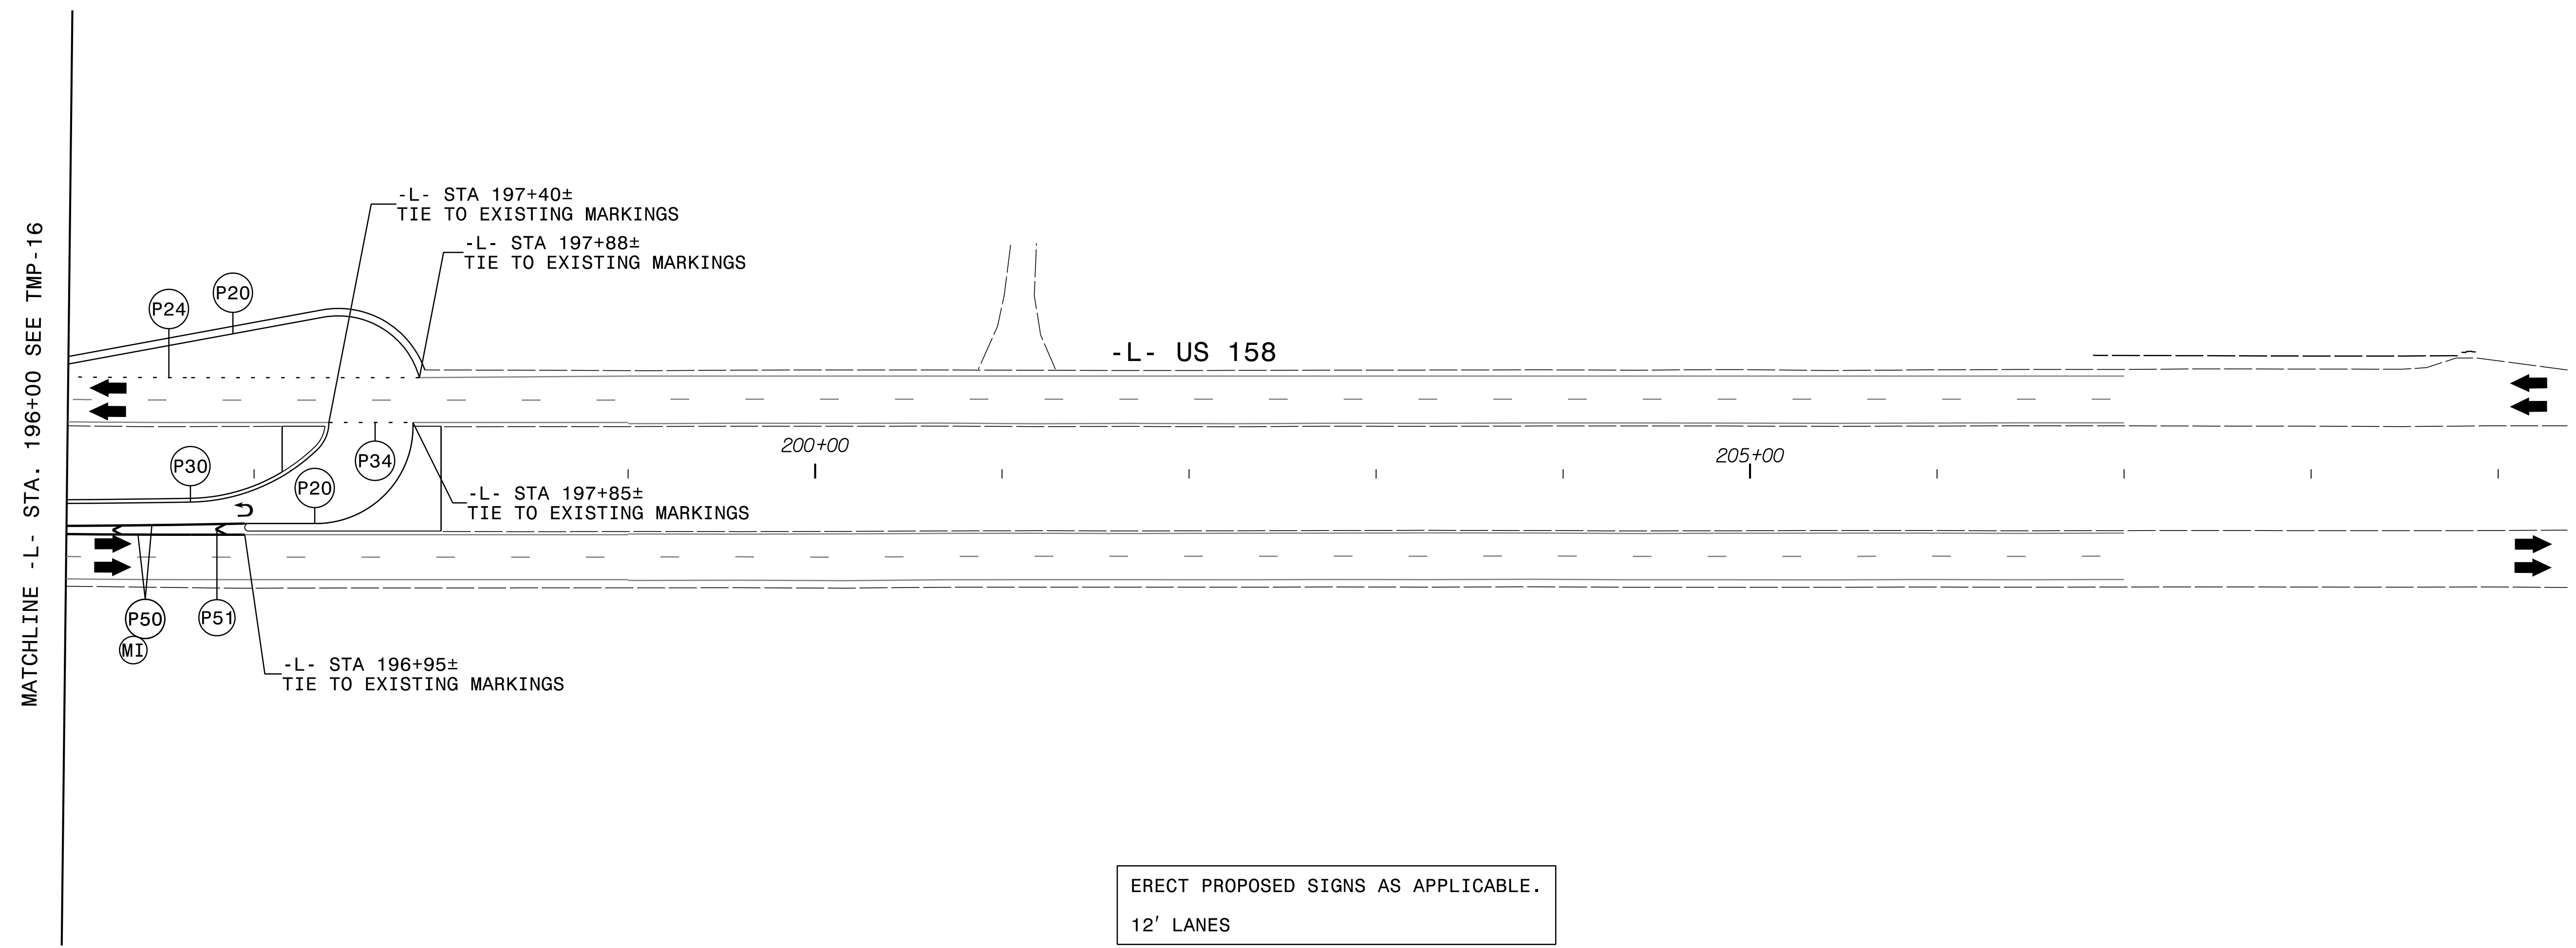



1/9/2023
 W5701B-TMP_PSH17.dgn
 KBISBY

APPROVED:  DATE: 1/9/2023 SEAL 		<p>PHASE II - STEP 1</p>
<p>DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED</p>		

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-18

RK&K
P: (919) 878-9560
8601 Six Forks Road, Forum 1, Suite 700
Raleigh, North Carolina 27615-3960
NC License No. F-0112
Engineers | Construction Managers | Planners | Scientists
www.rkk.com
Responsive People | Creative Solutions

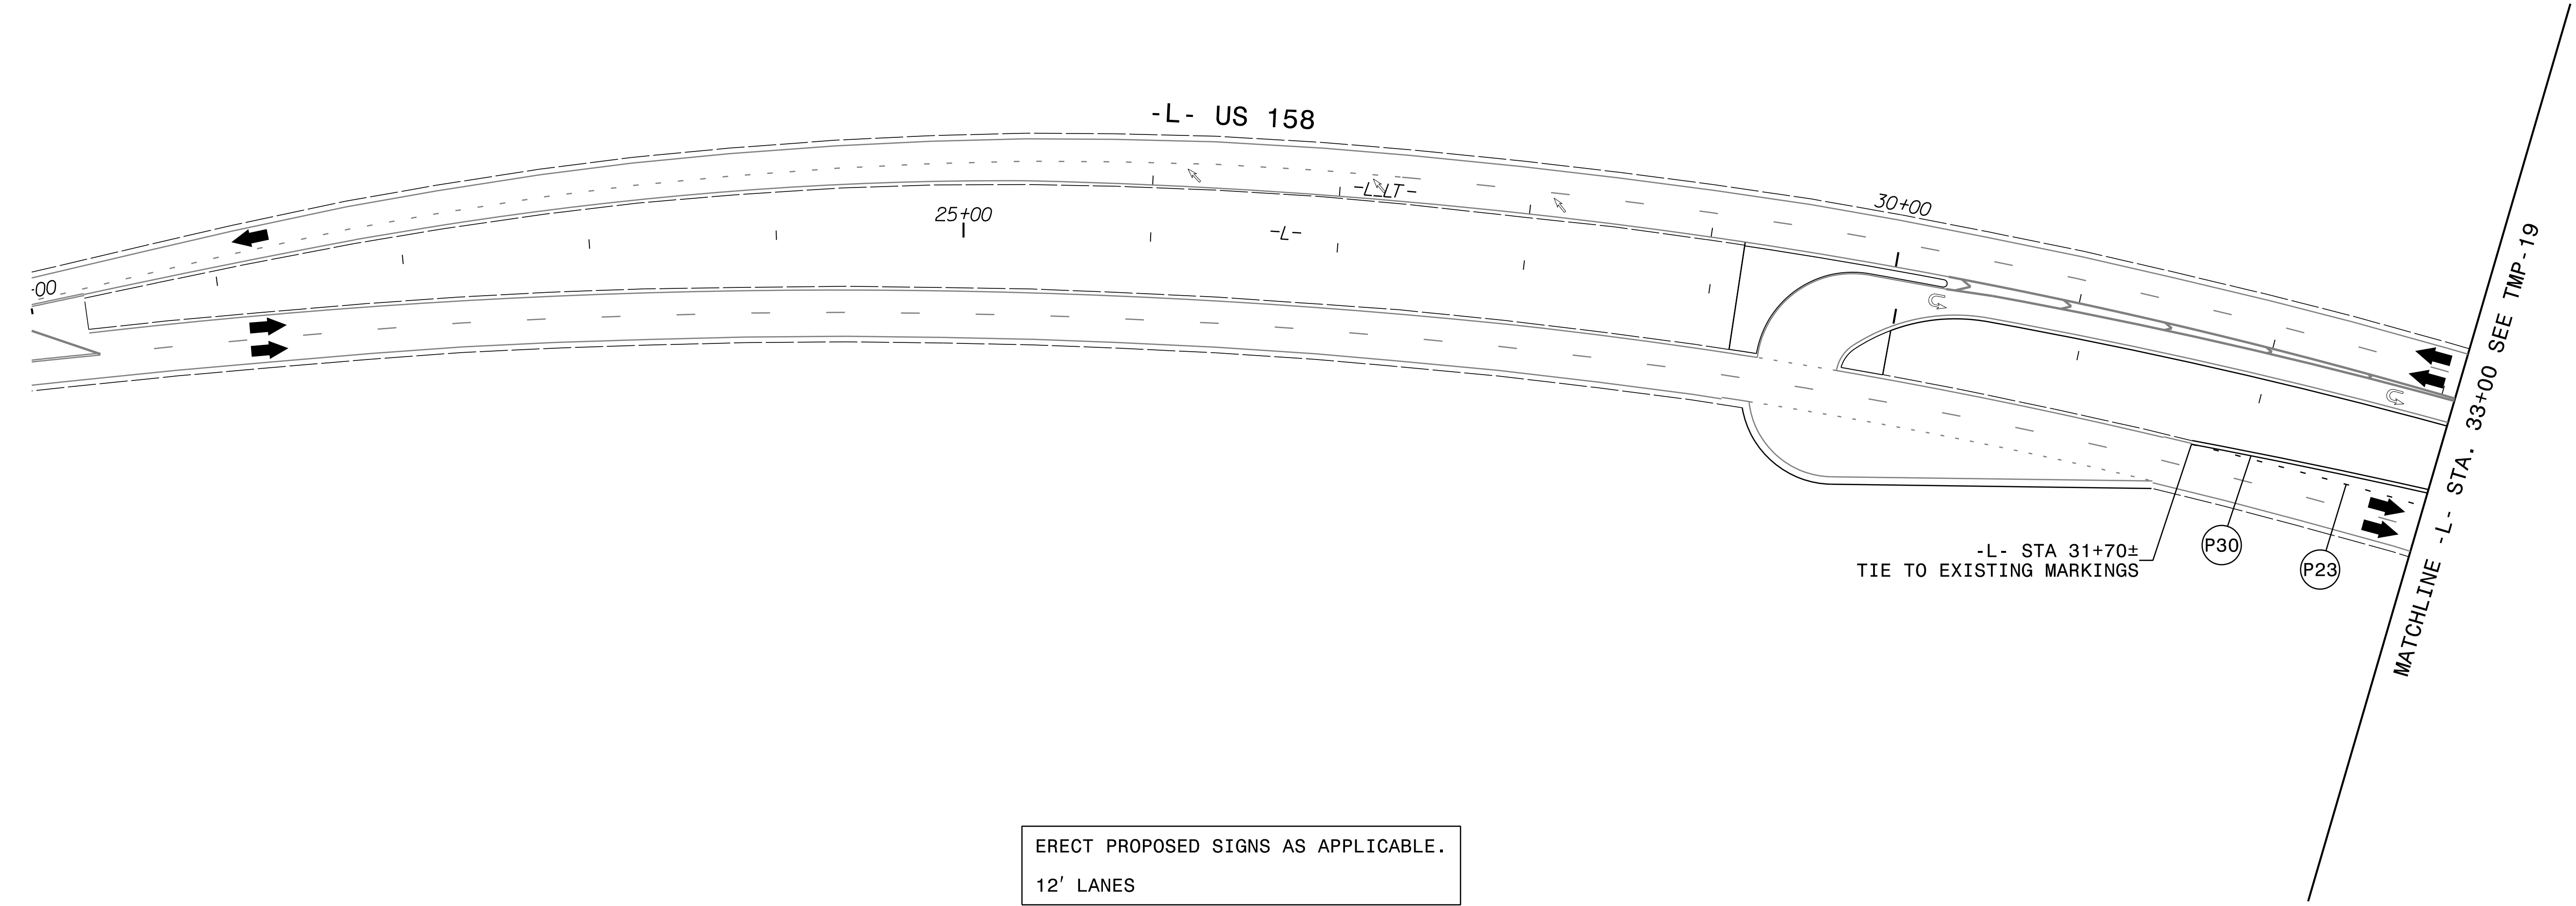

ERECT PROPOSED SIGNS AS APPLICABLE.
12' LANES

1/9/2023
W5701B-TMP_PSH18.dgn
KBISBY

APPROVED: *Kevin Bishy*
BDO0802628912472


DATE: 1/9/2023

SEAL

**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**



PHASE II - STEP 3

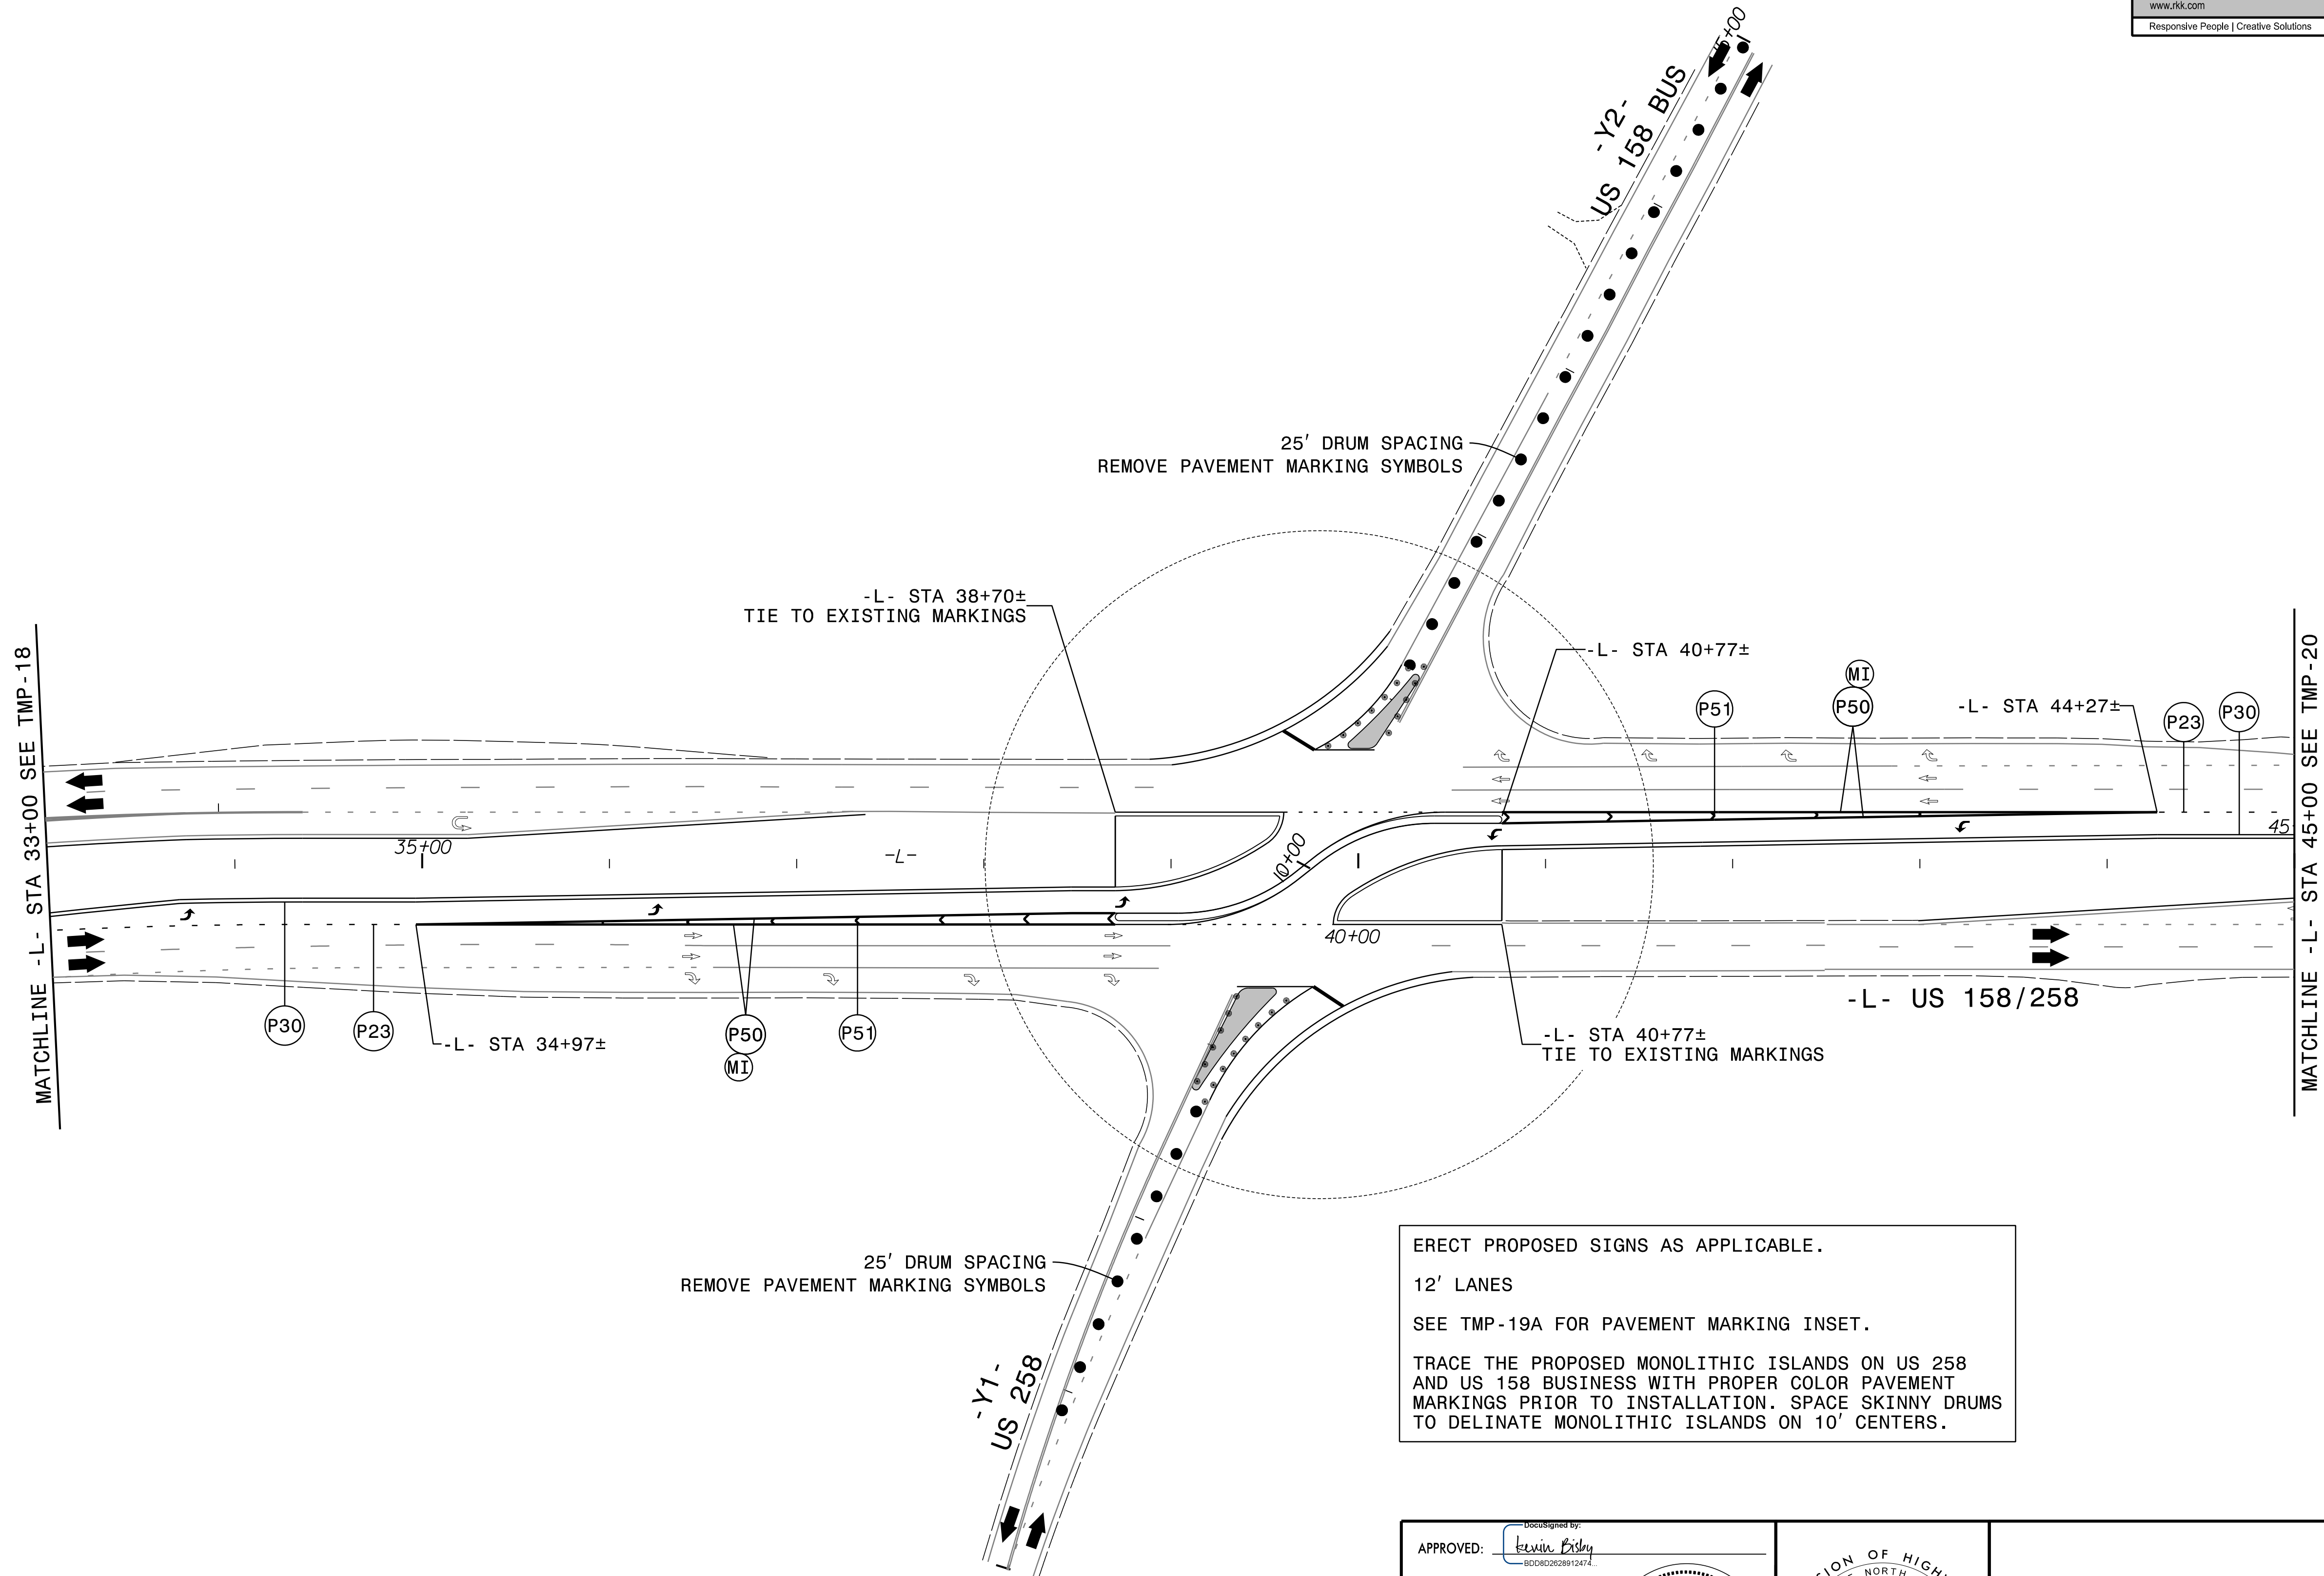

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES
 SEE TMP-19A FOR PAVEMENT MARKING INSET.
 TRACE THE PROPOSED MONOLITHIC ISLANDS ON US 258 AND US 158 BUSINESS WITH PROPER COLOR PAVEMENT MARKINGS PRIOR TO INSTALLATION. SPACE SKINNY DRUMS TO DELINEATE MONOLITHIC ISLANDS ON 10' CENTERS.


1/9/2023
 W5701B-TMP_PSH19.dgn
 KB/sby

APPROVED: *Kevin Esby*
 DATE: 1/9/2023
 SEAL

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**



PHASE II - STEPS 3 AND 4

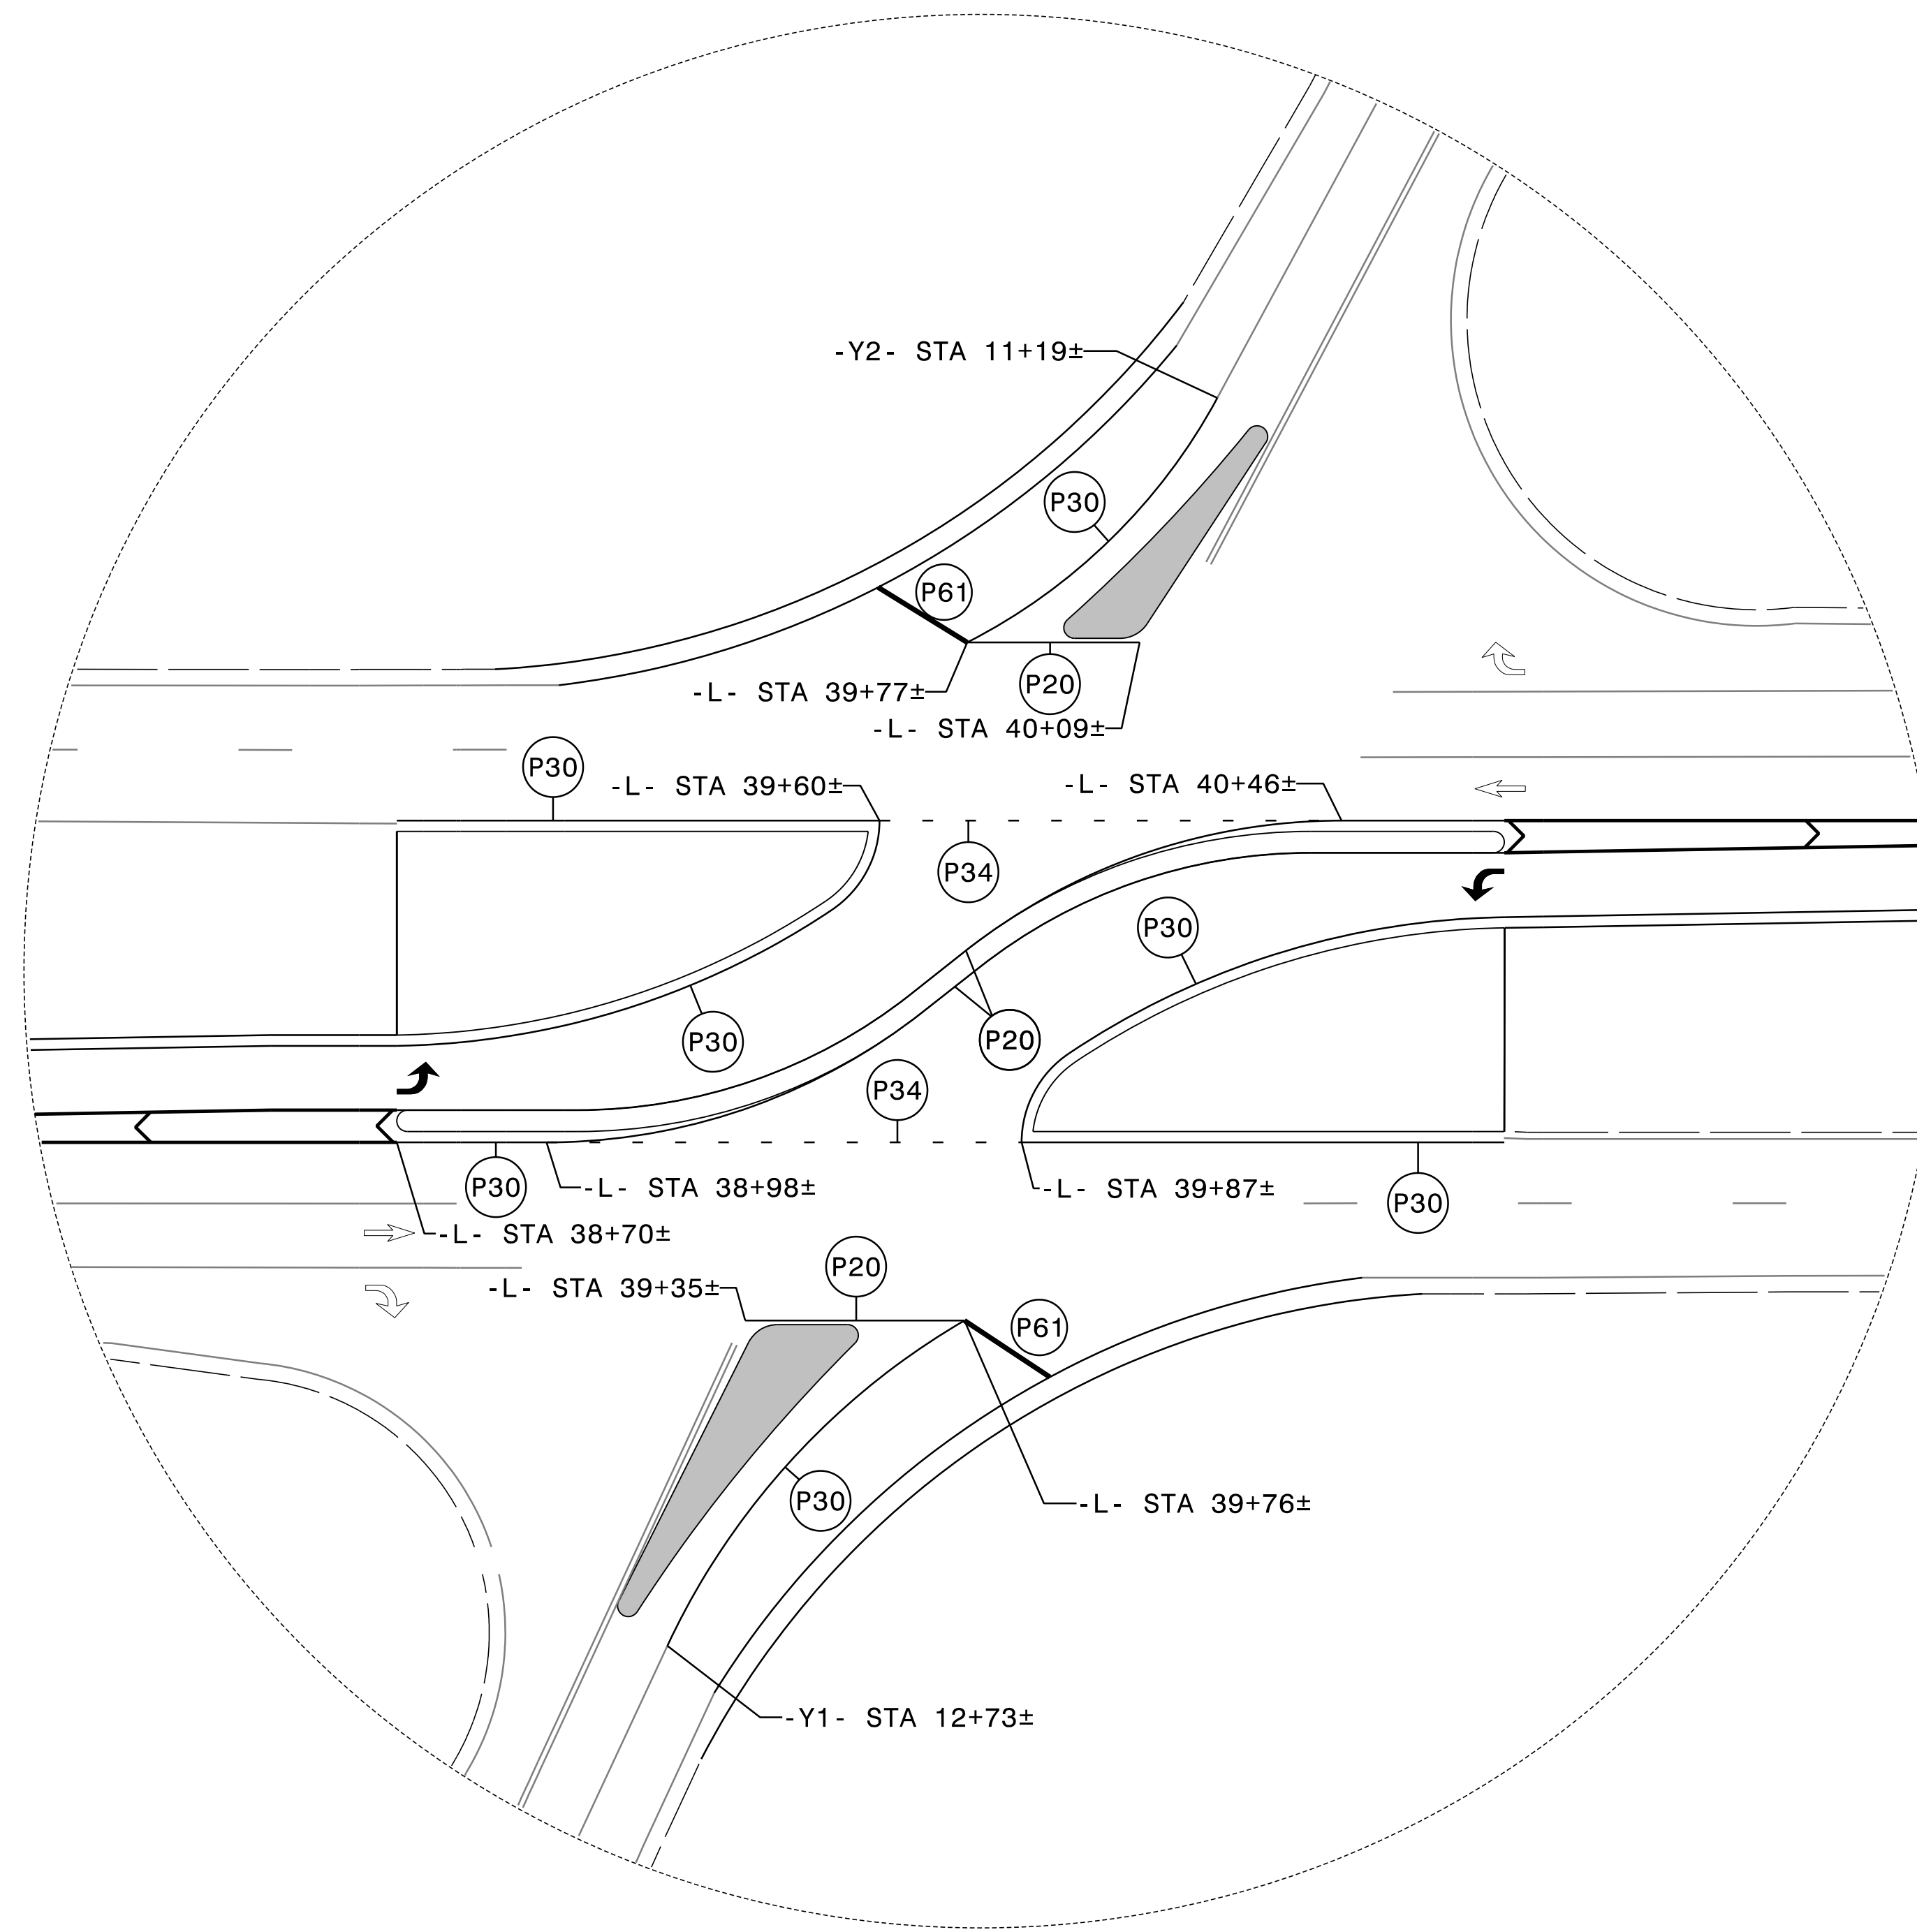


1/9/2023
 W5701B_TMP_PSH19A.dgn
 KBISBY

APPROVED: *Kevin Bisy*
800802628912472

DATE: 1/9/2023

SEAL


**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

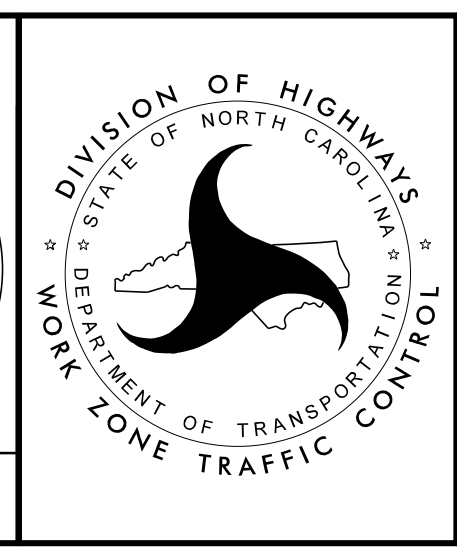

**PHASE II - STEP 3
 PAVEMENT MARKINGS**

PROJ. REFERENCE NO.	SHEET NO.
W-5701B	TMP-20

RK&K
 P: (919) 878-9560
 8601 Six Forks Road, Forum 1, Suite 700
 Raleigh, North Carolina 27615-3960
 NC License No. F-0112
 Engineers | Construction Managers | Planners | Scientists
 www.rkk.com
 Responsive People | Creative Solutions

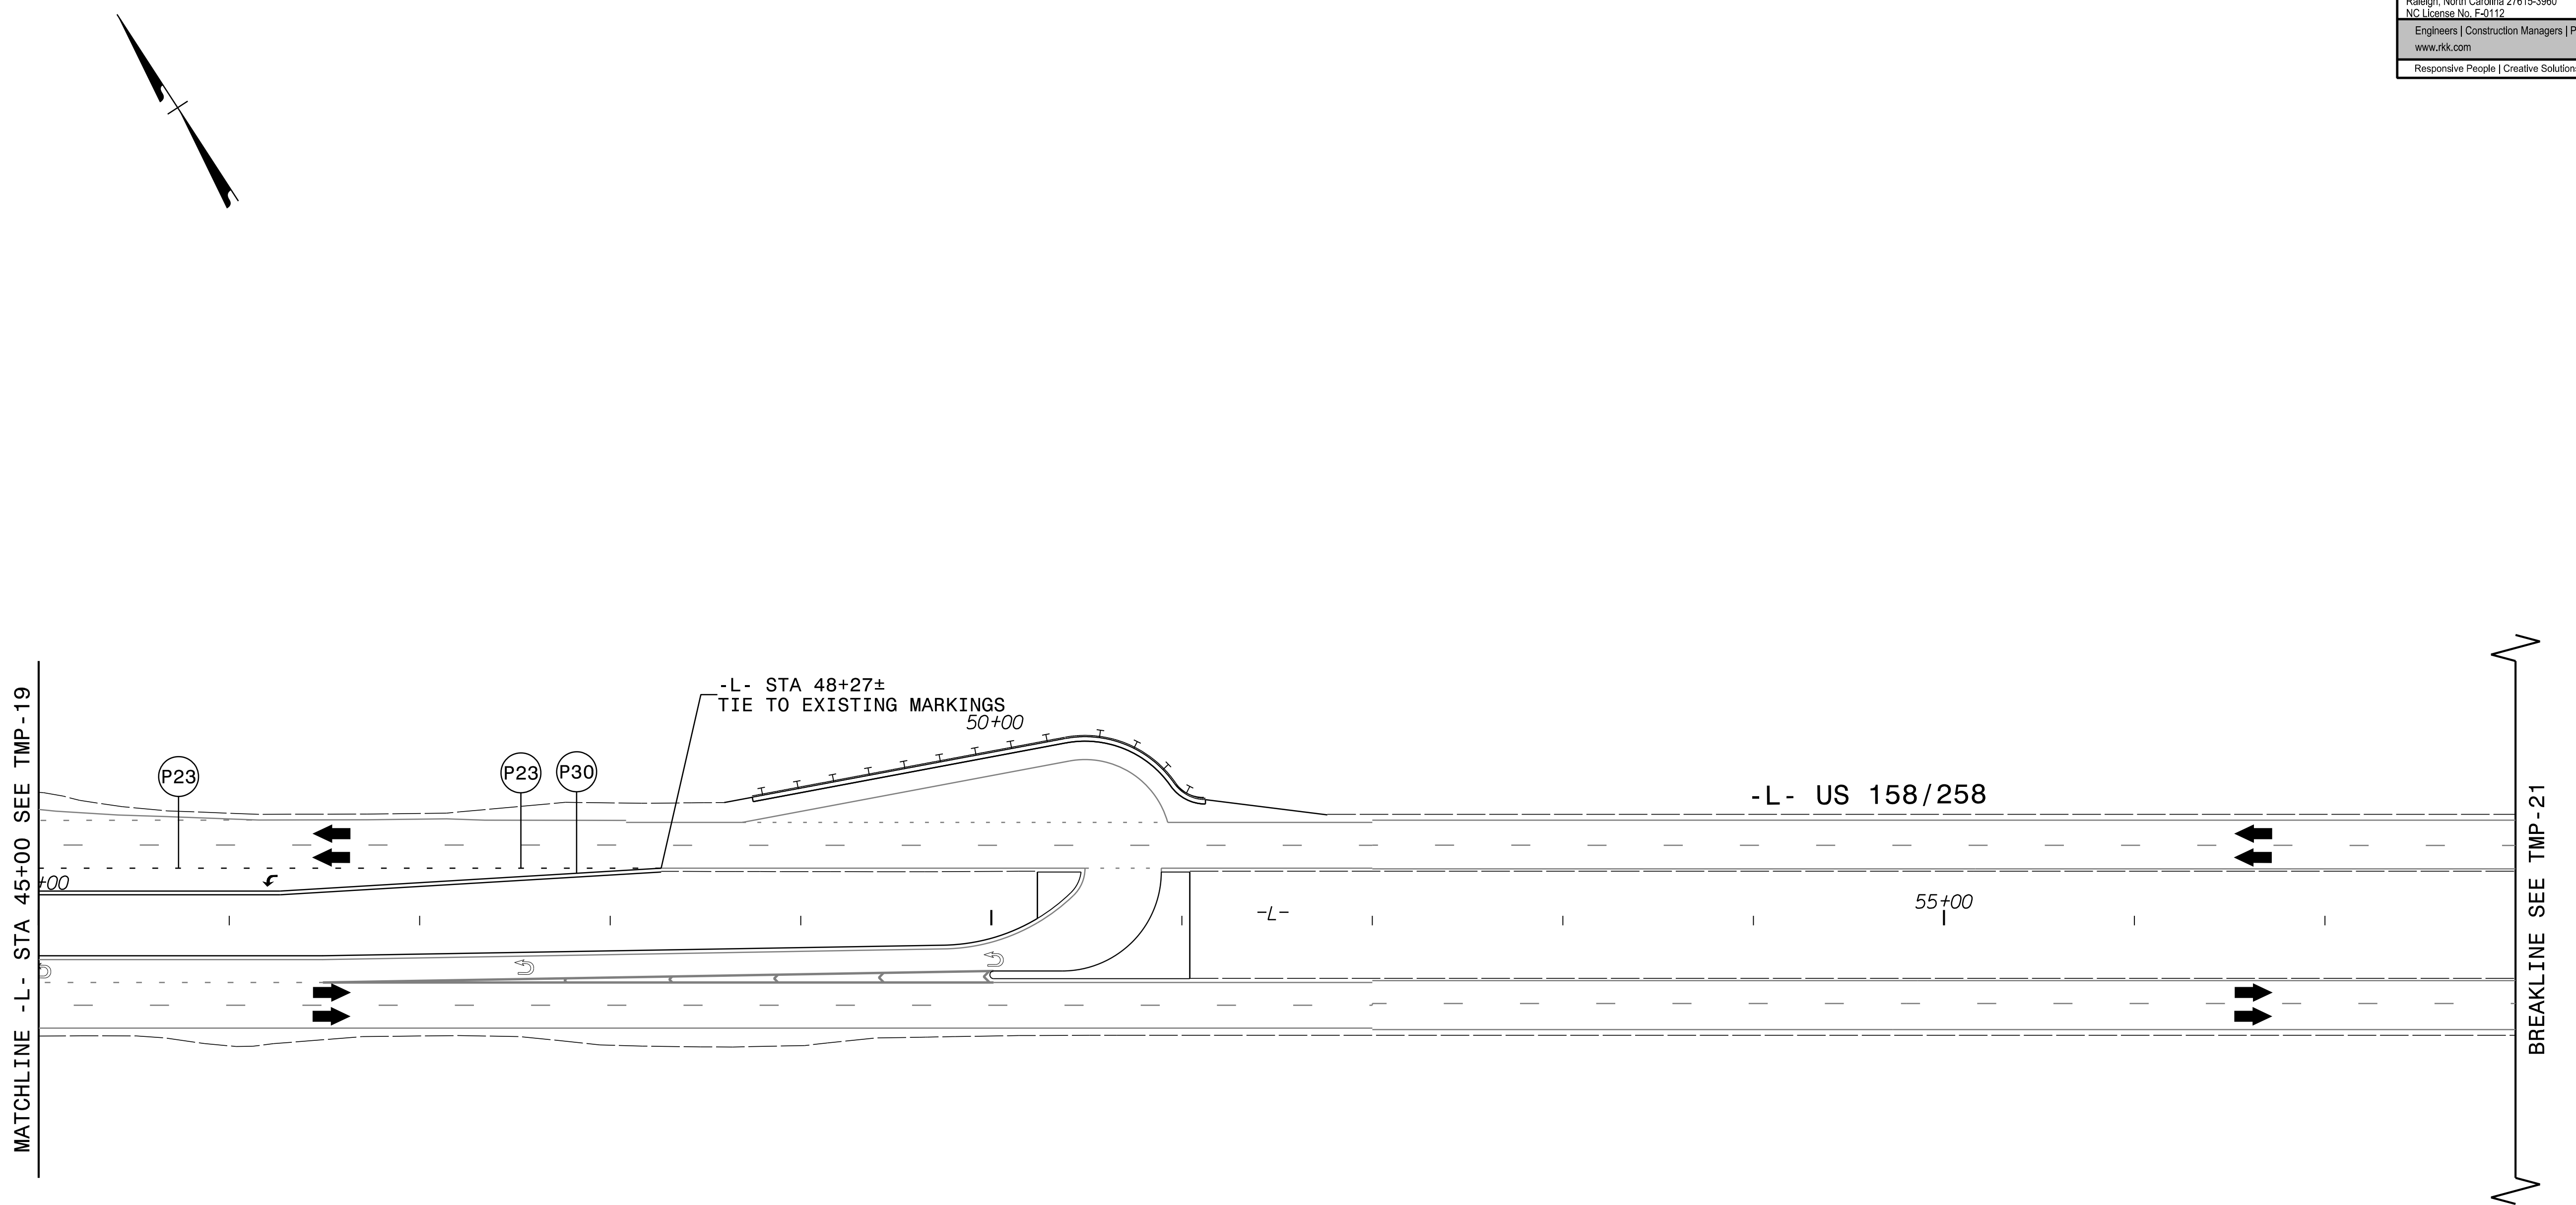

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES

1/9/2023
 W5701B_TMP_PSH20.dgn
 KB/bsby

APPROVED: *Kevin Esley*
800802628912472



DATE: 1/9/2023

SEAL

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**



PHASE II - STEP 3

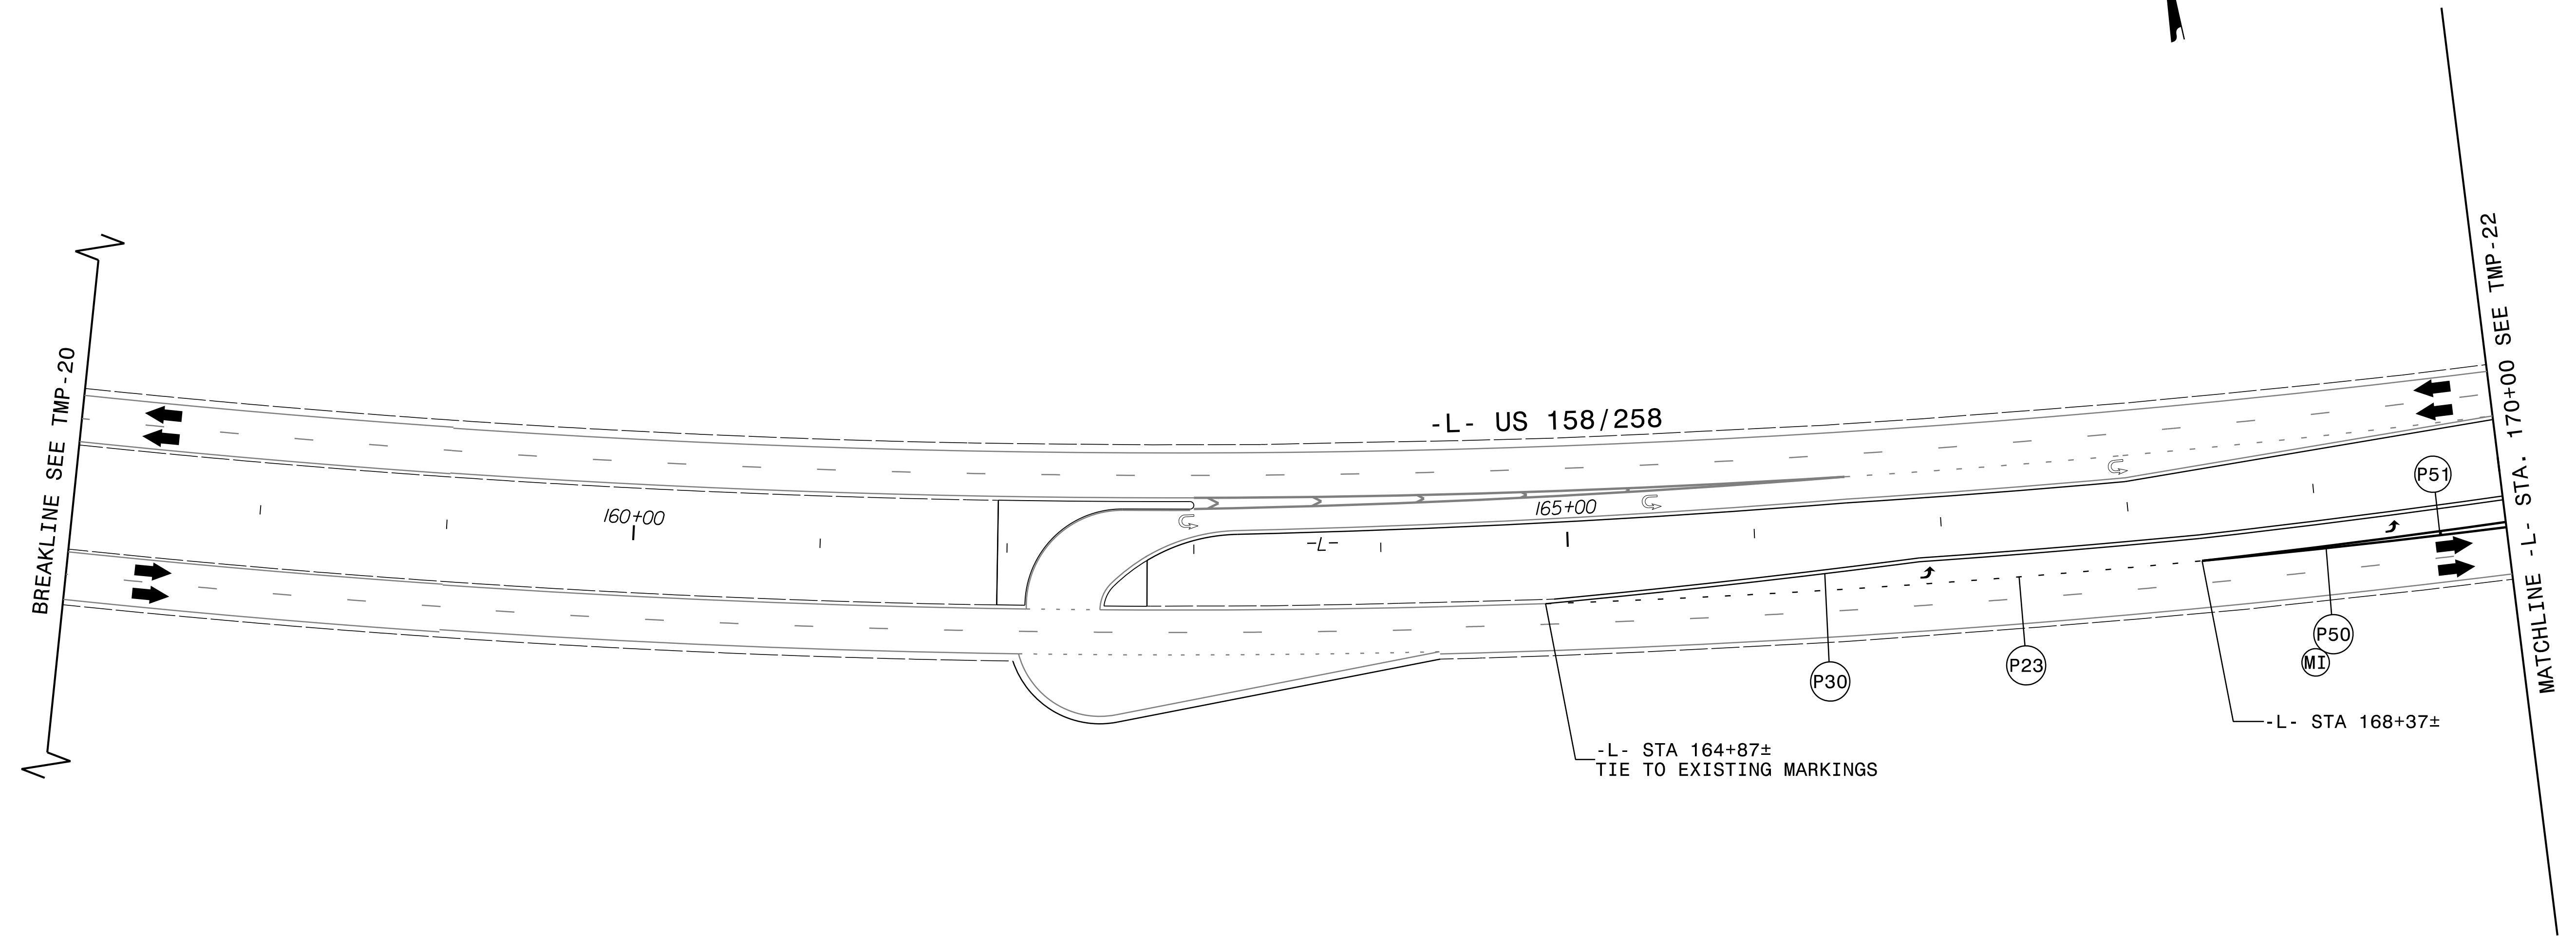

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES


1/9/2023
 W5701B-TMP_PSH21.dgn
 KB/bsby

APPROVED: *Kevin Bishy*
800802628912472


DATE: 1/9/2023

SEAL

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

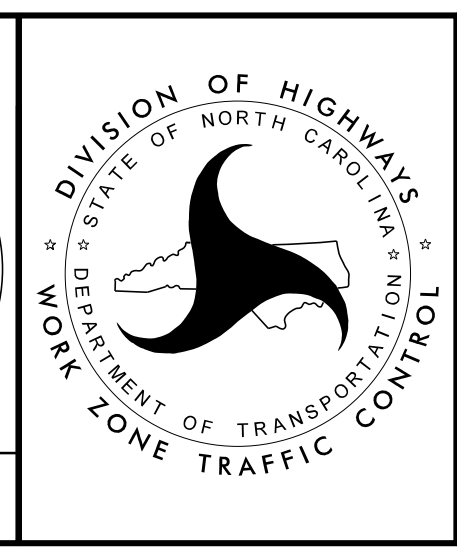

PHASE II - STEP 3

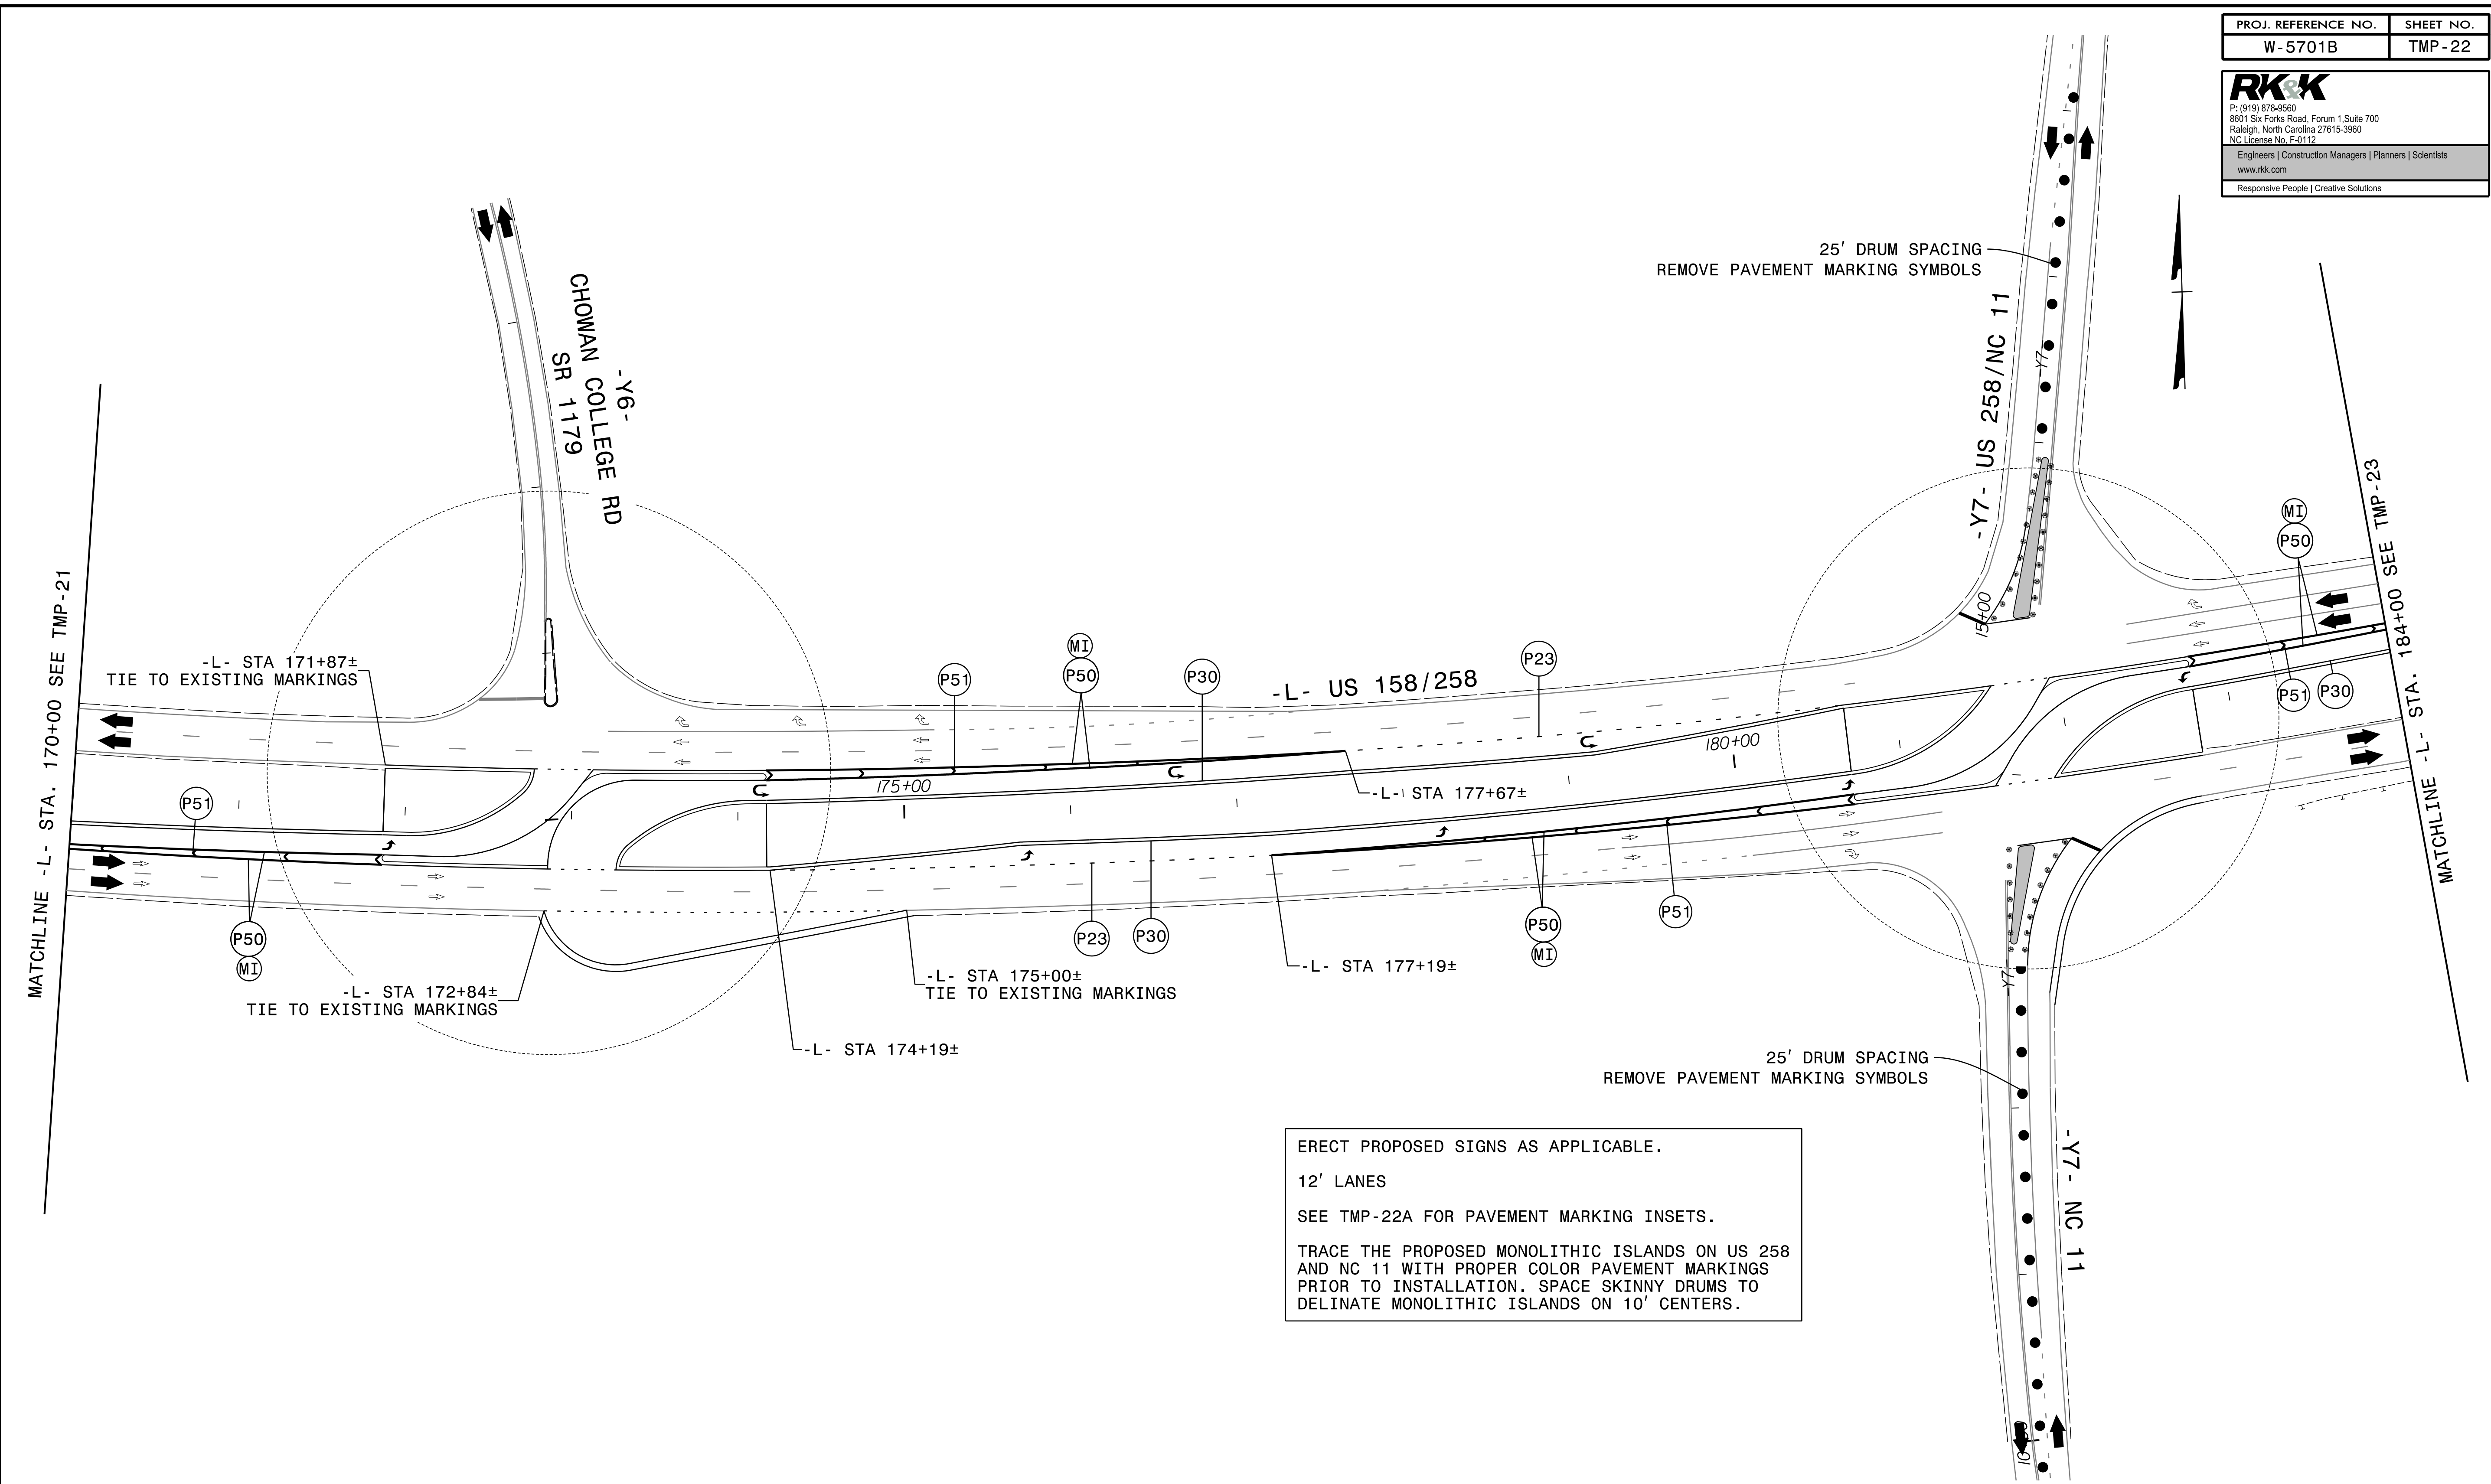

25' DRUM SPACING
 REMOVE PAVEMENT MARKING SYMBOLS


25' DRUM SPACING
 REMOVE PAVEMENT MARKING SYMBOLS

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES
 SEE TMP-22A FOR PAVEMENT MARKING INSETS.
 TRACE THE PROPOSED MONOLITHIC ISLANDS ON US 258 AND NC 11 WITH PROPER COLOR PAVEMENT MARKINGS PRIOR TO INSTALLATION. SPACE SKINNY DRUMS TO DELINEATE MONOLITHIC ISLANDS ON 10' CENTERS.



1/9/2023
 W5701B_TMP_PSH22.dgn
 KBl/sby

APPROVED: *Kevin Esley*
 DATE: 1/9/2023

SEAL

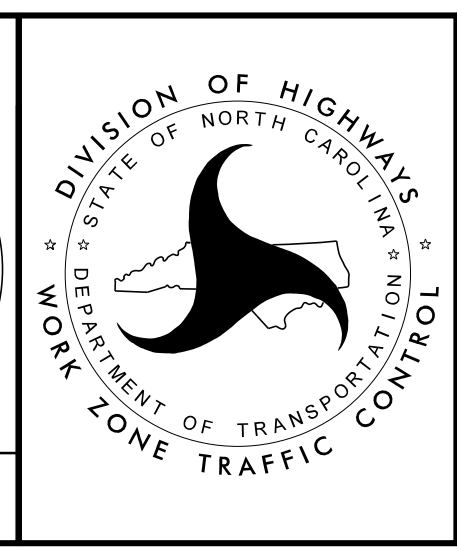

PHASE II - STEPS 3 AND 4

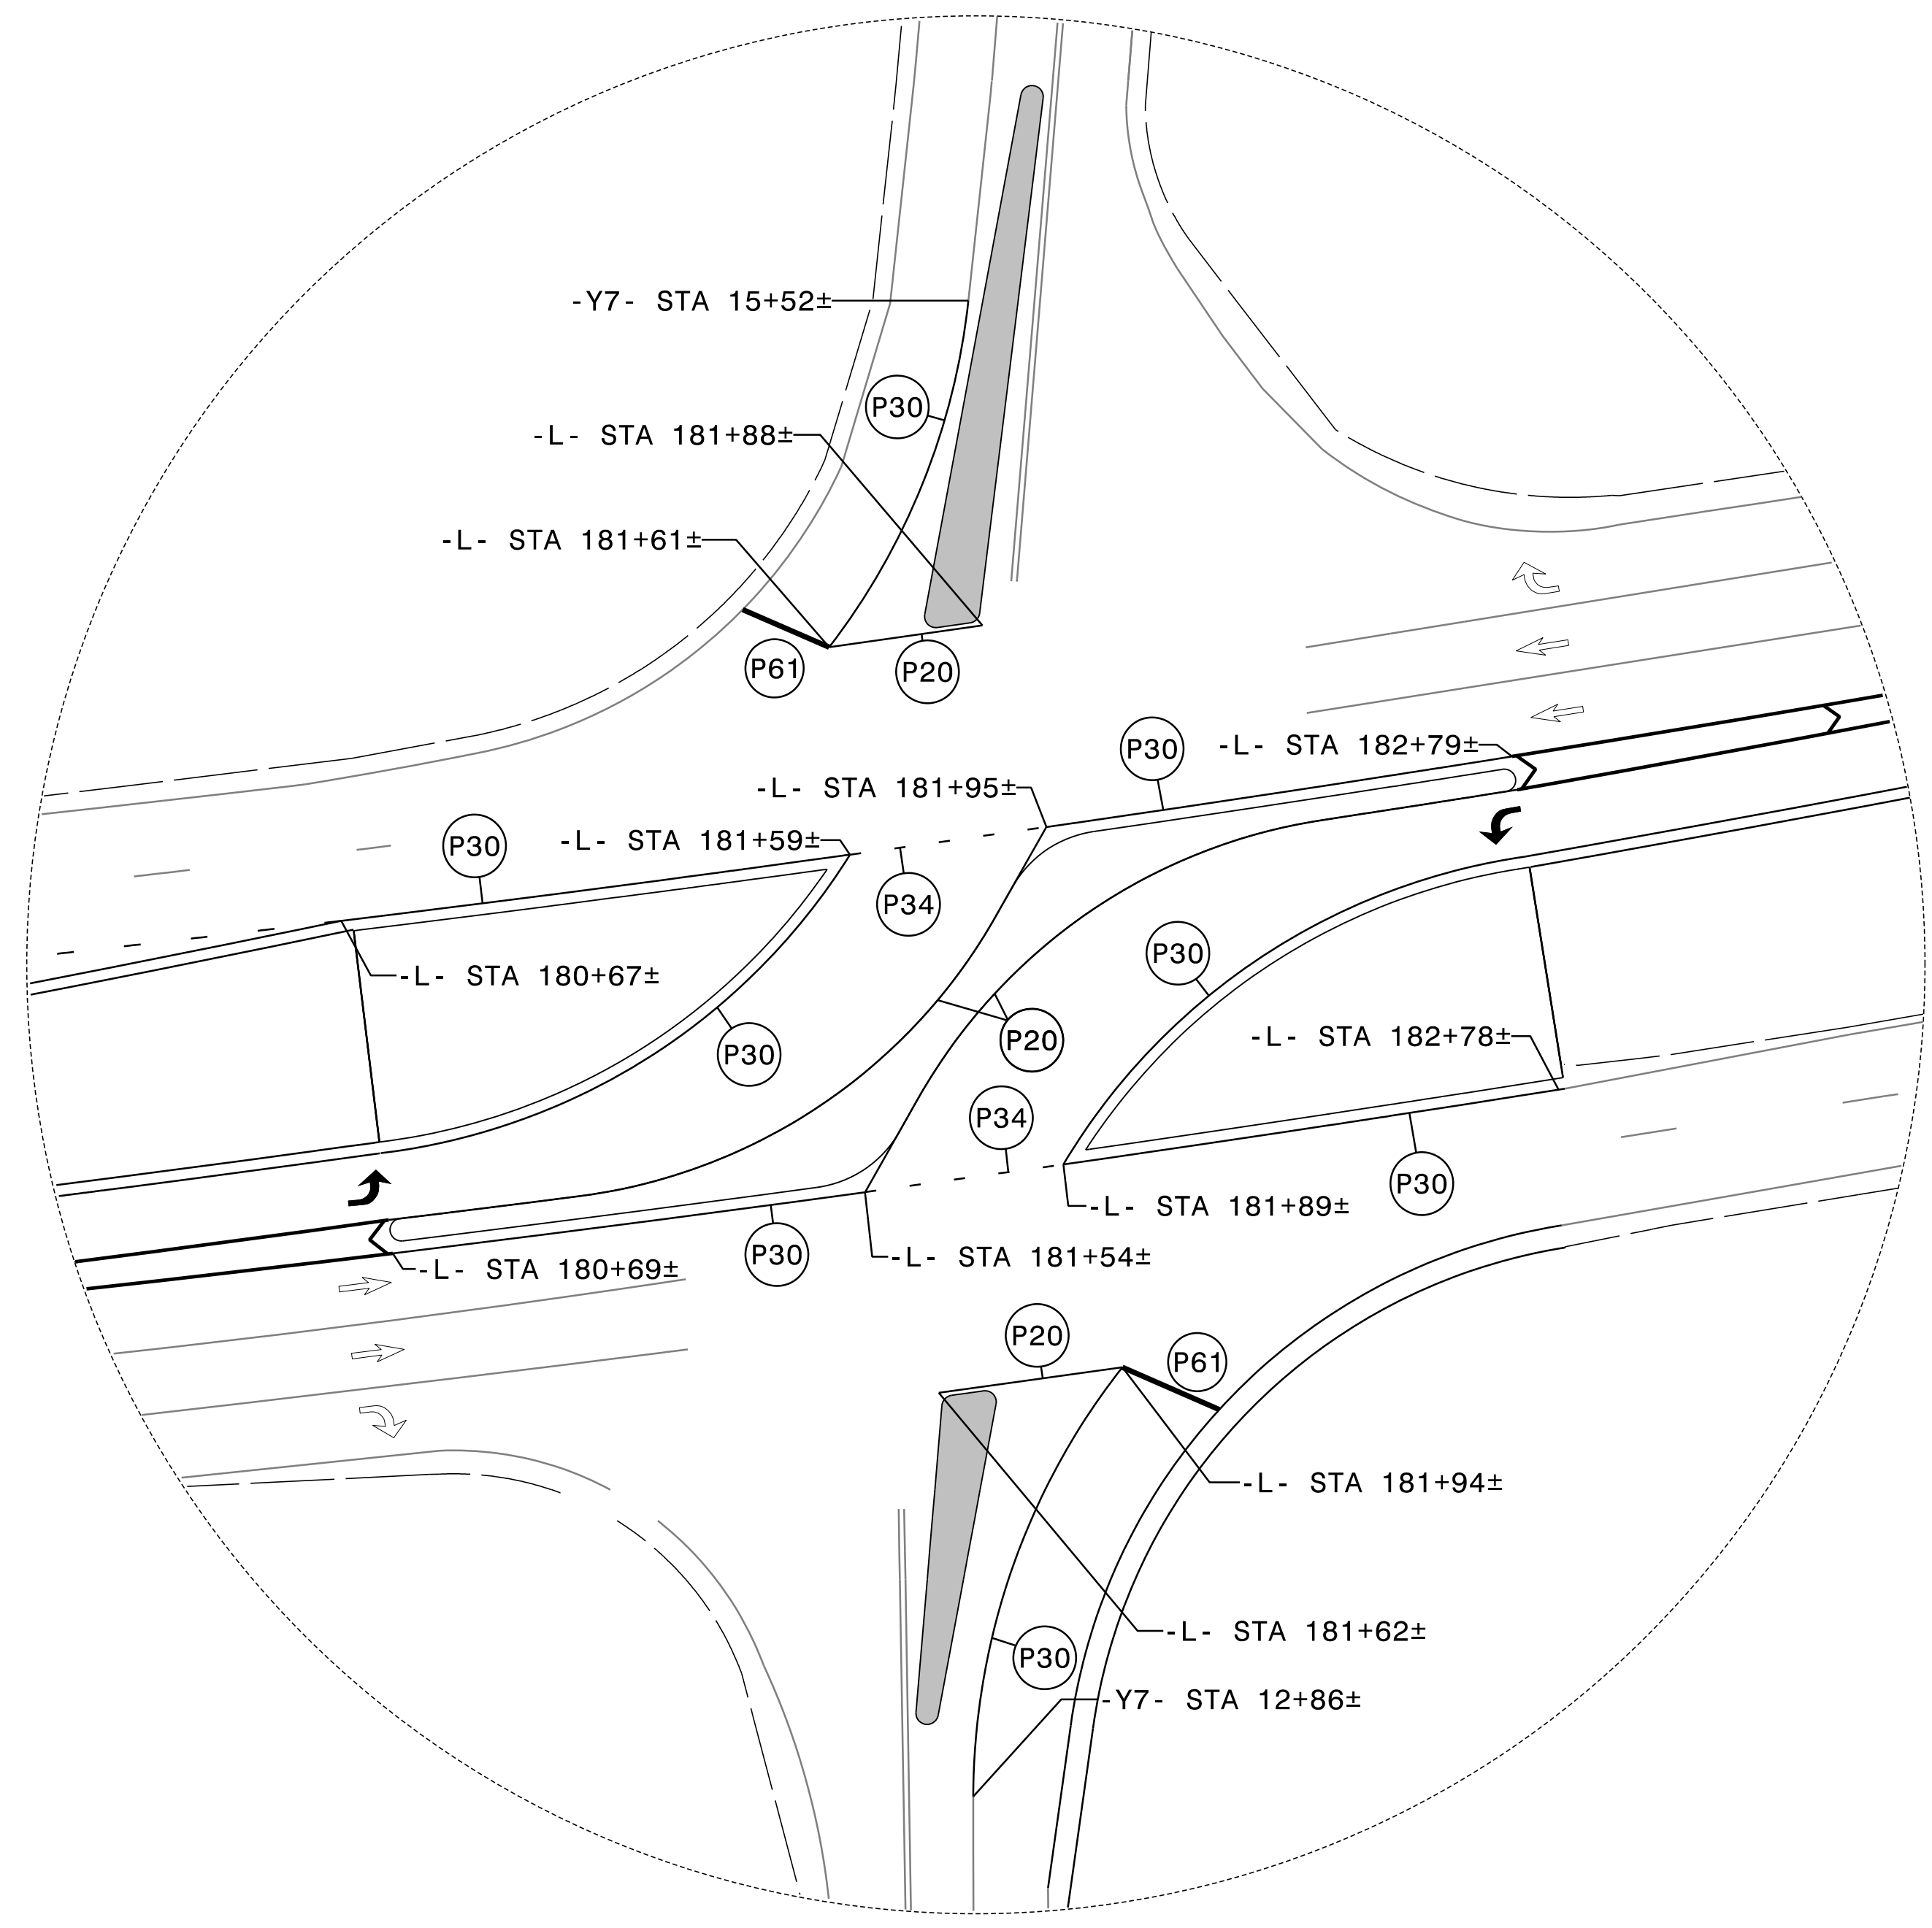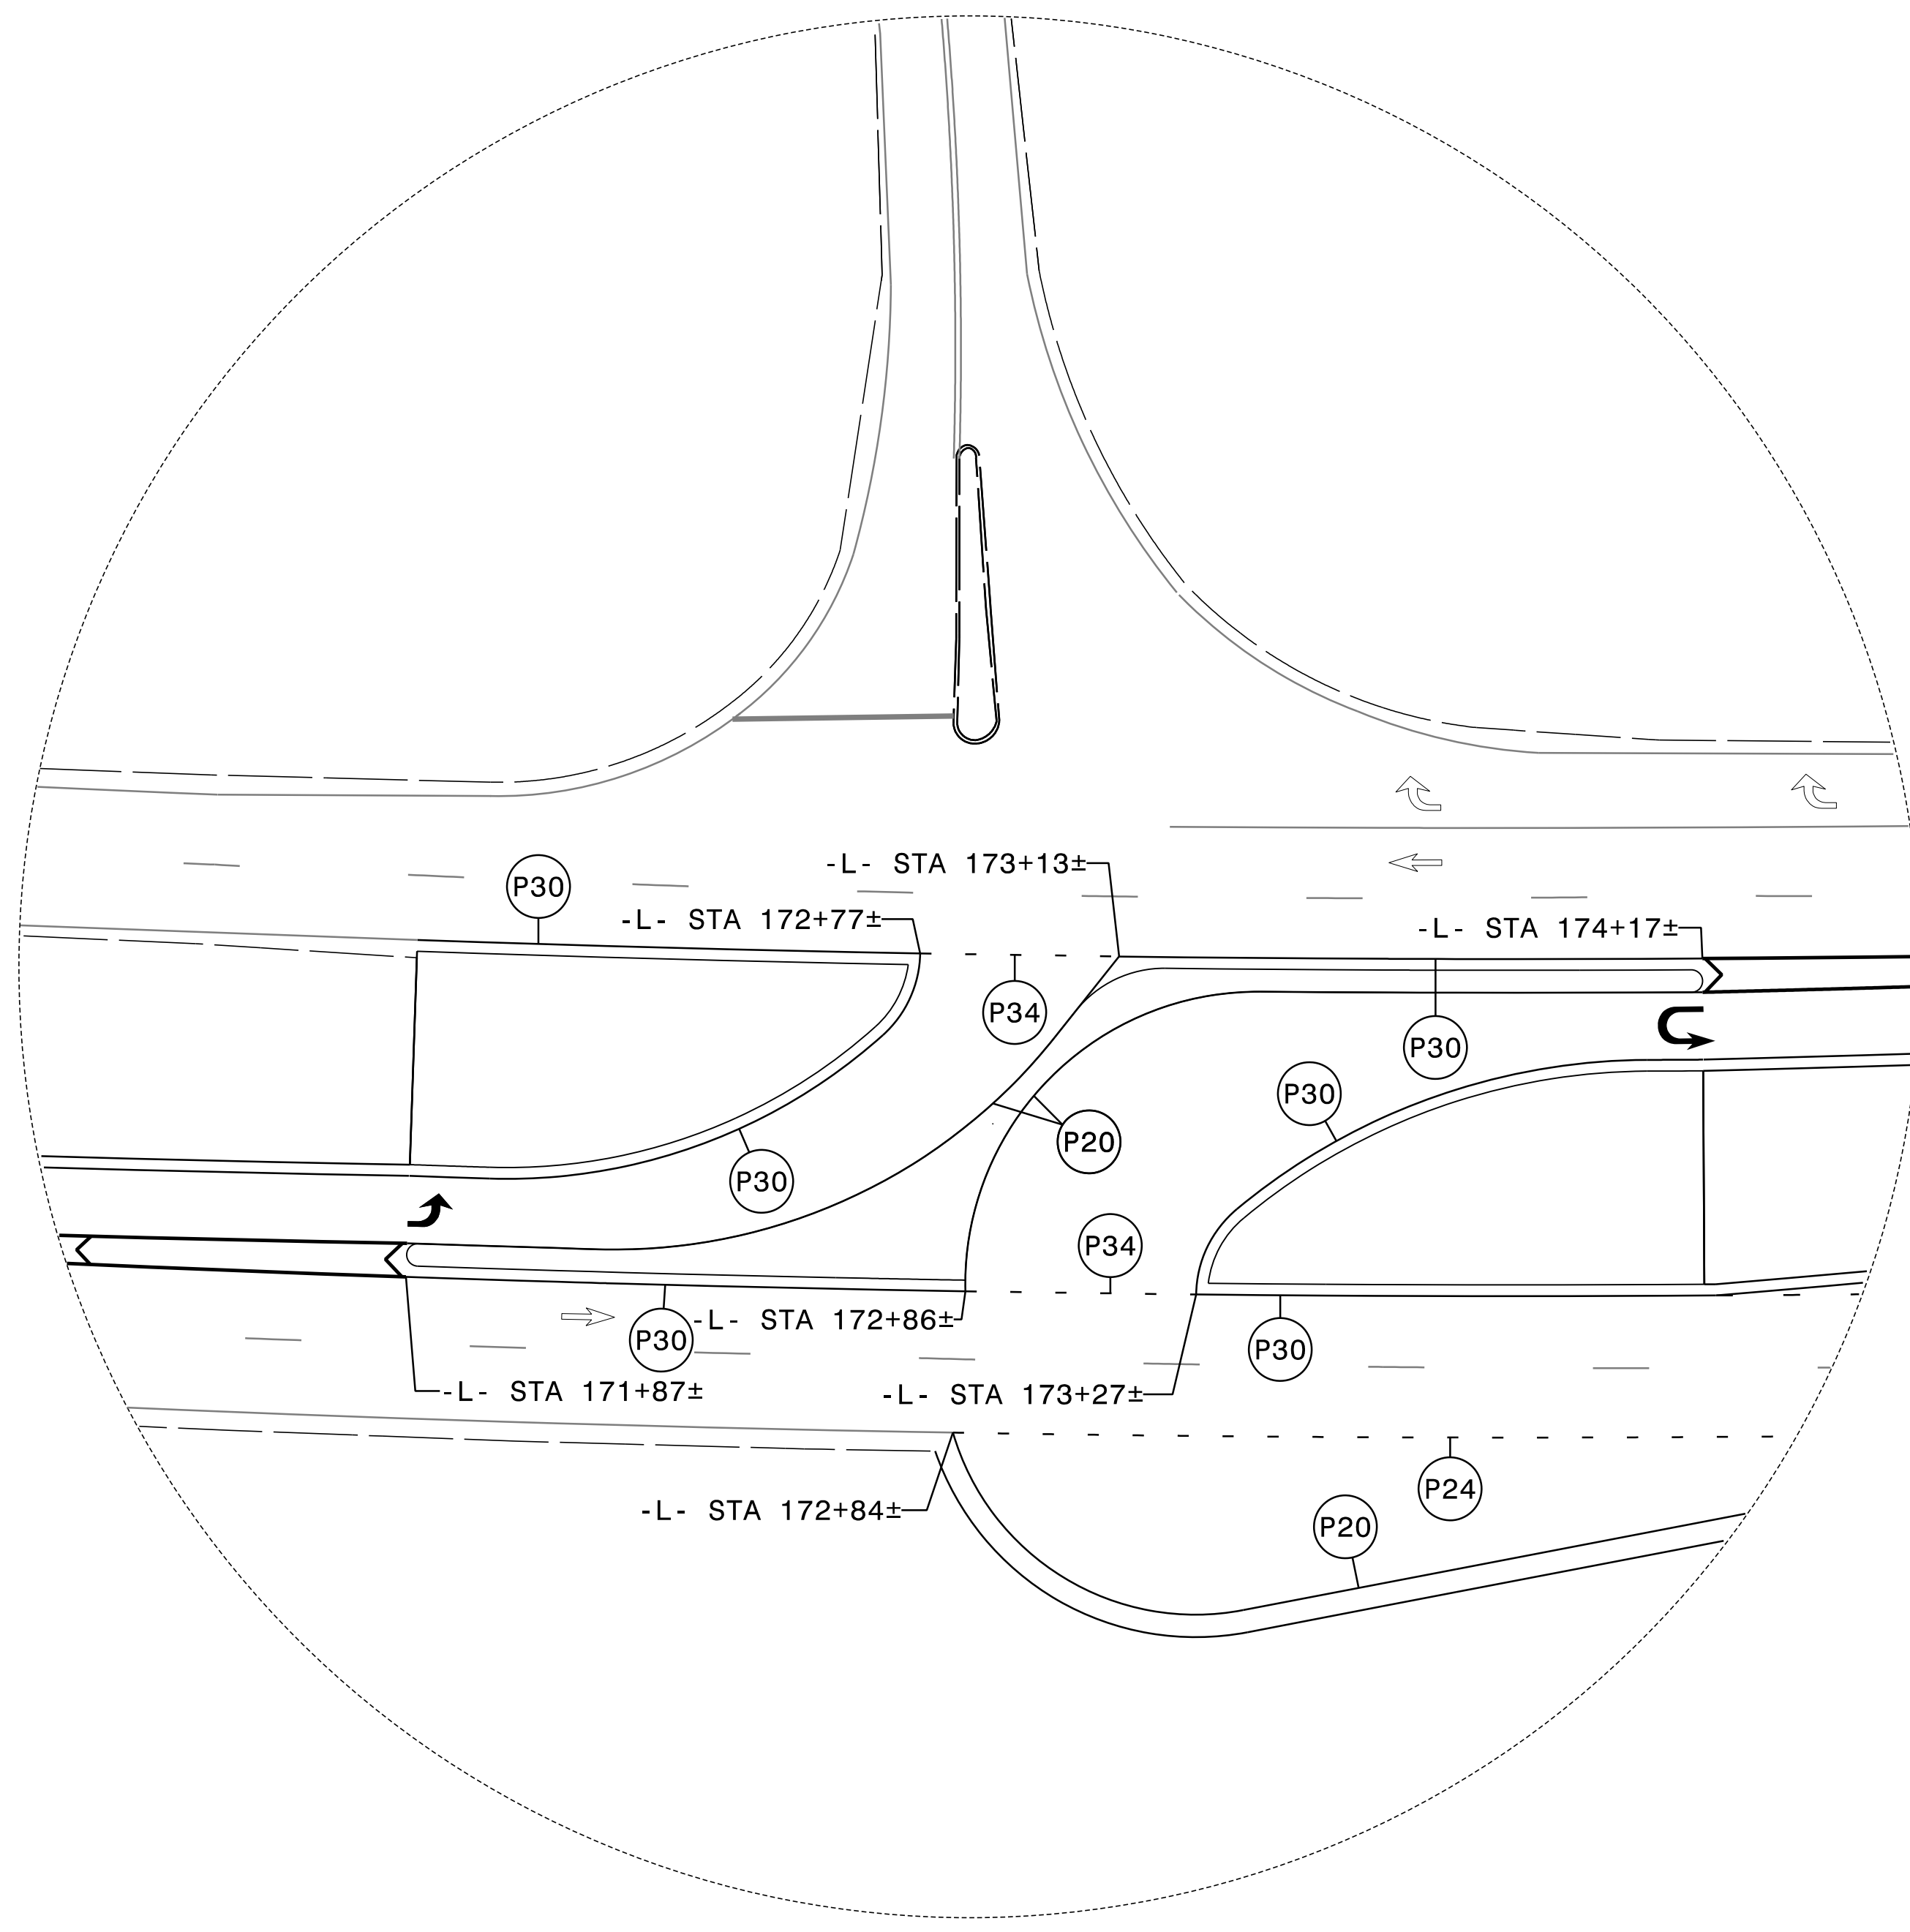


1/9/2023
 W5701B_TMP_PSH22A.dgn
 KBISBY

APPROVED: *Kevin Esley*
 DATE: 1/9/2023



SEAL

NORTH CAROLINA
PROFESSIONAL
ENGINEER
 KEVIN W. ESLEY
 SEAL 21047

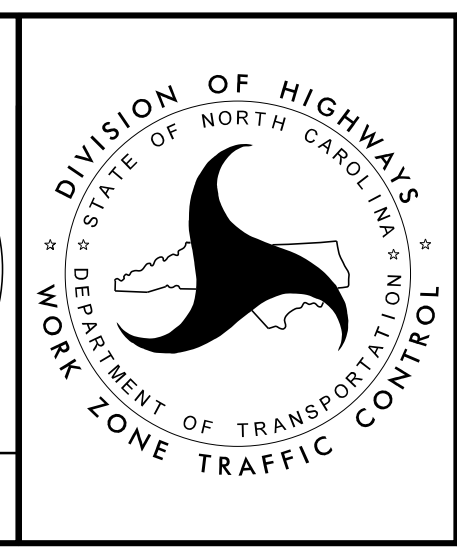

PHASE II - STEP 3
PAVEMENT MARKINGS

DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED

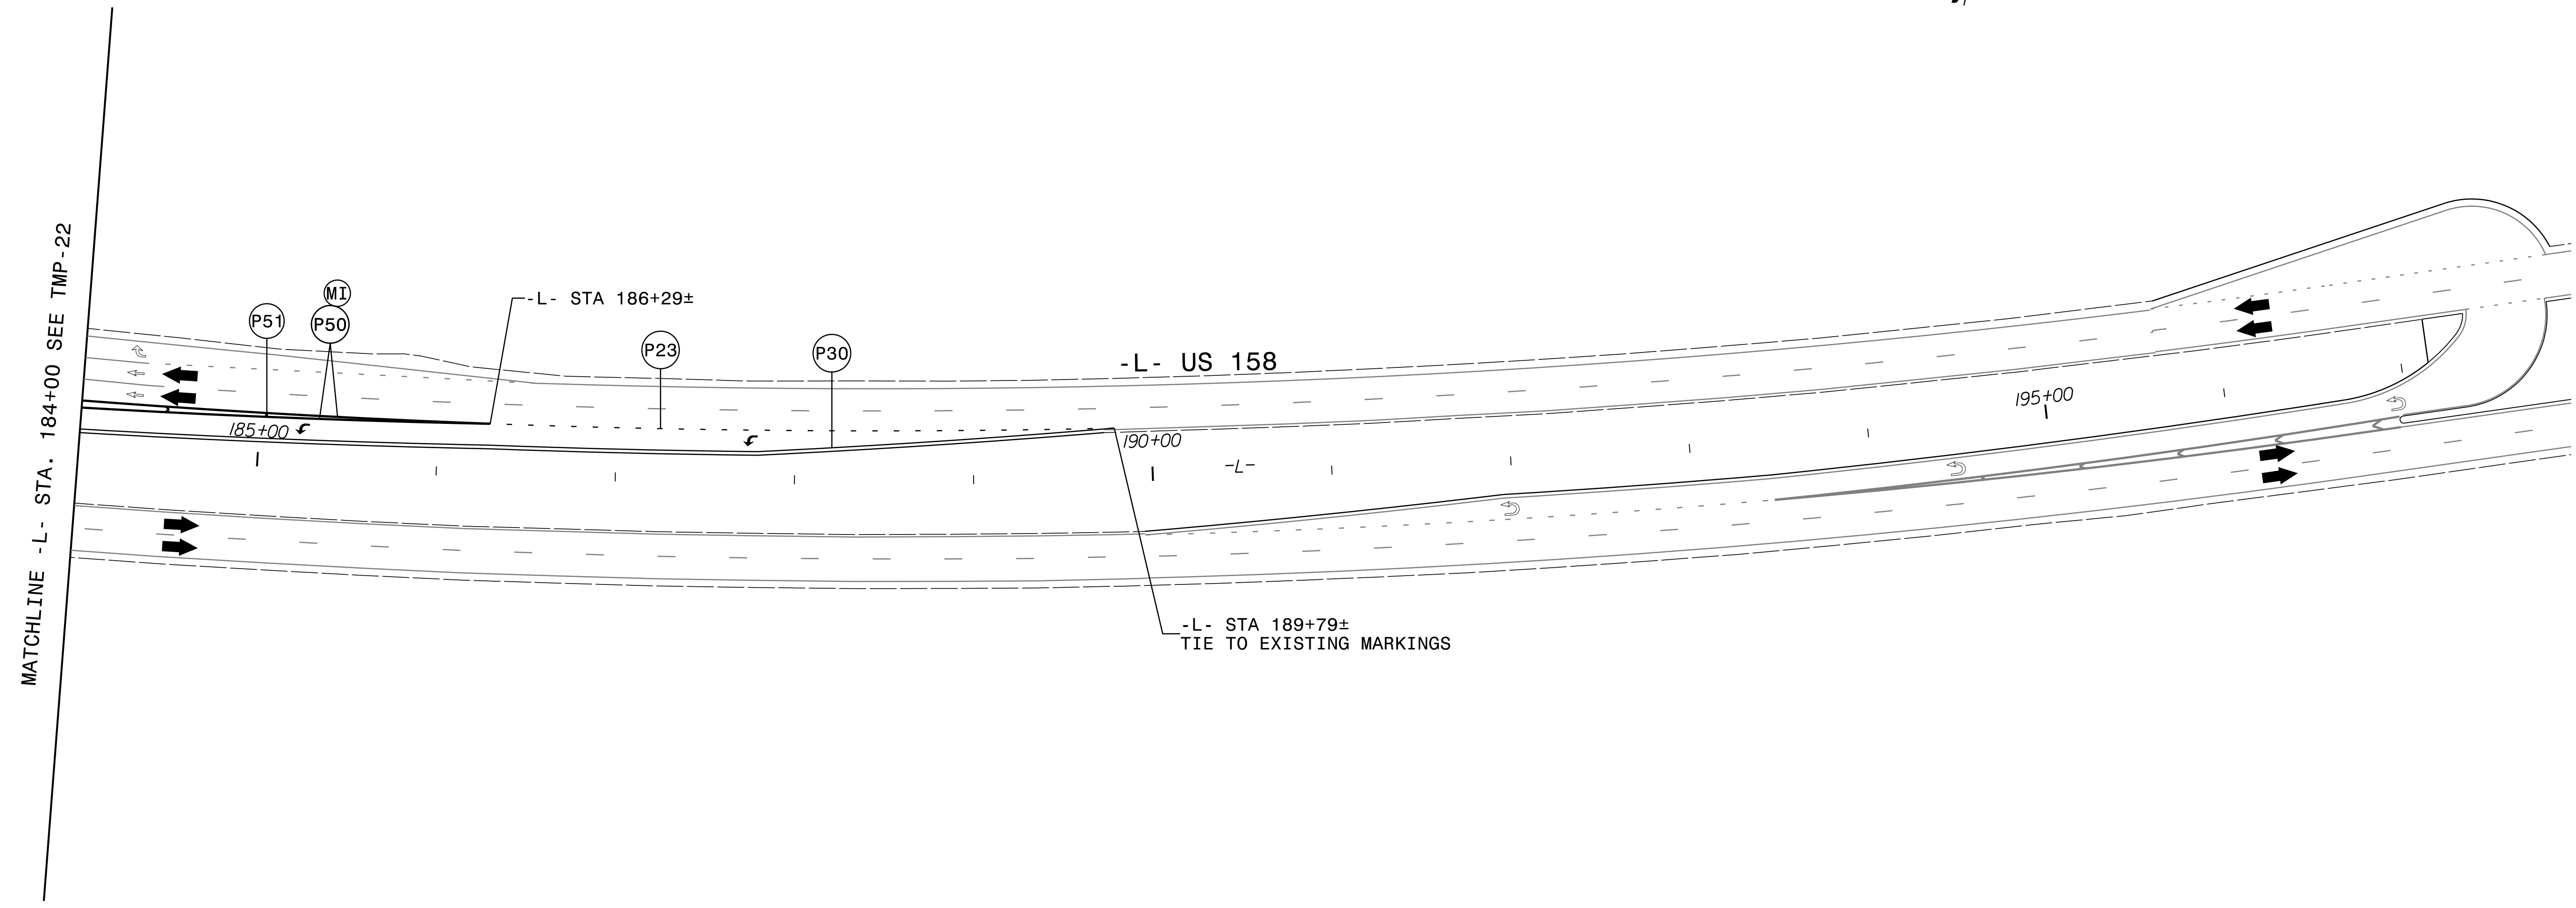

ERECT PROPOSED SIGNS AS APPLICABLE.
 12' LANES


1/9/2023
 W5701B_TMP_PSH23.dgn
 KB/sby

APPROVED: *Kevin B. Sot*
800802628912472

DATE: 1/9/2023

SEAL

**DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED**

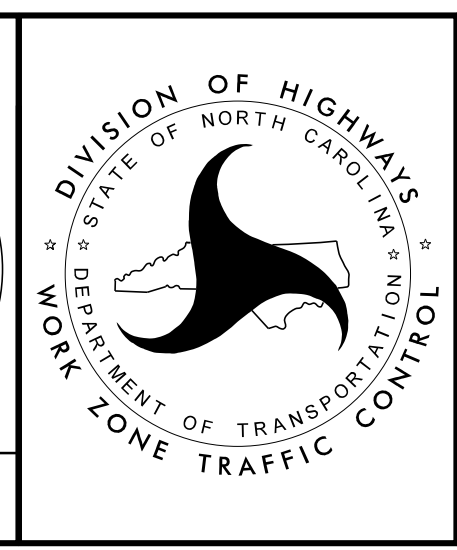

PHASE II - STEP 3
