

CONSTRUCT CURB & GUTTER, PAVEMENT UP TO THE FINAL LIFT, AND DRAINAGE USING TEMPORARY LANE CLOSURE AND FLAGGER CONTROL IN ACCORDANCE WITH NCDOT STD. DWG. 1101.02.

CONTRACTOR TO GRADE AREA BETWEEN EXISTING DAVIDSON STREET AND PROPOSED ROUNDABOUT TO MAINTAIN POSITIVE DRAINAGE IN ACCORDANCE WITH NCDOT STANDARD SPECS AND DRAWINGS



CONTRACTOR TO MAINTAIN POSITIVE DRAINAGE AND ACCESS TO THE LAKE NORMAN YMCA VIA DAVIDSON STREET USING WEDGING, TEMPORARY LANE CLOSURE, AND FLAGGER CONTROL IN ACCORDANCE WITH NCDOT STD. DWG. 1101.02.

CONTRACTOR TO MAINTAIN ACCESS TO ALL DRIVEWAYS

CONTRACTOR TO MAINTAIN ACCESS TO ALL DRIVEWAYS


PLACE PAINTED PAVEMENT MARKINGS IN FINAL PATTERN SEE STRIPING PLAN (THIS SET)

NOTE: CONTRACTOR TO COORDINATE WITH RAILROAD TO COMPLETE WORK

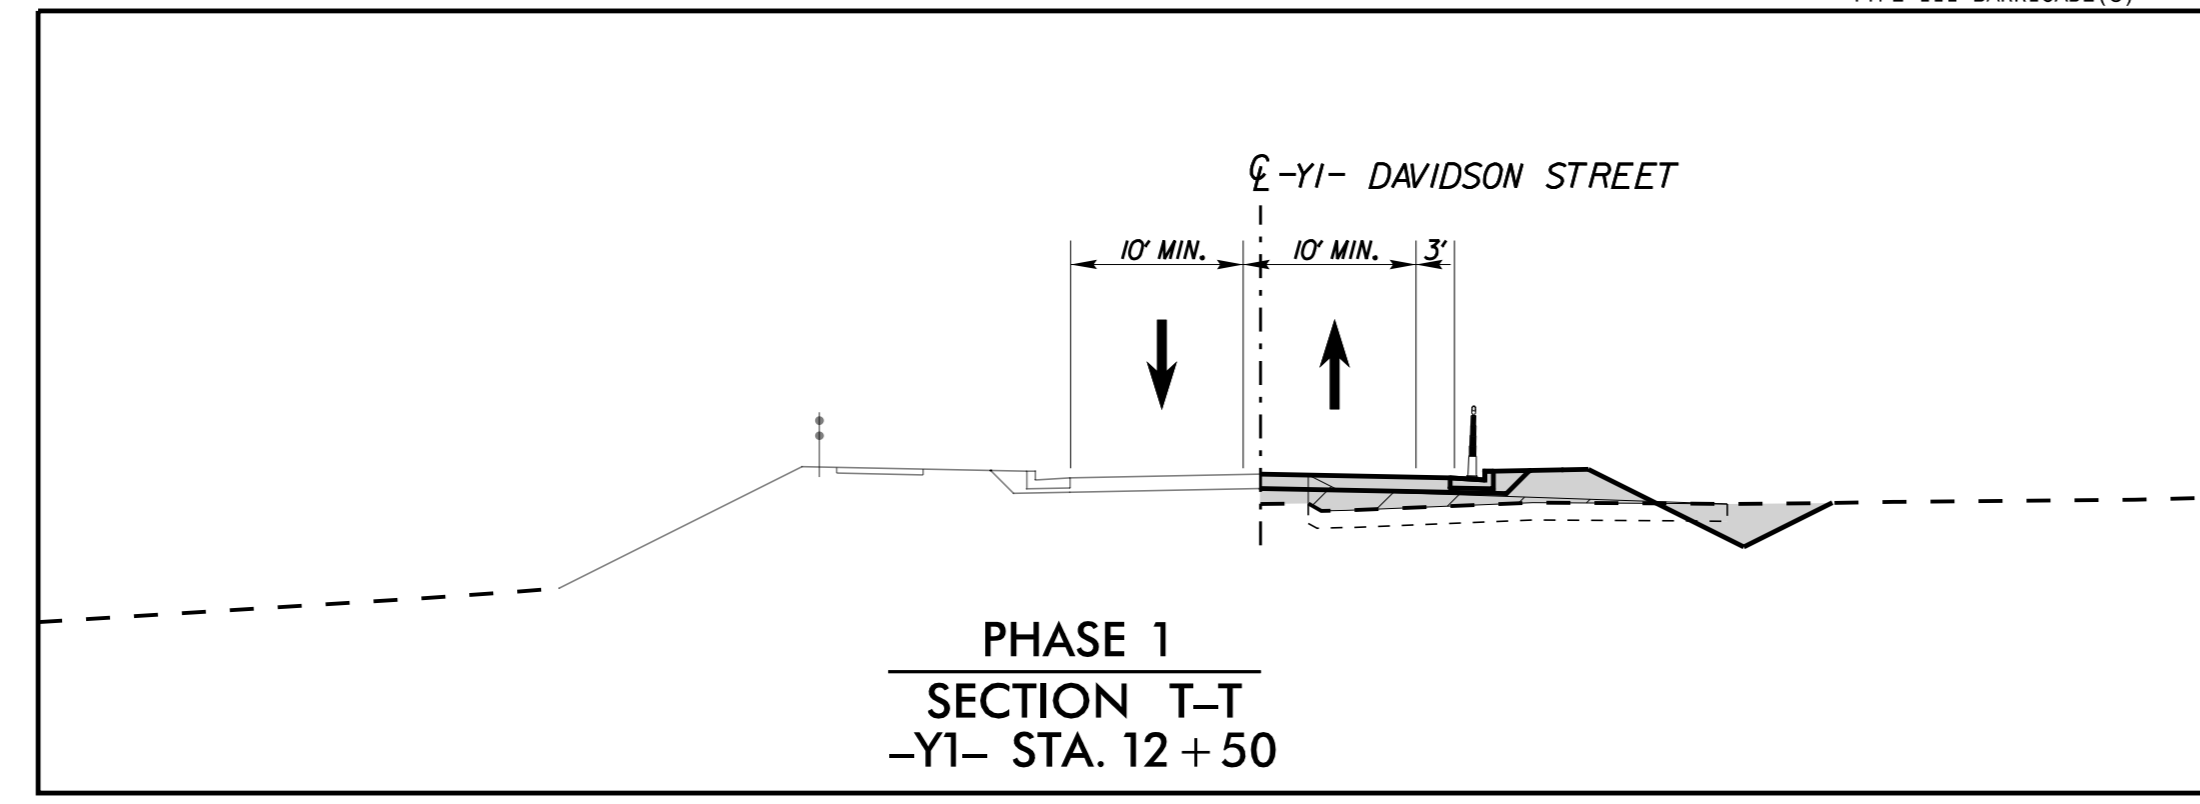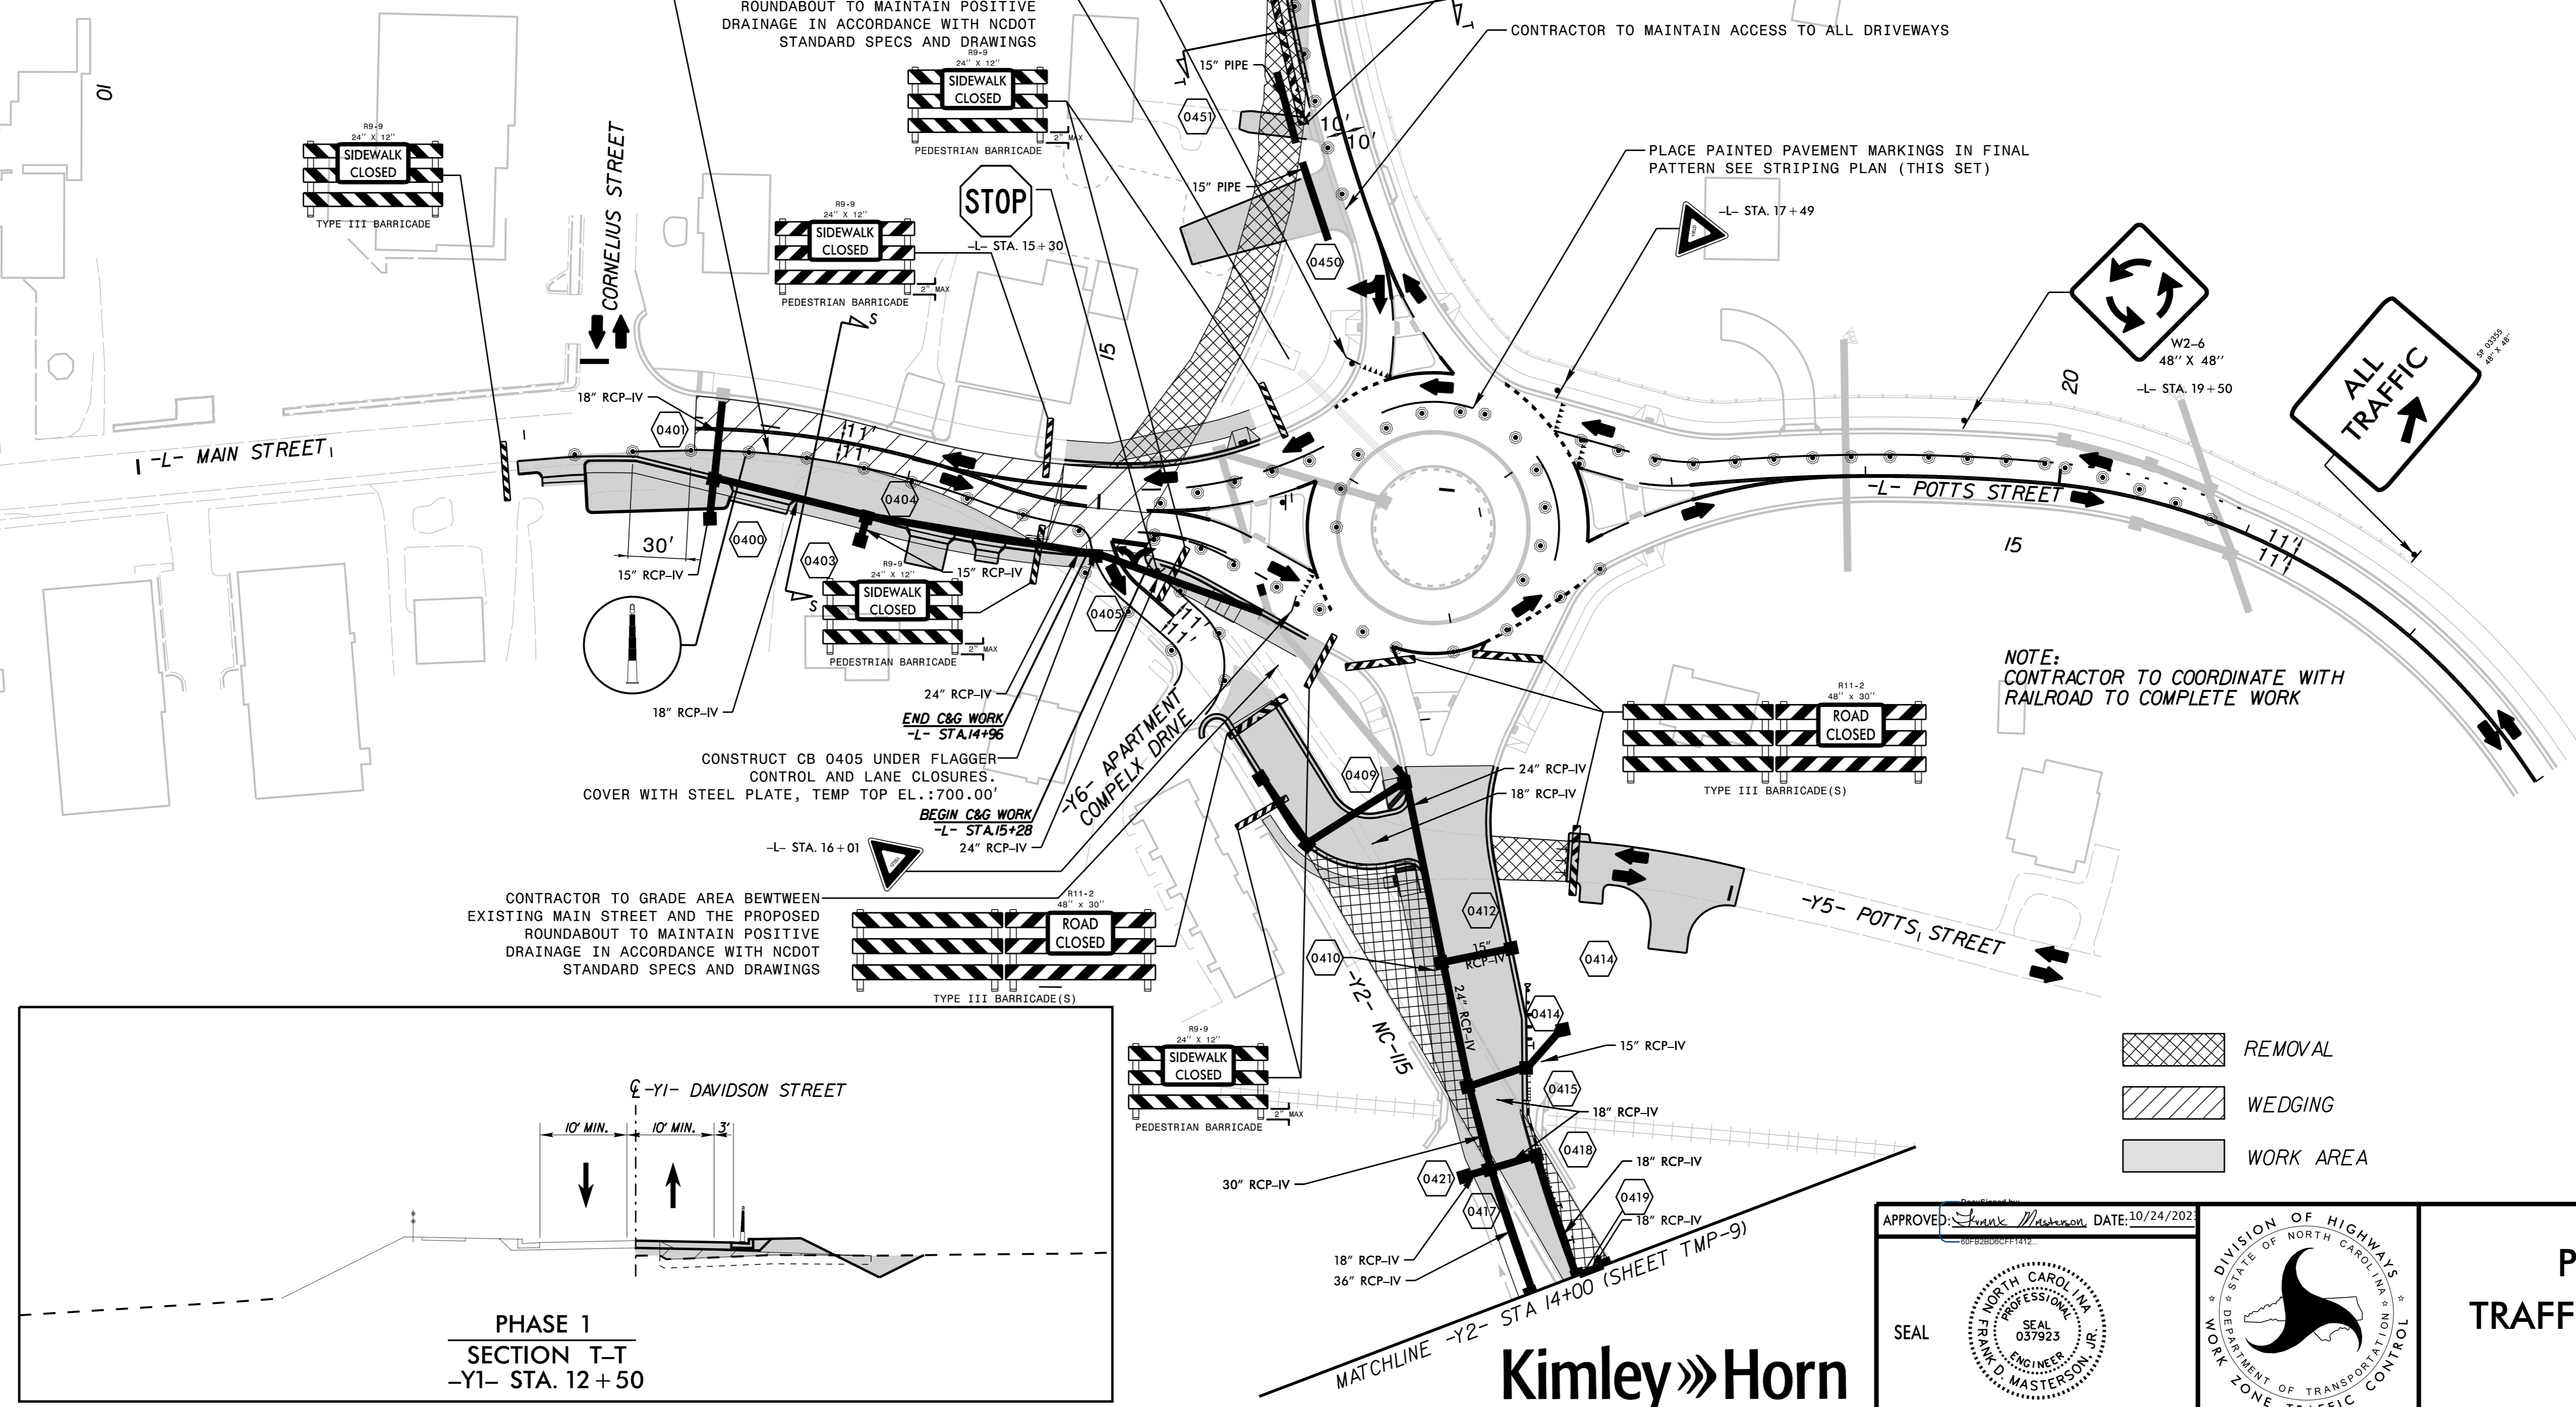

- REMOVAL
- WEDGING
- WORK AREA

APPROVED: *[Signature]* DATE: 10/24/2022



**PHASE 1D  
TRAFFIC CONTROL  
DETAILS**



10/16/2023 K:\CHL\PRJ\01036361\_U-5873\_Potts-Main\TrafficControl\CPSheets\U-5873\_rdy\_tmp\_08.dgn
