
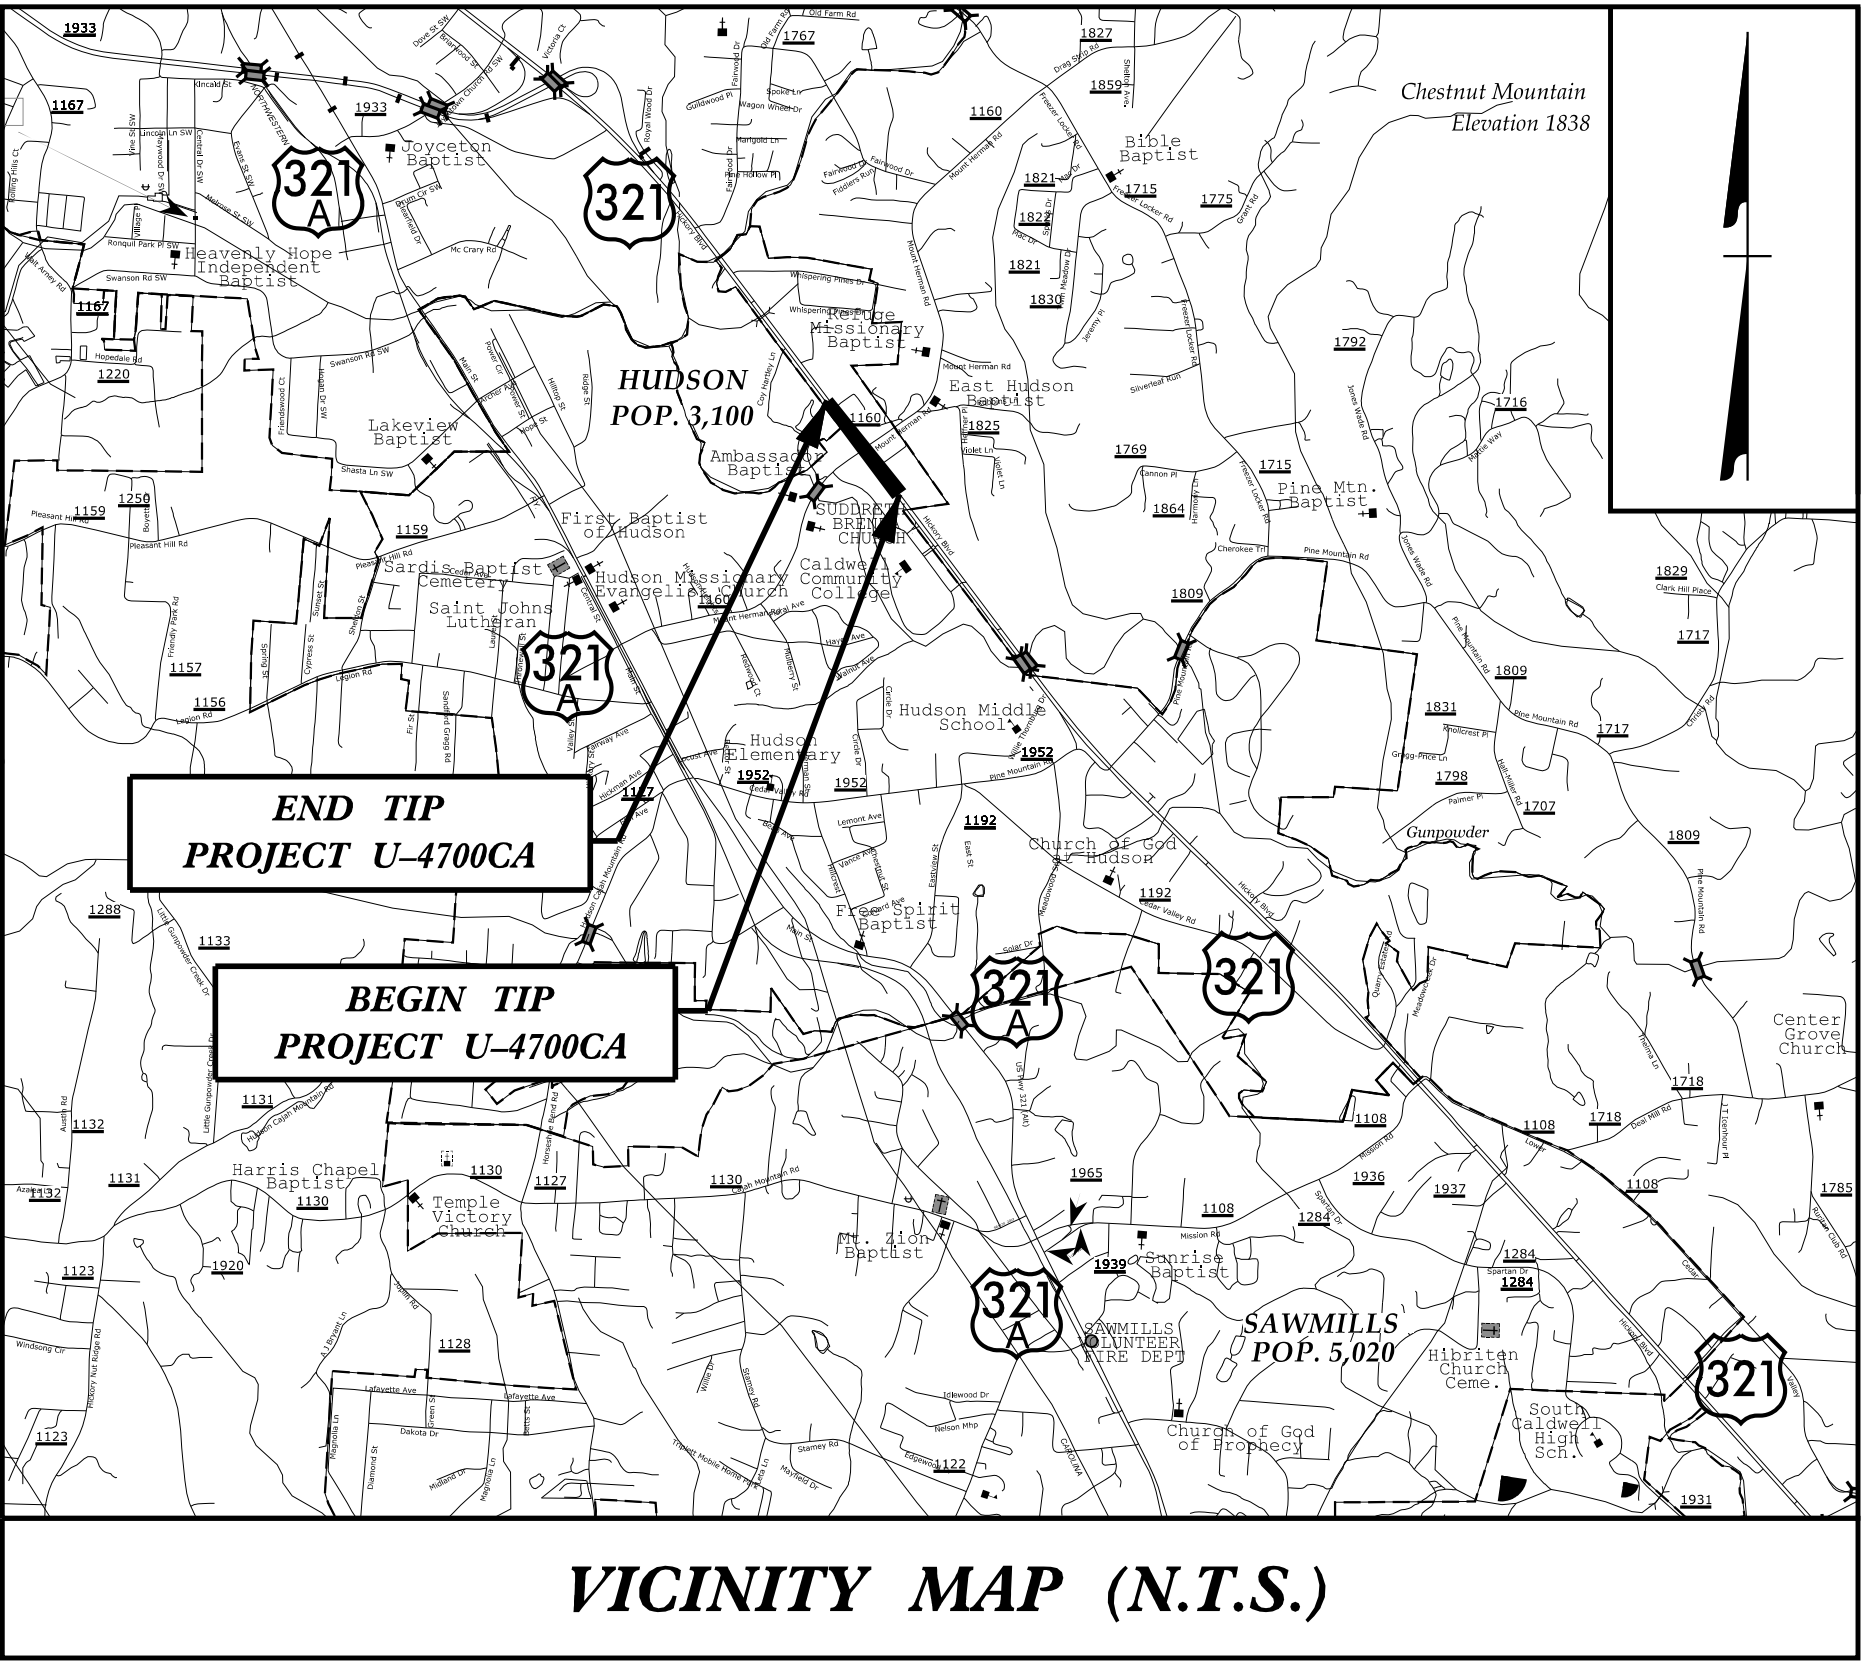


STATE OF NORTH CAROLINA
DIVISION OF HIGHWAYS

TRANSPORTATION MANAGEMENT PLAN

CALDWELL COUNTY
DIVISION II

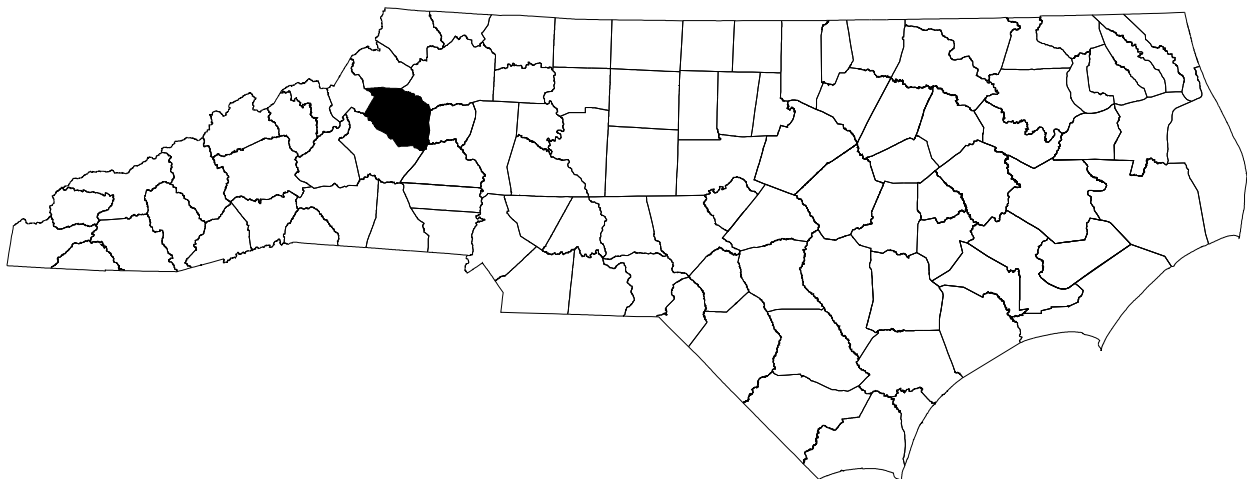

VICINITY MAP (N.T.S.)

LOCATION: US 321 (HICKORY BLVD) AT SR 1160 (MOUNT HERMAN ROAD)

INDEX OF SHEETS

SHEET NO.	TITLE
TMP-1	TITLE SHEET AND INDEX OF SHEETS
TMP-1A	LIST OF APPLICABLE ROADWAY STANDARD DRAWINGS AND LEGEND
TMP-1B	GENERAL NOTES, LOCAL NOTES AND MANAGEMENT STRATEGIES
TMP-2	TYPICAL SECTIONS
TMP-3	TEMPORARY TRAFFIC CONTROL PHASING
TMP-4 THRU TMP-6	TEMPORARY TRAFFIC CONTROL PHASE I DETAIL
TMP-7 THRU TMP-9	TEMPORARY TRAFFIC CONTROL PHASE II DETAIL

SHEET NO.
TMP-1

U-4700CA


TIP PROJECT:

DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED


APPROVED: [Signature]

DATE: 6/5/2026 | 6:19:46 AM PDT

SEAL



Johnson, Mirmiran, & Thompson Inc.
4700 Falls of Neuse Rd, Suite 100,
Raleigh, NC, 27609
License No: C-3097



PLANS PREPARED BY:


CHARLES J. YOUNG, P.E.
TRAFFIC CONTROL ENGINEER

JOSHUA ROEMER, P.E.
TRAFFIC CONTROL DESIGN ENGINEER

NCDOT CONTACTS:

ZACHARY CLARK, P.E.
PROJECT ENGINEER

SHEENA GREEN
PROJECT DESIGN ENGINEER



ROADWAY STANDARD DRAWINGS

THE FOLLOWING ROADWAY STANDARDS AS SHOWN IN "ROADWAY STANDARD DRAWINGS" - N.C. DEPARTMENT OF TRANSPORTATION - RALEIGH, N.C., DATED JANUARY 2024 ARE APPLICABLE TO THIS PROJECT AND BY REFERENCE HEREBY ARE CONSIDERED A PART OF THESE PLANS:

STD. NO.	TITLE
1101.01	WORK ZONE ADVANCE WARNING SIGNS
1101.02	TEMPORARY LANE CLOSURES
1101.03	TEMPORARY ROAD CLOSURES
1101.04	TEMPORARY SHOULDER CLOSURES
1101.05	WORK ZONE VEHICLE ACCESSES
1101.11	TRAFFIC CONTROL DESIGN TABLES
1110.01	STATIONARY WORK ZONE SIGNS
1110.02	PORTABLE WORK ZONE SIGNS
1115.01	FLASHING ARROW BOARDS
1130.01	DRUMS
1135.01	CONES
1145.01	BARRICADES - TYPE III
1150.01	FLAGGERS
1160.01	TEMPORARY CRASH CUSHION - REFLECTIVE END TREATMENT
1165.01	TRUCK MOUNTED ATTENUATOR
1180.01	SKINNY DRUMS
1205.01	PAVEMENT MARKINGS - LINE TYPES AND OFFSETS
1205.02	PAVEMENT MARKINGS - TWO-LANE AND MULTI-LANE ROADWAYS
1205.04	PAVEMENT MARKINGS - INTERSECTIONS
1205.05	PAVEMENT MARKINGS - TURN LANES
1205.08	PAVEMENT MARKINGS - SYMBOLS AND WORD MESSAGES
1205.09	PAVEMENT MARKINGS - PAINTED ISLANDS
1205.15	PAVEMENT MARKINGS - REDUCED CONFLICT INTERSECTIONS
1250.01	RAISED PAVEMENT MARKERS INSTALLATION SPACING
1251.01	RAISED PAVEMENT MARKERS - PERMANENT AND TEMPORARY
1261.01	GUARDRAIL AND BARRIER DELINEATORS - INSTALLATION SPACING
1261.02	GUARDRAIL AND BARRIER DELINEATORS - TYPES AND MOUNTING
1262.01	GUARDRAIL END DELINEATION

MANAGEMENT STRATEGIES

THE FOLLOWING LISTED WORK ZONE STRATEGIES ARE RECOMMENDED FOR INCLUSION WITHIN THIS TRANSPORTATION MANAGEMENT PLAN (TMP).

RECOMMENDED STRATEGIES:

- TRAFFIC MANAGEMENT STRATEGIES:
- LANE SHIFTS OR CLOSURES
 - SHOULDER CLOSURES
 - ONE-LANE, TWO WAY OPERATION (FLAGGING)
 - NIGHT WORK
 - WEEKEND WORK
 - WORK HOUR RESTRICTIONS FOR PEAK TRAVEL
 - WORK ZONE PATTERN MASKINGS

CONTRACTING & INNOVATIVE CONSTRUCTION STRATEGIES:

INTERMEDIATE CONTRACT TIMES / LIQUIDATED DAMAGES

PROJ. REFERENCE NO.	SHEET NO.
U-4700CA	TMP - 1A

LEGEND

GENERAL

- DIRECTION OF TRAFFIC FLOW
- DIRECTION OF PEDESTRIAN TRAFFIC FLOW
- EXIST. PVMT.
- NORTH ARROW
- PROPOSED PVMT.
- TEMP. SHORING (LOCATION PURPOSES ONLY)

- WORK AREA
- REMOVAL
- WEDGING
- TEMPORARY PAVEMENT
- TEMPORARY STONE (ABC)

SIGNALS

- EXISTING
- PROPOSED
- TEMPORARY

PAVEMENT MARKINGS

- EXISTING LINES
- TEMPORARY LINES

TEMPORARY PAVEMENT MARKING

SYMBOL	DESCRIPTION	SYMBOL	DESCRIPTION
PAVEMENT MARKING LINES		PAVEMENT MARKING SYMBOLS & CHARACTERS	
4" PAINT			
P1	WHITE EDGELINE	P70	LEFT TURN ARROW
P2	WHITE SOLID LANE LINE	P71	RIGHT TURN ARROW
P3	10 FT. WHITE SKIP	P72	STRAIGHT ARROW
P4	3 FT. - 9 FT./SP WHITE MINISKIP	P74	COMBO. RIGHT/STRAIGHT ARROW
P5	2 FT. - 6 FT./SP WHITE MINISKIP	P77	U-TURN ARROW
P10	YELLOW EDGELINE		
P13	YELLOW DOUBLE CENTER		
P14	2 FT. - 6 FT./SP YELLOW MINISKIP		
24" PAINT			
P61	WHITE STOPBAR		

TRAFFIC CONTROL DEVICES

- BARRICADE (TYPE III)
- CONE
- DRUM SKINNY DRUM TUBULAR MARKER
- TEMPORARY CRASH CUSHION
- FLASHING ARROW BOARD
- FLAGGER
- LAW ENFORCEMENT
- TRUCK MOUNTED ATTENUATOR (TMA)
- CHANGEABLE MESSAGE SIGN

TEMPORARY SIGNING

- PORTABLE SIGN
- STATIONARY SIGN
- STATIONARY OR PORTABLE SIGN

PAVEMENT MARKERS

- CRYSTAL/CRYSTAL
- CRYSTAL/RED
- YELLOW/YELLOW

PAVEMENT MARKING SYMBOLS

- PAVEMENT MARKING SYMBOLS

ROADWAY STANDARD
DRAWINGS & LEGEND

APPROVED:

DATE: 6/5/2026 | 6:19:46 AM PDT

SEAL

DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED

GENERAL NOTES

LANE AND SHOULDER CLOSURE REQUIREMENTS

- C) REMOVE LANE CLOSURE DEVICES FROM THE LANE WHEN WORK IS NOT BEING PERFORMED BEHIND THE LANE CLOSURE OR WHEN A LANE CLOSURE IS NO LONGER NEEDED OR AS DIRECTED BY THE ENGINEER.
- D) WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING WITHIN 15 FT OF AN OPEN TRAVEL LANE, CLOSE THE NEAREST OPEN SHOULDER USING ROADWAY STANDARD DRAWING NO. 1101.04 UNLESS THE WORK AREA IS PROTECTED BY BARRIER OR GUARDRAIL OR A LANE CLOSURE IS INSTALLED.
- E) WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING WITHIN 5 FT OF AN OPEN TRAVEL LANE ON AN UNDIVIDED FACILITY, CLOSE THE NEAREST OPEN TRAVEL LANE USING ROADWAY STANDARD DRAWING NO. 1101.02 UNLESS THE WORK AREA IS PROTECTED BY BARRIER OR GUARDRAIL.

WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING WITHIN 10 FT OF AN OPEN TRAVEL LANE ON A DIVIDED FACILITY, CLOSE THE NEAREST OPEN TRAVEL LANE USING ROADWAY STANDARD DRAWING NO. 1101.02 UNLESS THE WORK AREA IS PROTECTED BY BARRIER OR GUARDRAIL.

- F) WHEN PERSONNEL AND/OR EQUIPMENT ARE WORKING WITHIN A LANE OF TRAVEL OF AN UNDIVIDED OR DIVIDED FACILITY, CLOSE THE LANE ACCORDING TO THE TRAFFIC CONTROL PLANS, ROADWAY STANDARD DRAWINGS, OR AS DIRECTED BY THE ENGINEER. CONDUCT THE WORK SO THAT ALL PERSONNEL AND/OR EQUIPMENT REMAIN WITHIN THE CLOSED TRAVEL LANE.
- G) DO NOT INSTALL MORE THAN ONE LANE CLOSURE IN ANY ONE DIRECTION ON US 321.

PAVEMENT EDGE DROP OFF REQUIREMENTS

- H) DO NOT EXCEED A DIFFERENCE OF 2 INCHES IN ELEVATION BETWEEN OPEN LANES OF TRAFFIC FOR NOMINAL LIFTS OF 1.5 INCHES. INSTALL ADVANCE WARNING "UNEVEN LANES" SIGNS (W8-11) 500 FT IN ADVANCE AND A MINIMUM OF EVERY HALF MILE THROUGHOUT THE UNEVEN AREA.

TRAFFIC PATTERN ALTERATIONS

- I) NOTIFY THE ENGINEER THIRTY (30) CALENDAR DAYS PRIOR TO ANY TRAFFIC PATTERN ALTERATION.

SIGNING

- J) INSTALL ADVANCE WORK ZONE WARNING SIGNS WHEN WORK IS WITHIN 40 FT FROM THE EDGE OF TRAVEL LANE AND NO MORE THAN THREE (3) DAYS PRIOR TO THE BEGINNING OF CONSTRUCTION.
- K) PROVIDE SIGNING AND DEVICES REQUIRED TO CLOSE THE ROAD ACCORDING TO THE ROADWAY STANDARD DRAWINGS AND TRAFFIC CONTROL PLANS.

PROVIDE SIGNING REQUIRED FOR THE OFF-SITE DETOUR ROUTE AS SHOWN IN THE TRAFFIC CONTROL PLANS.
- L) ENSURE ALL NECESSARY SIGNING IS IN PLACE PRIOR TO ALTERING ANY TRAFFIC PATTERN.
- M) INSTALL BLACK ON ORANGE "DIP" SIGNS (W8-2) AND/OR "BUMP" SIGNS (W8-1) 500 FT IN ADVANCE OF THE UNEVEN AREA, OR AS DIRECTED BY THE ENGINEER.

LOCAL NOTES:

- 1) EMERGENCY VEHICLE ACCESS MUST BE MAINTAINED AT ALL TIMES.
- 2) NOTIFY THE CALDWELL COUNTY SCHOOL BOARD 30 DAYS BEFORE ANY LANE CLOSURES.

TRAFFIC CONTROL DEVICES

- N) WHEN LANE CLOSURES ARE NOT IN EFFECT SPACE CHANNELIZING DEVICES IN WORK AREAS NO GREATER IN FEET THAN TWICE THE POSTED SPEED LIMIT (MPH) EXCEPT, 10 FT ON-CENTER IN RADII, AND 3 FT OFF THE EDGE OF AN OPEN TRAVELWAY. REFER TO STANDARD SPECIFICATIONS FOR ROADS AND STRUCTURES SECTIONS 1130 (DRUMS), 1135 (CONES) AND 1180 (SKINNY DRUMS) FOR ADDITIONAL REQUIREMENTS.
- O) PLACE TYPE III BARRICADES, WITH "ROAD CLOSED" SIGN R11-2 ATTACHED, OF SUFFICIENT LENGTH TO CLOSE ENTIRE ROADWAY.
- P) PLACE ADDITIONAL SETS OF THREE CHANNELIZING DEVICES PERPENDICULAR TO THE EDGE OF TRAVELWAY ON 220 FT CENTERS WHEN UNOPENED LANES ARE CLOSED TO TRAFFIC.

PAVEMENT MARKINGS AND MARKERS

- Q) INSTALL TEMPORARY PAVEMENT MARKINGS AND TEMPORARY PAVEMENT MARKERS ON INTERIM LAYERS OF PAVEMENT AS FOLLOWS:

ROAD NAME	MARKING	MARKER
HICKORY BLVD. (US 321)	PAINT	TEMPORARY RAISED
ALL OTHER ROADS	PAINT	NONE

- R) PLACE ONE APPLICATION OF PAINT FOR TEMPORARY TRAFFIC PATTERNS. PLACE A SECOND APPLICATION OF PAINT SIX (6) MONTHS AFTER THE INITIAL APPLICATION AND EVERY SIX MONTHS AS DIRECTED BY THE ENGINEER.
- S) TIE PROPOSED PAVEMENT MARKING LINES TO EXISTING PAVEMENT MARKING LINES.
- T) REMOVE/REPLACE ANY CONFLICTING/DAMAGED PAVEMENT MARKINGS AND MARKERS BY THE END OF EACH DAY'S OPERATION.
- U) TRACE THE EXISTING AND PROPOSED MONOLITHIC ISLAND LOCATIONS WITH PROPER COLOR PAVEMENT MARKINGS PRIOR TO REMOVAL AND INSTALLATION. PLACE DRUMS TO DELINEATE ANY EXISTING AND PROPOSED MONOLITHIC ISLANDS AFTER REMOVAL AND BEFORE INSTALLATION.

MISCELLANEOUS

- V) LAW ENFORCEMENT MAY BE USED TO MAINTAIN TRAFFIC THROUGH THE WORK AREA AND/OR INTERSECTIONS AS DIRECTED BY THE ENGINEER.
- W) ALL CURB RAMP LOCATIONS SHALL BE DERIVED FROM STATIONING SHOWN ON PAVEMENT MARKING PLANS OR AS DIRECTED BY THE ENGINEER IN COORDINATION WITH THE SIGNING AND DELINEATION UNIT.
- X) WHEN CONSTRUCTING DRAINAGE ADJACENT TO TRAFFIC, INSTALL TEMPORARY STEEL PLATES AS DIRECTED BY THE ENGINEER. WORK IN CONTINUOUS MANNER TO TO PERFORM THE WORK IN THE FOLLOWING SEQUENCE, STEPS 1 THRU 5.


1. CLOSE THE APPROPRIATE TRAVEL LANE TO TRAFFIC USING NCDOT RSD 1101.02
2. CONSTRUCT PROPOSED STRUCTURE OR INSTALL PRE-CAST DRAINAGE STRUCTURE AS SHOWN IN THE CONSTRUCTION PLANS AND COVER WITH STEEL PLATES TO PROTECT STRUCTURE DURING CURING.
3. OPEN TRAVEL LANE TO EXISITING PATTERN BY THE END OF EACH WORK PERIOD.
4. WHEN PROPERLY CURED, CLOSE THE APPROPRIATE TRAVEL LANE USING NCDOT RSD 1101.02, BACKFILL AND PAVE, IF REQUIRED, UP TO THE EDGE AND ELEVATION OF EXISITING PAVEMENT (SEE CONSTRUCTION PLANS.)
5. OPEN TRAVEL LANE TO EXISITING TRAFFIC PATTERN BY THE END OF THE WORK PERIOD.
- Y) CONTRACTOR IS TO MAINTAIN PEDESTRIAN TRAFFIC AT ALL TIMES AND PROVIDE APPROPRIATE TRAFFIC CONTROL ACCORDING TO ADA COMPLIANCE AND AS REQUIRED BY THE ENGINEER.


APPROVED: _____


DATE: 6/5/2026 | 6:19:46 AM PDT

SEAL



DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED

Signed by: 
0A82B26F320D4421






TRANSPORTATION
OPERATIONS
PLAN

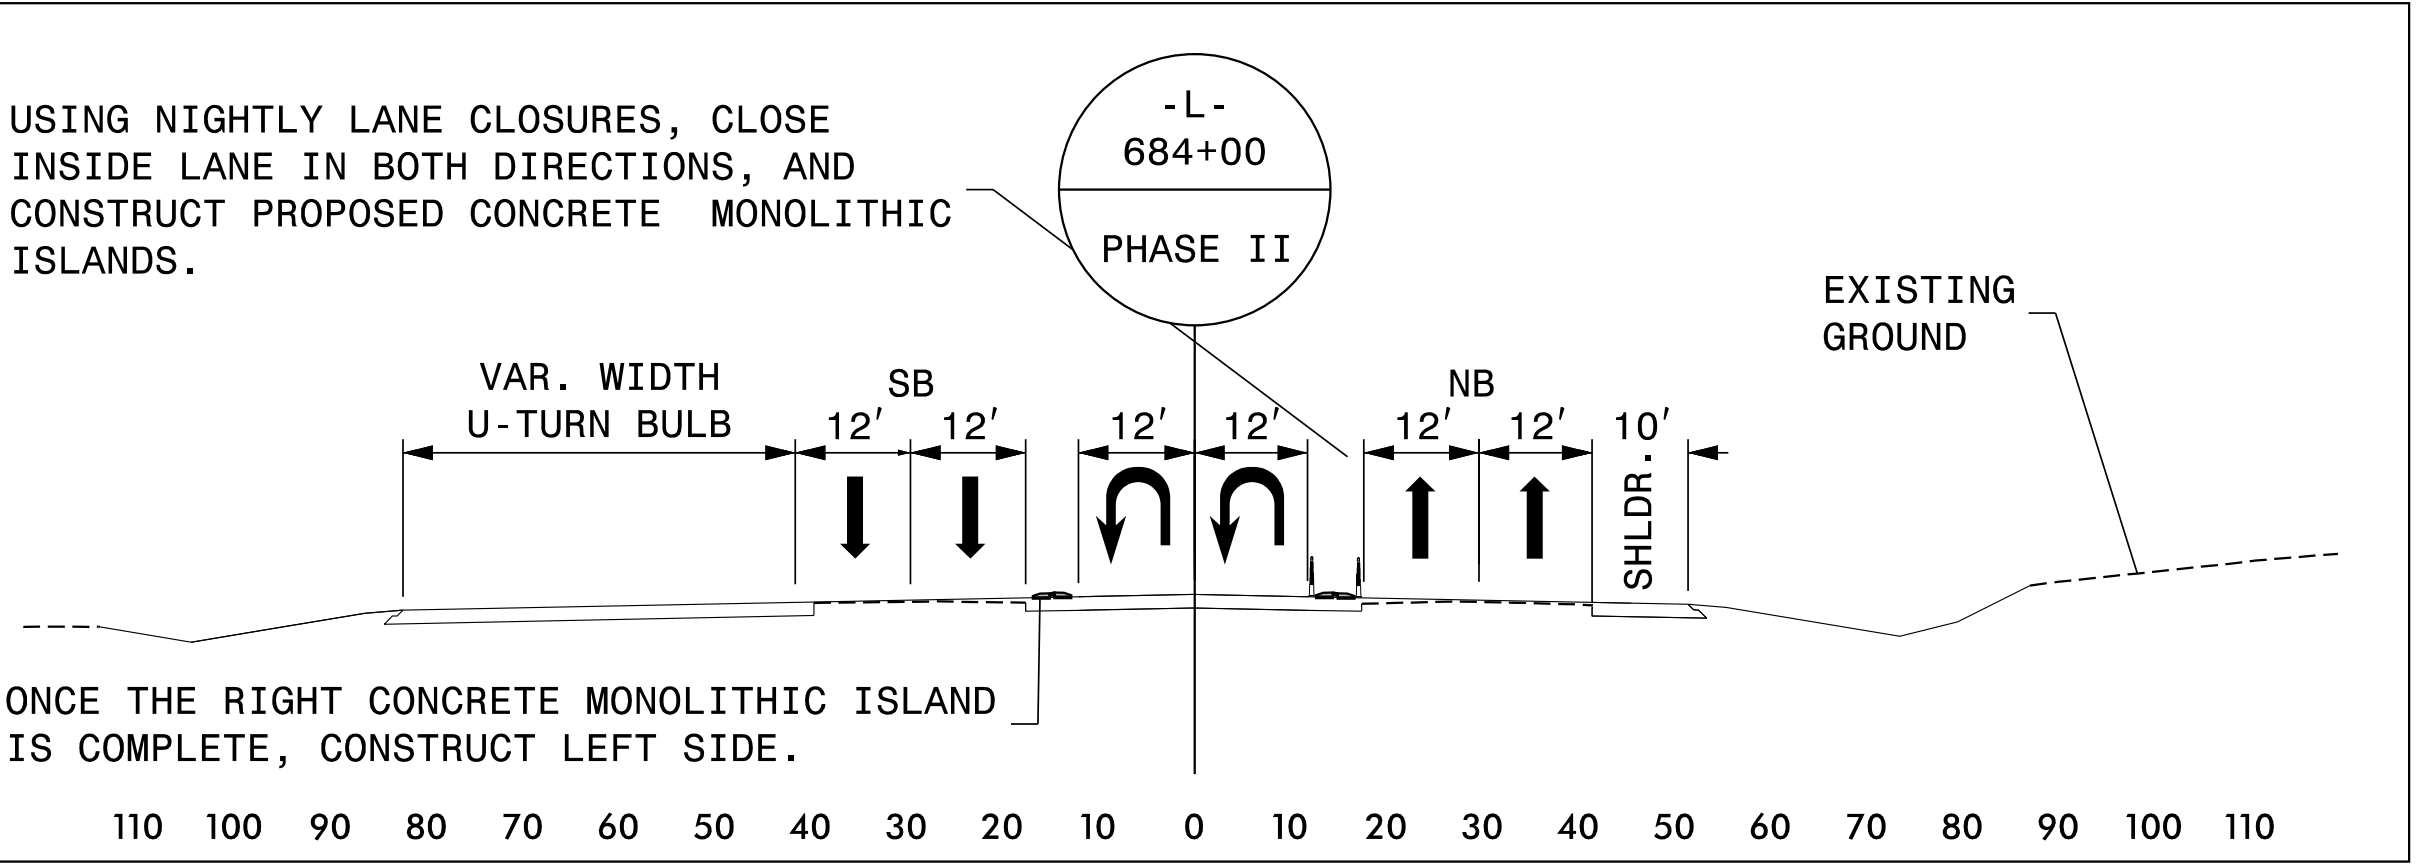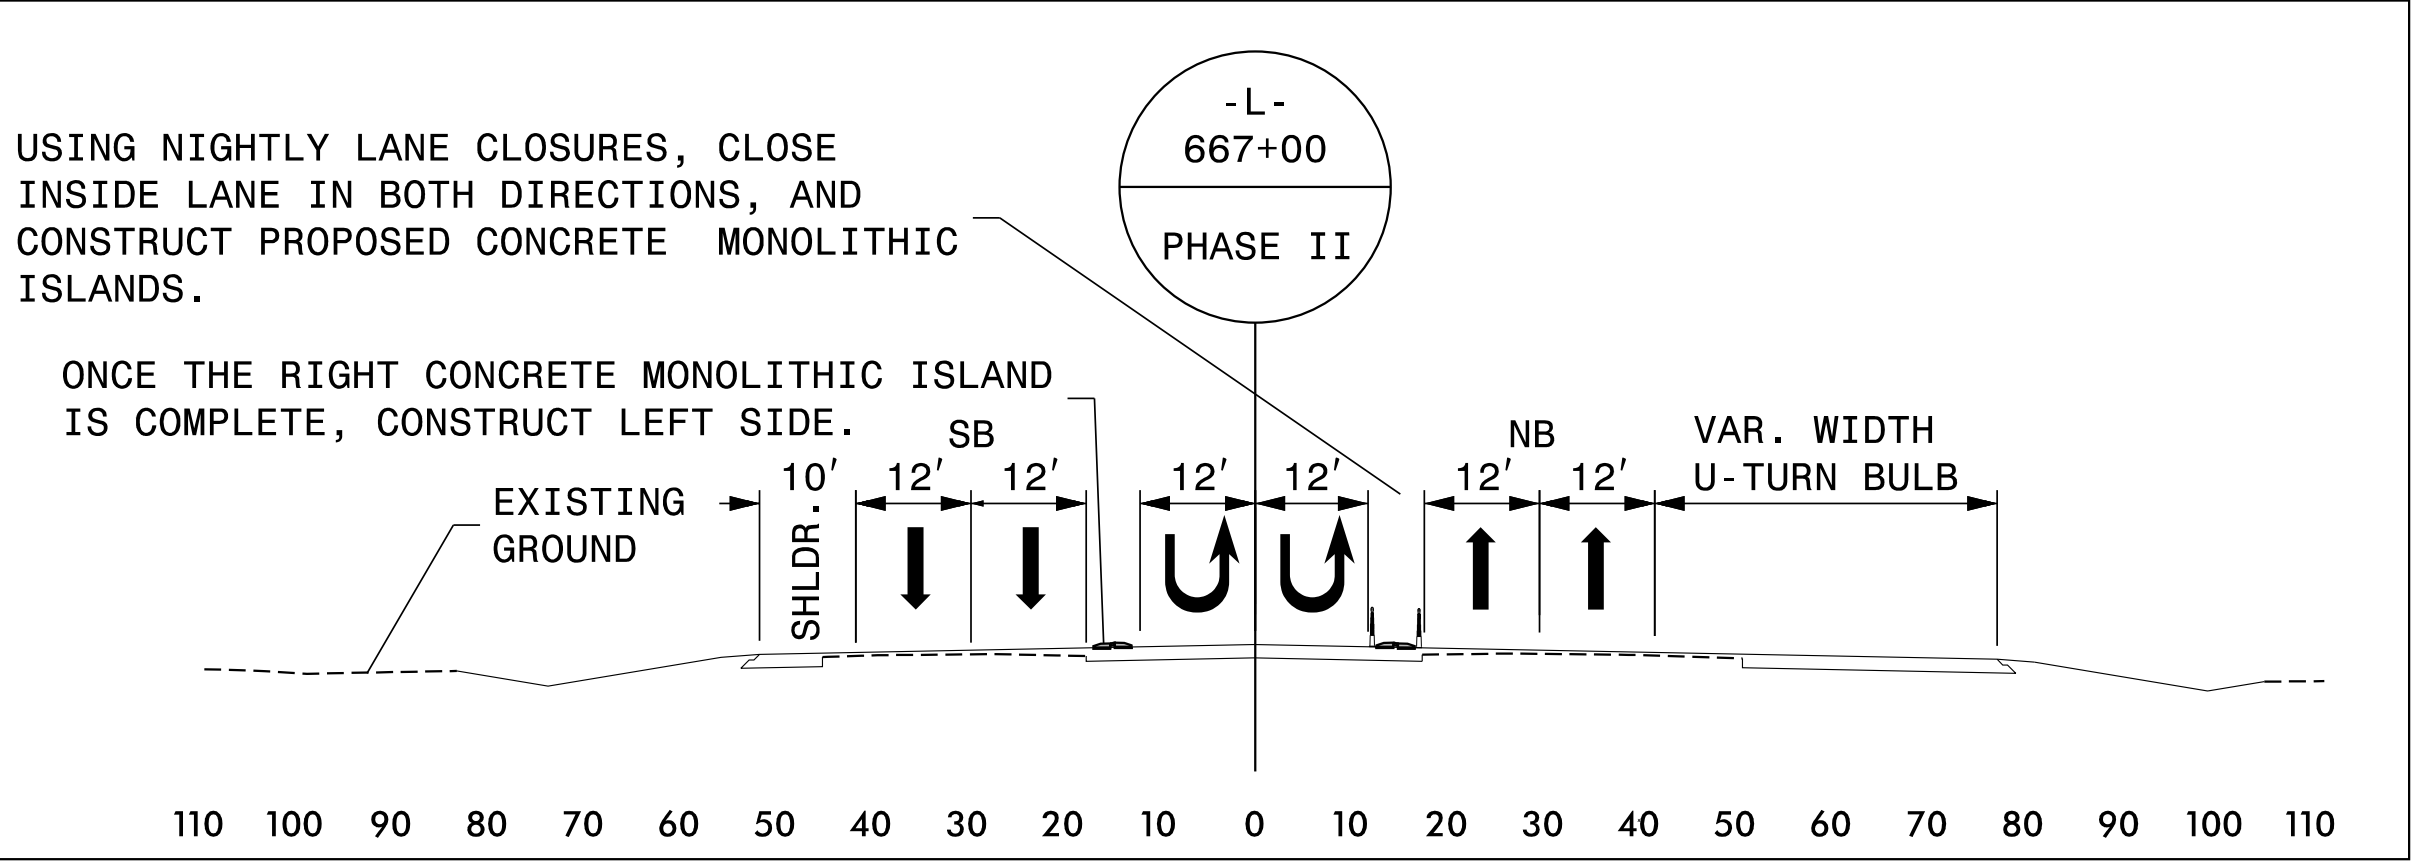

5/6/2026 2:46:55 PM
...\\TCP\\U4700CA_TMP-2.dgn
User:cmiddle



APPROVED: _____ DATE: 6/5/2026 6:19:46 AM PDT SEAL  DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED		TYPICAL SECTIONS
---	---	------------------------------------

PROJ. REFERENCE NO.	SHEET NO.
U-4700CA	TMP-3

PHASING

REPLACE MARKINGS AND RETURN TO THE CURRENT TRAFFIC PATTERN AT THE END OF EACH WORK PERIOD UNLESS OTHERWISE NOTED IN THE PHASING OR DIRECTED BY THE ENGINEER.

MAINTAIN VEHICULAR ACCESS TO ALL RESIDENCES AND BUSINESS DURING THE LIFE OF THE CONTRACT UNLESS OTHERWISE NOTED IN THE PHASING OR DIRECTED BY THE ENGINEER.

PAVE PROPOSED CONSTRUCTION UP TO BUT NOT INCLUDING THE FINAL LAYER OF SURFACE COURSE, IN ALL PHASES UNTIL STATED TO INSTALL THE FINAL LAYER OF SURFACE COURSE.

PHASE I

STEP 1: - ERECT WORK ZONE ADVANCED WARNING SIGNS USING ROADWAY STANDARD DRAWINGS NO. 1101.01, SHEETS 2 & 3 OF 3.

NOTE: STEP 2 SHALL BE COMPLETED IN A CONTINUOUS OPERATION.

- STEP 2: - USING NARROW LANES AND ROADWAY STANDARD DRAWINGS NO. 1101.02, SHEETS 1,3 & 7 OF 19, AND FLAGGERS AS NECESSARY, PERFORM THE FOLLOWING (SEE SHEETS TMP-5 THRU TMP-7):
- MILL -L- US 321 (HICKORY BLVD.) FROM -L- STA. 664+20 +/- TO -L- STA. 665+20+/- AND FROM -L- STA. 685+57 +/- TO -L- STA. 686+57 +/-, AND -Y- SR 1160 (MT. HERMAN RD.) FROM -Y- STA. 10+00 +/- TO -Y- STA. 10+50 +/-, AND FROM -Y- STA. 13+90 +/- TO -Y- STA. 15+50 +/-.
 - WIDEN AND/OR WEDGE (AND INSTALL DRAINAGE) ALONG -L- US 321 (HICKORY BLVD.) FROM -L- STA. 664+20 +/- TO -L- STA. 686+57 +/-, AND -Y- SR 1160 (MT. HERMAN RD.) FROM -Y- STA. 10+00 +/- TO -Y- STA. 15+50 +/-.
 - REMOVE EXISTING PAVEMENT AS NECESSARY, OR AS DIRECTED BY THE ENGINEER.

NOTE: MAINTAIN ORIGINAL TRAFFIC PATTERN AT THE END OF EACH WORK PERIOD UNTIL ALL OF PHASE I WORK IS COMPLETE.

PHASE II

STEP 1: - AWAY FROM TRAFFIC, CONSTRUCT SIDEWALKS AS SHOWN ON THE ROADWAY PLANS.

NOTE: MAINTAIN CLOSURE OF PROPOSED PEDESTRIAN FACILITIES DURING CONSTRUCTION AND/OR UNTIL CONNECTIVITY CAN BE MAINTAINED.

STEP 2: - USING NARROW LANES AND ROADWAY STANDARD DRAWINGS NO. 1101.02, SHEETS 1,3 & 7 OF 19, AND FLAGGERS AS NECESSARY, CONSTRUCT CONCRETE MONOLITHIC ISLANDS ALONG -L- US 321 (HICKORY BLVD.), AND -Y- SR 1160 (MT. HERMAN RD.) AND COMPLETE CONCRETE MEDIAN DRAINAGE INSTALLATION (SEE SHEETS TMP-7 THRU TMP-9).

NOTE: PLACE SKINNY DRUMS ALONG OUTSIDE EDGE OF CONCRETE ISLANDS AT THE END OF EACH WORK PERIOD, WHEN LANE CLOSURES ARE NO LONGER IN EFFECT.

STEP 3: - USING NARROW LANES AND ROADWAY STANDARD DRAWINGS NO. 1101.02, SHEETS 1,3 & 7 OF 19, AND FLAGGERS AS NECESSARY, PLACE FINAL LAYER OF SURFACE COURSE AND TEMPORARY PAVEMENT MARKINGS AND MARKERS, AND SHIFT TRAFFIC TO PHASE II TRAFFIC PATTERNS (SEE SHEETS TMP-7 THRU TMP-9).



NOTE: UTILIZE SKINNY DRUMS TO DESIGNATE PROPOSED CONCRETE MONOLITHIC ISLANDS UNTIL CONSTRUCTION IS COMPLETE.

STEP 4: - USING NARROW LANES AND ROADWAY STANDARD DRAWINGS NO. 1101.02, SHEETS 1,3 & 7 OF 19, AND FLAGGERS AS NECESSARY, COMPLETE ALL REMAINING WORK AND PLACE FINAL PAVEMENT MARKINGS AND MARKERS (SEE FINAL PAVEMENT MARKING PLANS).

STEP 5: - REMOVE ALL TRAFFIC CONTROL DEVICES.





Johnson, Mirmiran, & Thompson Inc.
4700 Falls of Neuse Rd, Suite 100,
Raleigh, NC, 27609
License No: C-3097

APPROVED: _____	Signed by:  6A8D86CF3D844404
DATE: 6/5/2026 6:19:46 AM PDT	
SEAL	
DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED	




TEMPORARY TRAFFIC
CONTROL PHASING

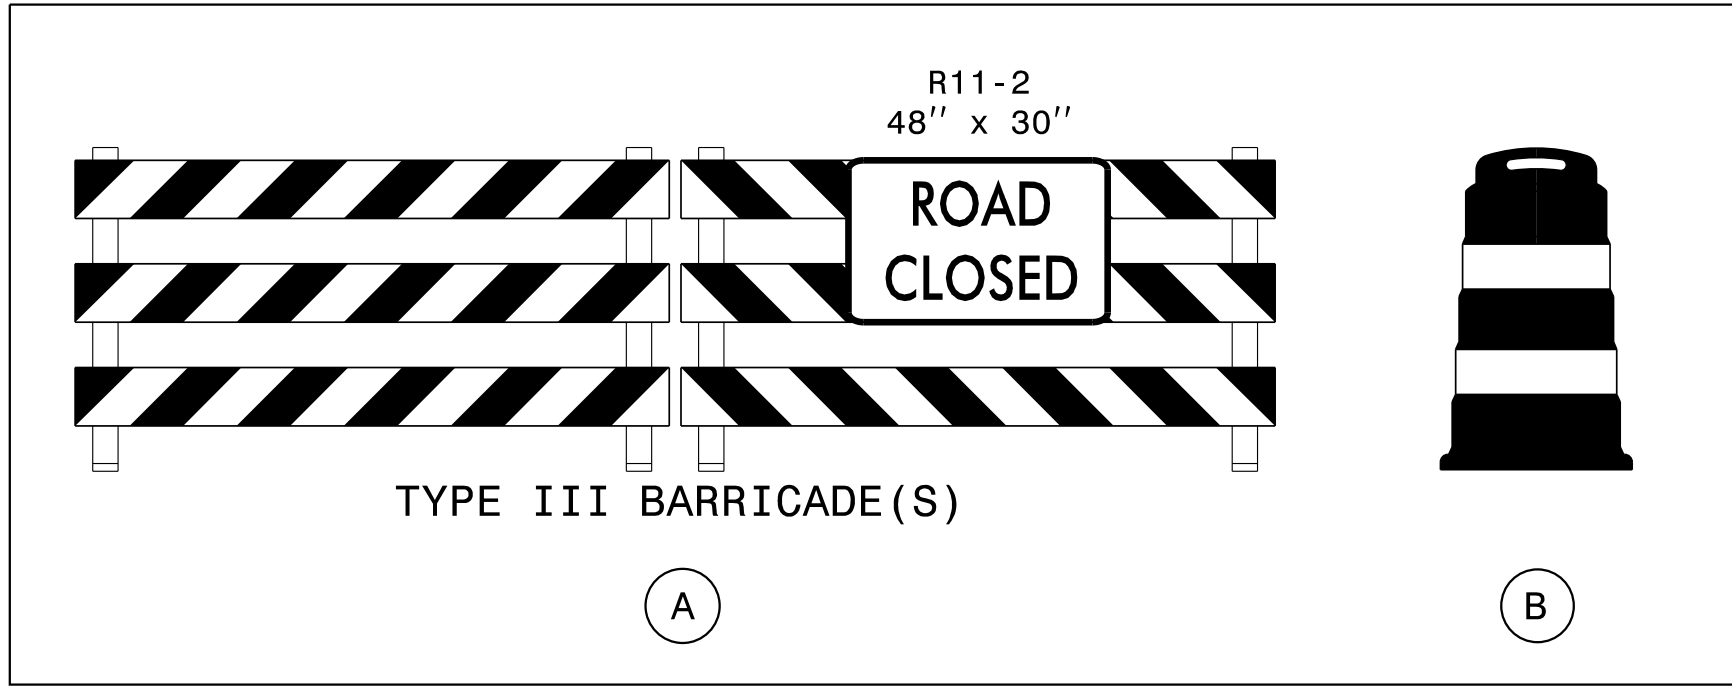

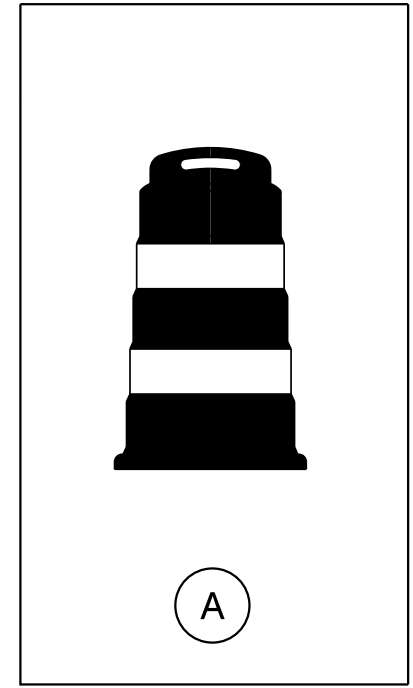

680



MATCHLINE -L- STA. 670+00.00
SEE SHEET TMP-4

MATCHLINE -L- STA. 682+00.00
SEE SHEET TMP-6

5/6/2026 2:57:42 PM
...\\TCP\\U4700CA_TMP-5.dgn
User:cmriddle




Johnson, Mirmiran, & Thompson Inc.
4700 Falls of Neuse Rd, Suite 100,
Raleigh, NC, 27609
License No: C-3097


APPROVED: _____

DATE: 6/5/2026 | 6:19:46 AM PDT

SEAL





**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**



TEMPORARY TRAFFIC CONTROL PHASE I DETAIL

PROJ. REFERENCE NO.	SHEET NO.
U-4700CA	TMP-6

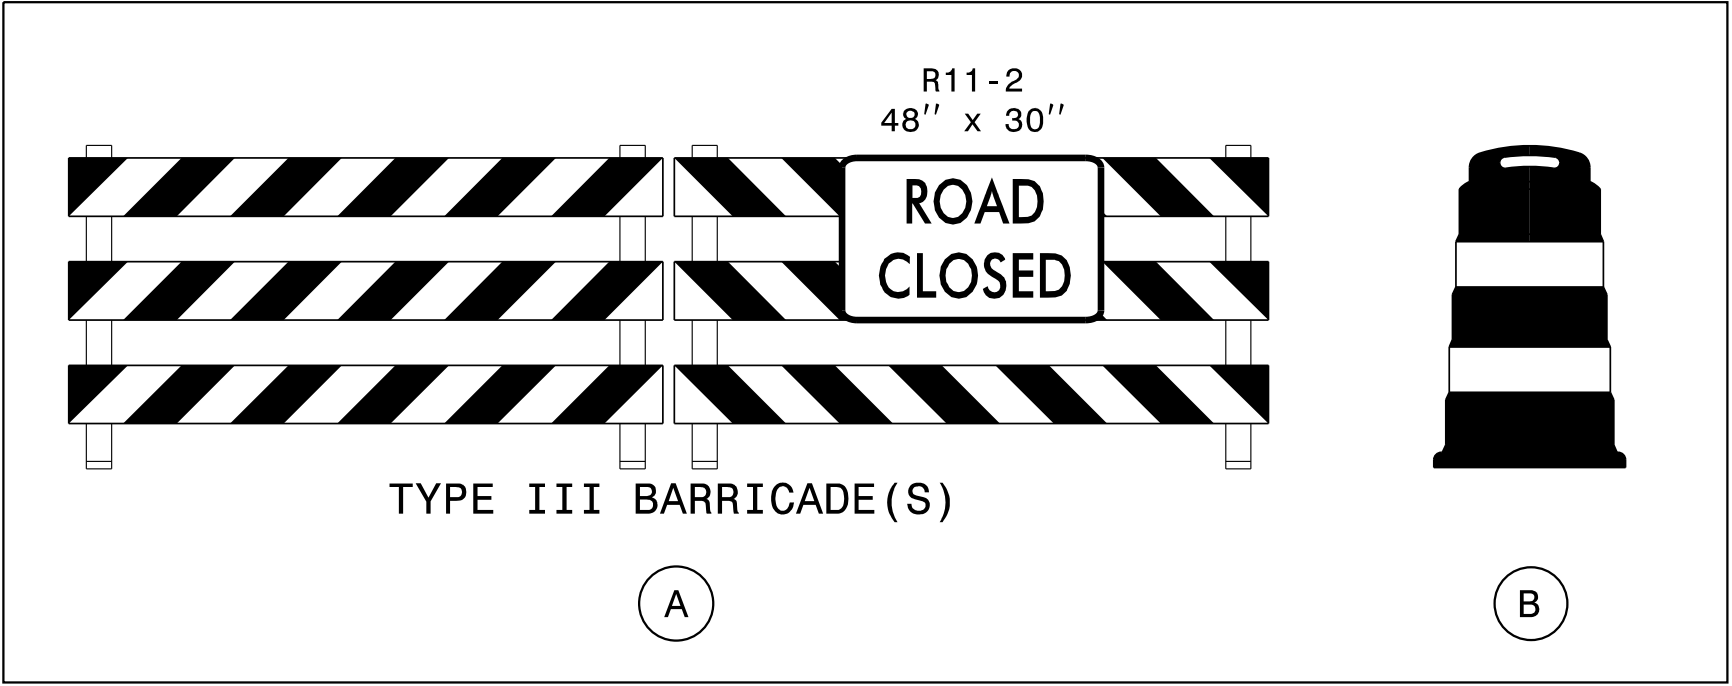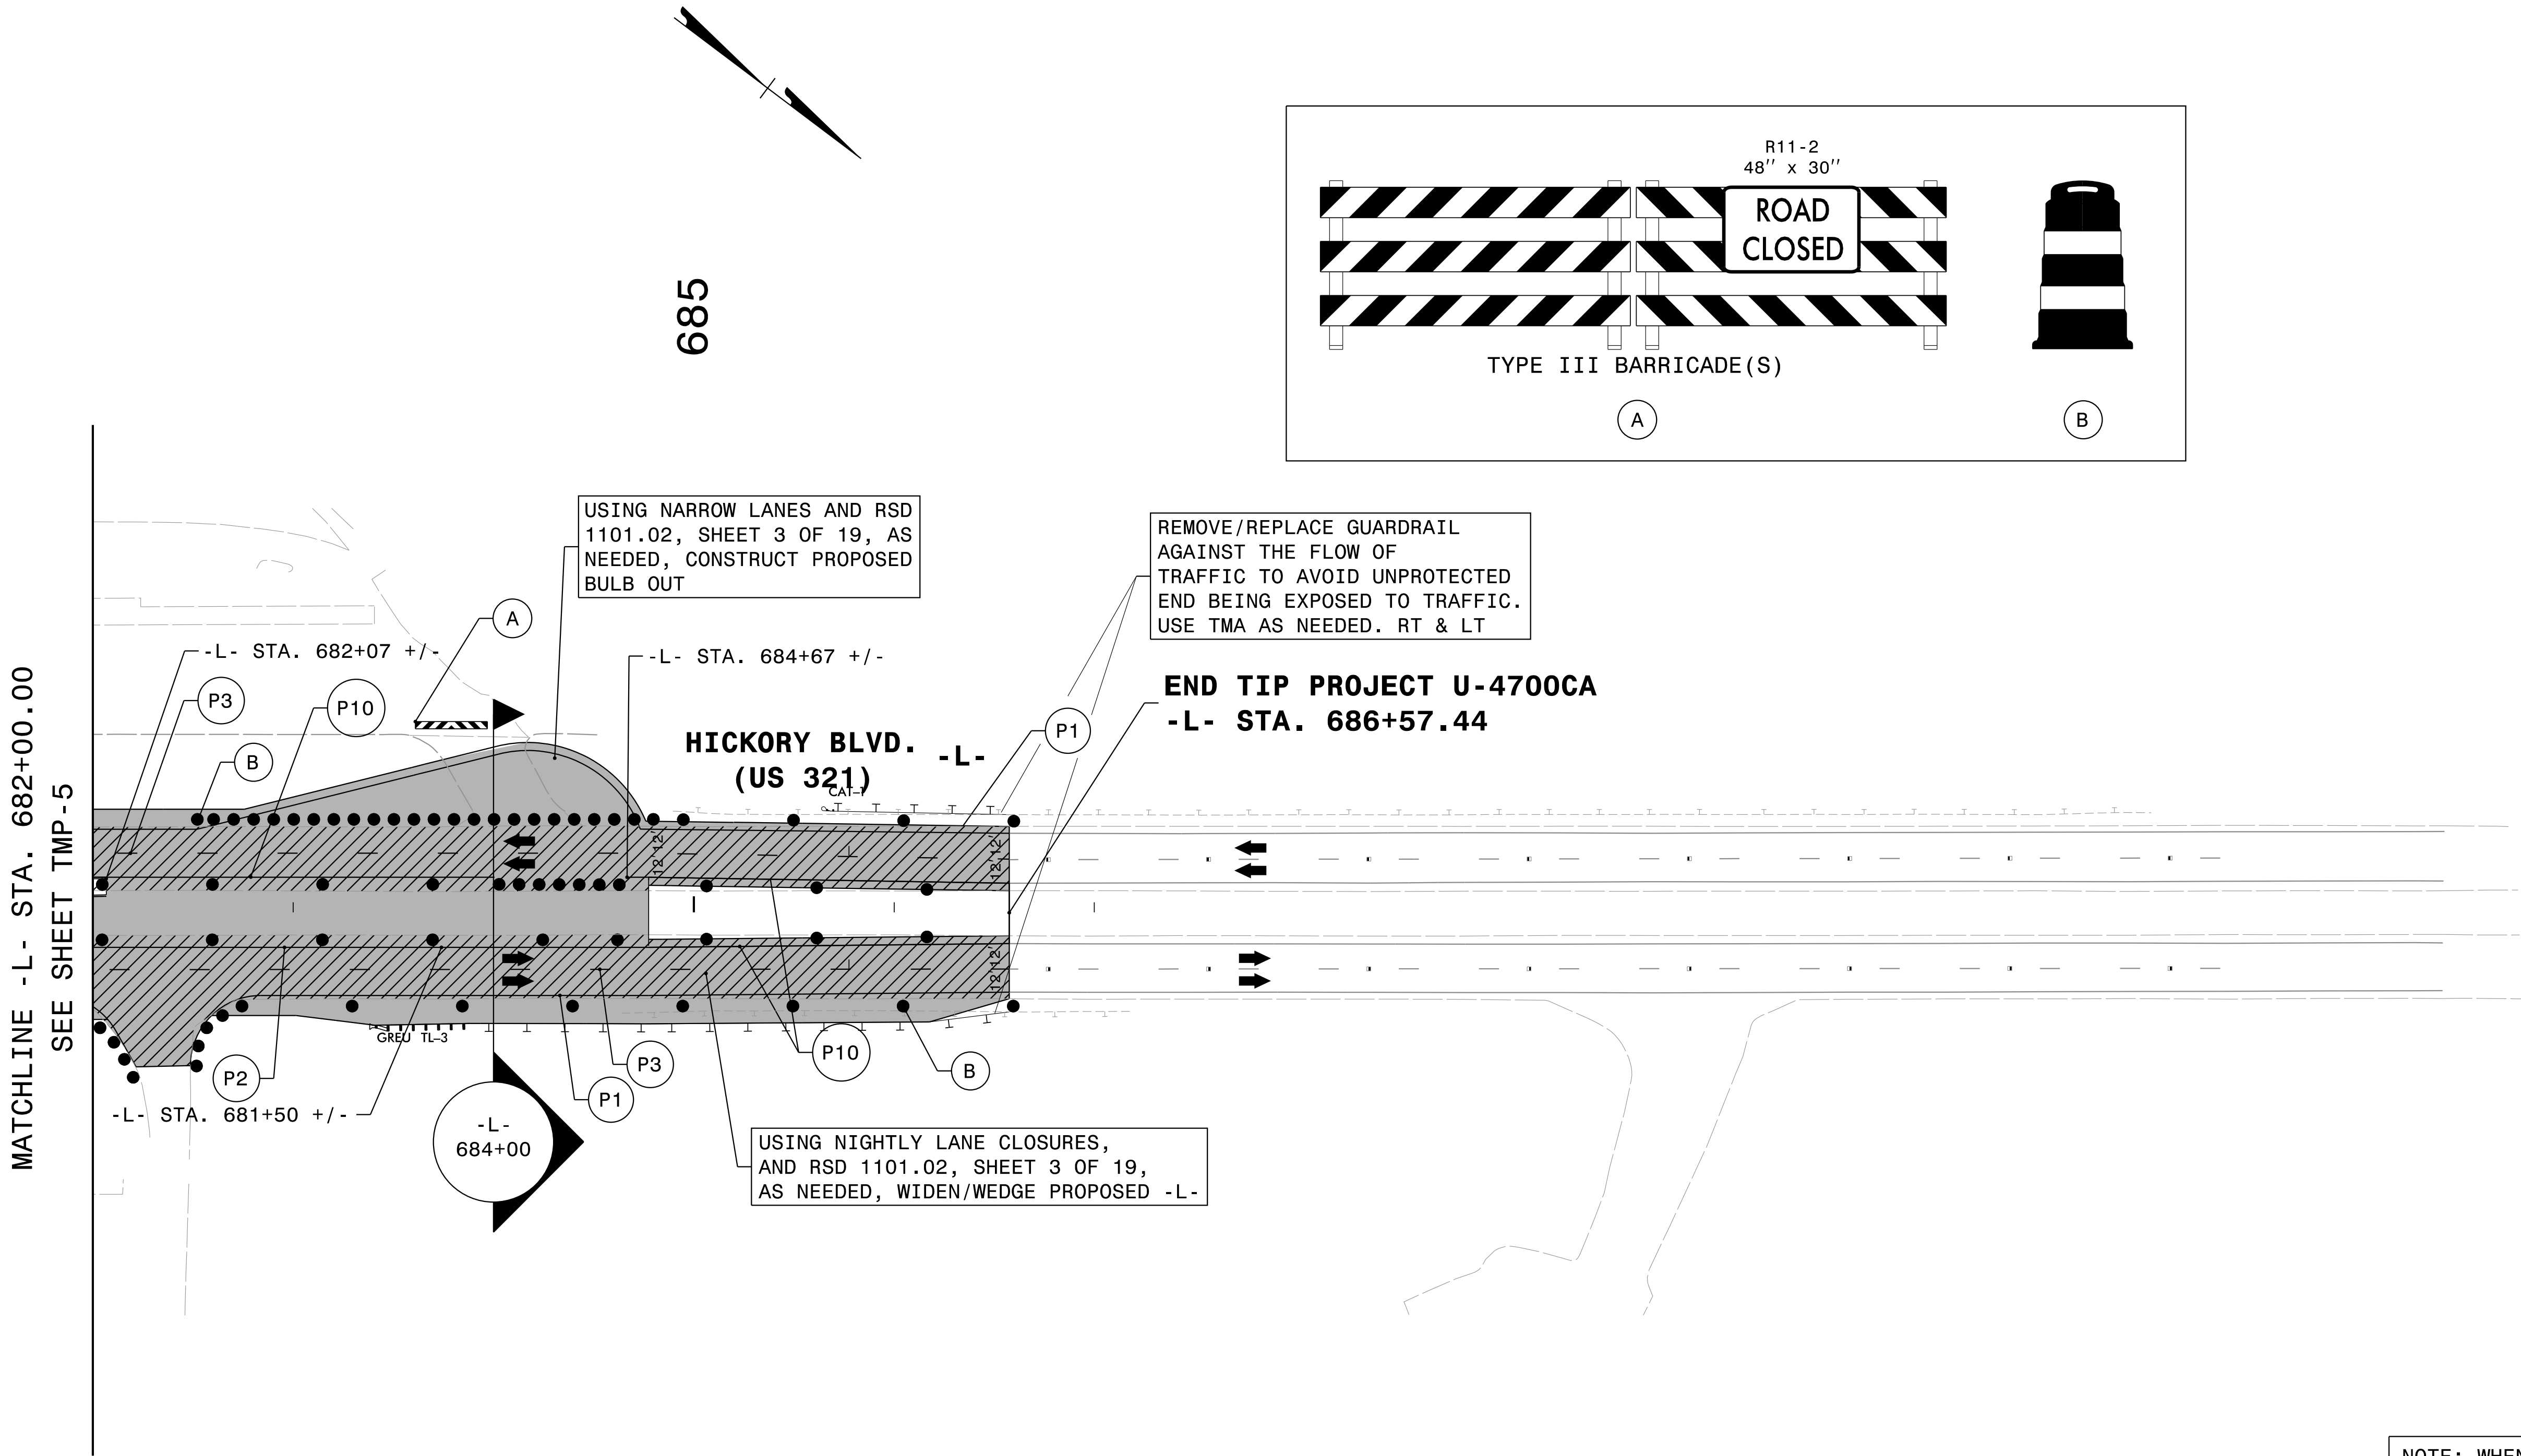

NOTE: WHEN REMOVING AND REPLACING GUARDRAIL ENSURE NO UNPROTECTED END IS EXPOSED TO TRAFFIC.

5/6/2026 2:57:23 PM
...\\TCP\\U4700CA-TMP-6.dgn
User:cmriddle


JMT
Johnson, Mirmiran, & Thompson Inc.
4700 Falls of Neuse Rd, Suite 100,
Raleigh, NC, 27609
License No: C-3097

APPROVED: _____
DATE: 6/5/2026 | 6:19:46 AM PDT


SEAL

Seal: NORTH CAROLINA PROFESSIONAL ENGINEER SEAL 046062 CHARLES J. YOUNG

DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED



TEMPORARY TRAFFIC
CONTROL PHASE I
DETAIL




**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**



TEMPORARY TRAFFIC CONTROL PHASE II DETAIL

PROJ. REFERENCE NO.	SHEET NO.
U-4700CA	TMP-8

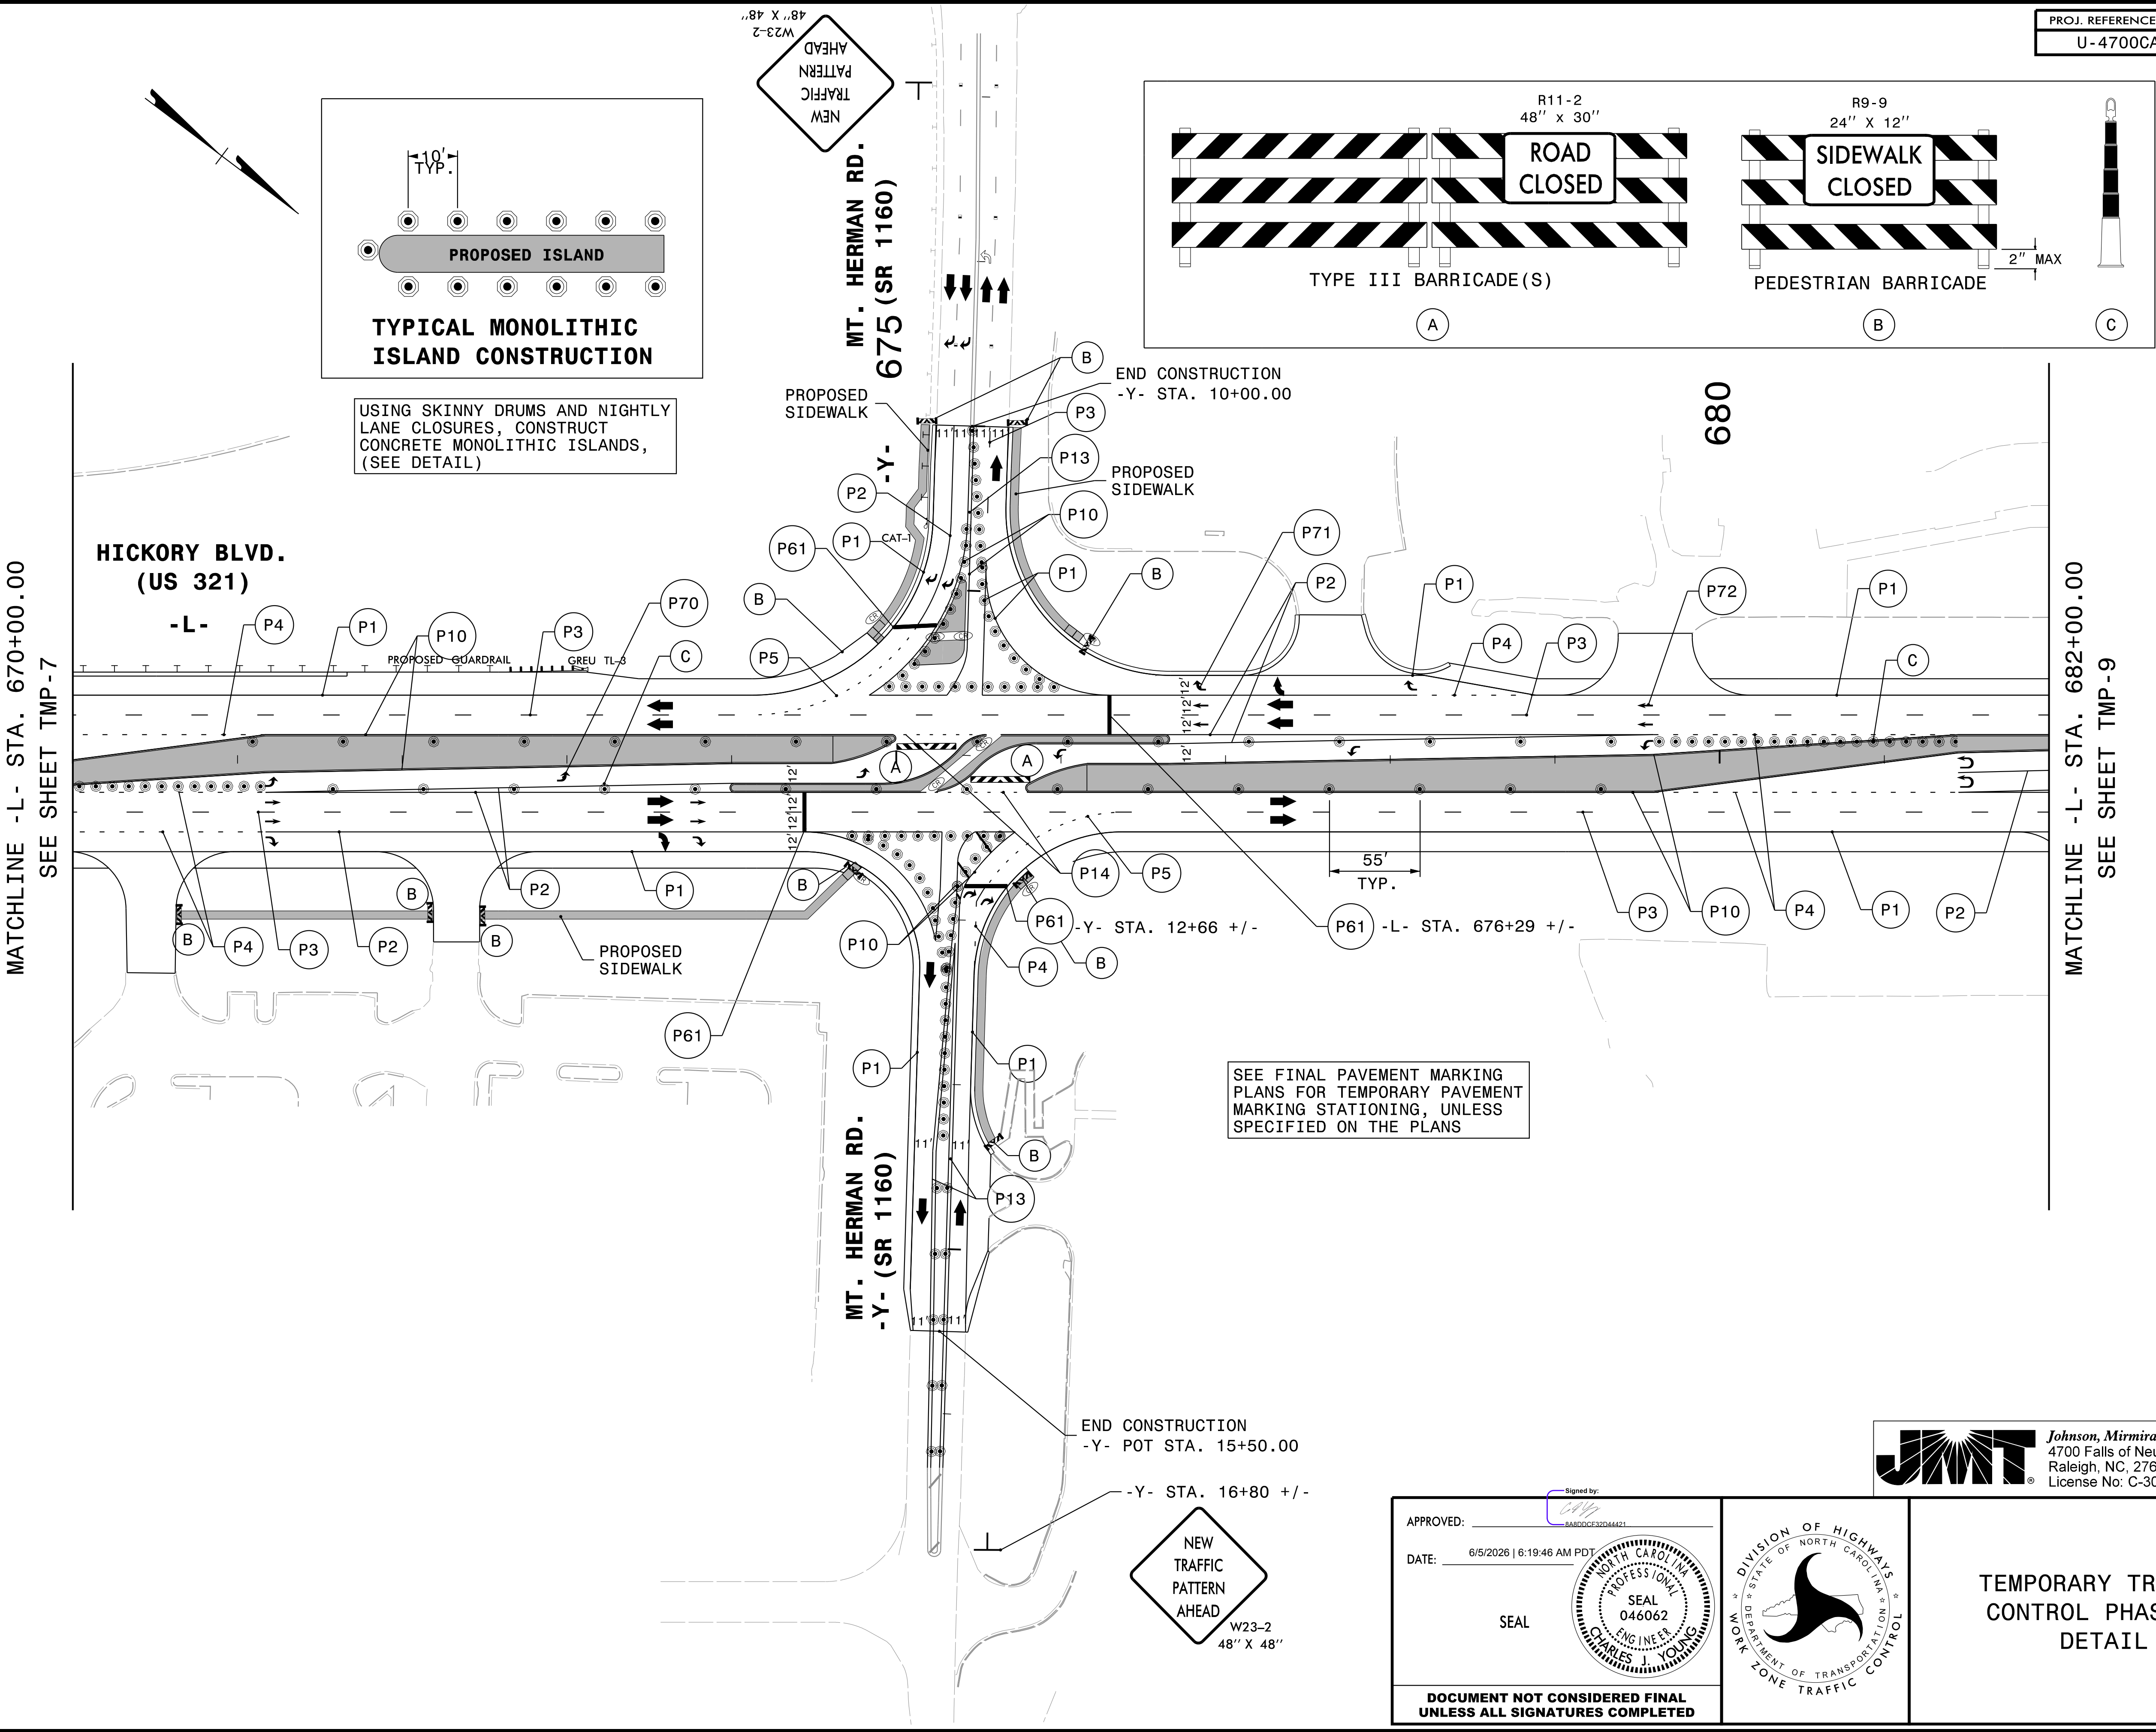




Johnson, Mirmiran, & Thompson, Inc.
4700 Falls of Neuse Rd, Suite 100,
Raleigh, NC, 27609
License No: C-3097


APPROVED: _____
DATE: 6/5/2026 | 6:19:46 AM PDT
SEAL

Signed by:

8A8DDCE32D44421




**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**



**TEMPORARY TRAFFIC
CONTROL PHASE II
DETAIL**


PROJ. REFERENCE NO.	SHEET NO.
U-4700CA	TMP-9

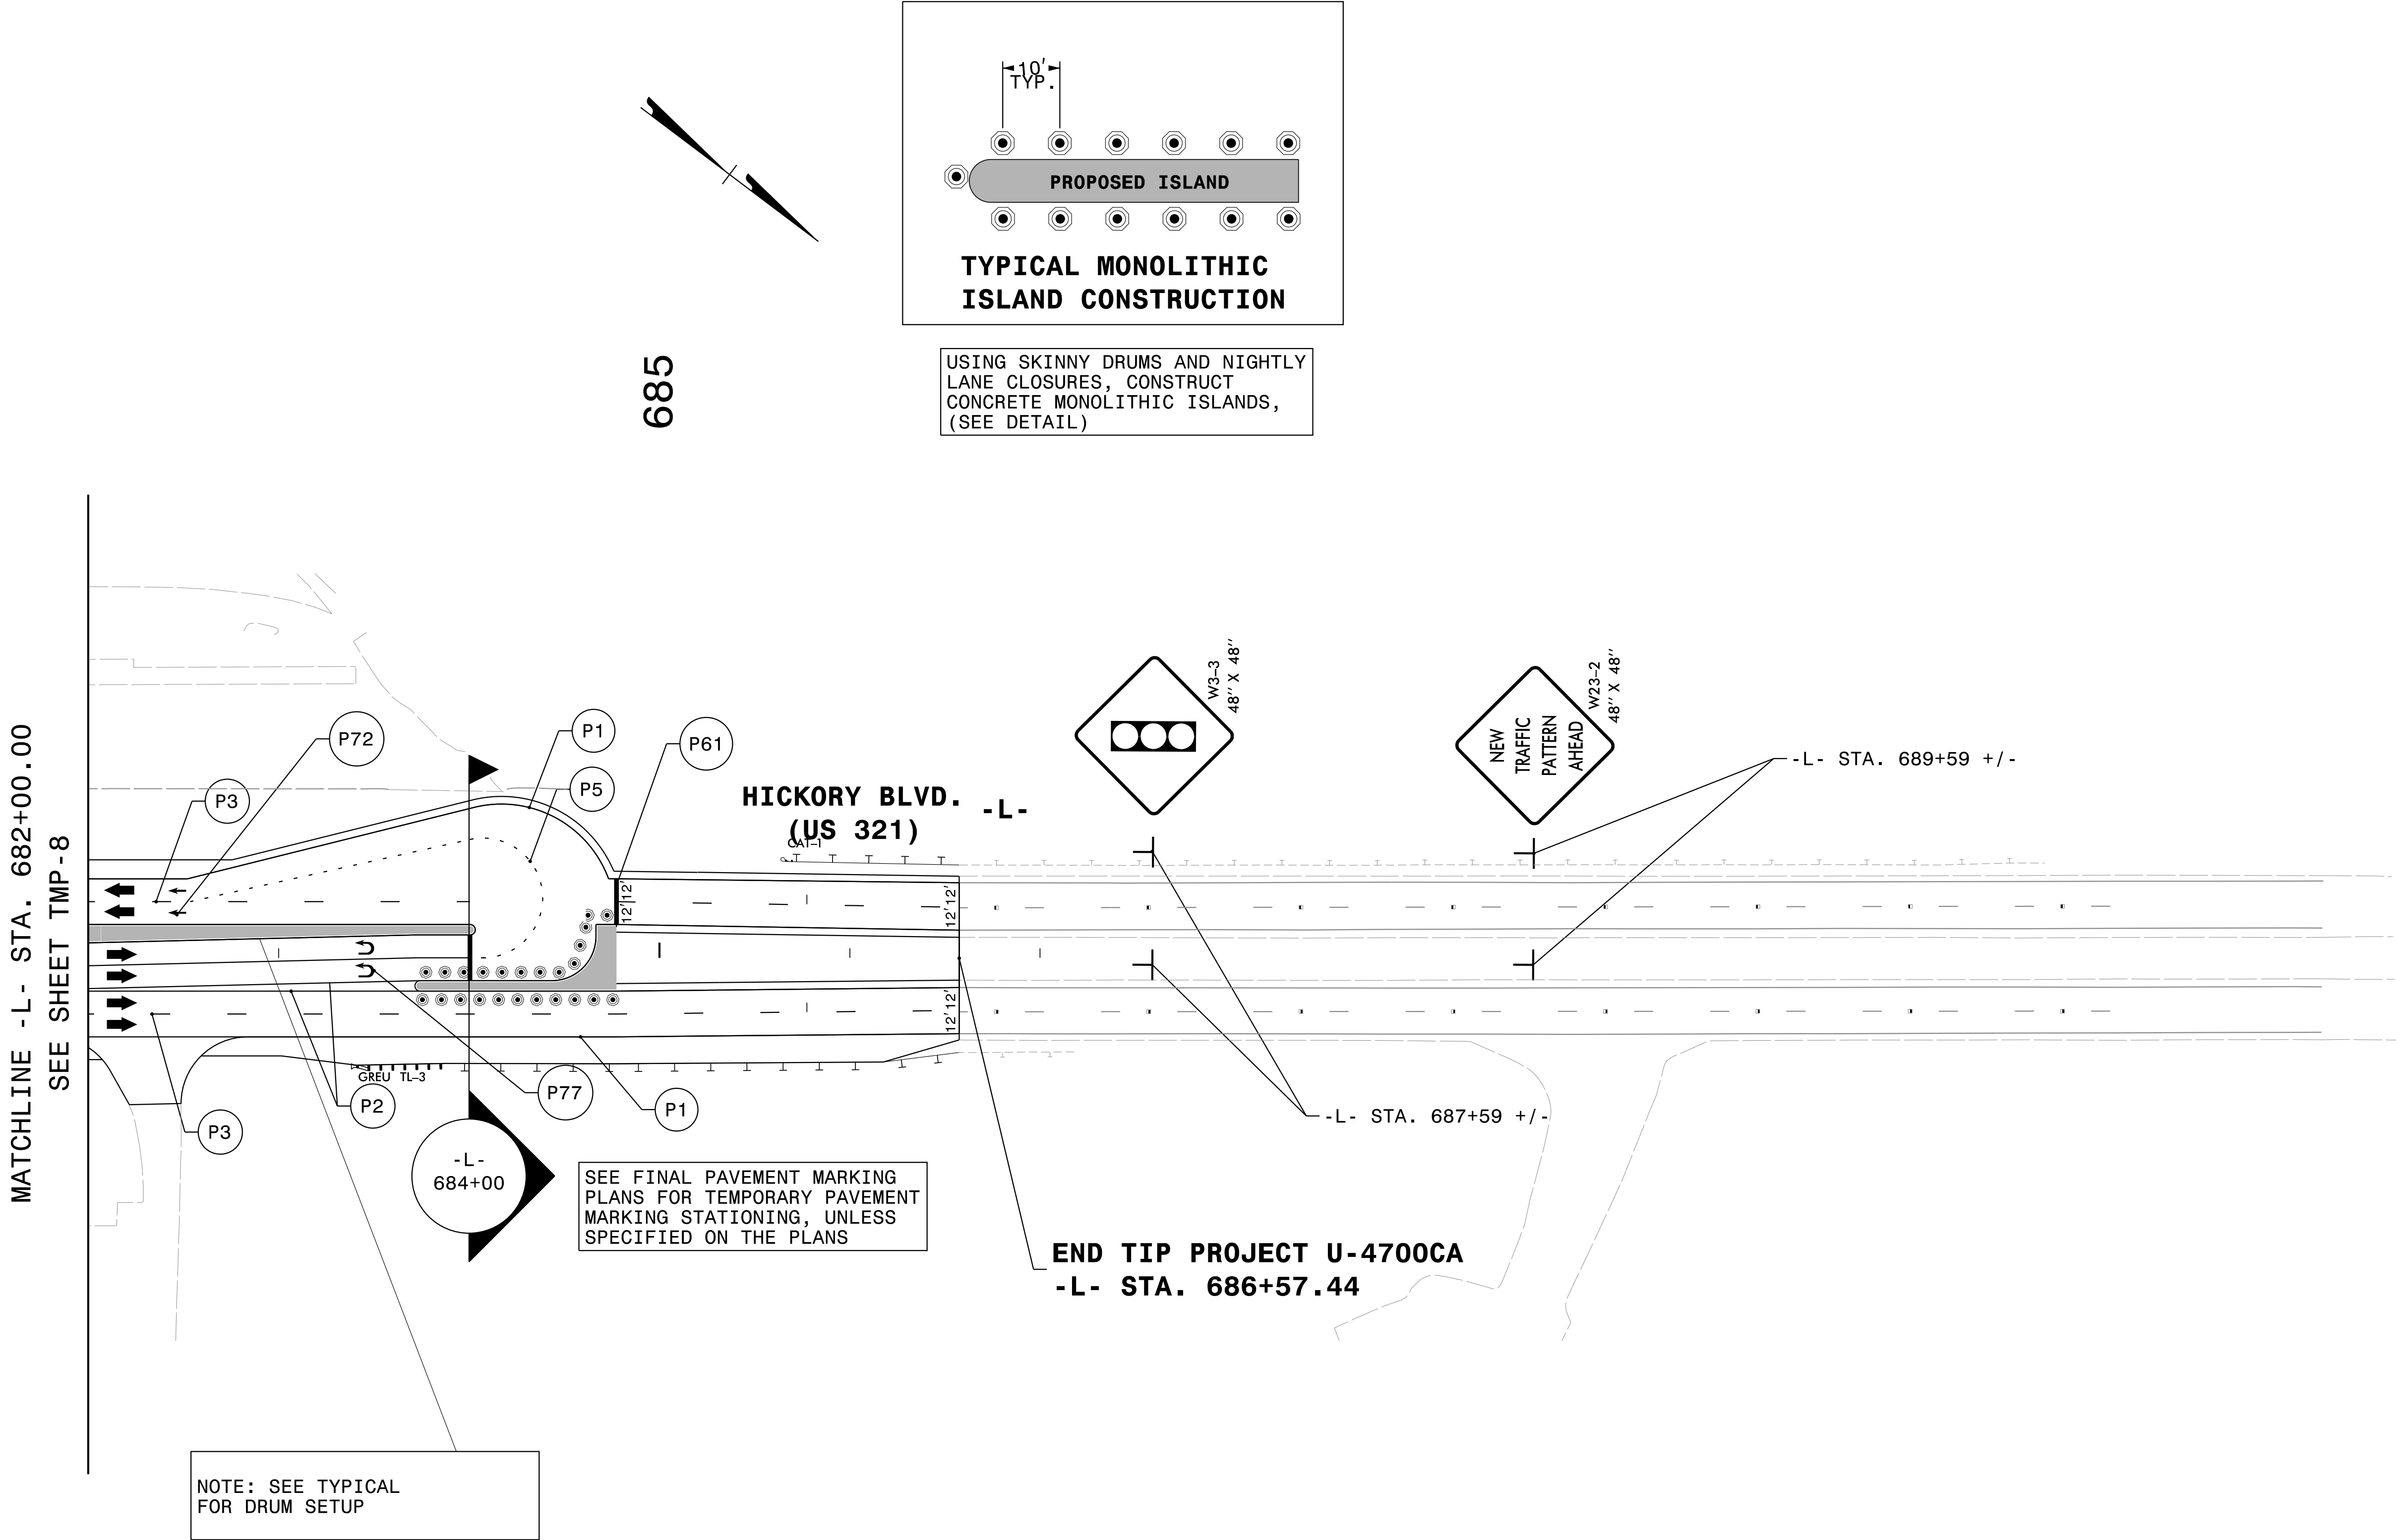

5/6/2026 3:33:17 PM
...\\TCP\\U4700CA_TMP-9.dgn
User:cmriddle


JMT
Johnson, Mirmiran, & Thompson Inc.
4700 Falls of Neuse Rd, Suite 100,
Raleigh, NC, 27609
License No: C-3097

APPROVED: _____
DATE: 6/5/2026 | 6:19:46 AM PDT

SEAL


Signed by: _____
0480DC932D44421...

DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED



TEMPORARY TRAFFIC
CONTROL PHASE II
DETAIL
