

SPAN A


SPAN C

NOTES

PAYMENT FOR CLASS II SURFACE PREPARATION IS BASED ON THE SQUARE FEET OF ADDITIONAL DEMOLITION REQUIRED FOLLOWING INITIAL HYDRO-DEMOLITION OF THE BRIDGE DECK. SEE SPECIAL PROVISIONS.


REPAIR LOCATIONS AND ESTIMATED QUANTITIES ARE BASED ON THE BEST INFORMATION AVAILABLE. IF ADDITIONAL REPAIRS NOT SHOWN ON THE DRAWINGS ARE DEEMED NECESSARY BY THE ENGINEER, THE ENGINEER WILL NOTE ON THE DRAWINGS THE APPROXIMATE LOCATIONS AND DESCRIPTION OF THE REPAIRS AND ENTER THE ACTUAL QUANTITIES INTO THE AS-BUILT REPAIR QUANTITY TABLE.

FOR SECTION A-A, AND B-B. SEE "JOINT DETAILS LMC OVERLAY", SHEET.

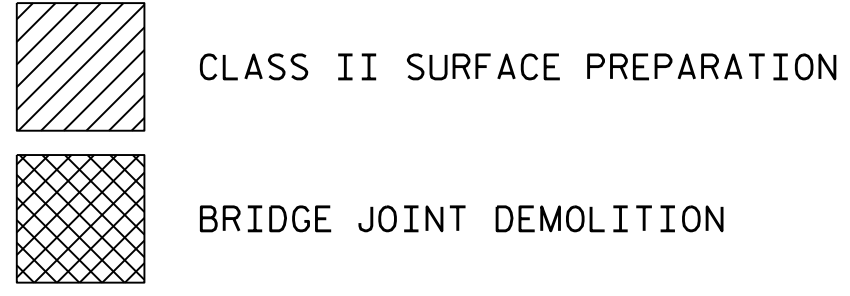

AS-BUILT REPAIR QUANTITY TABLE		
DECK SURFACE REPAIR SPAN A		
	ESTIMATE	ACTUAL
CONCRETE FOR DECK REPAIR	2.9 CU. FT.	
CLASS II SURFACE PREPARATION	1.3 SQ. YDS.	
LMC-ES MATERIALS	9.7 CU. YDS.	
PLACING & FINISHING LMC-ES OVERLAY	233.0 SQ. YDS.	
SCARIFYING BRIDGE DECK	233.0 SQ. YDS.	
HYDRO-DEMOLITION OF BRIDGE DECK	233.0 SQ. YDS.	
GROOVING BRIDGE FLOORS	1979.8 SQ. FT.	
BRIDGE JOINT DEMOLITION	34.0 SQ. FT.	
APPROACH SLAB		
	ESTIMATE	ACTUAL
CONCRETE FOR DECK REPAIR	0.0 CU. FT.	
CLASS II SURFACE PREPARATION	0.0 SQ. YDS.	
LMC-ES MATERIALS	2.9 CU. YDS.	
PLACING & FINISHING LMC-ES OVERLAY	69.6 SQ. YDS.	
SCARIFYING BRIDGE DECK	69.6 SQ. YDS.	
HYDRO-DEMOLITION OF BRIDGE DECK	69.6 SQ. YDS.	
GROOVING BRIDGE FLOORS	571.8 SQ. FT.	
AS-BUILT REPAIR QUANTITY TABLE		
DECK SURFACE REPAIR SPAN C		
	ESTIMATE	ACTUAL
CONCRETE FOR DECK REPAIR	0.0 CU. FT.	
CLASS II SURFACE PREPARATION	0.0 SQ. YDS.	
LMC-ES MATERIALS	14.9 CU. YDS.	
PLACING & FINISHING LMC-ES OVERLAY	357.6 SQ. YDS.	
SCARIFYING BRIDGE DECK	357.6 SQ. YDS.	
HYDRO-DEMOLITION OF BRIDGE DECK	357.6 SQ. YDS.	
GROOVING BRIDGE FLOORS	2863.8 SQ. FT.	
BRIDGE JOINT DEMOLITION	34.0 SQ. FT.	
APPROACH SLAB		
	ESTIMATE	ACTUAL
CONCRETE FOR DECK REPAIR	3.5 CU. FT.	
CLASS II SURFACE PREPARATION	1.6 SQ. YDS.	
LMC-ES MATERIALS	3.1 CU. YDS.	
PLACING & FINISHING LMC-ES OVERLAY	75.5 SQ. YDS.	
SCARIFYING BRIDGE DECK	75.5 SQ. YDS.	
HYDRO-DEMOLITION OF BRIDGE DECK	75.5 SQ. YDS.	
GROOVING BRIDGE FLOORS	622.9 SQ. FT.	

DRAWN BY : R.L.PUTEK DATE : 01/2019
 CHECKED BY : A.M.LEE DATE : 03/2019



PROJECT NO. 15BPR.40
 BUNCOMBE COUNTY
 BRIDGE NO. 100495

SHEET 1 OF 2
 DEPARTMENT OF TRANSPORTATION
 RALEIGH
 DECK SURFACE REPAIR
 SPANS A & C
 WITH
 APPROACH SLABS

REVISIONS						SHEET NO.
NO.	BY:	DATE:	NO.	BY:	DATE:	
1			3			S2-04
2			4			TOTAL SHEETS 14

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED
