DocuSign Envelope ID: 48AC2A16-59	991-4076-BD02-530A912254 රූ	4D2
	6/2/99	
		-
SNC		
REVISIONS		
		_
	с Бр	
	8/18/202111:33:19 AM \U4986_1s_rw03e-3.dgn User:baboules	
	:33:19 3:19 s	
	8/2021 U4906 ser:bai	

PERMANENT EASEMENT CONTROL SHEET

ROW MARKER PERMANENT EASEMENT-E								
ALIGN	STATION	OFFSET	NORTH	EAST				
Y3	18+67.81	-30.00	399449.0877	2460848.5915				

I, William T. Robbins, II, a ProfessionalLand Surveyor in the state of North Carolina hereby certify to the best of my knowledge and belief that the following work item(s)(Base map Compilation, R/W Staking)performed under my responsible charge meet NCDOT Survey Standards as directed in the NCDOT Location & Surveys guidelines and procedures.

lfurther certify that the right of way and permanent easement points shown herein and outlined in the tables shown hereon (localized coordinates, station/offset) have been checked and are accurate representations of the right of way and permanent easement points depicted on the corresponding highway plans. Lalso certify that the right of way and permanent easement points shown herein have been field monumented under my supervision from existing survey controlprovided by others; that the depicted property data shown herein were surveyed by others; and these monuments denote the right of way and easement boundaries at the time of staking which may be subject to change due to right of way revisions (See deeds for final determination).

Witness my original signature, registration number and seal this 18th day of August, 2021.

L-4192

PLS #



ProfessionalLand Surveyor

ROW MARKER PERMANENT EASEMENT-E

ALIGN	STATION	OFFSET	I NORTH	EAST
Y4	10+99.03	-72.00	395203.0785	2462991.6121
Y4	11+08.00	-71.25	395203.0235	2462982.6060
Y 4	11+08.00	-32.77	395241.3528	2462979.1673
Y4	14+38.27	63.37	395307.5915	2462641.6241
Y4	14+85.33	62.86	395302.8766	2462594.8010
Y4	15+85.90	61.76	395292.8001	2462494.7332


ROW MARKER PERMANENT EASEMENT-E

ALIGN	STATION	OFFSET	NORTH	EAST
Y5	11+75.00	-30.18	407278.8041	2452683.7423
Y5	11+75.00	-50.00	407289.3121	2452700.5497
Y5	11+85.00	30.21	407238.3786	2452637.7958
Y5	11+85.00	60.00	407222.6508	2452612.4916
Y5	12+15.00	-50.00	407254.2281	2452722.0162
Y5	12+15.00	-29.10	407243.5515	2452704.0470
Y5	12+25.00	60.00	407189.7708	2452632.3253
Y5	12+25.00	30.68	407204.5777	2452657.6287

NOTES:

1. IF FURTHER INFORMATION REGARDING PROJECT CONTROL IS NEEDED PLEASE CONTACT THE LOCATION AND SURVEYS UNIT.

2. PROJECT CONTROL WAS ESTABLISHED USING GNSS, THE GLOBAL NAVIGATION SATELLITE SYSTEM

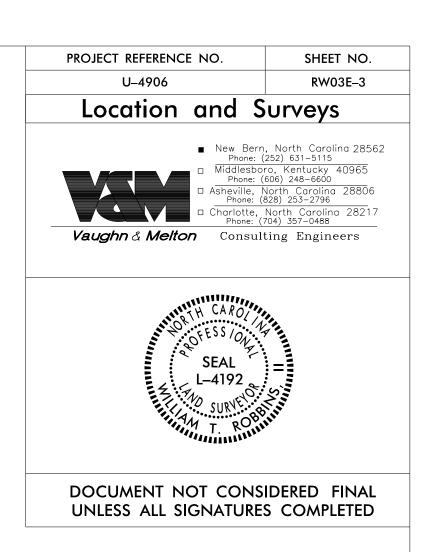

Seal
