


PLANS PREPARED FOR THE NCDOT BY:

M MOTT MACDONALD 1 & E, LLC
1101 HAYNES STREET, SUITE 101
RALEIGH, NC 27604
NC LICENSE NO. F-0669

TEMPORARY PAVEMENT LOCATION S1-3 ON OUTSIDE SHOULDER ON SB I-95 ON -L- FROM STA 538+47+/- TO STA 585+42+/- FOR TEMPORARY TRAFFIC PATTERN (36,899 SF)	TEMPORARY PAVEMENT LOCATION S1-8 ON OUTSIDE SHOULDER OF NB I-95 ON -L- FROM STA 561+00+/- TO STA 578+02+/- FOR PLACEMENT OF TEMPORARY PCB (6,040 SF)	TEMPORARY PAVEMENT LOCATION S1-56 ON THE LEFT SIDE OF -Y4- FROM STA 21+13+/- TO STA 23+75+/- FOR PLACEMENT OF TEMPORARY PCB (752 SF)	TEMPORARY PAVEMENT LOCATION S1-57 ON THE LEFT SIDE OF -Y4- FROM STA 25+65+/- TO STA 30+90+/- FOR PLACEMENT OF TEMPORARY PCB (1385 SF)
TEMPORARY PAVEMENT LOCATION S1-4 ON OUTSIDE SHOULDER ON SB I-95 ON -L- FROM STA 538+47+/- TO STA 574+80+/- FOR THE PLACEMENT OF TEMPORARY PCB (10,931 SF)	TEMPORARY PAVEMENT LOCATION S1-9 ON INSIDE SHOULDER OF NB I-95 ON -L- FROM STA 574+50+/- TO STA 582+41+/- FOR TEMPORARY TRAFFIC PATTERN (6,143 SF)		
TEMPORARY PAVEMENT LOCATION S1-5 ON OUTSIDE SHOULDER ON SB I-95 ON -L- FROM STA 574+80+/- TO STA 581+39+/- FOR TEMPORARY TRAFFIC PATTERN (2447 SF)	TEMPORARY PAVEMENT LOCATION S1-10 ON INSIDE SHOULDER OF SB I-95 ON -L- FROM STA 573+35+/- TO STA 585+42+/- FOR TEMPORARY TRAFFIC PATTERN (7,843 SF)		
TEMPORARY PAVEMENT LOCATION S1-6 ON OUTSIDE SHOULDER OF NB I-95 ON -L- FROM STA 548+49+/- TO STA 578+02+/- FOR TEMPORARY TRAFFIC PATTERN (23,603 SF)			

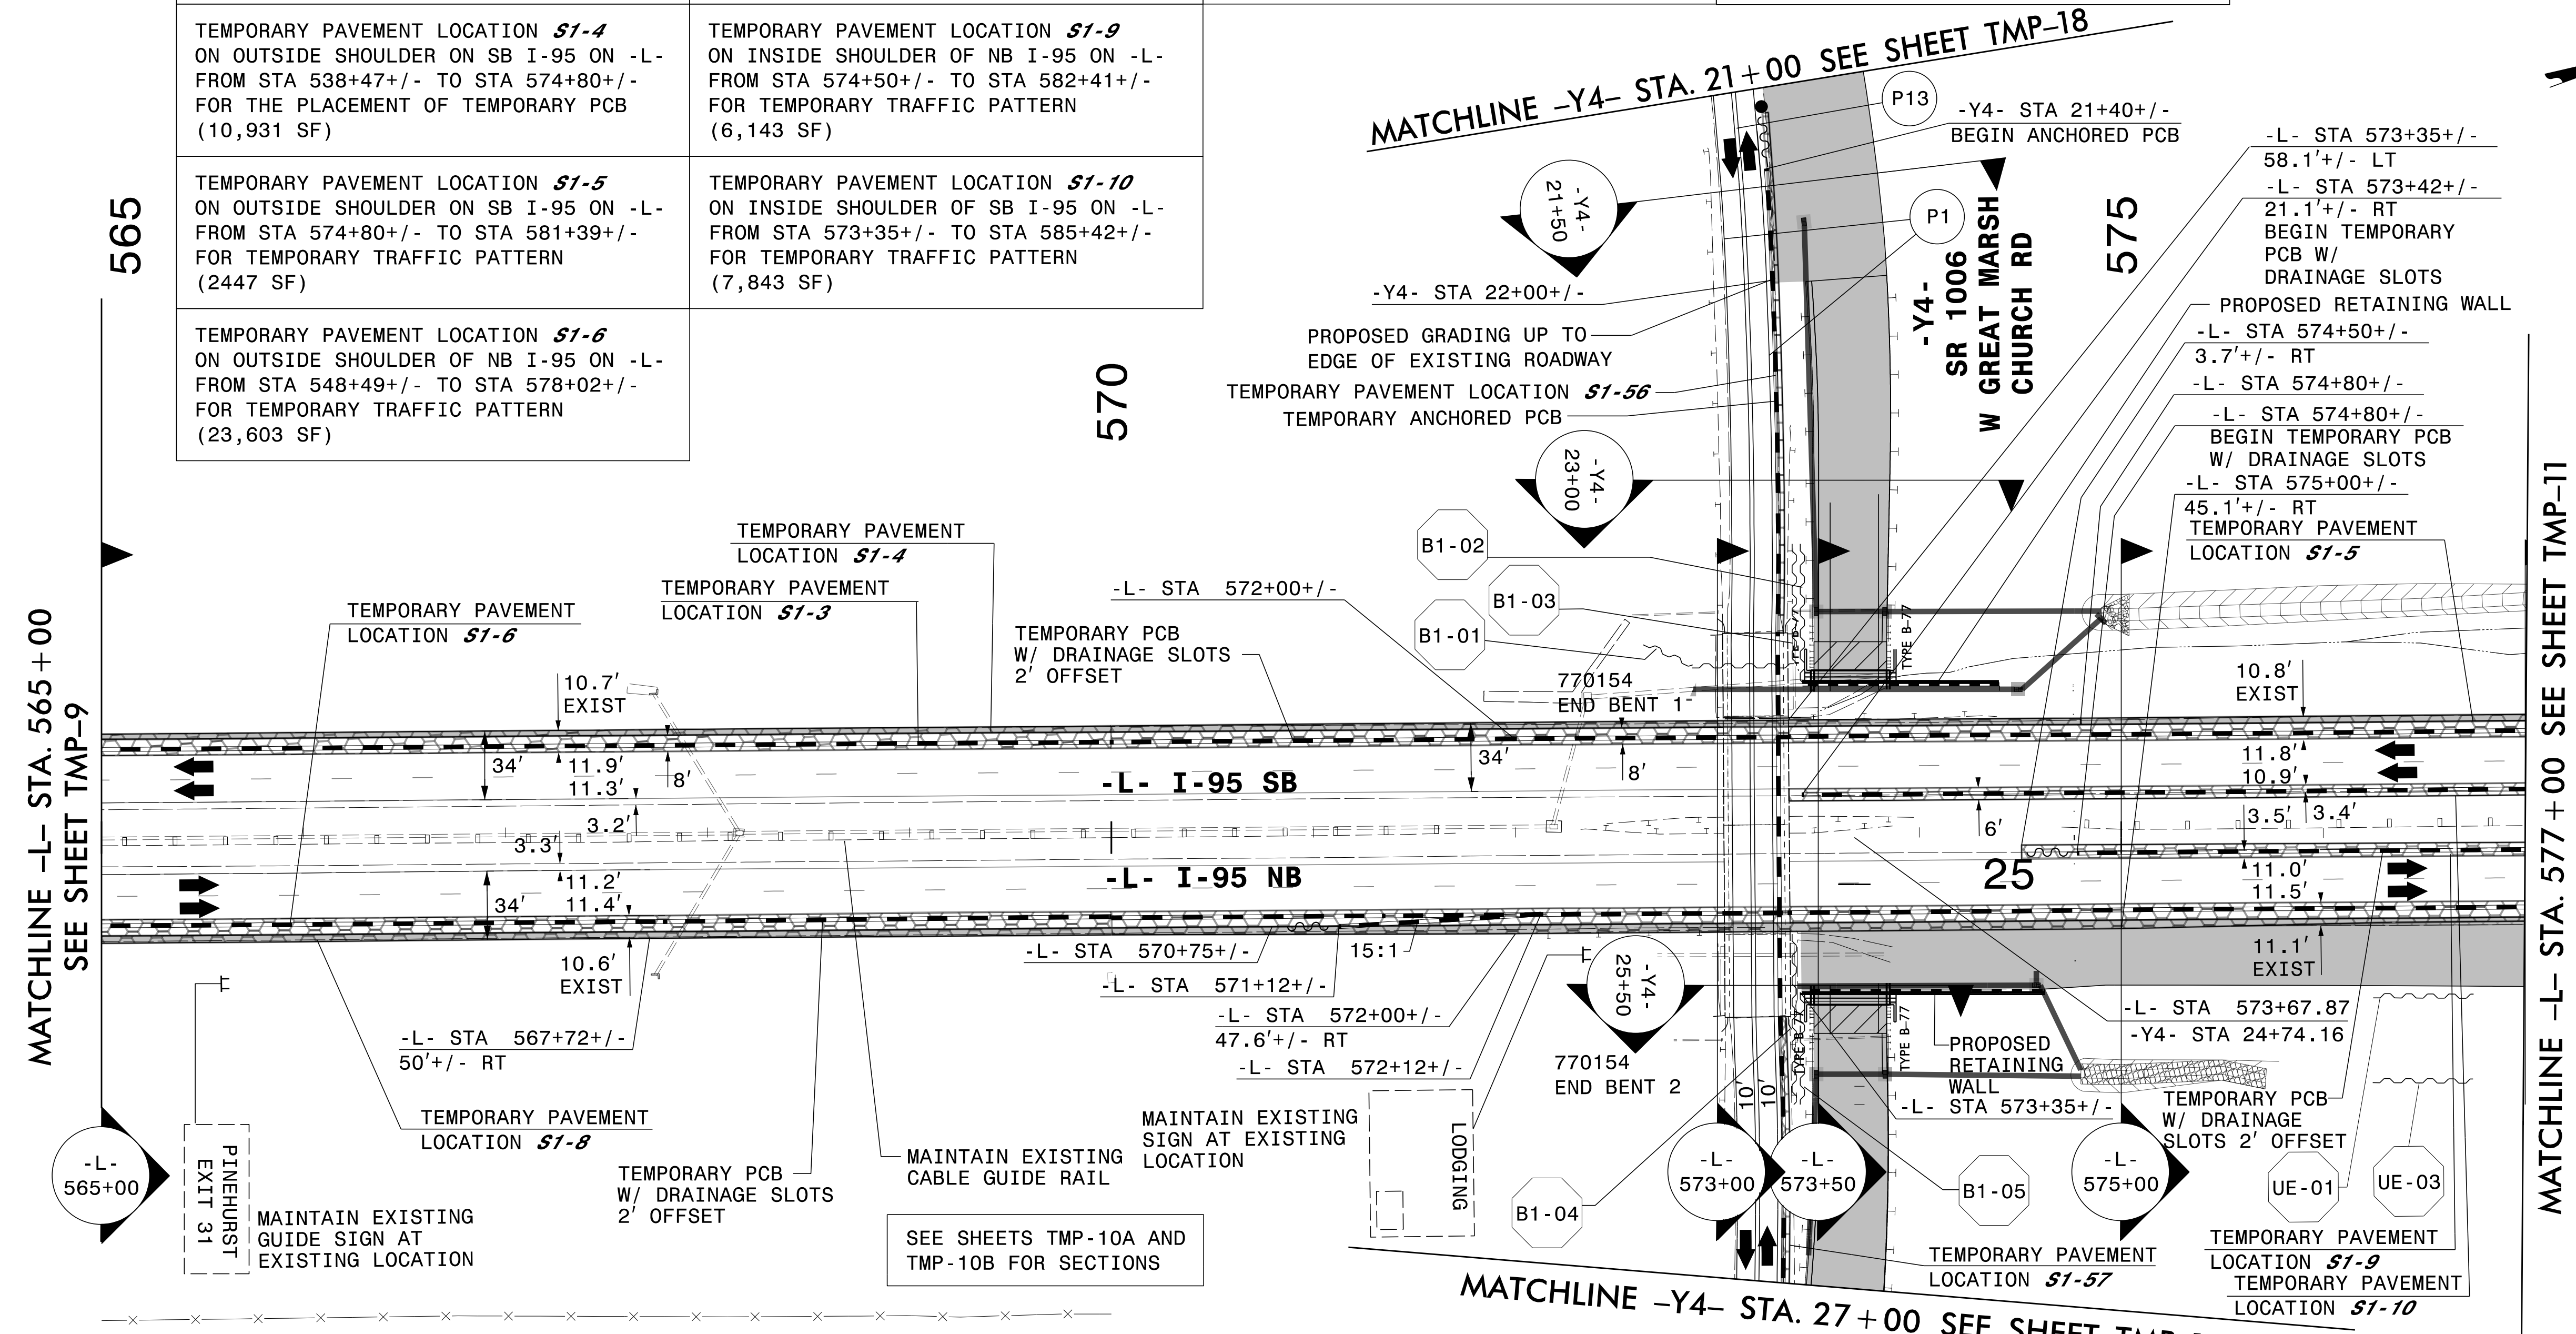

MATCHLINE -L- STA. 565 + 00
SEE SHEET TMP-9

MATCHLINE -L- STA. 577 + 00
SEE SHEET TMP-11

- | | | | |
|--|--|--|--|
| B1-01 QUANTITY = 765.4 SF
TEMPORARY SHORING ON -L-
FROM STA 572+64+/-, 96.4' LT
TO STA 572+88+/-, 85' LT
TO STA 573+38+/-, 85' LT
(SEE SHEET TMP-2TS2 FOR
TEMPORARY SHORING NOTES) | B1-02 QUANTITY = 1074.8 SF
TEMPORARY SHORING ON -Y4-
FROM STA 23+31.50+/-, 25.75' RT
TO STA 24+00+/-, 25.75' RT
(SEE SHEET TMP-2TS2 FOR
TEMPORARY SHORING NOTES) | B1-03 QUANTITY = 966.2 SF
TEMPORARY SHORING ON -Y4-
FROM STA 23+31.50+/-, 29.75' RT
TO STA 24+18+/-, 29.75' RT
(SEE SHEET TMP-2TS2 FOR
TEMPORARY SHORING NOTES) | UE-03 QUANTITY = 5440 SF
TEMPORARY SHORING ON -L-
FROM STA 576+25+/-, 120' RT
TO STA 576+75+/-, 120' RT
(SEE SHEET TMP-2TS15 FOR
TEMPORARY SHORING NOTES) |
| B1-04 QUANTITY = 1042.7 SF
TEMPORARY SHORING ON -Y4-
FROM STA 25+24.50+/-, 29.75' RT
TO STA 26+09+/-, 29.75' RT
(SEE SHEET TMP-2TS2 FOR
TEMPORARY SHORING NOTES) | B1-05 QUANTITY = 882.2 SF
TEMPORARY SHORING ON -Y4-
FROM STA 25+54+/-, 25.75' RT
TO -Y4- STA 26+09+/-, 25.75' RT
(SEE SHEET TMP-2TS2 FOR
TEMPORARY SHORING NOTES) | UE-01 QUANTITY = 245 SF
TEMPORARY SHORING ON -L-
FROM STA 576+25+/-, 78' RT
TO STA 576+75+/-, 78' RT
(SEE SHEET TMP-2TS15 FOR
TEMPORARY SHORING NOTES) | |

APPROVED: *Lois D. Stouchko*
DATE: _____
SEAL 034437
LOIS D. STOUCHKO
ENGINEER
NORTH CAROLINA



SECTION 1

**TEMPORARY TRAFFIC CONTROL
PHASE I**

4/18/2022
G:\50100191\NV5_1-5987B\TrafficControl\Tc\200_105_1-5987B_TMP-10_Phase I.dgn
User:ST086227

**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**
