


PLANS PREPARED FOR THE NCDOT BY:
M MOTT MACDONALD I & E, LLC
 1101 HAYNES STREET, SUITE 101
 RALEIGH, NC 27604
M MOTT MACDONALD
 NC LICENSE NO. F-0669

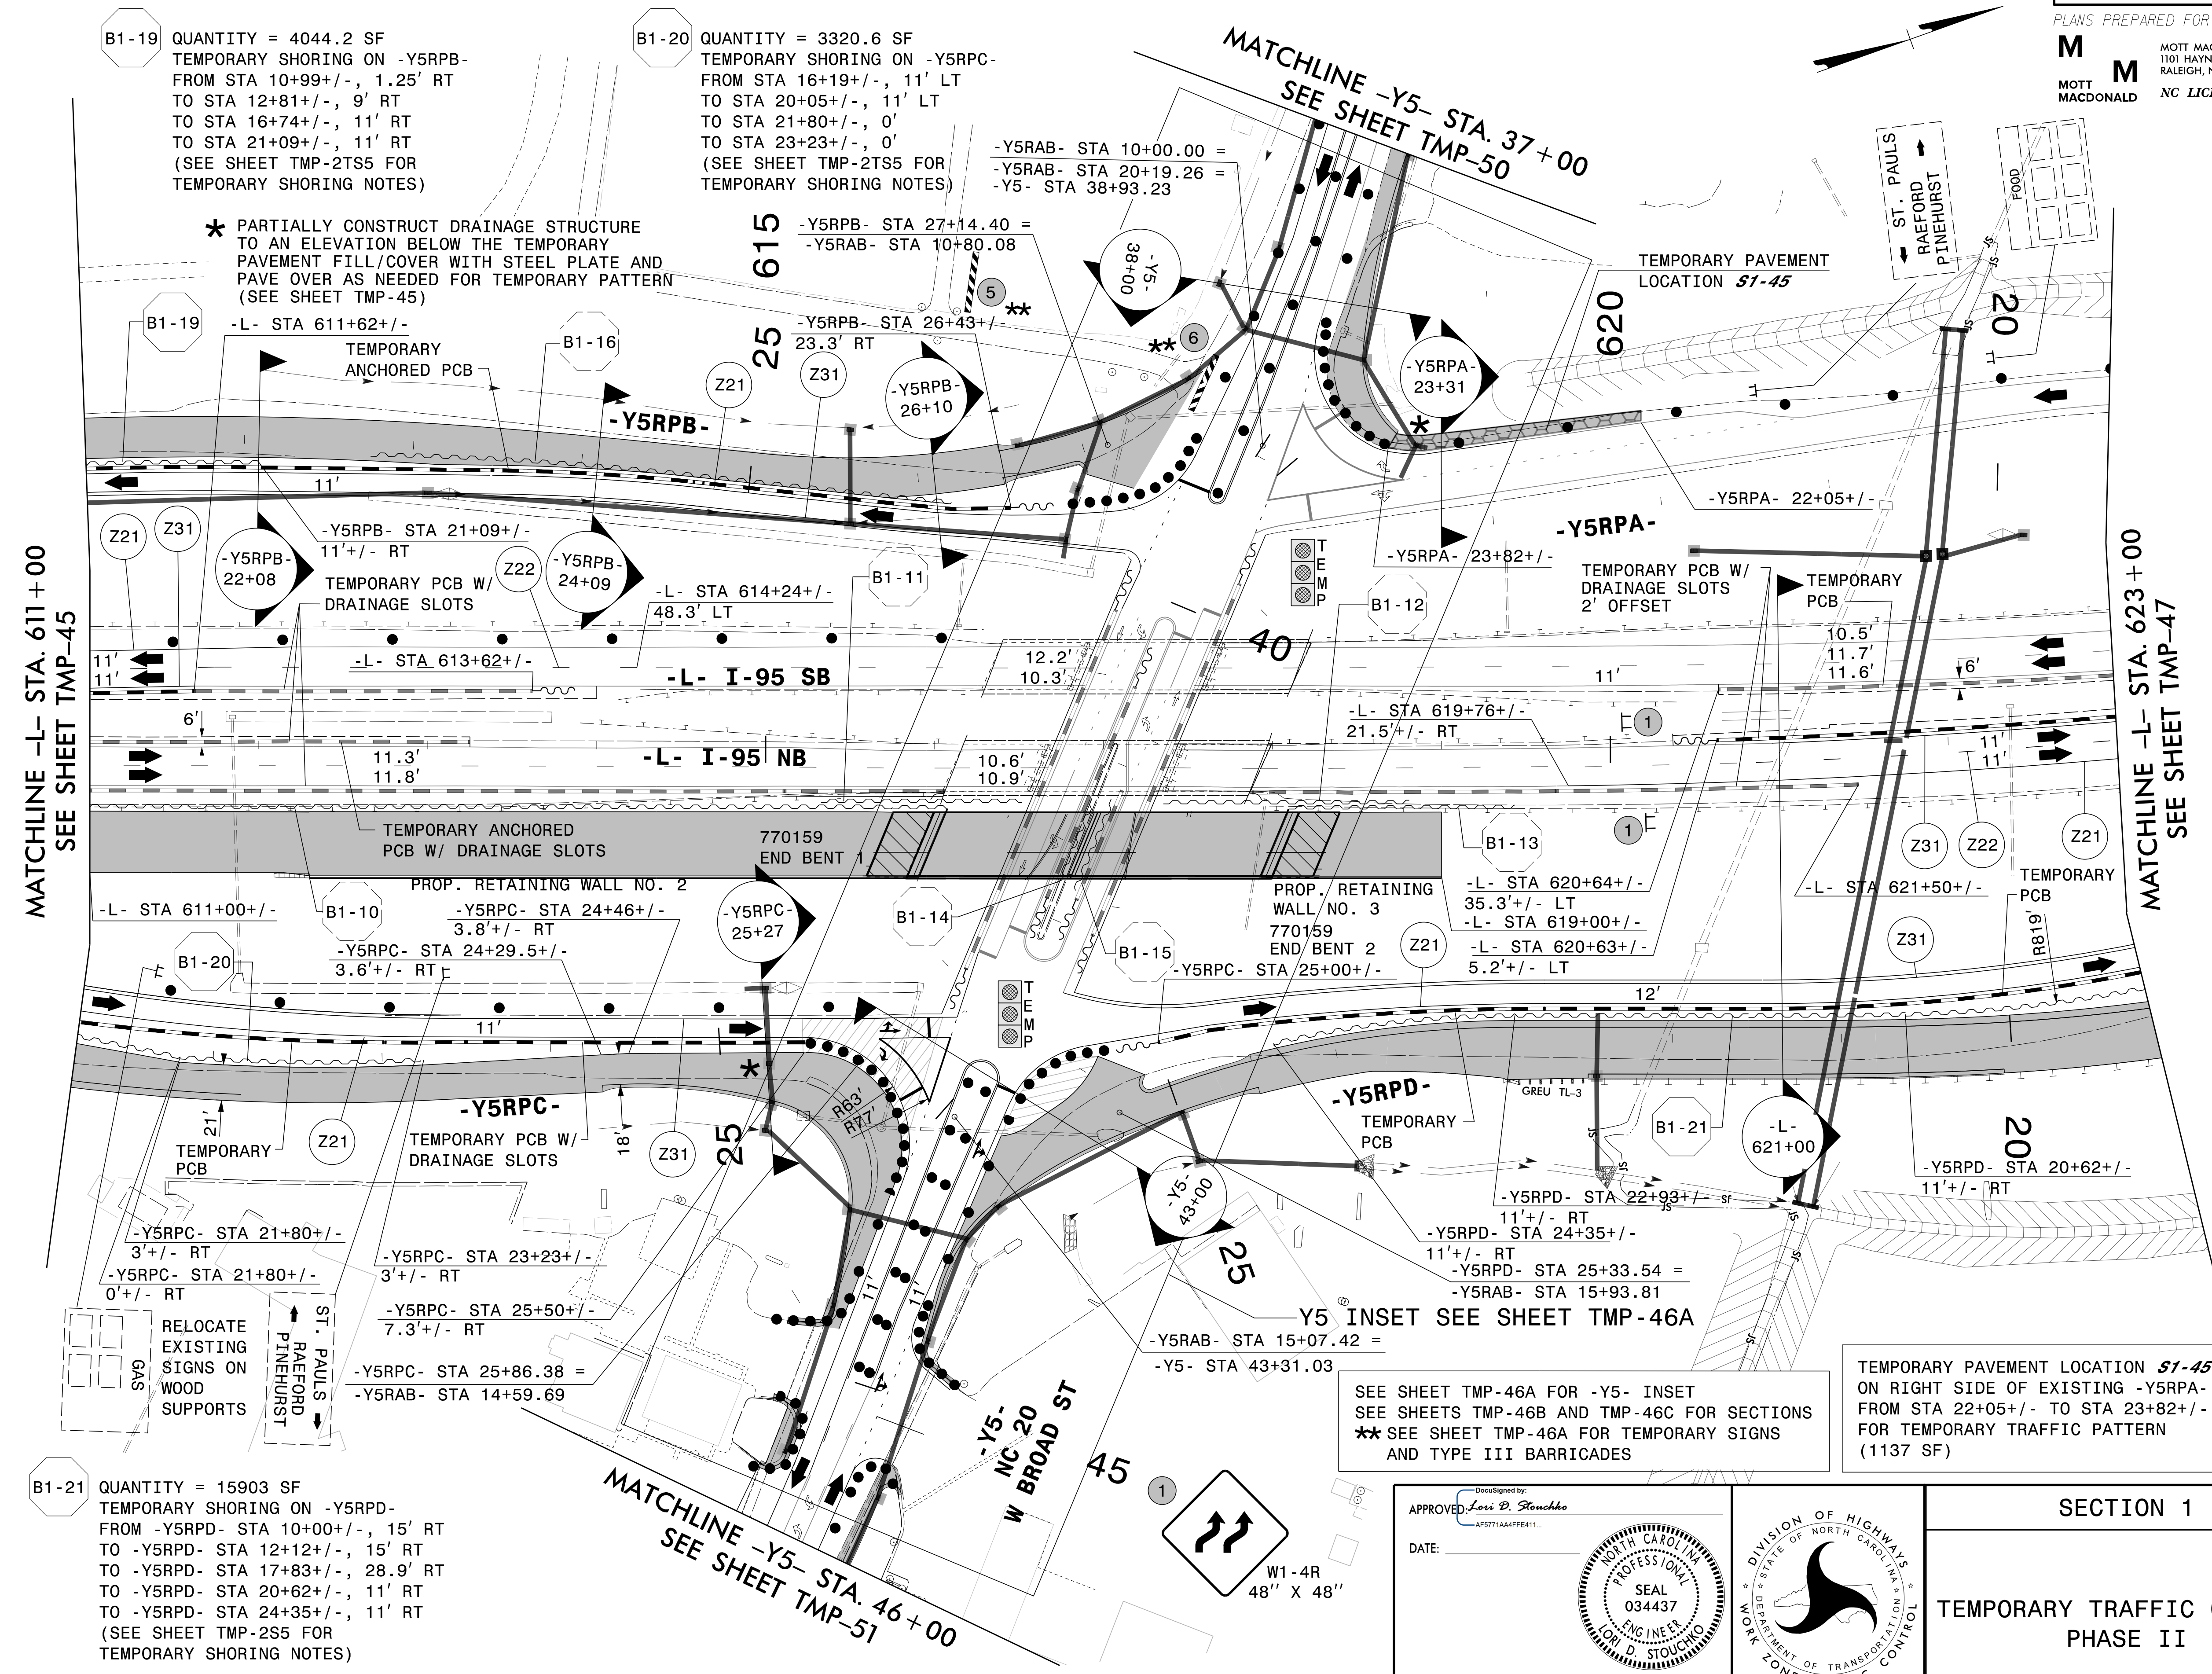

B1-19 QUANTITY = 4044.2 SF
 TEMPORARY SHORING ON -Y5RPB-
 FROM STA 10+99+/-, 1.25' RT
 TO STA 12+81+/-, 9' RT
 TO STA 16+74+/-, 11' RT
 TO STA 21+09+/-, 11' RT
 (SEE SHEET TMP-2TS5 FOR
 TEMPORARY SHORING NOTES)

B1-20 QUANTITY = 3320.6 SF
 TEMPORARY SHORING ON -Y5RPC-
 FROM STA 16+19+/-, 11' LT
 TO STA 20+05+/-, 11' LT
 TO STA 21+80+/-, 0'
 TO STA 23+23+/-, 0'
 (SEE SHEET TMP-2TS5 FOR
 TEMPORARY SHORING NOTES)

* PARTIALLY CONSTRUCT DRAINAGE STRUCTURE
 TO AN ELEVATION BELOW THE TEMPORARY
 PAVEMENT FILL/COVER WITH STEEL PLATE AND
 PAVE OVER AS NEEDED FOR TEMPORARY PATTERN
 (SEE SHEET TMP-45)

MATCHLINE -L- STA. 611+00
SEE SHEET TMP-45

MATCHLINE -L- STA. 623+00
SEE SHEET TMP-47

B1-21 QUANTITY = 15903 SF
 TEMPORARY SHORING ON -Y5RPD-
 FROM -Y5RPD- STA 10+00+/-, 15' RT
 TO -Y5RPD- STA 12+12+/-, 15' RT
 TO -Y5RPD- STA 17+83+/-, 28.9' RT
 TO -Y5RPD- STA 20+62+/-, 11' RT
 TO -Y5RPD- STA 24+35+/-, 11' RT
 (SEE SHEET TMP-2S5 FOR
 TEMPORARY SHORING NOTES)


SEE SHEET TMP-46A FOR -Y5- INSET
 SEE SHEETS TMP-46B AND TMP-46C FOR SECTIONS
 ** SEE SHEET TMP-46A FOR TEMPORARY SIGNS
 AND TYPE III BARRICADES

TEMPORARY PAVEMENT LOCATION *S1-45*
 ON RIGHT SIDE OF EXISTING -Y5RPA-
 FROM STA 22+05+/- TO STA 23+82+/-
 FOR TEMPORARY TRAFFIC PATTERN
 (1137 SF)

3/28/2022
 G:\50100191\NV5_I-5987B\TrafficControl\I-95\200_261_I-5987B_TMP-46_Phase II.dgn
 User:ST086227

APPROVED: *Lois D. Stouchko*
 DATE: _____
 W1-4R
 48" X 48"

DOCUMENT NOT CONSIDERED FINAL
 UNLESS ALL SIGNATURES COMPLETED



SECTION 1
 TEMPORARY TRAFFIC CONTROL
 PHASE II
