Docusign Envelope ID: E362FD81-5EE7-40C6-9BE4-F0401C0A1896

CULVERT CONSTRUCTION SEQUENCE STA. 10+67 –Y3A–

PROJECT REFERENCE NO.	SHEET NO.
A-0009CD	EC-05B/CONST.45
R/W SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER
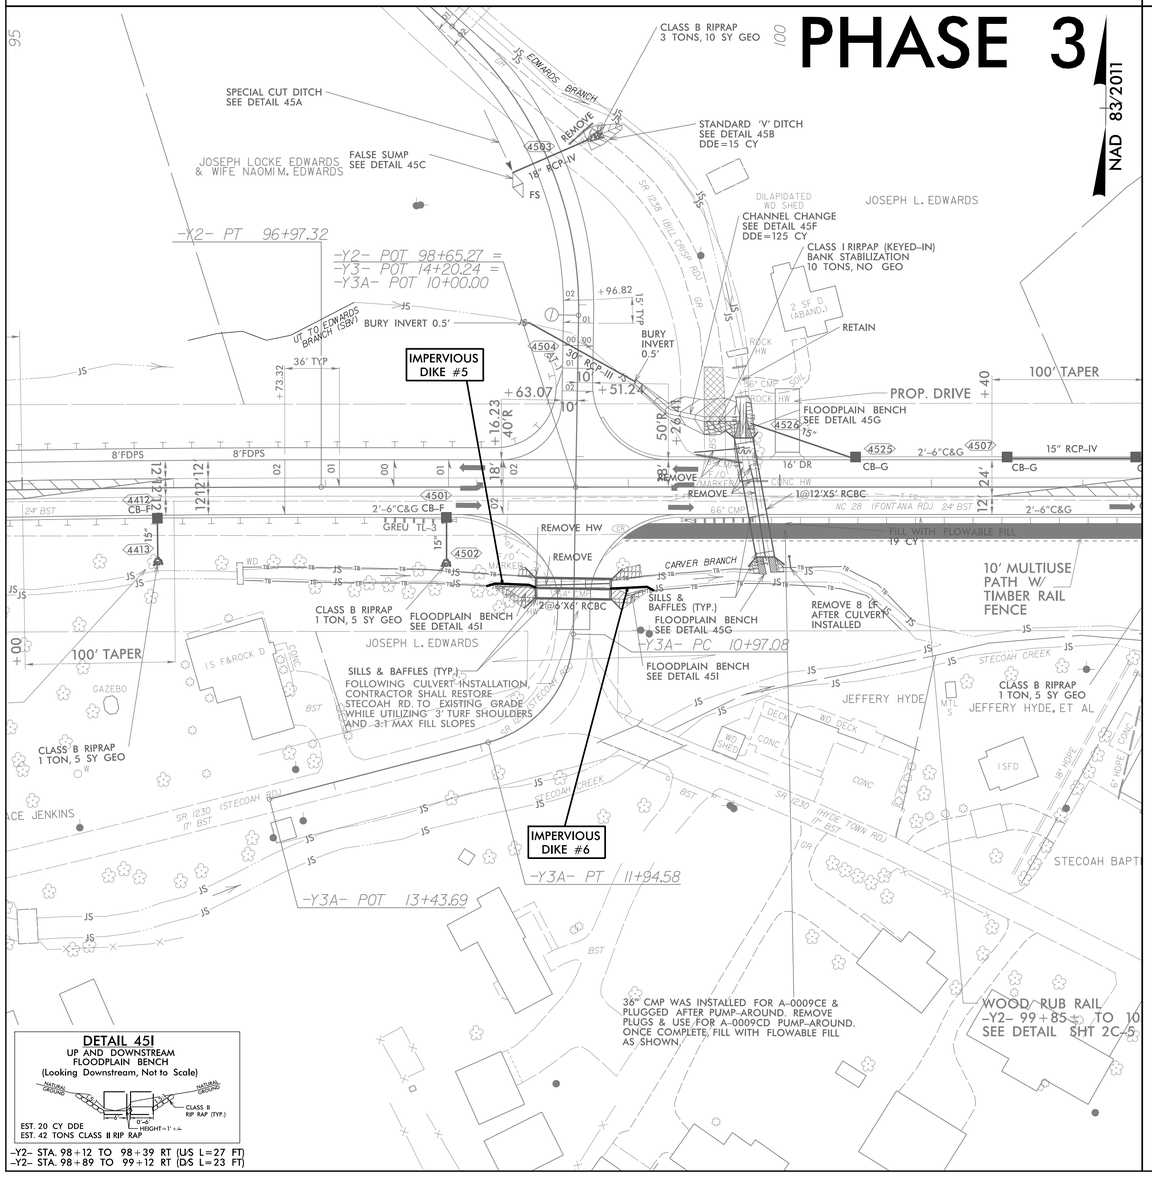
1. REMOVE IMPERVIOUS DIKES #3 & #4 AND INSTALL IMPERVIOUS DIKES #5 & #6, DIRECTING FLOW THROUGH NORTHERNMOST 6′ X 6′ RCBC.
2. REMOVE 36″ TEMPORARY PIPE AND INSTALL SOUTHERNMOST 6′ X 6′ RCBC.
3. COMPLETE INLET/OUTLET CHANNEL IMPROVEMENTS.
4. REMOVE IMPERVIOUS DIKES AND ANY REMAINING SPECIAL STILLING BASINS AND REESTABLISH STREAM.
5. COMPLETE ROADWAY CONSTRUCTION ACCORDING TO TRAFFIC CONTROL PLANS.
