8/17/99

PROJECT REFERENCE NO.	SHEET NO.
U-3330	EC-12/CONST.10
R/W SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

CULVERT CONSTRUCTION SEQUENCE STA. 113 + 47.97

PHASE 2

5. INSTALL IMPERVIOUS DIKES AND DIVERT WATER TO 66" STEEL PIPE.

6. REMOVE SPECIAL STILLING BASINS #1. INSTALL BASIN #3.

7. INSTALL 10' OF 2-6'X7' RCBC ON INLET END, 23' OF 2-6'X7' RCBC ON OUTLET END, AND REMAINING HEADWALLS AND WINGWALLS.

8. INSTALL CHANNEL IMPROVEMENTS AND RIP RAP UPSTREAM AND DOWNSTREAM.

9. REMOVE SPECIAL STILLING BASINS AND DIKES.

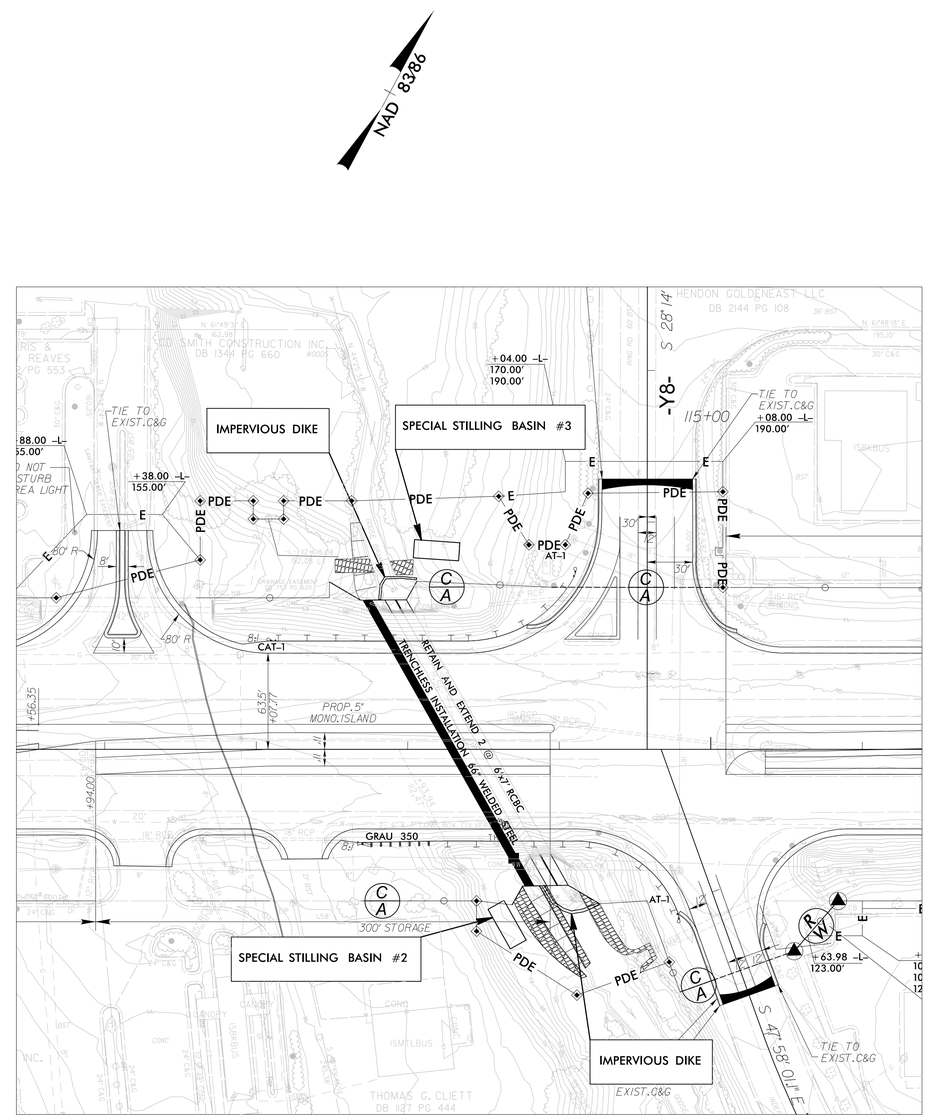

MULKEY
ENGINEERS & CONSULTANTS
PO Box 33127
Raleigh, N.C. 27636
(919) 851-1912
(919) 851-1918 (FAX)
WWW.MULKEYINC.COM
NC LICENSE NO. C-1021

SYMBOL SIGN NAME
