STATE	STATE PROJECT REFERENCE NO.	SHEET NO.	TOTAL SHEETS
N.C.	U-4751	1	40

REFERENCE: U-4751

PROJECT: 40191

STATE OF NORTH CAROLINA
DEPARTMENT OF TRANSPORTATION
DIVISION OF HIGHWAYS
GEOTECHNICAL ENGINEERING UNIT

STRUCTURE SUBSURFACE INVESTIGATION

COUNTY *NEW HANOVER*

PROJECT DESCRIPTION *SR 1409 (MILITARY CUTOFF ROAD) TO US 17 IN WILMINGTON*

SITE DESCRIPTION *NOISE WALL 13 AT -L- STA. 128+50, LEFT.*

CONTENTS

SHEET NO.	DESCRIPTION
1	TITLE SHEET
2	LEGEND
3-6	SITE PLANS WITH BORING LOCATIONS AND WALL ENVELOPES WITH BORING DATA
7-39	BORING AND CPT LOGS
40	SITE PHOTOGRAPHS

CAUTION NOTICE

THE SUBSURFACE INFORMATION AND THE SUBSURFACE INVESTIGATION ON WHICH IT IS BASED WERE MADE FOR THE PURPOSE OF STUDY, PLANNING AND DESIGN, AND NOT FOR CONSTRUCTION OR PAY PURPOSES. THE VARIOUS FIELD BORING LOGS, ROCK CORES AND SOIL TEST DATA AVAILABLE MAY BE REVIEWED OR INSPECTED IN RALEIGH BY CONTACTING THE N. C. DEPARTMENT OF TRANSPORTATION, GEOTECHNICAL ENGINEERING UNIT AT (919) 707-6850. THE SUBSURFACE PLANS AND REPORTS, FIELD BORING LOGS, ROCK CORES AND SOIL TEST DATA ARE NOT PART OF THE CONTRACT.

GENERAL SOIL AND ROCK STRATA DESCRIPTIONS AND INDICATED BOUNDARIES ARE BASED ON A GEOTECHNICAL INTERPRETATION OF ALL AVAILABLE SUBSURFACE DATA AND MAY NOT NECESSARILY REFLECT THE ACTUAL SUBSURFACE CONDITIONS BETWEEN BORINGS OR BETWEEN SAMPLED STRATA WITHIN THE BOREHOLE. THE LABORATORY SAMPLE DATA AND THE IN SITU (IN-PLACE) TEST DATA CAN BE RELIED ON ONLY TO THE DEGREE OF RELIABILITY INHERENT IN THE STANDARD TEST METHOD. THE OBSERVED WATER LEVELS OR SOIL MOISTURE CONDITIONS INDICATED IN THE SUBSURFACE INVESTIGATIONS ARE AS RECORDED AT THE TIME OF THE INVESTIGATION. THESE WATER LEVELS OR SOIL MOISTURE CONDITIONS MAY VARY CONSIDERABLY WITH TIME ACCORDING TO CLIMATIC CONDITIONS INCLUDING TEMPERATURES, PRECIPITATION AND WIND, AS WELL AS OTHER NON-CLIMATIC FACTORS.

THE BIDDER OR CONTRACTOR IS CAUTIONED THAT DETAILS SHOWN ON THE SUBSURFACE PLANS ARE PRELIMINARY ONLY AND IN MANY CASES THE FINAL DESIGN DETAILS ARE DIFFERENT. FOR BIDDING AND CONSTRUCTION PURPOSES, REFER TO THE CONSTRUCTION PLANS AND DOCUMENTS FOR FINAL DESIGN INFORMATION ON THIS PROJECT. THE DEPARTMENT DOES NOT WARRANT OR GUARANTEE THE SUFFICIENCY OR ACCURACY OF THE INVESTIGATION MADE, NOR THE INTERPRETATIONS MADE, OR OPINION OF THE DEPARTMENT AS TO THE TYPE OF MATERIALS AND CONDITIONS TO BE ENCOUNTERED. THE BIDDER OR CONTRACTOR IS CAUTIONED TO MAKE SUCH INDEPENDENT SUBSURFACE INVESTIGATIONS AS HE DEEMS NECESSARY TO SATISFY HIMSELF AS TO CONDITIONS TO BE ENCOUNTERED ON THE PROJECT. THE CONTRACTOR SHALL HAVE NO CLAIM FOR ADDITIONAL COMPENSATION OR FOR AN EXTENSION OF TIME FOR ANY REASON RESULTING FROM THE ACTUAL CONDITIONS ENCOUNTERED AT THE SITE DIFFERING FROM THOSE INDICATED IN THE SUBSURFACE INFORMATION.

NOTES:
1. THE INFORMATION CONTAINED HEREIN IS NOT IMPLIED OR GUARANTEED BY THE N. C. DEPARTMENT OF TRANSPORTATION AS ACCURATE NOR IS IT CONSIDERED PART OF THE PLANS, SPECIFICATIONS OR CONTRACT FOR THE PROJECT.
2. BY HAVING REQUESTED THIS INFORMATION, THE CONTRACTOR SPECIFICALLY WAIVES ANY CLAIMS FOR INCREASED COMPENSATION OR EXTENSION OF TIME BASED ON DIFFERENCES BETWEEN THE CONDITIONS INDICATED HEREIN AND THE ACTUAL CONDITIONS AT THE PROJECT SITE.

PERSONNEL

W. S. HUNSBERGER

MID-ATLANTIC DRILLING

INVESTIGATED BY *WSH*

DRAWN BY *WSH*

CHECKED BY *J. R. HAMM*

SUBMITTED BY *FALCON*

DATE *JUNE 2015*

NORTH CAROLINA PROFESSIONAL SEAL 36283 ENGINEER W. SCOTT HUNSBERGER

DocuSigned by:
W. Scott Hunsberger
EA39AB9EDF5845A...
SIGNATURE

7/15/2015
DATE

PROJECT REFERENCE NO.	SHEET NO.
U-4751	2

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
DIVISION OF HIGHWAYS
GEOTECHNICAL ENGINEERING UNIT

SUBSURFACE INVESTIGATION

SOIL AND ROCK LEGEND, TERMS, SYMBOLS, AND ABBREVIATIONS

SOIL DESCRIPTION

SOIL IS CONSIDERED UNCONSOLIDATED, SEMI-CONSOLIDATED, OR WEATHERED EARTH MATERIALS THAT CAN BE PENETRATED WITH A CONTINUOUS FLIGHT POWER AUGER AND YIELD LESS THAN 100 BLOWS PER FOOT ACCORDING TO THE STANDARD PENETRATION TEST (AASHTO T 206, ASTM D1586). SOIL CLASSIFICATION IS BASED ON THE AASHTO SYSTEM. BASIC DESCRIPTIONS GENERALLY INCLUDE THE FOLLOWING: CONSISTENCY, COLOR, TEXTURE, MOISTURE, AASHTO CLASSIFICATION, AND OTHER PERTINENT FACTORS SUCH AS MINERALOGICAL COMPOSITION, ANGULARITY, STRUCTURE, PLASTICITY, ETC. FOR EXAMPLE,
VERY STIFF, GRAY, SILTY CLAY, MOIST WITH INTERBEDDED FINE SAND LAYERS, HIGHLY PLASTIC, A-7-6

SOIL LEGEND AND AASHTO CLASSIFICATION

GENERAL CLASS.	GRANULAR MATERIALS (≤ 35% PASSING #200)							SILT-CLAY MATERIALS (> 35% PASSING #200)				ORGANIC MATERIALS		
GROUP CLASS.	A-1		A-3	A-2				A-4	A-5	A-6	A-7	A-1, A-2 A-3	A-4, A-5 A-6, A-7	
	A-1-a	A-1-b		A-2-4	A-2-5	A-2-6	A-2-7				A-7-5, A-7-6			
SYMBOL														
% PASSING #10 #40 #200	50 MX 30 MX 15 MX	50 MX 25 MX	51 MN 10 MX	35 MX	35 MX	35 MX	35 MX	36 MN	36 MN	36 MN	36 MN	GRANULAR SOILS	SILT-CLAY SOILS	MUCK, PEAT
MATERIAL PASSING #40 LL PI	— 6 MX		— NP	40 MX 10 MX	41 MN 10 MX	40 MX 11 MN	41 MN 11 MN	40 MX 10 MX	41 MN 10 MX	40 MX 11 MN	41 MN 11 MN	SOILS WITH LITTLE OR MODERATE AMOUNTS OF ORGANIC MATTER		HIGHLY ORGANIC SOILS
GROUP INDEX	0		0	0		4 MX		8 MX	12 MX	16 MX	NO MX			
USUAL TYPES OF MAJOR MATERIALS	STONE FRAGS. GRAVEL, AND SAND		FINE SAND	SILTY OR CLAYEY GRAVEL AND SAND				SILTY SOILS		CLAYEY SOILS				
GEN. RATING AS SUBGRADE	EXCELLENT TO GOOD							FAIR TO POOR				FAIR TO POOR	POOR	UNSUITABLE

PI OF A-7-5 SUBGROUP IS ≤ LL - 30 ; PI OF A-7-6 SUBGROUP IS > LL - 30

CONSISTENCY OR DENSENESS

PRIMARY SOIL TYPE	COMPACTNESS OR CONSISTENCY	RANGE OF STANDARD PENETRATION RESISTENCE (N-VALUE)	RANGE OF UNCONFINED COMPRESSIVE STRENGTH ($TONS/FT^2$)
GENERALLY GRANULAR MATERIAL (NON-COHESIVE)	VERY LOOSE LOOSE MEDIUM DENSE DENSE VERY DENSE	< 4 4 TO 10 10 TO 30 30 TO 50 > 50	N/A
GENERALLY SILT-CLAY MATERIAL (COHESIVE)	VERY SOFT SOFT MEDIUM STIFF STIFF VERY STIFF HARD	< 2 2 TO 4 4 TO 8 8 TO 15 15 TO 30 > 30	< 0.25 0.25 TO 0.5 0.5 TO 1.0 1 TO 2 2 TO 4 > 4

TEXTURE OR GRAIN SIZE

U.S. STD. SIEVE SIZE	4	10	40	60	200	270
OPENING (MM)	4.76	2.00	0.42	0.25	0.075	0.053

BOULDER (BLDR.)	COBBLE (COB.)	GRAVEL (GR.)	COARSE SAND (CSE. SD.)	FINE SAND (F SD.)	SILT (SL.)	CLAY (CL.)

GRAIN SIZE	MM	305	75	2.0	0.25	0.05	0.005
	IN.	12	3				

SOIL MOISTURE - CORRELATION OF TERMS

SOIL MOISTURE SCALE (ATTERBERG LIMITS)	FIELD MOISTURE DESCRIPTION	GUIDE FOR FIELD MOISTURE DESCRIPTION
	- SATURATED - (SAT.)	USUALLY LIQUID; VERY WET, USUALLY FROM BELOW THE GROUND WATER TABLE
LL — LIQUID LIMIT		
PLASTIC RANGE (PI)	- WET - (W)	SEMISOLID; REQUIRES DRYING TO ATTAIN OPTIMUM MOISTURE
PL — PLASTIC LIMIT		
OM — OPTIMUM MOISTURE SL — SHRINKAGE LIMIT	- MOIST - (M)	SOLID; AT OR NEAR OPTIMUM MOISTURE
	- DRY - (D)	REQUIRES ADDITIONAL WATER TO ATTAIN OPTIMUM MOISTURE

PLASTICITY

	PLASTICITY INDEX (PI)	DRY STRENGTH
NON PLASTIC	0-5	VERY LOW
SLIGHTLY PLASTIC	6-15	SLIGHT
MODERATELY PLASTIC	16-25	MEDIUM
HIGHLY PLASTIC	26 OR MORE	HIGH

COLOR

DESCRIPTIONS MAY INCLUDE COLOR OR COLOR COMBINATIONS (TAN, RED, YELLOW-BROWN, BLUE-GRAY). MODIFIERS SUCH AS LIGHT, DARK, STREAKED, ETC. ARE USED TO DESCRIBE APPEARANCE.

GRADATION

WELL GRADED - INDICATES A GOOD REPRESENTATION OF PARTICLE SIZES FROM FINE TO COARSE.
UNIFORMLY GRADED - INDICATES THAT SOIL PARTICLES ARE ALL APPROXIMATELY THE SAME SIZE.
GAP-GRADED - INDICATES A MIXTURE OF UNIFORM PARTICLE SIZES OF TWO OR MORE SIZES.

ANGULARITY OF GRAINS

THE ANGULARITY OR ROUNDNESS OF SOIL GRAINS IS DESIGNATED BY THE TERMS: ANGULAR, SUBANGULAR, SUBROUNDED, OR ROUNDED.

MINERALOGICAL COMPOSITION

MINERAL NAMES SUCH AS QUARTZ, FELDSPAR, MICA, TALC, KAOLIN, ETC. ARE USED IN DESCRIPTIONS WHEN THEY ARE CONSIDERED OF SIGNIFICANCE.

COMPRESSIBILITY

SLIGHTLY COMPRESSIBLE	LL < 31
MODERATELY COMPRESSIBLE	LL = 31 - 50
HIGHLY COMPRESSIBLE	LL > 50

PERCENTAGE OF MATERIAL

ORGANIC MATERIAL	GRANULAR SOILS	SILT - CLAY SOILS	OTHER MATERIAL	
TRACE OF ORGANIC MATTER	2 - 3%	3 - 5%	TRACE	1 - 10%
LITTLE ORGANIC MATTER	3 - 5%	5 - 12%	LITTLE	10 - 20%
MODERATELY ORGANIC	5 - 10%	12 - 20%	SOME	20 - 35%
HIGHLY ORGANIC	> 10%	> 20%	HIGHLY	35% AND ABOVE

GROUND WATER

- WATER LEVEL IN BORE HOLE IMMEDIATELY AFTER DRILLING
- STATIC WATER LEVEL AFTER 24 HOURS
- PW — PERCHED WATER, SATURATED ZONE, OR WATER BEARING STRATA
- SPRING OR SEEP

MISCELLANEOUS SYMBOLS

- ROADWAY EMBANKMENT (RE) WITH SOIL DESCRIPTION
- SOIL SYMBOL
- ARTIFICIAL FILL (AF) OTHER THAN ROADWAY EMBANKMENT
- INFERRED SOIL BOUNDARY
- INFERRED ROCK LINE
- ALLUVIAL SOIL BOUNDARY
- 25/025 — DIP & DIP DIRECTION OF ROCK STRUCTURES
- SPT, DPT, DMT, VST, PMT — TEST BORING
- AUGER BORING
- CORE BORING
- MW — MONITORING WELL
- PIEZOMETER INSTALLATION
- SLOPE INDICATOR INSTALLATION
- CONE PENETROMETER TEST
- SOUNDING ROD
- TEST BORING WITH CORE
- SPT N-VALUE

RECOMMENDATION SYMBOLS

- UNDERCUT EXCAVATION
- SHALLOW UNDERCUT
- UNCLASSIFIED EXCAVATION - UNSUITABLE WASTE
- UNCLASSIFIED EXCAVATION - ACCEPTABLE DEGRADABLE ROCK
- UNCLASSIFIED EXCAVATION - ACCEPTABLE, BUT NOT TO BE USED IN THE TOP 3 FEET OF EMBANKMENT OR BACKFILL

ABBREVIATIONS

AR - AUGER REFUSAL
BT - BORING TERMINATED
CL. - CLAY
CPT - CONE PENETRATION TEST
CSE. - COARSE
DMT - DILATOMETER TEST
DPT - DYNAMIC PENETRATION TEST
e - VOID RATIO
F - FINE
FOSS. - FOSSILIFEROUS
FRAC. - FRACTURED, FRACTURES
FRAGS. - FRAGMENTS
HI. - HIGHLY
MED. - MEDIUM
MICA. - MICACEOUS
MOD. - MODERATELY
NP - NON PLASTIC
ORG. - ORGANIC
PMT - PRESSUREMETER TEST
SAP. - SAPROLITIC
SD. - SAND, SANDY
SL. - SILT, SILTY
SLI. - SLIGHTLY
TCR - TRICONE REFUSAL
w - MOISTURE CONTENT
V - VERY
VST - VANE SHEAR TEST
WEA. - WEATHERED
γ - UNIT WEIGHT
γ_d - DRY UNIT WEIGHT

SAMPLE ABBREVIATIONS

S - BULK
SS - SPLIT SPOON
ST - SHELBY TUBE
RS - ROCK
RT - RECOMPACTED TRIAXIAL
CBR - CALIFORNIA BEARING RATIO

EQUIPMENT USED ON SUBJECT PROJECT

DRILL UNITS:
- [ ] CME-45C
- [ ] CME-55
- [ ] CME-550
- [ ] VANE SHEAR TEST
- [ ] PORTABLE HOIST
- [X] CME-45B
- [ ] _____

ADVANCING TOOLS:
- [X] CLAY BITS
- [ ] 6" CONTINUOUS FLIGHT AUGER
- [ ] 8" HOLLOW AUGERS
- [ ] HARD FACED FINGER BITS
- [ ] TUNG.-CARBIDE INSERTS
- [ ] CASING [ ] W/ ADVANCER
- [ ] TRICONE _____" STEEL TEETH
- [ ] TRICONE _____" TUNG.-CARB.
- [ ] CORE BIT
- [ ] _____

HAMMER TYPE:
- [X] AUTOMATIC [ ] MANUAL

CORE SIZE:
- [ ] -B _____ [ ] -H _____
- [ ] -N _____

HAND TOOLS:
- [ ] POST HOLE DIGGER
- [ ] HAND AUGER
- [ ] SOUNDING ROD
- [ ] VANE SHEAR TEST
- [ ] _____

ROCK DESCRIPTION

HARD ROCK IS NON-COASTAL PLAIN MATERIAL THAT WOULD YIELD SPT REFUSAL IF TESTED. AN INFERRED ROCK LINE INDICATES THE LEVEL AT WHICH NON-COASTAL PLAIN MATERIAL WOULD YIELD SPT REFUSAL. SPT REFUSAL IS PENETRATION BY A SPLIT SPOON SAMPLER EQUAL TO OR LESS THAN 0.1 FOOT PER 60 BLOWS IN NON-COASTAL PLAIN MATERIAL, THE TRANSITION BETWEEN SOIL AND ROCK IS OFTEN REPRESENTED BY A ZONE OF WEATHERED ROCK.
ROCK MATERIALS ARE TYPICALLY DIVIDED AS FOLLOWS:

WEATHERED ROCK (WR)	NON-COASTAL PLAIN MATERIAL THAT WOULD YIELD SPT N VALUES > 100 BLOWS PER FOOT IF TESTED.
CRYSTALLINE ROCK (CR)	FINE TO COARSE GRAIN IGNEOUS AND METAMORPHIC ROCK THAT WOULD YIELD SPT REFUSAL IF TESTED. ROCK TYPE INCLUDES GRANITE, GNEISS, GABBRO, SCHIST, ETC.
NON-CRYSTALLINE ROCK (NCR)	FINE TO COARSE GRAIN METAMORPHIC AND NON-COASTAL PLAIN SEDIMENTARY ROCK THAT WOULD YEILD SPT REFUSAL IF TESTED. ROCK TYPE INCLUDES PHYLLITE, SLATE, SANDSTONE, ETC.
COASTAL PLAIN SEDIMENTARY ROCK (CP)	COASTAL PLAIN SEDIMENTS CEMENTED INTO ROCK, BUT MAY NOT YIELD SPT REFUSAL. ROCK TYPE INCLUDES LIMESTONE, SANDSTONE, CEMENTED SHELL BEDS, ETC.

WEATHERING

FRESH	ROCK FRESH, CRYSTALS BRIGHT, FEW JOINTS MAY SHOW SLIGHT STAINING. ROCK RINGS UNDER HAMMER IF CRYSTALLINE.
VERY SLIGHT (V SLI.)	ROCK GENERALLY FRESH, JOINTS STAINED, SOME JOINTS MAY SHOW THIN CLAY COATINGS IF OPEN, CRYSTALS ON A BROKEN SPECIMEN FACE SHINE BRIGHTLY. ROCK RINGS UNDER HAMMER BLOWS IF OF A CRYSTALLINE NATURE.
SLIGHT (SLI.)	ROCK GENERALLY FRESH, JOINTS STAINED AND DISCOLORATION EXTENDS INTO ROCK UP TO 1 INCH. OPEN JOINTS MAY CONTAIN CLAY. IN GRANITOID ROCKS SOME OCCASIONAL FELDSPAR CRYSTALS ARE DULL AND DISCOLORED. CRYSTALLINE ROCKS RING UNDER HAMMER BLOWS.
MODERATE (MOD.)	SIGNIFICANT PORTIONS OF ROCK SHOW DISCOLORATION AND WEATHERING EFFECTS. IN GRANITOID ROCKS, MOST FELDSPARS ARE DULL AND DISCOLORED, SOME SHOW CLAY. ROCK HAS DULL SOUND UNDER HAMMER BLOWS AND SHOWS SIGNIFICANT LOSS OF STRENGTH AS COMPARED WITH FRESH ROCK.
MODERATELY SEVERE (MOD. SEV.)	ALL ROCK EXCEPT QUARTZ DISCOLORED OR STAINED. IN GRANITOID ROCKS, ALL FELDSPARS DULL AND DISCOLORED AND A MAJORITY SHOW KAOLINIZATION. ROCK SHOWS SEVERE LOSS OF STRENGTH AND CAN BE EXCAVATED WITH A GEOLOGIST'S PICK. ROCK GIVES "CLUNK" SOUND WHEN STRUCK. *IF TESTED, WOULD YIELD SPT REFUSAL*
SEVERE (SEV.)	ALL ROCK EXCEPT QUARTZ DISCOLORED OR STAINED. ROCK FABRIC CLEAR AND EVIDENT BUT REDUCED IN STRENGTH TO STRONG SOIL. IN GRANITOID ROCKS ALL FELDSPARS ARE KAOLINIZED TO SOME EXTENT. SOME FRAGMENTS OF STRONG ROCK USUALLY REMAIN. *IF TESTED, WOULD YIELD SPT N VALUES > 100 BPF*
VERY SEVERE (V SEV.)	ALL ROCK EXCEPT QUARTZ DISCOLORED OR STAINED. ROCK FABRIC ELEMENTS ARE DISCERNIBLE BUT MASS IS EFFECTIVELY REDUCED TO SOIL STATUS, WITH ONLY FRAGMENTS OF STRONG ROCK REMAINING. SAPROLITE IS AN EXAMPLE OF ROCK WEATHERED TO A DEGREE THAT ONLY MINOR VESTIGES OF ORIGINAL ROCK FABRIC REMAIN. *IF TESTED, WOULD YIELD SPT N VALUES < 100 BPF*
COMPLETE	ROCK REDUCED TO SOIL. ROCK FABRIC NOT DISCERNIBLE, OR DISCERNIBLE ONLY IN SMALL AND SCATTERED CONCENTRATIONS. QUARTZ MAY BE PRESENT AS DIKES OR STRINGERS. SAPROLITE IS ALSO AN EXAMPLE.

ROCK HARDNESS

VERY HARD	CANNOT BE SCRATCHED BY KNIFE OR SHARP PICK. BREAKING OF HAND SPECIMENS REQUIRES SEVERAL HARD BLOWS OF THE GEOLOGIST'S PICK.
HARD	CAN BE SCRATCHED BY KNIFE OR PICK ONLY WITH DIFFICULTY. HARD HAMMER BLOWS REQUIRED TO DETACH HAND SPECIMEN.
MODERATELY HARD	CAN BE SCRATCHED BY KNIFE OR PICK. GOUGES OR GROOVES TO 0.25 INCHES DEEP CAN BE EXCAVATED BY HARD BLOW OF A GEOLOGIST'S PICK. HAND SPECIMENS CAN BE DETACHED BY MODERATE BLOWS.
MEDIUM HARD	CAN BE GROOVED OR GOUGED 0.05 INCHES DEEP BY FIRM PRESSURE OF KNIFE OR PICK POINT. CAN BE EXCAVATED IN SMALL CHIPS TO PEICES 1 INCH MAXIMUM SIZE BY HARD BLOWS OF THE POINT OF A GEOLOGIST'S PICK.
SOFT	CAN BE GROVED OR GOUGED READILY BY KNIFE OR PICK. CAN BE EXCAVATED IN FRAGMENTS FROM CHIPS TO SEVERAL INCHES IN SIZE BY MODERATE BLOWS OF A PICK POINT. SMALL, THIN PIECES CAN BE BROKEN BY FINGER PRESSURE.
VERY SOFT	CAN BE CARVED WITH KNIFE. CAN BE EXCAVATED READILY WITH POINT OF PICK. PIECES 1 INCH OR MORE IN THICKNESS CAN BE BROKEN BY FINGER PRESSURE. CAN BE SCRATCHED READILY BY FINGERNAIL.

FRACTURE SPACING

TERM	SPACING
VERY WIDE	MORE THAN 10 FEET
WIDE	3 TO 10 FEET
MODERATELY CLOSE	1 TO 3 FEET
CLOSE	0.16 TO 1 FOOT
VERY CLOSE	LESS THAN 0.16 FEET

BEDDING

TERM	THICKNESS
VERY THICKLY BEDDED	4 FEET
THICKLY BEDDED	1.5 - 4 FEET
THINLY BEDDED	0.16 - 1.5 FEET
VERY THINLY BEDDED	0.03 - 0.16 FEET
THICKLY LAMINATED	0.008 - 0.03 FEET
THINLY LAMINATED	< 0.008 FEET

INDURATION

FOR SEDIMENTARY ROCKS, INDURATION IS THE HARDENING OF MATERIAL BY CEMENTING, HEAT, PRESSURE, ETC.

FRIABLE	RUBBING WITH FINGER FREES NUMEROUS GRAINS; GENTLE BLOW BY HAMMER DISINTEGRATES SAMPLE.
MODERATELY INDURATED	GRAINS CAN BE SEPARATED FROM SAMPLE WITH STEEL PROBE; BREAKS EASILY WHEN HIT WITH HAMMER.
INDURATED	GRAINS ARE DIFFICULT TO SEPARATE WITH STEEL PROBE; DIFFICULT TO BREAK WITH HAMMER.
EXTREMELY INDURATED	SHARP HAMMER BLOWS REQUIRED TO BREAK SAMPLE; SAMPLE BREAKS ACROSS GRAINS.

TERMS AND DEFINITIONS

ALLUVIUM (ALLUV.) - SOILS THAT HAVE BEEN TRANSPORTED BY WATER.

AQUIFER - A WATER BEARING FORMATION OR STRATA.

ARENACEOUS - APPLIED TO ROCKS THAT HAVE BEEN DERIVED FROM SAND OR THAT CONTAIN SAND.

ARGILLACEOUS - APPLIED TO ALL ROCKS OR SUBSTANCES COMPOSED OF CLAY MINERALS, OR HAVING A NOTABLE PROPORTION OF CLAY IN THEIR COMPOSITION, SUCH AS SHALE, SLATE, ETC.

ARTESIAN - GROUND WATER THAT IS UNDER SUFFICIENT PRESSURE TO RISE ABOVE THE LEVEL AT WHICH IT IS ENCOUNTERED, BUT WHICH DOES NOT NECESSARILY RISE TO OR ABOVE THE GROUND SURFACE.

CALCAREOUS (CALC.) - SOILS THAT CONTAIN APPRECIABLE AMOUNTS OF CALCIUM CARBONATE.

COLLUVIUM - ROCK FRAGMENTS MIXED WITH SOIL DEPOSITED BY GRAVITY ON SLOPE OR AT BOTTOM OF SLOPE.

CORE RECOVERY (REC.) - TOTAL LENGTH OF ALL MATERIAL RECOVERED IN THE CORE BARREL DIVIDED BY TOTAL LENGTH OF CORE RUN AND EXPRESSED AS A PERCENTAGE.

DIKE - A TABULAR BODY OF IGNEOUS ROCK THAT CUTS ACROSS THE STRUCTURE OF ADJACENT ROCKS OR CUTS MASSIVE ROCK.

DIP - THE ANGLE AT WHICH A STRATUM OR ANY PLANAR FEATURE IS INCLINED FROM THE HORIZONTAL.

DIP DIRECTION (DIP AZIMUTH) - THE DIRECTION OR BEARING OF THE HORIZONTAL TRACE OF THE LINE OF DIP, MEASURED CLOCKWISE FROM NORTH.

FAULT - A FRACTURE OR FRACTURE ZONE ALONG WHICH THERE HAS BEEN DISPLACEMENT OF THE SIDES RELATIVE TO ONE ANOTHER PARALLEL TO THE FRACTURE.

FISSILE - A PROPERTY OF SPLITTING ALONG CLOSELY SPACED PARALLEL PLANES.

FLOAT - ROCK FRAGMENTS ON SURFACE NEAR THEIR ORIGINAL POSITION AND DISLODGED FROM PARENT MATERIAL.

FLOOD PLAIN (FP) - LAND BORDERING A STREAM, BUILT OF SEDIMENTS DEPOSITED BY THE STREAM.

FORMATION (FM.) - A MAPPABLE GEOLOGIC UNIT THAT CAN BE RECOGNIZED AND TRACED IN THE FIELD.

JOINT - FRACTURE IN ROCK ALONG WHICH NO APPRECIABLE MOVEMENT HAS OCCURRED.

LEDGE - A SHELF-LIKE RIDGE OR PROJECTION OF ROCK WHOSE THICKNESS IS SMALL COMPARED TO ITS LATERAL EXTENT.

LENS - A BODY OF SOIL OR ROCK THAT THINS OUT IN ONE OR MORE DIRECTIONS.

MOTTLED (MOT.) - IRREGULARLY MARKED WITH SPOTS OF DIFFERENT COLORS. MOTTLING IN SOILS USUALLY INDICATES POOR AERATION AND LACK OF GOOD DRAINAGE.

PERCHED WATER - WATER MAINTAINED ABOVE THE NORMAL GROUND WATER LEVEL BY THE PRESENCE OF AN INTERVENING IMPERVIOUS STRATUM.

RESIDUAL (RES.) SOIL - SOIL FORMED IN PLACE BY THE WEATHERING OF ROCK.

ROCK QUALITY DESIGNATION (RQD) - A MEASURE OF ROCK QUALITY DESCRIBED BY TOTAL LENGTH OF ROCK SEGMENTS EQUAL TO OR GREATER THAN 4 INCHES DIVIDED BY THE TOTAL LENGTH OF CORE RUN AND EXPRESSED AS A PERCENTAGE.

SAPROLITE (SAP.) - RESIDUAL SOIL THAT RETAINS THE RELIC STRUCTURE OR FABRIC OF THE PARENT ROCK.

SILL - AN INTRUSIVE BODY OF IGNEOUS ROCK OF APPROXIMATELY UNIFORM THICKNESS AND RELATIVELY THIN COMPARED WITH ITS LATERAL EXTENT, THAT HAS BEEN EMPLACED PARALLEL TO THE BEDDING OR SCHISTOSITY OF THE INTRUDED ROCKS.

SLICKENSIDE - POLISHED AND STRIATED SURFACE THAT RESULTS FROM FRICTION ALONG A FAULT OR SLIP PLANE.

STANDARD PENETRATION TEST (PENETRATION RESISTANCE) (SPT) - NUMBER OF BLOWS (N OR BPF) OF A 140 LB. HAMMER FALLING 30 INCHES REQUIRED TO PRODUCE A PENETRATION OF 1 FOOT INTO SOIL WITH A 2 INCH OUTSIDE DIAMETER SPLIT SPOON SAMPLER. SPT REFUSAL IS PENETRATION EQUAL TO OR LESS THAN 0.1 FOOT PER 60 BLOWS.

STRATA CORE RECOVERY (SREC.) - TOTAL LENGTH OF STRATA MATERIAL RECOVERED DIVIDED BY TOTAL LENGTH OF STRATUM AND EXPRESSED AS A PERCENTAGE.

STRATA ROCK QUALITY DESIGNATION (SRQD) - A MEASURE OF ROCK QUALITY DESCRIBED BY TOTAL LENGTH OF ROCK SEGMENTS WITHIN A STRATUM EQUAL TO OR GREATER THAN 4 INCHES DIVIDED BY THE TOTAL LENGTH OF STRATA AND EXPRESSED AS A PERCENTAGE.

TOPSOIL (TS.) - SURFACE SOILS USUALLY CONTAINING ORGANIC MATTER.

BENCH MARK: BL-16 LOCATED SOUTHWEST OF WATER TREATMENT PLANT
• SEE NOTES SECTION FOR ADDITIONAL BENCH MARKS
ELEVATION: 41.24 FEET

NOTES:

UCP: UNDIVIDED COASTAL PLAIN

BENCH MARK: BL-20 STA. 190+44.62 -BL- ELEV: 43.06 FT

BENCH MARK: MANHOLE TOP STA . 127+84.02 72.03' RT -L- ELEV: 41.18 FT

LT.: LIGHT

DK.: DARK

W/: WITH

DATE: 8-15-14

8/6/13

PROJECT REFERENCE NO.	SHEET NO.
U-4751	3 OF 40

PEDEA ENGINEER

INCOMPLETE PLANS
DO NOT USE FOR R/W ACQUISITION

PRELIMINARY PLANS
DO NOT USE FOR CONSTRUCTION

PLAN AND PROFILE OF NOISE WALL 13

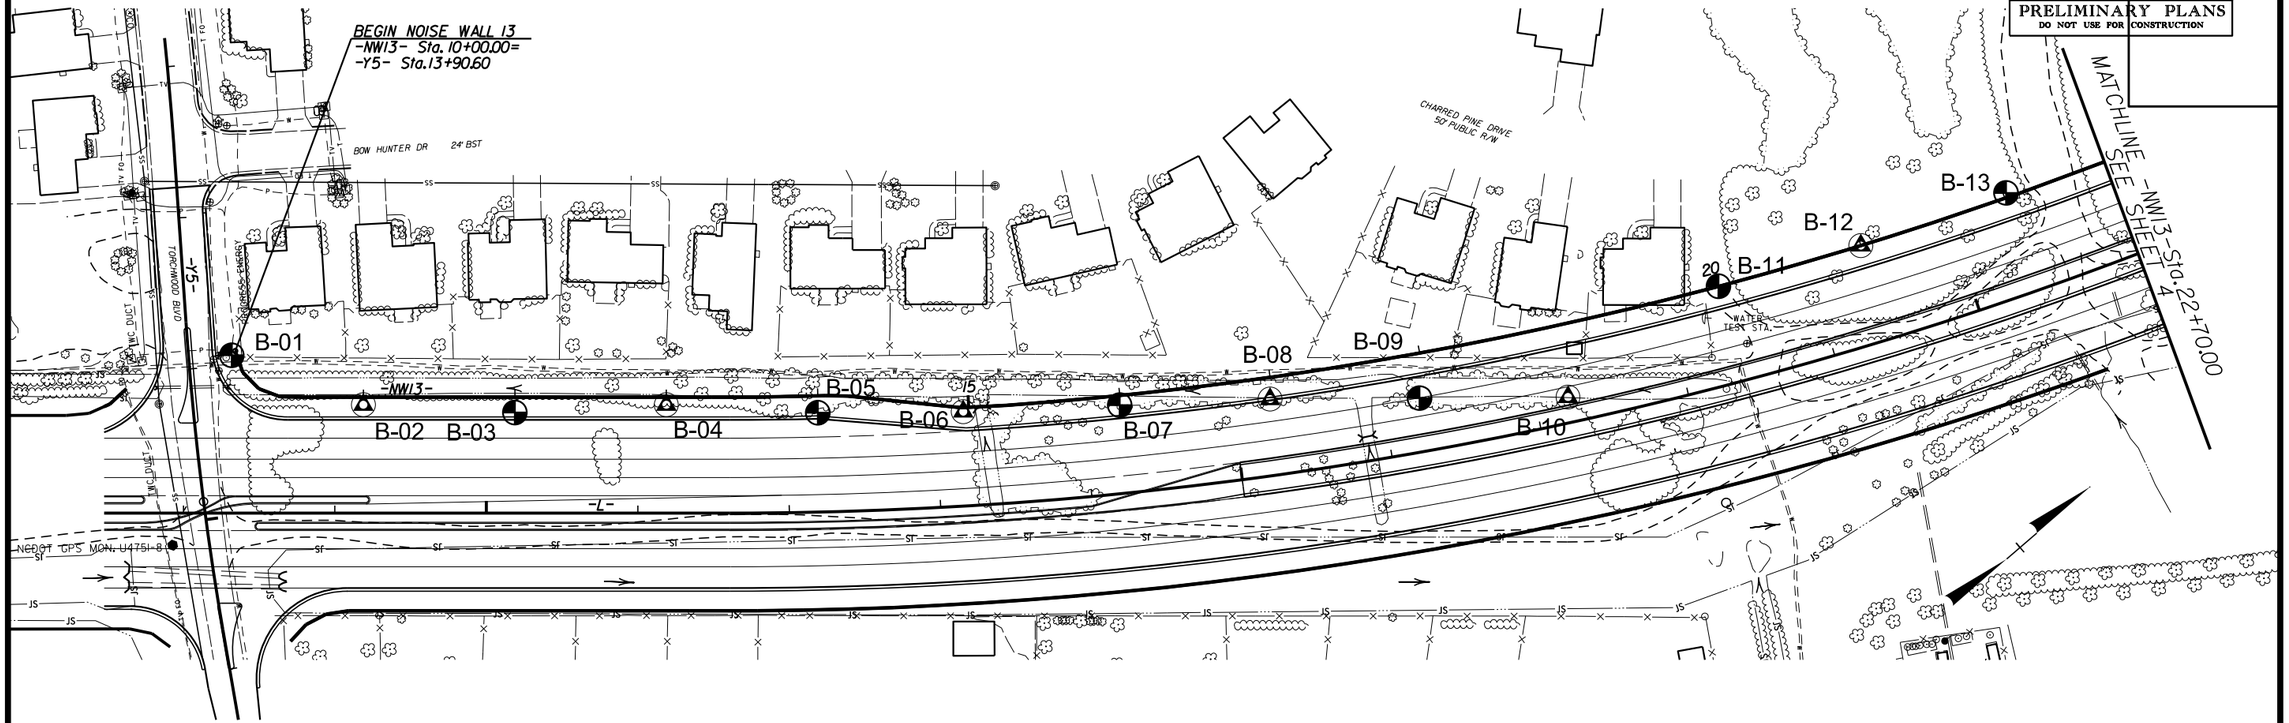

NOISE WALL 13 DESIGN DATA

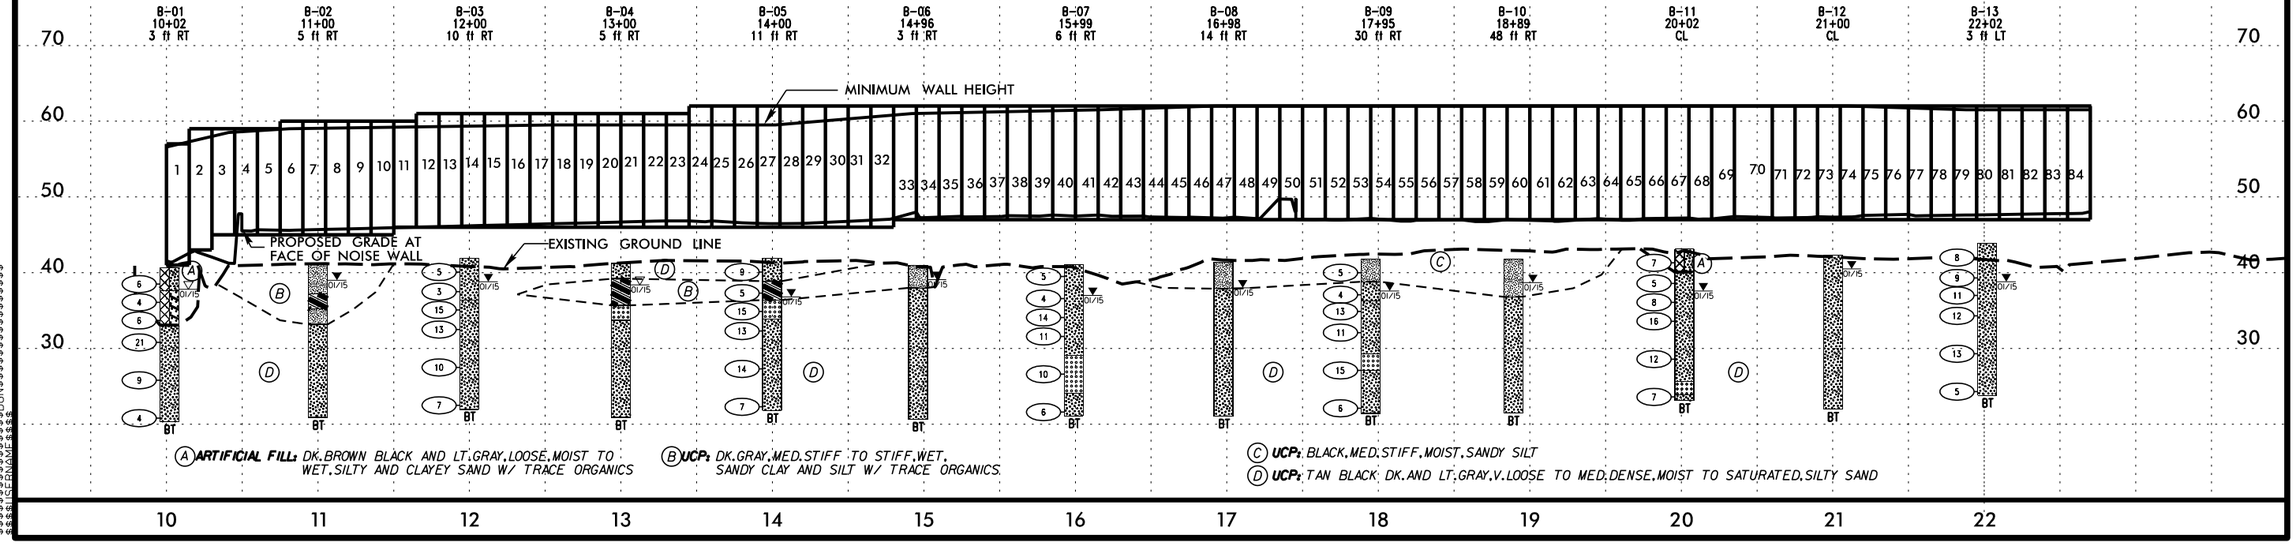

(A) **ARTIFICIAL FILL:** DK.BROWN BLACK AND LT.GRAY,LOOSE,MOIST TO WET,SILTY AND CLAYEY SAND W/ TRACE ORGANICS

(B) **UCP:** DK.GRAY,MED.STIFF TO STIFF,WET, SANDY CLAY AND SILT W/ TRACE ORGANICS.

(C) **UCP:** BLACK,MED.STIFF,MOIST,SANDY SILT

(D) **UCP:** TAN BLACK DK.AND LT.GRAY,V.LOOSE TO MED.DENSE,MOIST TO SATURATED,SILTY SAND

SYSTEM FILE: $$$$

8/6/13

PROJECT REFERENCE NO.	SHEET NO.
U-4751	4 OF 40

PEDEA ENGINEER

INCOMPLETE PLANS
DO NOT USE FOR R/W ACQUISITION

PRELIMINARY PLANS
DO NOT USE FOR CONSTRUCTION

PLAN AND PROFILE OF NOISE WALL 13

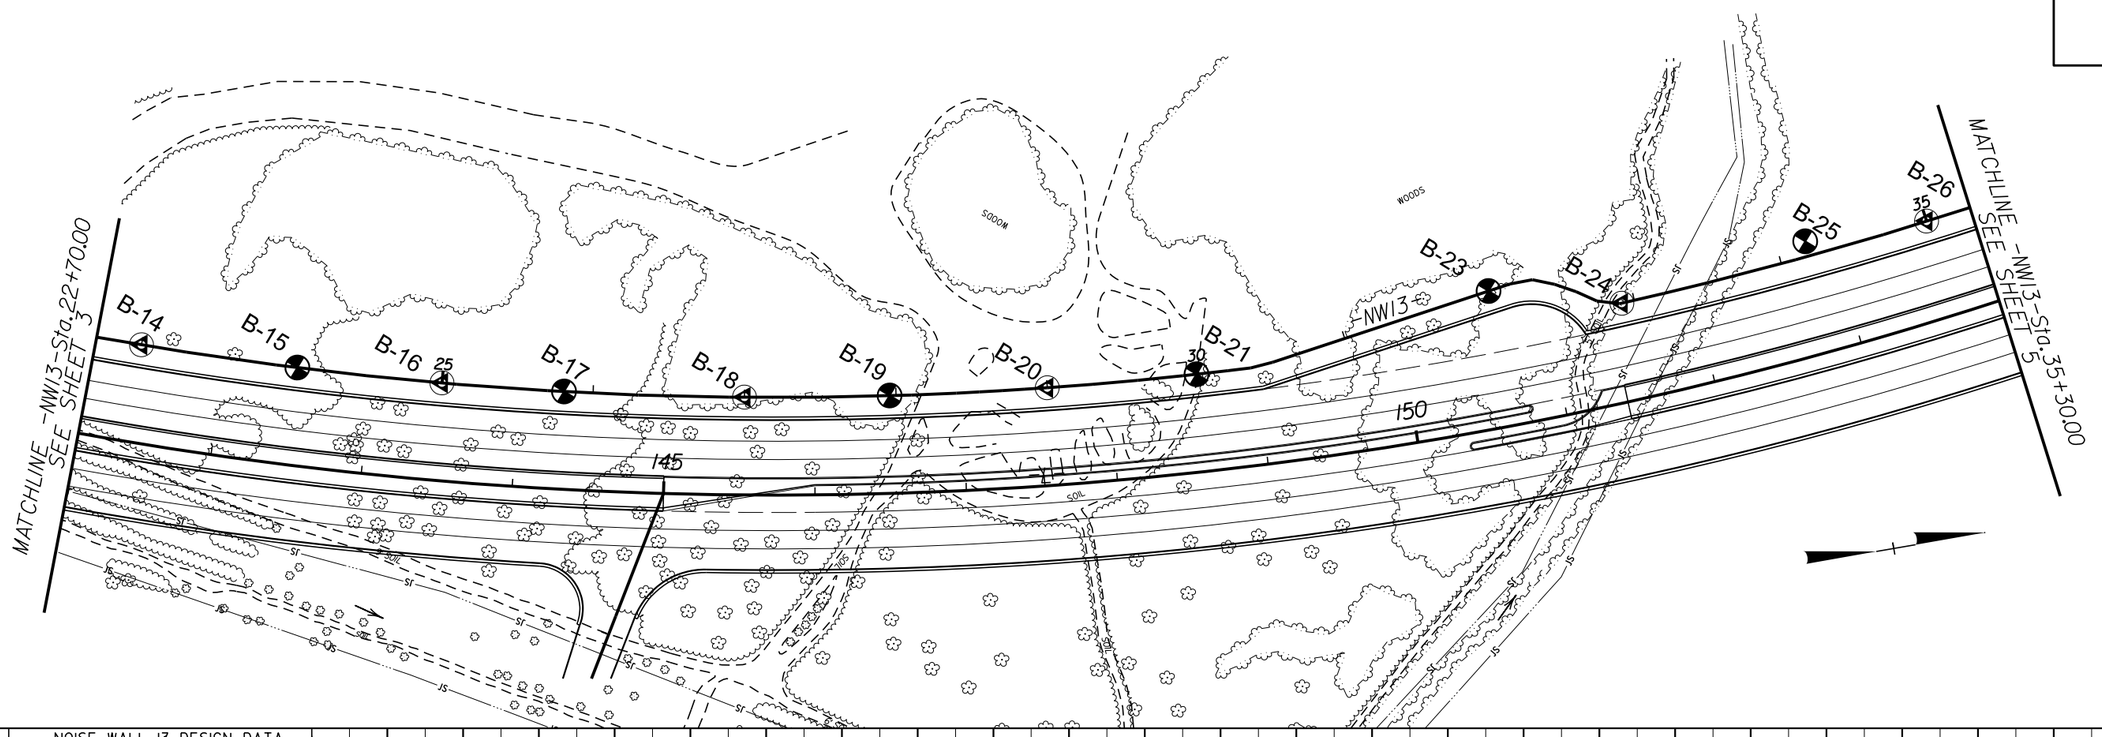

NOISE WALL 13 DESIGN DATA

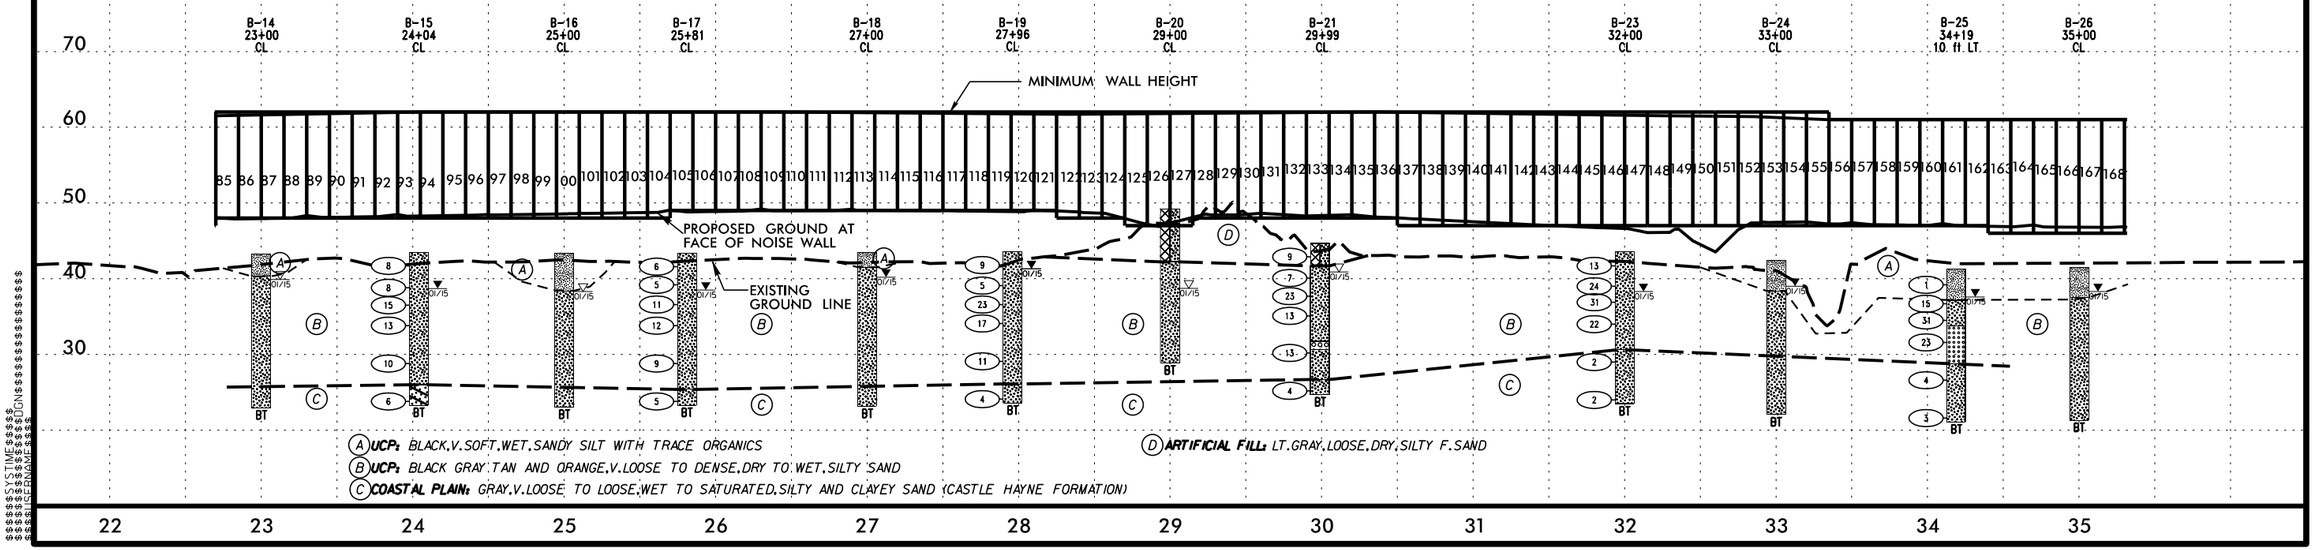

22 23 24 25 26 27 28 29 30 31 32 33 34 35

$SYSTIME $SYSDATE $SYSDWG $USERNAME

8/6/13

PROJECT REFERENCE NO.	SHEET NO.
U-4751	5 OF 40

PEDEA ENGINEER

INCOMPLETE PLANS
DO NOT USE FOR R/W ACQUISITION

PRELIMINARY PLANS
DO NOT USE FOR CONSTRUCTION

PLAN AND PROFILE OF NOISE WALL 13

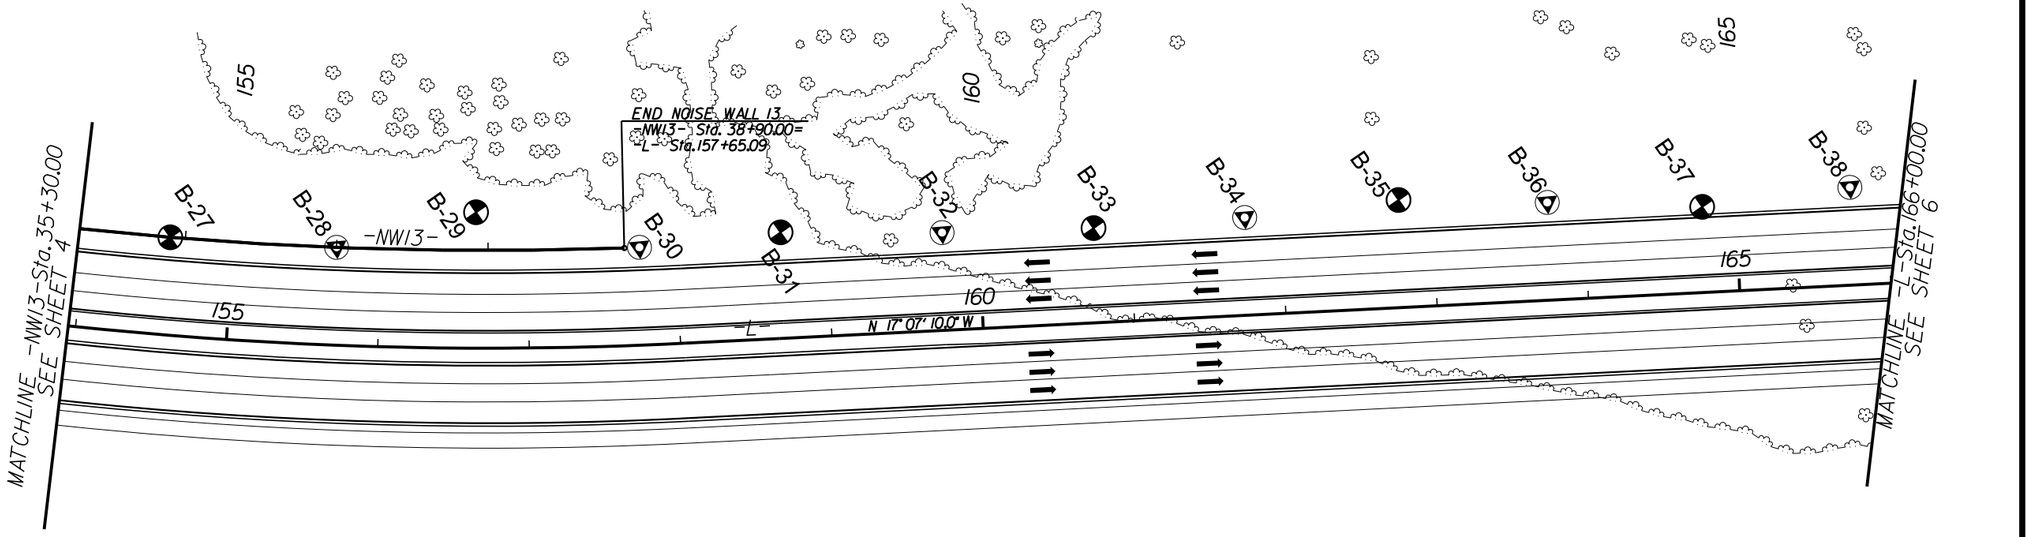

NOISE WALL 13 DESIGN DATA																													

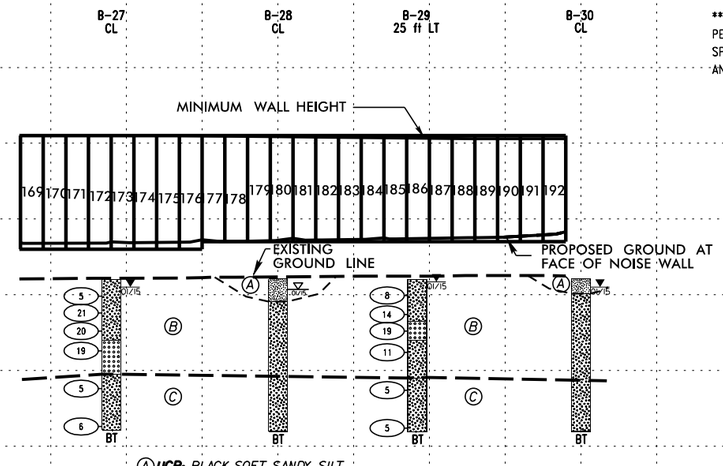

**NOTE: BORINGS B-31 THROUGH B-38 WERE PERFORMED PRIOR TO WALL ENVELOPE REVISIONS. SPT BORING LOGS CAN BE FOUND ON SHEETS 13-16 AND CPT LOGS CAN BE FOUND ON SHEETS 32-38.

Ⓐ **UCP:** BLACK, SOFT, SANDY SILT
Ⓑ **UCP:** BLACK BROWN TAN AND GRAY, LOOSE TO MED. DENSE, WET, SILTY SAND
Ⓒ **COASTAL PLAIN:** LT. GRAY, LOOSE, SATURATED, SILTY SAND (CASTLE HAYNE FORMATION)

35 36 37 38 39

SYSTIME $$$$

8/6/13

PROJECT REFERENCE NO.	SHEET NO.
U-4751	6 OF 40

PEDEA ENGINEER

INCOMPLETE PLANS
DO NOT USE FOR R/W ACQUISITION

PRELIMINARY PLANS
DO NOT USE FOR CONSTRUCTION

PLAN AND PROFILE OF NOISE WALL 13

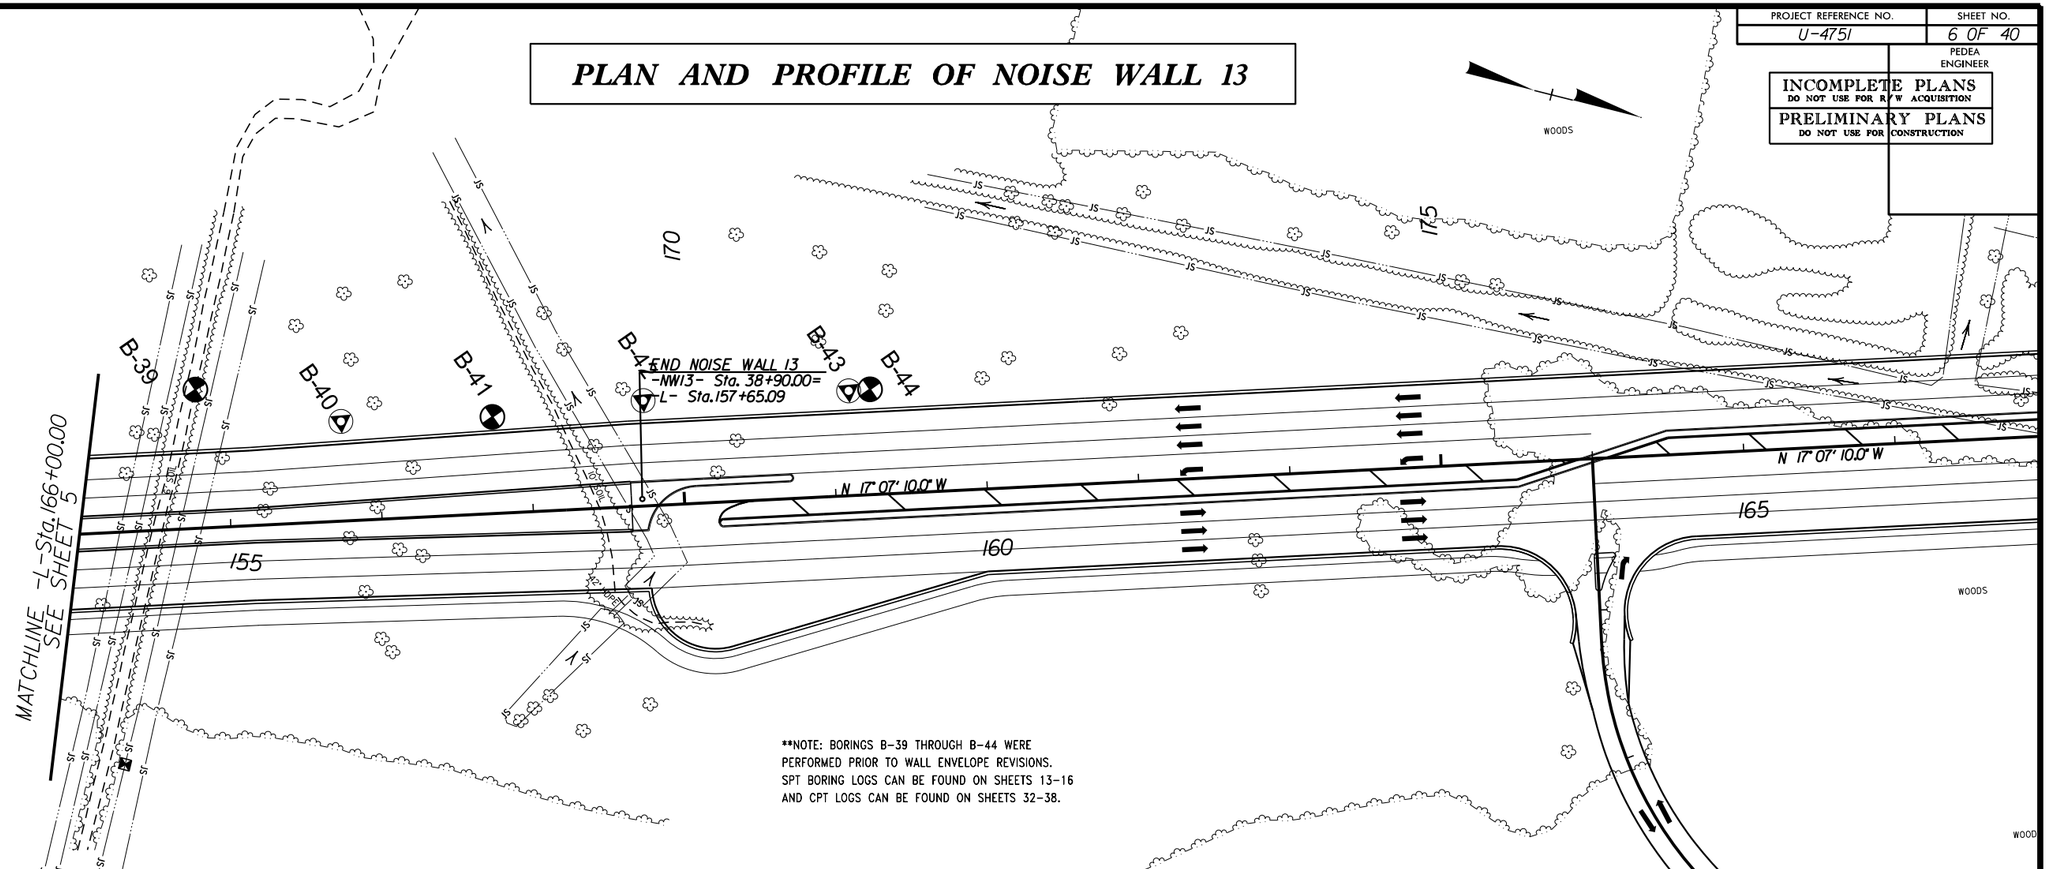

**NOTE: BORINGS B-39 THROUGH B-44 WERE PERFORMED PRIOR TO WALL ENVELOPE REVISIONS. SPT BORING LOGS CAN BE FOUND ON SHEETS 13-16 AND CPT LOGS CAN BE FOUND ON SHEETS 32-38.

NOISE WALL 13 DESIGN DATA

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-01	**STATION** 10+02	**OFFSET** 3 ft RT	**ALIGNMENT** -NW13-	**0 HR.** 2.8
COLLAR ELEV. 40.6 ft	**TOTAL DEPTH** 20.3 ft	**NORTHING** 197,256	**EASTING** 2,354,770	**24 HR.** FIAD
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/19/15	**COMP. DATE** 01/19/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
										ELEV. (ft) DEPTH (ft)
45										
40										40.6 0.3' TOPSOIL 0.0
	39.5	1.1	2	4	2	6		W		**ARTIFICIAL FILL** DK. BROWN, SILTY F. SAND (A-2-4)
	37.1	3.5	1	2	2	4		W		37.6 3.0 LT. GRAY, CLAYEY SAND (A-2-6) W/ TRACE ORGANICS
35	34.7	5.9	1	3	3	6		W		33.1 7.5 **UNDIVIDED COASTAL PLAIN** TAN AND GRAY, SILTY SAND (A-2-4)
	31.8	8.8	8	9	12	21		W		
30										
	26.8	13.8	2	4	5	9		W		
25										
	21.8	18.8	WOH	2	2	4		W		20.3 20.3 Boring Terminated at Elevation 20.3 ft in loose sand.

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-03	**STATION** 12+00	**OFFSET** 10 ft RT	**ALIGNMENT** -NW13-	**0 HR.** 0.2
COLLAR ELEV. 40.9 ft	**TOTAL DEPTH** 19.9 ft	**NORTHING** 197,373	**EASTING** 2,354,921	**24 HR.** 3.1
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/14/15	**COMP. DATE** 01/14/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
40										40.9 0.5' TOPSOIL 0.0
	40.1	0.8	2	2	3	5		M		**UNDIVIDED COASTAL PLAIN** BLACK AND GRAY, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS
	37.5	3.4	WOH	1	2	3		W		35.4 5.5 GRAY AND TAN, SILTY F. TO MED. SAND (A-2-4)
35	35.1	5.8	3	6	9	15		W		
	32.5	8.4	5	6	7	13		Sat.		
30										
	27.5	13.4	4	4	6	10		W		
25										
	22.5	18.4	4	4	3	7		W		21.0 19.9 Boring Terminated at Elevation 21.0 ft in loose sand.

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BOREHOLE REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-05	**STATION** 14+00	**OFFSET** 11 ft RT	**ALIGNMENT** -NW13-	**0 HR.** 4.6
COLLAR ELEV. 41.9 ft	**TOTAL DEPTH** 20.1 ft	**NORTHING** 197,524	**EASTING** 2,355,052	**24 HR.** 5.1
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/14/15	**COMP. DATE** 01/14/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45											
	41.1	0.8	3	4	5	9		M		41.9 0.8' TOPSOIL	0.0
40	38.3	3.6	2	2	3	5				**UNDIVIDED COASTAL PLAIN** BLACK AND GRAY, SILTY SAND (A-2-4)	
	35.9	6.0	4	6	9	15		W		38.9 DK. GRAY, F. SANDY CLAY (A-6) W/ TRACE ORGANICS	3.0
35	33.3	8.6	5	5	8	13		W		36.4 LT. GRAY, SILTY F. SAND (A-3)	5.5
	28.3	13.6	4	6	8	14		Sat.		33.9 TAN AND LT. GRAY, SILTY F. TO CSE. SAND (A-2-4)	8.0
30	23.3	18.6	3	3	4	7		W		21.8 Boring Terminated at Elevation 21.8 ft in loose sand.	20.1
25											

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-07	**STATION** 15+99	**OFFSET** 6 ft RT	**ALIGNMENT** -NW13-	**0 HR.** 1.1
COLLAR ELEV. 41.1 ft	**TOTAL DEPTH** 20.0 ft	**NORTHING** 197,678	**EASTING** 2,355,179	**24 HR.** 4.1
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/14/15	**COMP. DATE** 01/14/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
	40.5	0.6	2	3	2	5		M		41.1 0.7' TOPSOIL 0.0
40	37.6	3.5	WOH	1	3	4				**UNDIVIDED COASTAL PLAIN** BLACK DK. GRAY AND TAN, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS AND ROOTS
	35.1	6.0	5	7	7	14		W		
35	32.6	8.5	3	5	6	11		W		
	27.6	13.5	4	4	6	10		W		29.1 LT. GRAY AND TAN, SILTY F. SAND (A-3) 12.0
30	22.6	18.5	3	2	4	6		Sat.		24.1 LT. TO DK. GRAY, MED. TO CSE. SAND (A-2-4) 17.0
25								Sat.		21.1 Boring Terminated at Elevation 21.1 ft in loose sand. 20.0

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BOREHOLE REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-09	**STATION** 17+95	**OFFSET** 30 ft RT	**ALIGNMENT** -NW13-	**0 HR.** 3.7
COLLAR ELEV. 41.8 ft	**TOTAL DEPTH** 20.2 ft	**NORTHING** 197,830	**EASTING** 2,355,305	**24 HR.** 4.2
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/14/15	**COMP. DATE** 01/14/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
										ELEV. (ft) DEPTH (ft)
45										
	41.0	0.8	2	2	3	5		M		41.8 0.0 0.8' TOPSOIL
40	38.1	3.7	1	1	3	4		M		**UNDIVIDED COASTAL PLAIN** BLACK, F. SANDY SILT (A-4)
	35.9	5.9	5	5	8	13		W		38.8 3.0 BLACK AND DK. GRAY, SILTY F. SAND (A-2-4)
35	33.1	8.7	5	5	6	11		W		36.3 5.5 TAN AND GRAY, SILTY F. SAND (A-2-4)
30	28.1	13.7	5	6	9	15		W		29.3 12.5 LT. GRAY, SILTY F. TO MED. SAND (A-3)
25	23.1	18.7	2	3	3	6		Sat.		27.1 14.7 LT. GRAY AND TAN, SILTY F. SAND (A-2-4)
										21.6 20.2 Boring Terminated at Elevation 21.6 ft in loose sand.

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-11	**STATION** 20+02	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 1.5
COLLAR ELEV. 43.1 ft	**TOTAL DEPTH** 20.0 ft	**NORTHING** 198,028	**EASTING** 2,355,378	**24 HR.** 5.5
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/14/15	**COMP. DATE** 01/14/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
	42.3	0.8	3	3	4	7		M		43.1 0.0 0.7' SAND ROADWAY
40	39.6	3.5	3	2	3	5		M		**ARTIFICIAL FILL** BLACK, SILTY F. SAND (A-2-4) W/ LAYER OF GEOTECH FABRIC @ 1'
	37.1	6.0	2	3	5	8		W		40.1 3.0 **UNDIVIDED COASTAL PLAIN** TAN DK. GRAY AND BLACK, SILTY F. SAND (A-2-4)
35	34.6	8.5	6	7	9	16		W		
30	29.6	13.5	5	5	7	12		Sat.		CSE. SAND LAYER @ 14.2'
25	24.6	18.5	3	3	4	7		Sat.		25.6 17.5 GRAY, SILTY MED. TO CSE. SAND (A-1-b) 23.9 19.2 23.1 20.0 GRAY AND TAN, SILTY F. TO MED. SAND (A-2-4) Boring Terminated at Elevation 23.1 ft in loose sand.

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-13	**STATION** 22+02	**OFFSET** 3 ft LT	**ALIGNMENT** -NW13-	**0 HR.** 5.0
COLLAR ELEV. 43.9 ft	**TOTAL DEPTH** 20.1 ft	**NORTHING** 198,212	**EASTING** 2,355,456	**24 HR.** 5.1
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/14/15	**COMP. DATE** 01/14/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
										ELEV. (ft) DEPTH (ft)
45										
	43.0	0.9	1	3	5	8		D		43.9 0.8' TOPSOIL 0.0
40	40.3	3.6	3	4	5	9				**UNDIVIDED COASTAL PLAIN** LT. AND DK. GRAY AND BROWN, SILTY F. TO CSE. SAND (A-2-4) W/ TRACE ORGANICS IN TOP 3 FEET
	38.0	5.9	3	4	7	11		W		
35	35.3	8.6	5	5	7	12		Sat.		
30	30.3	13.6	5	6	7	13		W		
25	25.3	18.6	3	2	3	5		W		23.8 20.1 Boring Terminated at Elevation 23.8 ft in loose sand.

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-15	**STATION** 24+04	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 3.4
COLLAR ELEV. 43.5 ft	**TOTAL DEPTH** 20.2 ft	**NORTHING** 198,401	**EASTING** 2,355,525	**24 HR.** 4.8
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/14/15	**COMP. DATE** 01/14/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
	42.7	0.8	4	3	5	8		M		43.5 0.7' TOPSOIL 0.0
40	39.8	3.7	4	4	4	8		M		**UNDIVIDED COASTAL PLAIN** TAN AND GRAY, SILTY F. TO CSE. SAND (A-2-4)
	37.5	6.0	4	7	8	15		W		
35	34.8	8.7	4	6	7	13		W		
30	29.8	13.7	4	5	5	10		W		CSE. SAND LAYER @ 14.2'
25	24.8	18.7	3	3	3	6		W		26.0 17.5 **COASTAL PLAIN** LT.GRAY, CLAYEY F. SAND (A-2-6) (CASTLE HAYNE FORMATION) 23.3 20.2 Boring Terminated at Elevation 23.3 ft in loose sand.

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BOREHOLE REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-17	**STATION** 25+81	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 4.3
COLLAR ELEV. 43.4 ft	**TOTAL DEPTH** 20.1 ft	**NORTHING** 198,572	**EASTING** 2,355,571	**24 HR.** 4.9
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/15/15	**COMP. DATE** 01/15/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45											
	42.6	0.8	2	3	3	6		M		43.4 0.8' TOPSOIL	0.0
40	40.2	3.2	1	2	3	5				**UNDIVIDED COASTAL PLAIN** BLACK AND DK. GRAY, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS @ 3.2'	
	37.6	5.8	4	5	6	11		W			
35	34.8	8.6	5	5	7	12		W			
30	29.8	13.6	3	4	5	9		W		25.4 **COASTAL PLAIN**	18.0
25	24.8	18.6	3	3	2	5		W		23.3 LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	20.1
										Boring Terminated at Elevation 23.3 ft in loose sand.	

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-19	**STATION** 27+96	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 1.9
COLLAR ELEV. 43.6 ft	**TOTAL DEPTH** 20.0 ft	**NORTHING** 198,783	**EASTING** 2,355,611	**24 HR.** 2.3
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/15/15	**COMP. DATE** 01/15/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
	42.8	0.8	4	4	5	9				43.6 0.7' TOPSOIL 0.0
40	40.1	3.5	2	2	3	5		W		**UNDIVIDED COASTAL PLAIN** BLACK AND DK. GRAY, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS FROM 0-3 FEET
	37.6	6.0	7	9	14	23		W		
35	35.1	8.5	6	7	10	17		W		
30	30.1	13.5	4	5	6	11		W		26.1 17.5
25	25.1	18.5	3	2	2	4		W		**COASTAL PLAIN** 23.6 LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION) 20.0
										Boring Terminated at Elevation 23.6 ft in loose sand.

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-21	**STATION** 29+99	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 3.8
COLLAR ELEV. 44.7 ft	**TOTAL DEPTH** 20.0 ft	**NORTHING** 198,985	**EASTING** 2,355,632	**24 HR.** FIAD
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/15/15	**COMP. DATE** 01/15/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45										44.7	0.0
	43.9	0.8	1	4	5	9		D		**ARTIFICIAL FILL** LT. GRAY, SILTY F. SAND (A-2-4)	
	41.1	3.6								41.7	3.0
40			3	3	4	7		W		**UNDIVIDED COASTAL PLAIN** DK. BROWN AND BLACK, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS FROM 3-9 FEET	
	38.7	6.0	10	11	12	23		W			
	36.1	8.6									
35			4	5	8	13		W			
	31.2	13.5								31.7	13.0
			4	6	7	13		W		30.6 TAN AND GRAY, SILTY CSE. SAND (A-1-b)	14.1
30										TAN, SILTY F. SAND (A-2-4)	
	26.2	18.5								26.7	18.0
25			2	2	2	4		Sat.		**COASTAL PLAIN** LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	
										24.7	20.0
										Boring Terminated at Elevation 24.7 ft in loose sand.	

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-23	**STATION** 32+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 1.4
COLLAR ELEV. 43.6 ft	**TOTAL DEPTH** 20.1 ft	**NORTHING** 199,185	**EASTING** 2,355,610	**24 HR.** 5.3
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/15/15	**COMP. DATE** 01/15/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										43.6 0.0
	42.7	0.9	3	5	8	13		M		0.7' TOPSOIL **UNDIVIDED COASTAL PLAIN** TAN AND BLACK, SILTY F. TO MED. SAND (A-2-4)
40	40.0	3.6	4	6	18	24		W		
	37.9	5.7	11	13	18	31		M		
35	35.0	8.6	8	9	13	22				
										30.6 13.0
30	30.0	13.6	1	1	1	2		Sat.		**COASTAL PLAIN** LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)
25	25.0	18.6	1	1	1	2		Sat.		23.5 20.1
										Boring Terminated at Elevation 23.5 ft in very loose sand.

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BOREHOLE REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-25	**STATION** 34+19	**OFFSET** 10 ft LT	**ALIGNMENT** -NW13-	**0 HR.** 1.8
COLLAR ELEV. 41.3 ft	**TOTAL DEPTH** 20.2 ft	**NORTHING** 199,396	**EASTING** 2,355,614	**24 HR.** 3.7
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45											
										41.3	0.0
										1.0' TOPSOIL/ROOTMAT	
40	40.2	1.1	WOH	WOH	1	1		W		**UNDIVIDED COASTAL PLAIN** BLACK, F. SANDY SILT (A-4) W/ TRACE ORGANICS	
	37.7	3.6	1	6	9	15		W			37.2 4.1
35	35.5	5.8	8	13	18	31		W		DK. BROWN ORANGE AND BROWN, SILTY F. TO MED. SAND (A-2-4)	
	32.6	8.7	5	9	14	23		W			33.8 7.5
30										ORANGE AND TAN, SILTY F. SAND (A-3)	
	27.6	13.7	3	2	2	4		W			28.8 12.5
25										**COASTAL PLAIN** LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	
	22.6	18.7	3	2	1	3		W			21.1 20.2
										Boring Terminated at Elevation 21.1 ft in very loose sand.	

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-27	**STATION** 35+90	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 1.4
COLLAR ELEV. 42.0 ft	**TOTAL DEPTH** 19.9 ft	**NORTHING** 199,566	**EASTING** 2,355,601	**24 HR.** 1.0
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45											
										42.0	0.0
										0.8' TOPSOIL/ROOTMAT	
40	40.8	1.2	2	2	3	5		W		**UNDIVIDED COASTAL PLAIN** BLACK AND BROWN, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS	
	38.6	3.4	6	9	12	21		W			
	36.2	5.8	5	8	12	20		W			
35	33.6	8.4	5	8	11	19		W			34.0 8.0
										TAN AND GRAY, SILTY F. TO MED. SAND (A-3)	
30	28.6	13.4	2	2	3	5		Sat.			29.5 12.5
										COASTAL PLAIN LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	
25	23.6	18.4	3	2	4	6		Sat.			22.1 19.9
										Boring Terminated at Elevation 22.1 ft in loose sand.	

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-29	**STATION** 37+92	**OFFSET** 25 ft LT	**ALIGNMENT** -NW13-	**0 HR.** 1.3
COLLAR ELEV. 42.0 ft	**TOTAL DEPTH** 20.1 ft	**NORTHING** 199,758	**EASTING** 2,355,536	**24 HR.** 0.3
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45											
										42.0	0.0
										0.7' TOPSOIL/ROOTMAT	
40	40.9	1.1	4	5	3	8		W		**UNDIVIDED COASTAL PLAIN** DK. GRAY AND BROWN, SILTY F. SAND (A-2-4)	
	38.4	3.6	4	6	8	14		W			
	36.2	5.8	6	8	11	19		W		36.5	5.5
35	33.4	8.6	7	4	7	11		W		BROWN, SILTY F. SAND (A-3)	
										34.0	8.0
										BROWN AND TAN, SILTY F. SAND (A-2-4)	
30	28.4	13.6	1	2	3	5		Sat.		29.0	13.0
										COASTAL PLAIN LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	
25	23.4	18.6	2	2	3	5		Sat.		21.9	20.1
										Boring Terminated at Elevation 21.9 ft in loose sand.	

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-31	**STATION** 158+70	**OFFSET** 65 ft LT	**ALIGNMENT** -L-	**0 HR.** 1.7
COLLAR ELEV. 42.2 ft	**TOTAL DEPTH** 20.0 ft	**NORTHING** 199,956	**EASTING** 2,355,499	**24 HR.** 0.4
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
										42.2 0.0
										0.7' TOPSOIL/ROOTMAT
40	41.1	1.1	3	8	7	15		W		**UNDIVIDED COASTAL PLAIN** DK. GRAY BROWN AND TAN, SILTY F. TO MED. SAND (A-2-4)
	38.7	3.5	4	6	9	15		W		
	36.5	5.7	5	8	11	19		W		36.7 5.5
35	33.7	8.5	3	5	8	13		W		TAN, SILTY F. TO MED. SAND (A-3)
										34.2 8.0
										TAN, SILTY SAND (A-2-4)
30	28.7	13.5	1	1	2	3		Sat.		29.7 12.5
										COASTAL PLAIN LT. GRAY, CLAYEY SAND (A-2-6) (CASTLE HAYNE FORMATION)
25	23.7	18.5	2	1	1	2		Sat.		25.2 17.0
										LT. GRAY, SILTY F. SAND (A-2-4)
										22.2 20.0
										Boring Terminated at Elevation 22.2 ft in very loose sand.
										NOTE: BORING PERFORMED BASED ON PRELIMINARY WALL ENVELOPE PRIOR TO REVISIONS AND THEREFORE IS REFERENCED TO -L-

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BOREHOLE REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-33	**STATION** 160+76	**OFFSET** 63 ft LT	**ALIGNMENT** -L-	**0 HR.** 2.6
COLLAR ELEV. 42.0 ft	**TOTAL DEPTH** 19.8 ft	**NORTHING** 200,156	**EASTING** 2,355,445	**24 HR.** 0.3
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45											
										42.0	0.0
										0.9' TOPSOIL/ROOTMAT	
	40.8	1.2	3	3	3	6		W		**UNDIVIDED COASTAL PLAIN** BROWN AND TAN, SILTY SAND (A-2-4) W/ TRACE ORGANICS	
40	38.5	3.5	2	3	4	7		W			
	36.3	5.7	5	5	7	12		W			
35	33.7	8.3	4	4	7	11		W			
30										29.0	13.0
	28.7	13.3	2	2	3	5		W		**COASTAL PLAIN** LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	
25	23.7	18.3	2	2	2	4		W		22.2	19.8
										Boring Terminated at Elevation 22.2 ft in loose sand.	
										NOTE: BORING PERFORMED BASED ON PRELIMINARY WALL ENVELOPE PRIOR TO REVISIONS AND THEREFORE IS REFERENCED TO -L-	

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-35	**STATION** 162+78	**OFFSET** 71 ft LT	**ALIGNMENT** -L-	**0 HR.** 2.0
COLLAR ELEV. 42.1 ft	**TOTAL DEPTH** 20.0 ft	**NORTHING** 200,346	**EASTING** 2,355,378	**24 HR.** 0.5
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
										42.1 0.5' TOPSOIL/ROOTMAT 0.0
	40.9	1.2	2	2	1	3		W		**UNDIVIDED COASTAL PLAIN** DK. BROWN, SILTY SAND (A-2-4)
40	38.7	3.4	1	3	5	8		W		39.1 3.0
	36.8	5.3	5	5	6	11		W		DK. BROWN, SANDY SILT (A-4) W/ MODERATE ORGANICS
35	33.6	8.5	3	4	6	10		M		37.1 5.0
										LT. GRAY AND TAN, SILTY F. SAND (A-2-4)
30										29.1 13.0
	28.6	13.5	3	3	2	5		W		**COASTAL PLAIN** LT. GRAY AND TAN, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)
25	23.6	18.5	2	1	1	2		W		22.1 20.0
										Boring Terminated at Elevation 22.1 ft in very loose sand.
										NOTE: BORING PERFORMED BASED ON PRELIMINARY WALL ENVELOPE PRIOR TO REVISIONS AND THEREFORE IS REFERENCED TO -L-

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-37	**STATION** 164+78	**OFFSET** 57 ft LT	**ALIGNMENT** -L-	**0 HR.** 1.1
COLLAR ELEV. 40.9 ft	**TOTAL DEPTH** 20.1 ft	**NORTHING** 200,542	**EASTING** 2,355,333	**24 HR.** 0.3
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION ELEV. (ft)	DEPTH (ft)
45											
										40.9	0.0
40	39.9	1.0	WOH	WOH	1	1		W		0.7' TOPSOIL/ROOTMAT	
	37.3	3.6	3	3	4	7		W		**UNDIVIDED COASTAL PLAIN** BLACK AND DK. GRAY, F. SANDY SILT (A-4)	
35	35.2	5.7	4	6	6	12		W		37.9	3.0
	32.3	8.6	4	4	3	7		W		LT. GRAY, CLAYEY SAND (A-2-6)	
30										35.9	5.0
	27.3	13.6	2	1	1	2		Sat.		LT. GRAY AND TAN, SILTY F. TO MED. SAND (A-2-4)	
25										28.4	12.5
	22.3	18.6	1	1	2	3		W		**COASTAL PLAIN** LT. GRAY, CLAYEY F. SAND (A-2-6) (CASTLE HAYNE FORMATION)	
										20.8	20.1
										Boring Terminated at Elevation 20.8 ft in very loose sand.	
										NOTE: BORING PERFORMED BASED ON PRELIMINARY WALL ENVELOPE PRIOR TO REVISIONS AND THEREFORE IS REFERENCED TO -L-	

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.	
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13				**GROUND WTR (ft)**
BORING NO. B-39	**STATION** 166+81	**OFFSET** 91 ft LT	**ALIGNMENT** -L-	**0 HR.** 1.7
COLLAR ELEV. 43.1 ft	**TOTAL DEPTH** 19.8 ft	**NORTHING** 200,725	**EASTING** 2,355,239	**24 HR.** 3.5
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic	
DRILLER Contract Driller	**START DATE** 01/16/15	**COMP. DATE** 01/16/15	**SURFACE WATER DEPTH** N/A	

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION
45										
	42.3	0.8	2	2	3	5		M		43.1 0.4' TOPSOIL/ROOTMAT 0.0
40	39.8	3.3	2	3	3	6		W		**UNDIVIDED COASTAL PLAIN** BLACK AND DK. GRAY, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS 40.1 3.0
	37.9	5.2	3	4	6	10		W		BLACK, F. SANDY SILT (A-4) W/ TRACE ORGANICS 38.1 5.0
35	34.8	8.3	8	8	11	19		W		BROWN TAN AND LT. GRAY, SILTY F. SAND (A-2-4)
30	29.8	13.3	2	2	1	3		Sat.		
25	24.8	18.3	1	1	1	2		W		26.1 17.0 **COASTAL PLAIN** LT. GRAY, CLAYEY F. SAND (A-2-6) (CASTLE HAYNE FORMATION) 23.3 19.8
										Boring Terminated at Elevation 23.3 ft in very loose sand.
										NOTE: BORING PERFORMED BASED ON PRELIMINARY WALL ENVELOPE PRIOR TO REVISIONS AND THEREFORE IS REFERENCED TO -L-

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13			**GROUND WTR (ft)**
BORING NO. B-41	**STATION** 168+76	**OFFSET** 64 ft LT	**ALIGNMENT** -L-	**0 HR.** 2.4
COLLAR ELEV. 40.6 ft	**TOTAL DEPTH** 20.1 ft	**NORTHING** 200,824	**EASTING** 2,355,236	**24 HR.** 3.9
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic
DRILLER Contract Driller	**START DATE** 01/15/15	**COMP. DATE** 01/15/15	**SURFACE WATER DEPTH** N/A

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION — ELEV. (ft)	DEPTH (ft)
45											
40	39.8	0.8	2	3	2	5 6		W		40.6 — 0.8' TOPSOIL/ROOTMAT	0.0
	36.8	3.8	2	3	3			W		**UNDIVIDED COASTAL PLAIN** BLACK AND LT. GRAY, SILTY F. SAND (A-2-4) W/ TRACE ORGANICS FROM 3' TO 5'	
35	34.5	6.1	9	12	12	24		M			
	32.0	8.6	6	7	8	15		W			
30											
	27.0	13.6	2	1	2	3		W		28.1 — LT. GRAY, CLAYEY F. SAND (A-2-6)	12.5
25										23.6 — **COASTAL PLAIN** LT. GRAY, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	17.0
	22.0	18.6	WOH	2	1	3		Sat.		20.5 — Boring Terminated at Elevation 20.5 ft in very loose sand.	20.1
										NOTE: BORING PERFORMED BASED ON PRELIMINARY WALL ENVELOPE PRIOR TO REVISIONS AND THEREFORE IS REFERENCED TO -L-	

WBS 40191.1.2	**TIP** U-4751	**COUNTY** NEW HANOVER	**GEOLOGIST** Hunsberger, W. S.
SITE DESCRIPTION SR 1409 (MILITARY CUTTOFF RD) TO US 17 IN WILMINGTON - NOISE WALL 13			**GROUND WTR (ft)**
BORING NO. B-44	**STATION** 171+26	**OFFSET** 69 ft LT	**ALIGNMENT** -L-	**0 HR.** 1.3
COLLAR ELEV. 41.7 ft	**TOTAL DEPTH** 20.0 ft	**NORTHING** 201,157	**EASTING** 2,355,129	**24 HR.** 3.4
DRILL RIG/HAMMER EFF./DATE MID1904 CME-45B 80% 10/14/2014		**DRILL METHOD** Mud Rotary	**HAMMER TYPE** Automatic
DRILLER Contract Driller	**START DATE** 01/15/15	**COMP. DATE** 01/15/15	**SURFACE WATER DEPTH** N/A

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT 0 25 50 75 100	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION	
45											
										41.7 — 0.9' TOPSOIL/ROOTMAT	0.0
40	40.9	0.8	2	2	2	4		M		**UNDIVIDED COASTAL PLAIN** BLACK, F. SANDY SILT (A-4) W/ TRACE ORGANICS	
	38.2	3.5	2	3	3	6		Sat.		38.7 — LT. AND DK. GRAY, SILTY F. TO MED. SAND (A-2-4) W/ TRACE ORGANICS AT 8.5 '	3.0
35	36.2	5.5	3	4	8	12		W			
	33.2	8.5	6	8	10	18		W			
30											
	28.2	13.5	3	3	2	5		Sat.		28.7 — **COASTAL PLAIN** LT. AND DK. GRAY AND TAN, SILTY F. SAND (A-2-4) (CASTLE HAYNE FORMATION)	13.0
25	23.2	18.5	1	2	2	4		W		21.7 — Boring Terminated at Elevation 21.7 ft in loose sand.	20.0
										NOTE: BORING PERFORMED BASED ON PRELIMINARY WALL ENVELOPE PRIOR TO REVISIONS AND THEREFORE IS REFERENCED TO -L-	

NCDOT BORE DOUBLE U4751_GEO_SWAL0013_GINT.GPJ NC_DOT.GDT 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-02	**BORING LOCATION** 11+00	**OFFSET** 5' RT	**ALIGNMENT** -NW13-	**0 HR.** 3.6	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.2 ft	**NORTHING** 197,300	**EASTING** 2,354,852		**24 HR.** 2.2	**DRILLER** CONTRACT DRILLER		

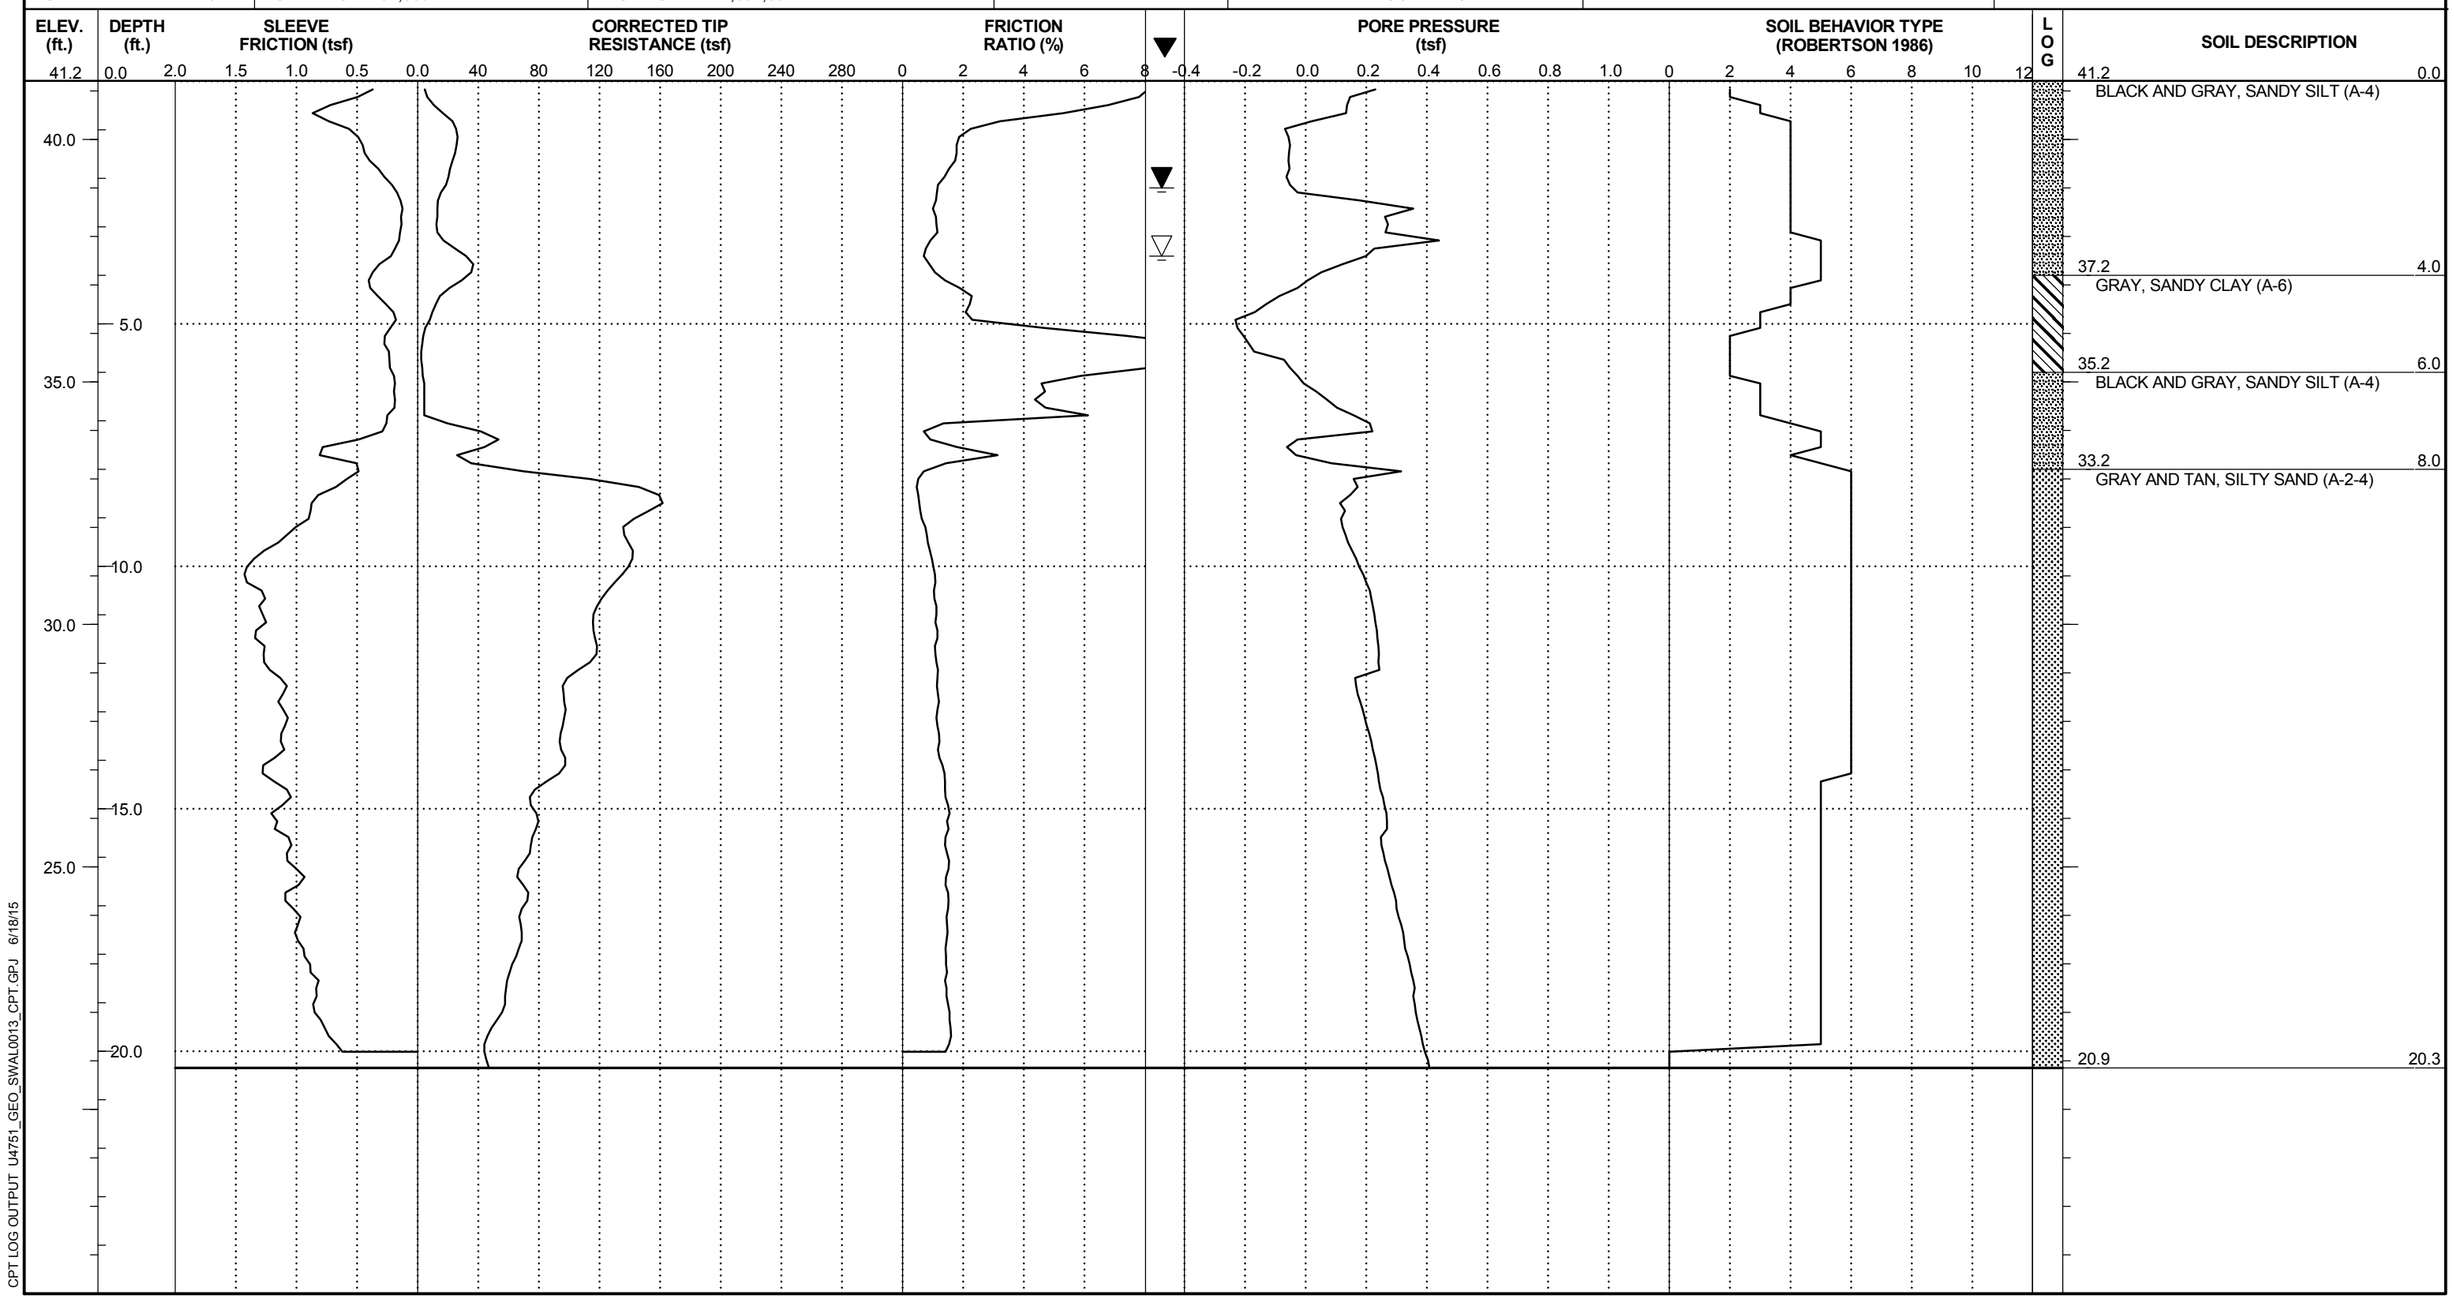

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-04	**BORING LOCATION** 13+00	**OFFSET** 5' RT	**ALIGNMENT** -NW13-	**0 HR.** 2.8	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.2 ft	**NORTHING** 197,452	**EASTING** 2,354,983		**24 HR.** CAVED	**DRILLER** CONTRACT DRILLER		

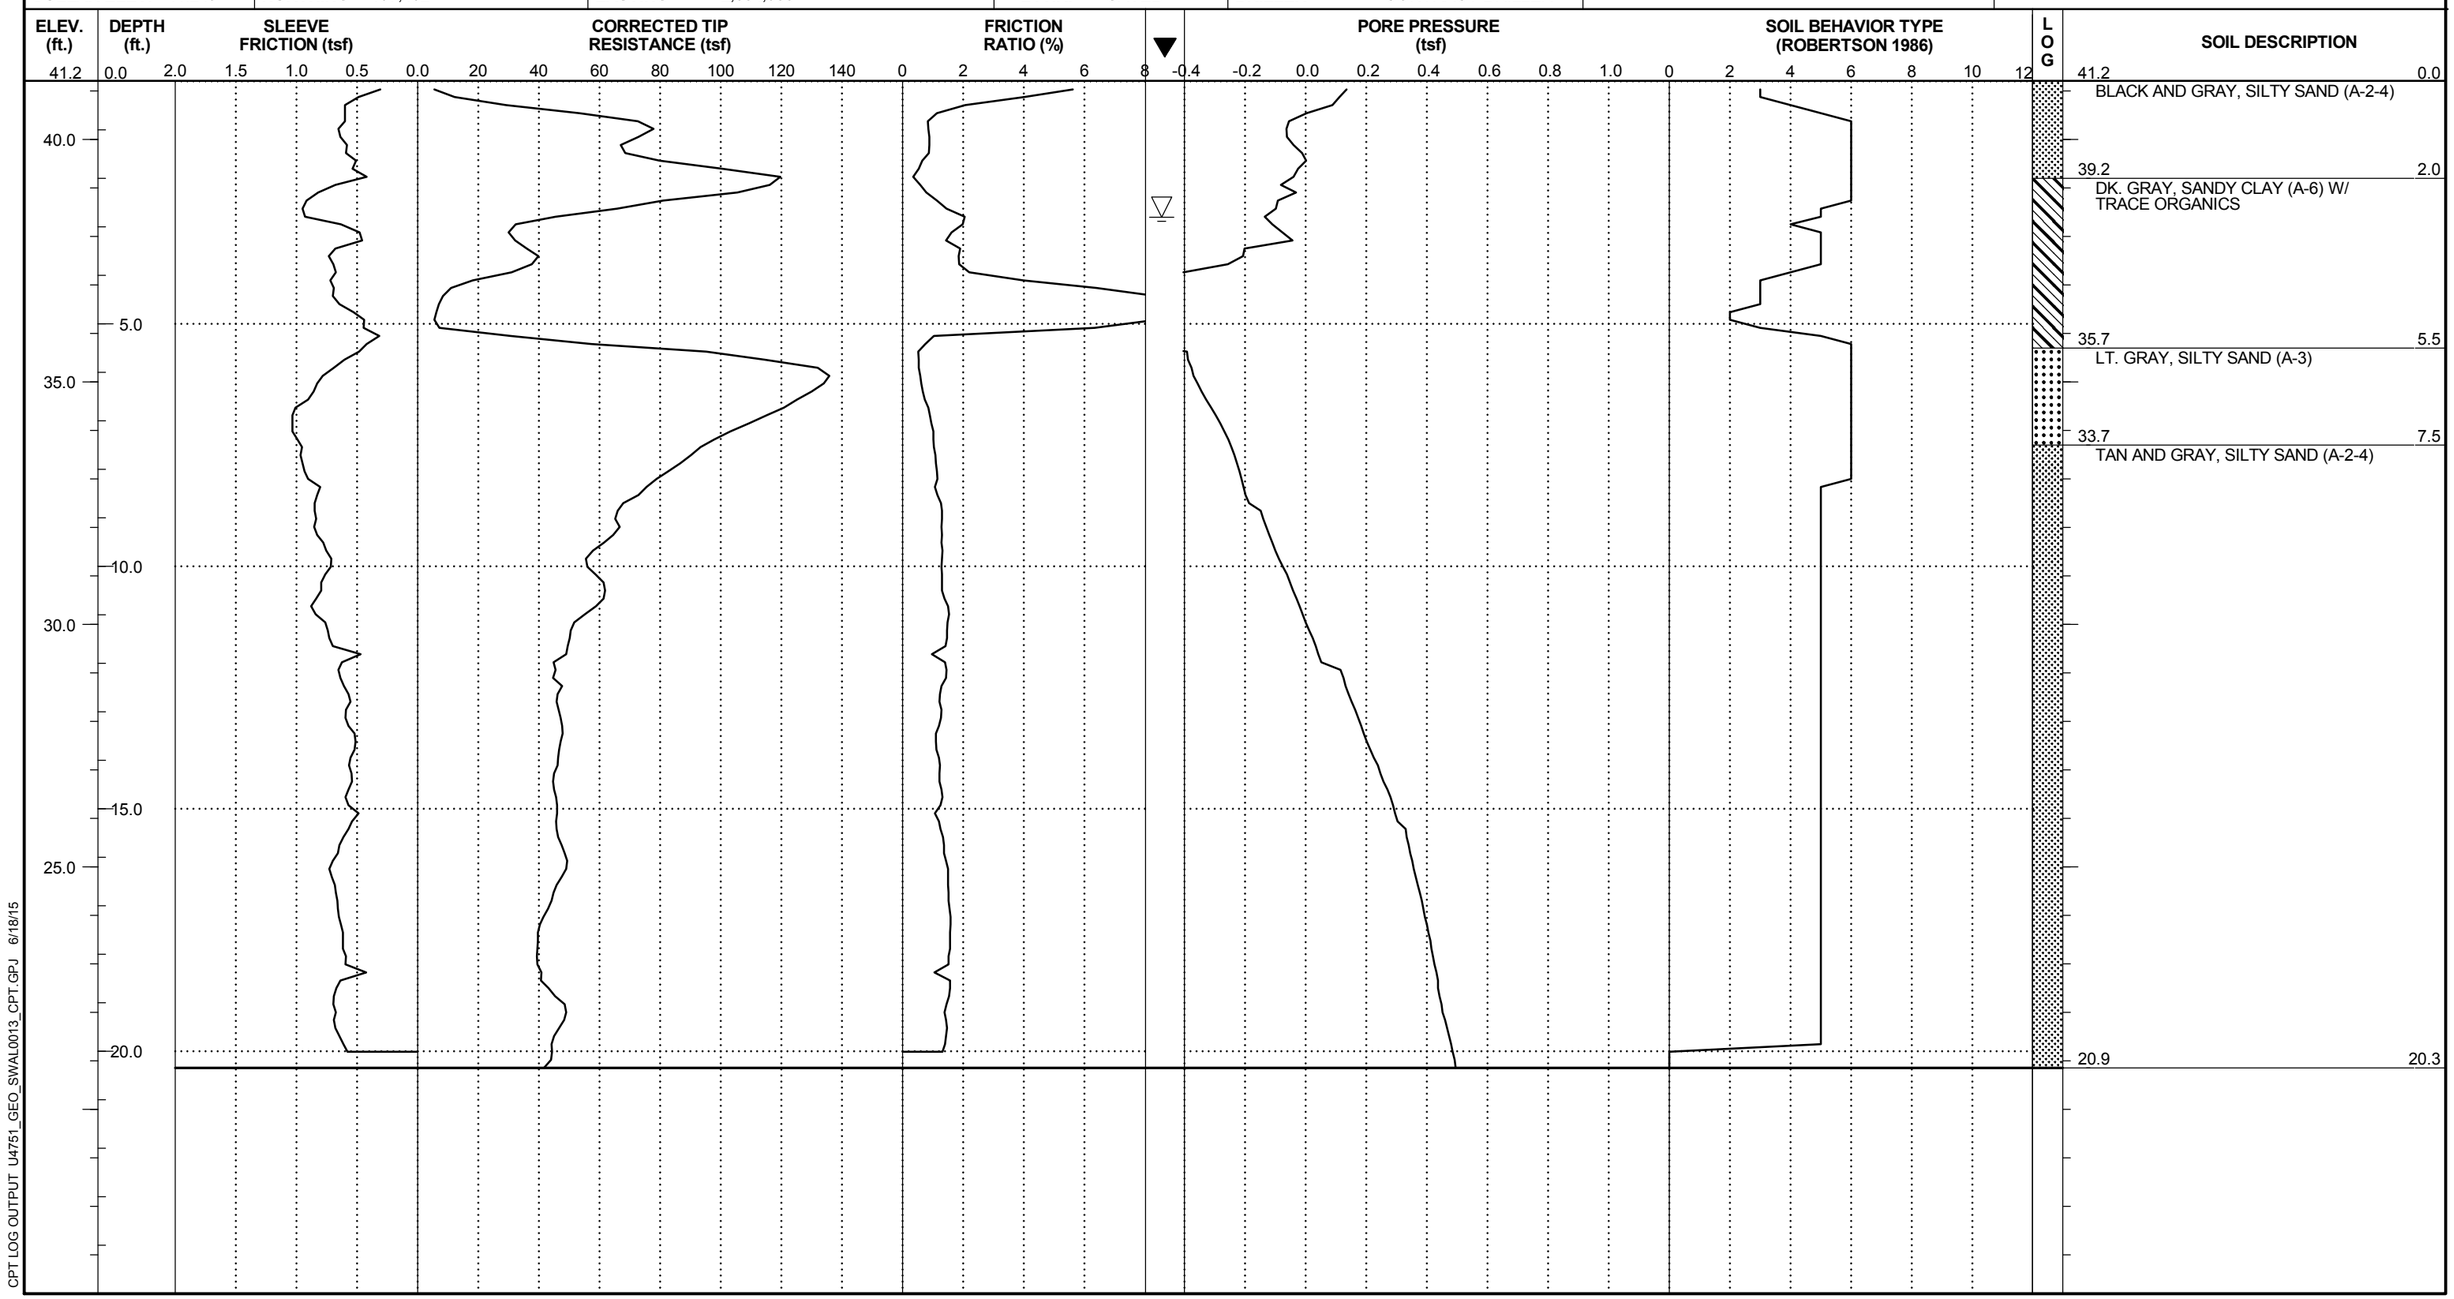

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-06	**BORING LOCATION** 14+96	**OFFSET** 3' RT	**ALIGNMENT** -NW13-	**0 HR.** 2.8	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.0 ft	**NORTHING** 197,597	**EASTING** 2,355,115		**24 HR.** 1.9	**DRILLER** CONTRACT DRILLER		

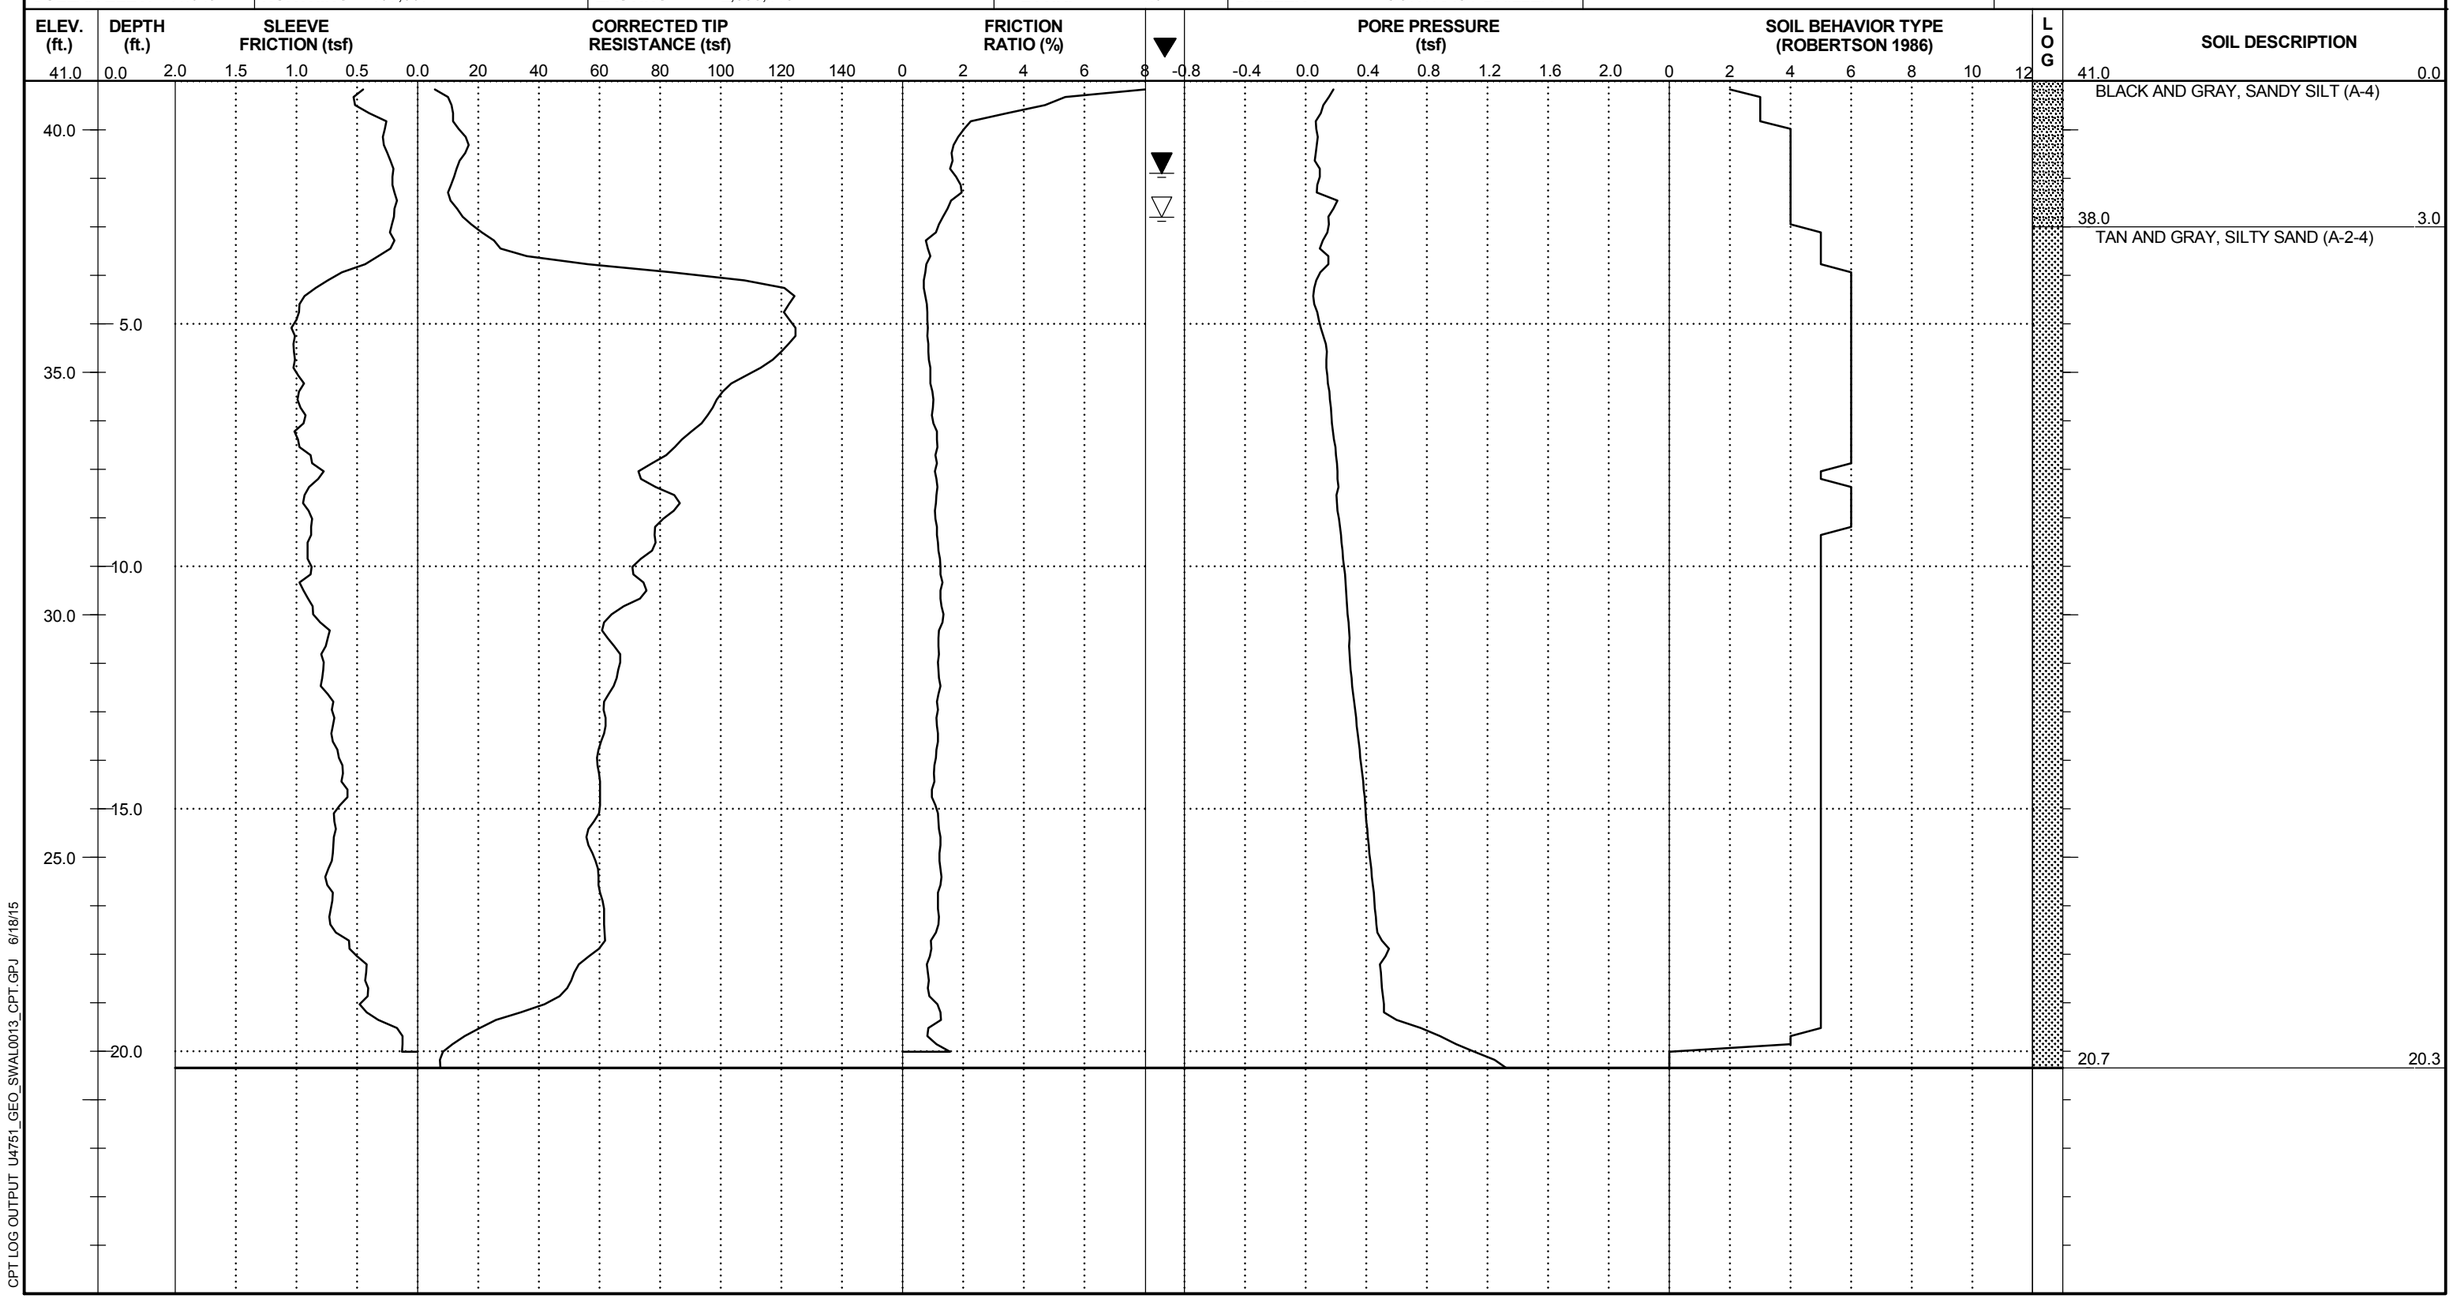

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-08	**BORING LOCATION** 16+98	**OFFSET** 14' RT	**ALIGNMENT** -NW13-	**0 HR.** 3.8	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.4 ft	**NORTHING** 197,755	**EASTING** 2,355,241		**24 HR.** 3.4	**DRILLER** CONTRACT DRILLER		

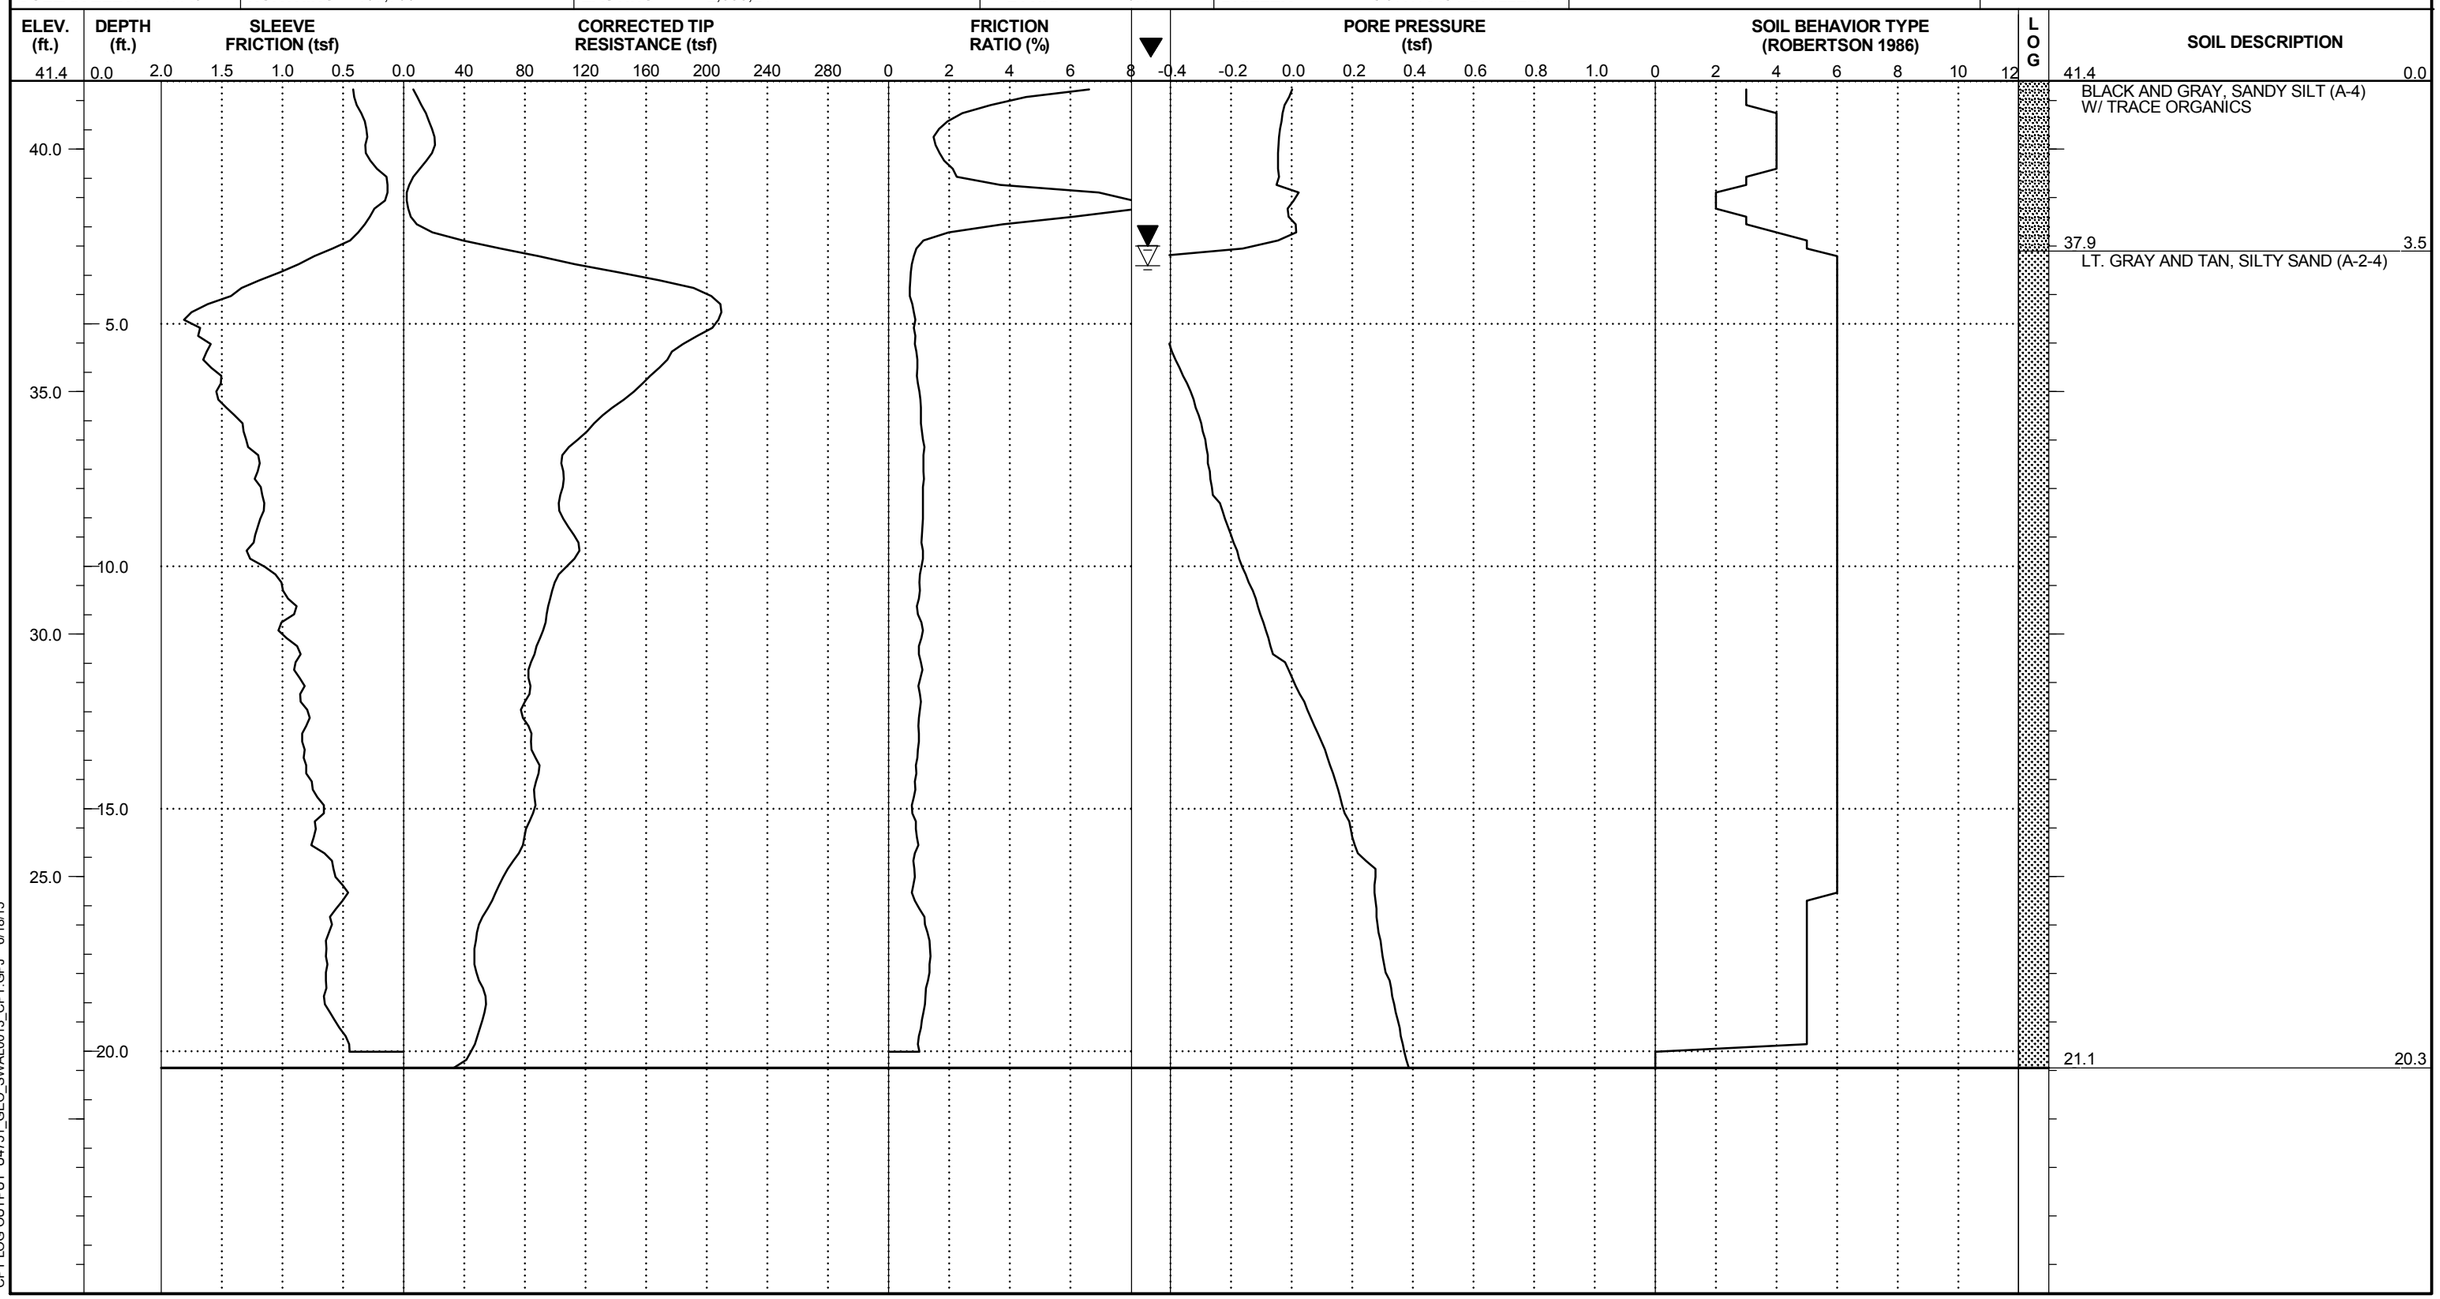

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-10	**BORING LOCATION** 18+89	**OFFSET** 48' RT	**ALIGNMENT** -NW13-	**0 HR.** 3.8	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.8 ft	**NORTHING** 197,905	**EASTING** 2,355,369		**24 HR.** 3.1	**DRILLER** CONTRACT DRILLER		

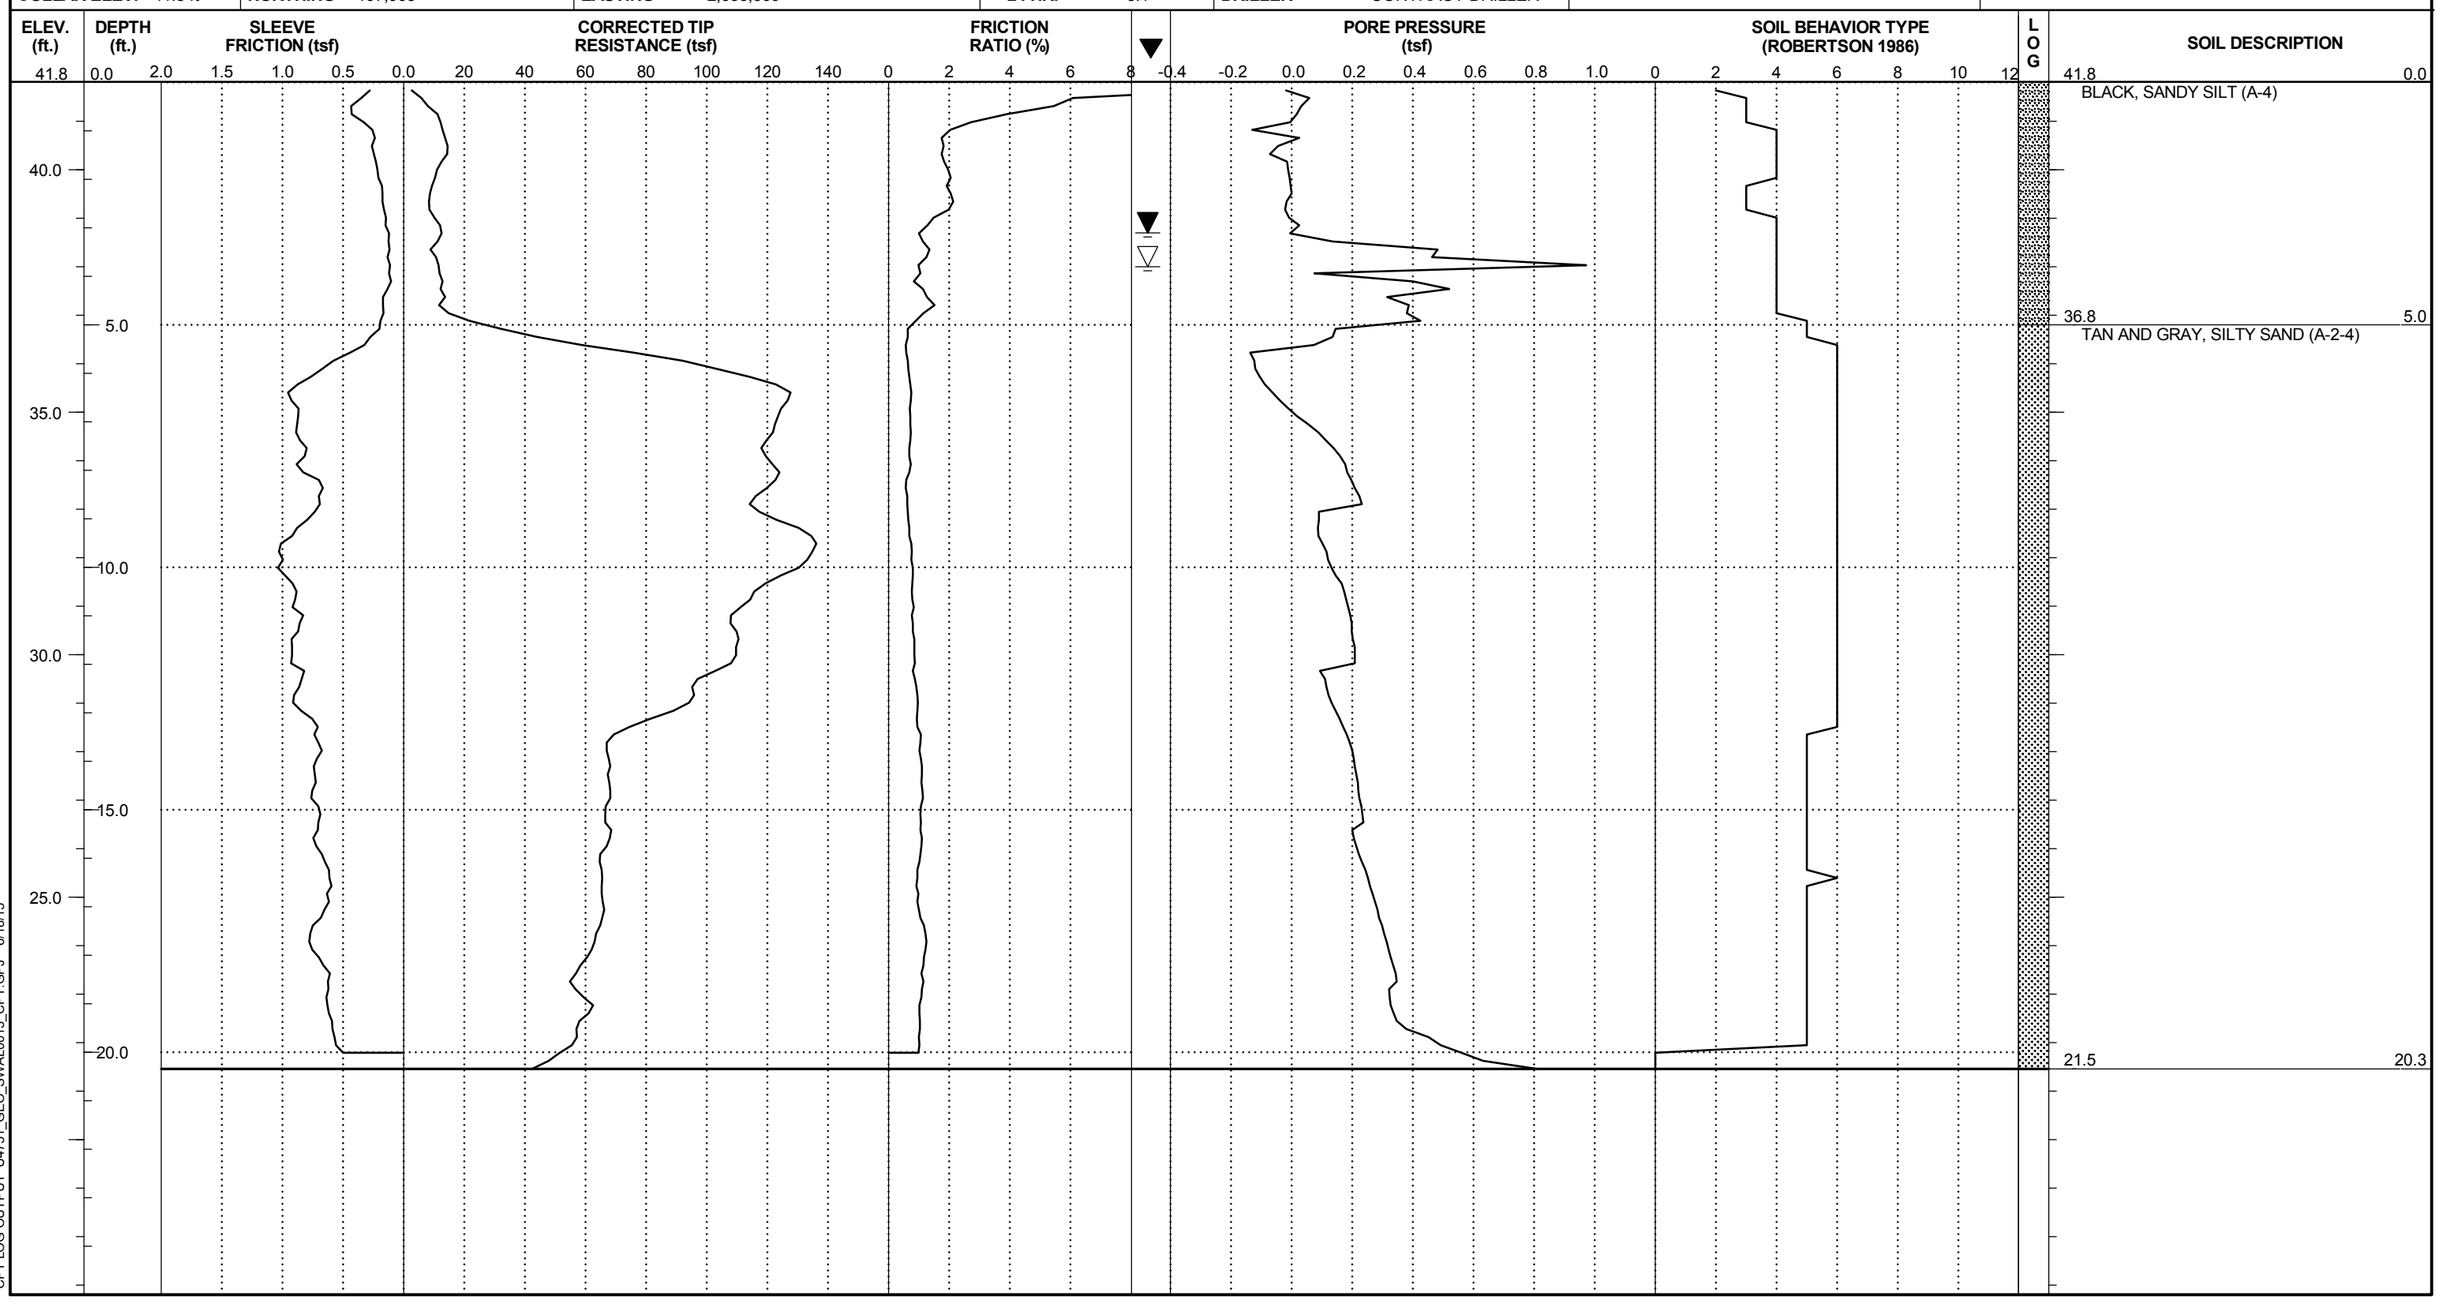

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-12	**BORING LOCATION** 21+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 4	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 42.3 ft	**NORTHING** 198,116	**EASTING** 2,355,420		**24 HR.** 1.8	**DRILLER** CONTRACT DRILLER		

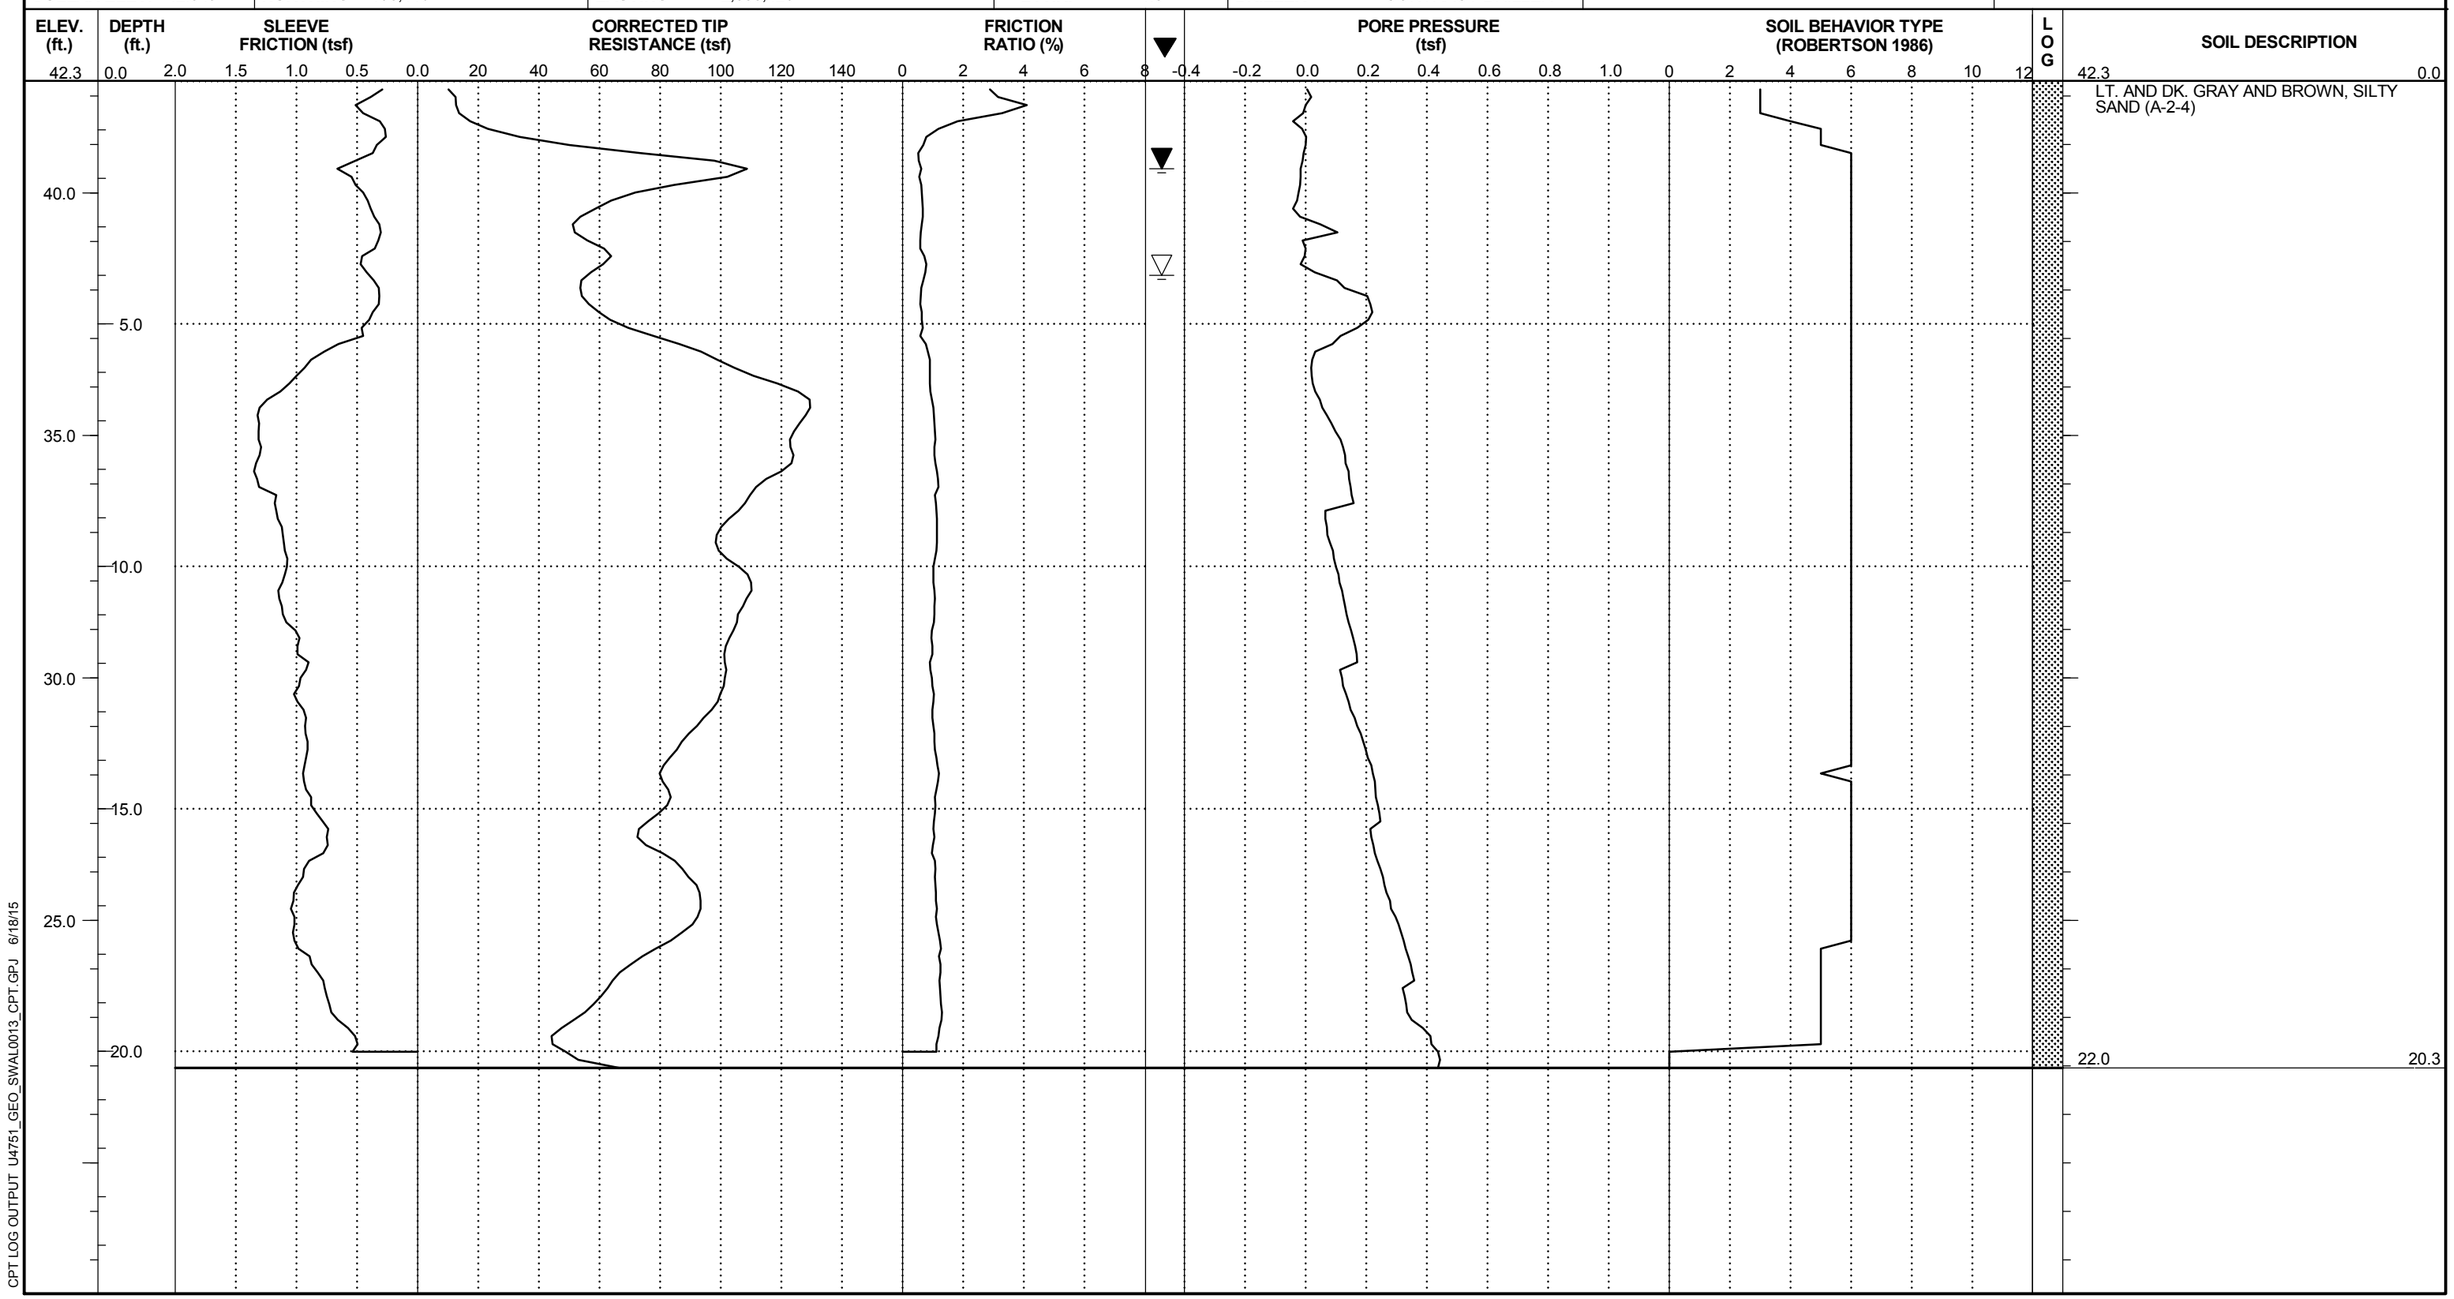

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-14	**BORING LOCATION** 23+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 3.4	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 43.3 ft	**NORTHING** 198,302	**EASTING** 2,355,493		**24 HR.** N/A	**DRILLER** CONTRACT DRILLER		

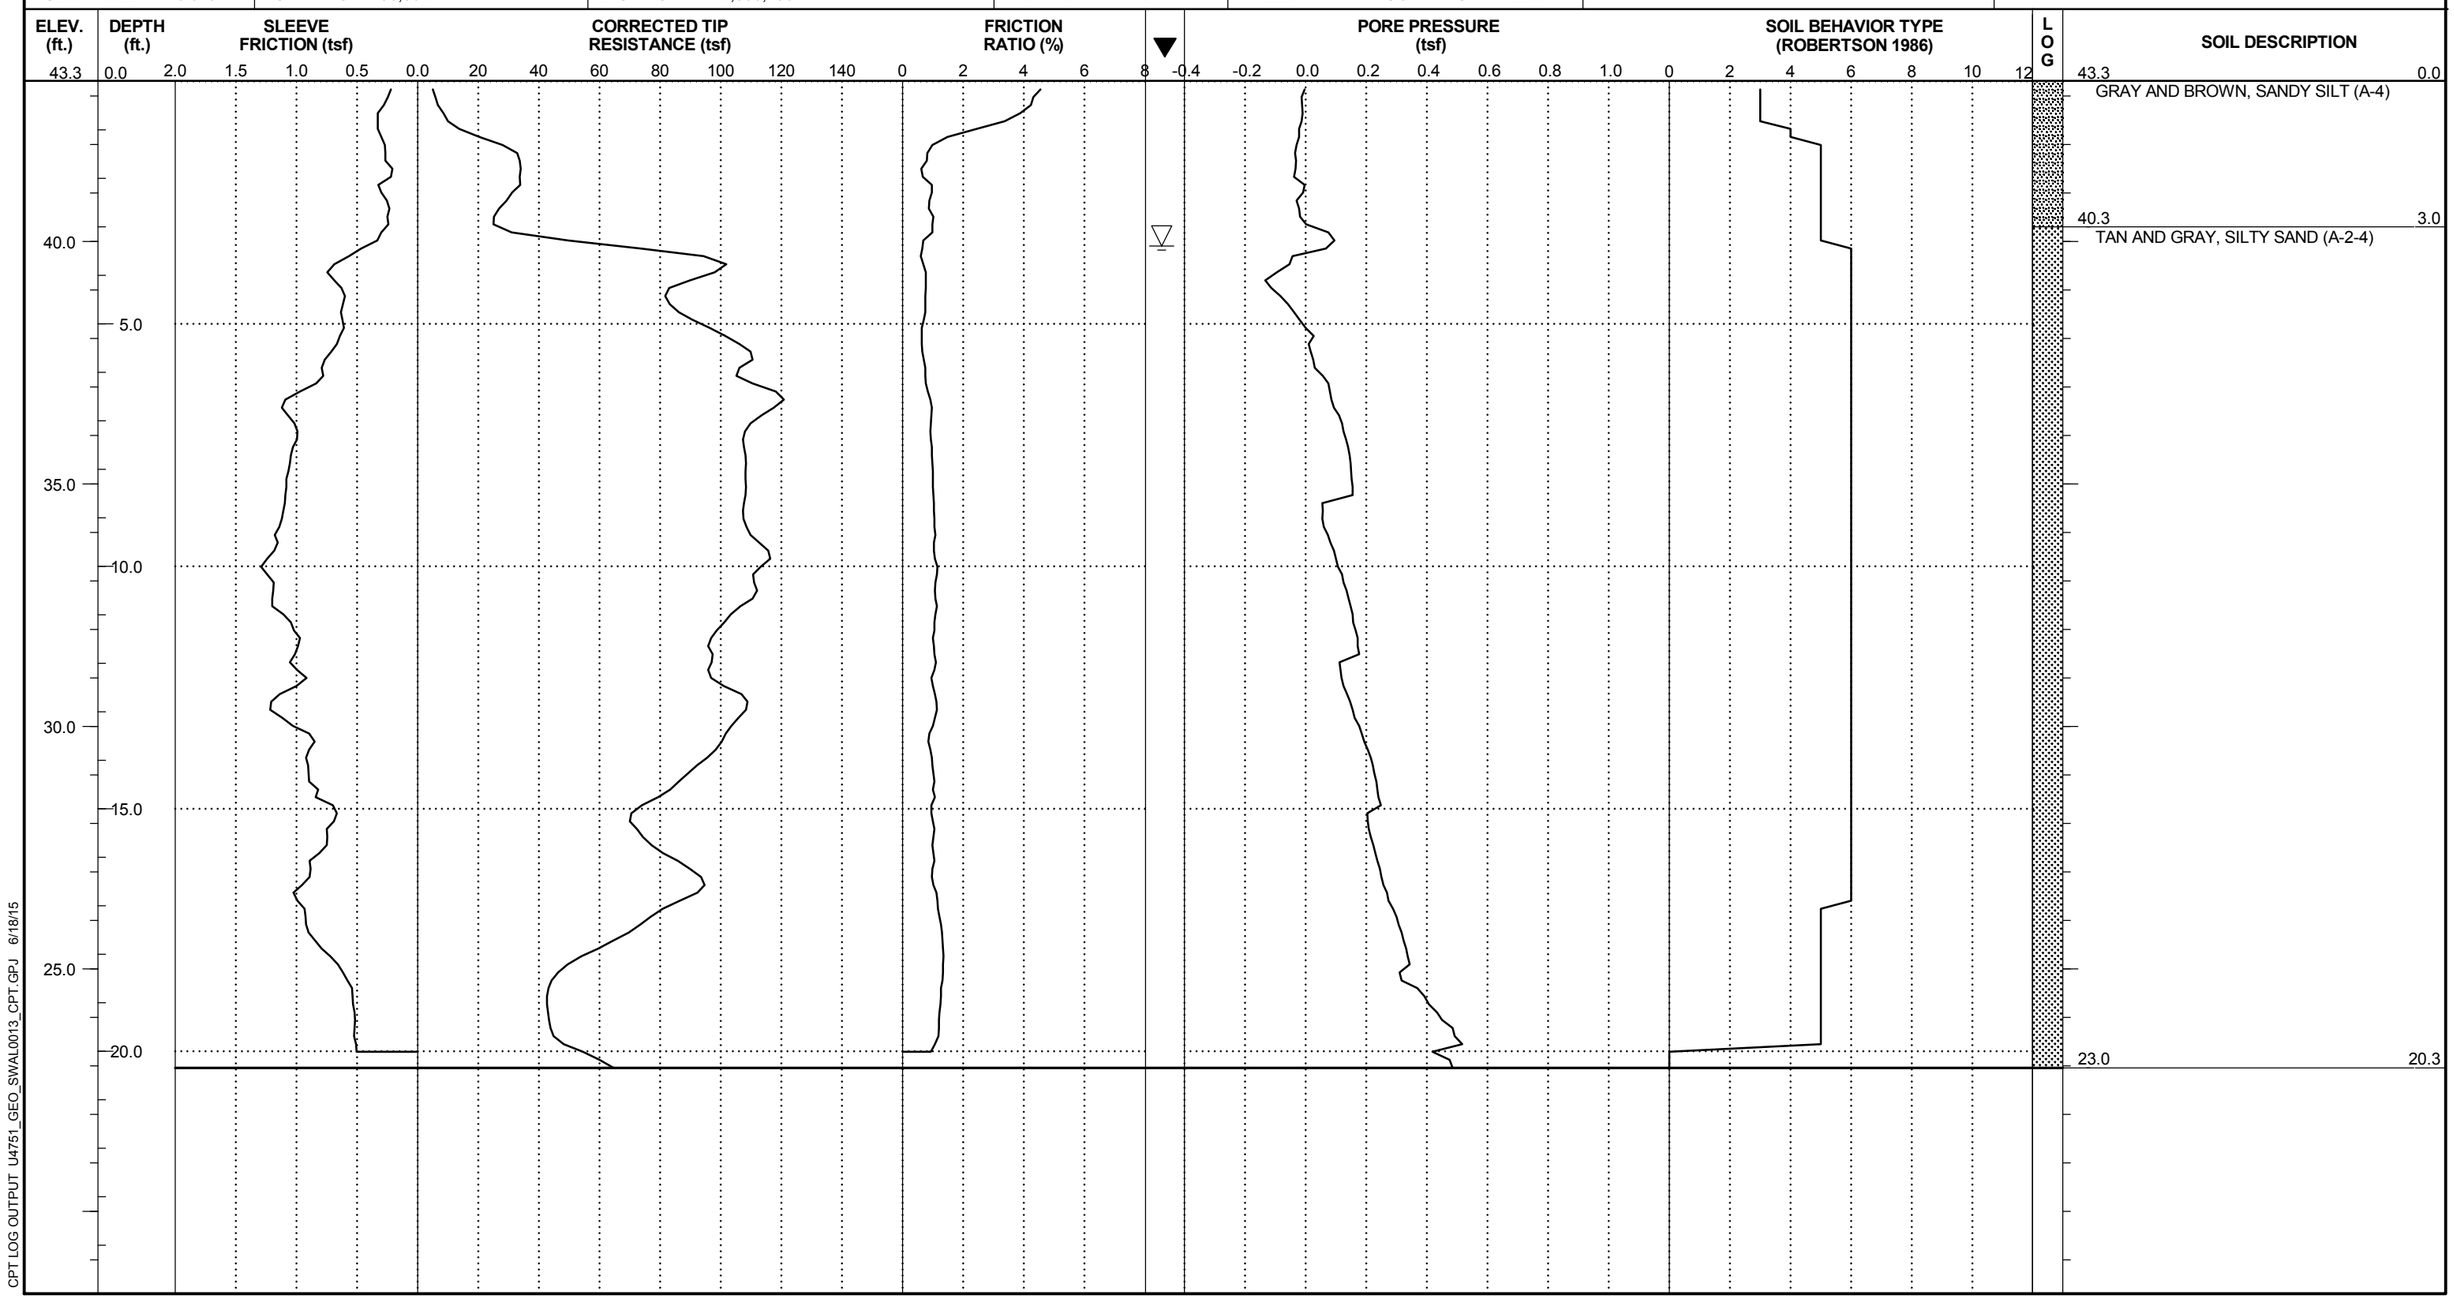

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-16	**BORING LOCATION** 25+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 5.1	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 43.4 ft	**NORTHING** 198,494	**EASTING** 2,355,552		**24 HR.** N/A	**DRILLER** CONTRACT DRILLER		

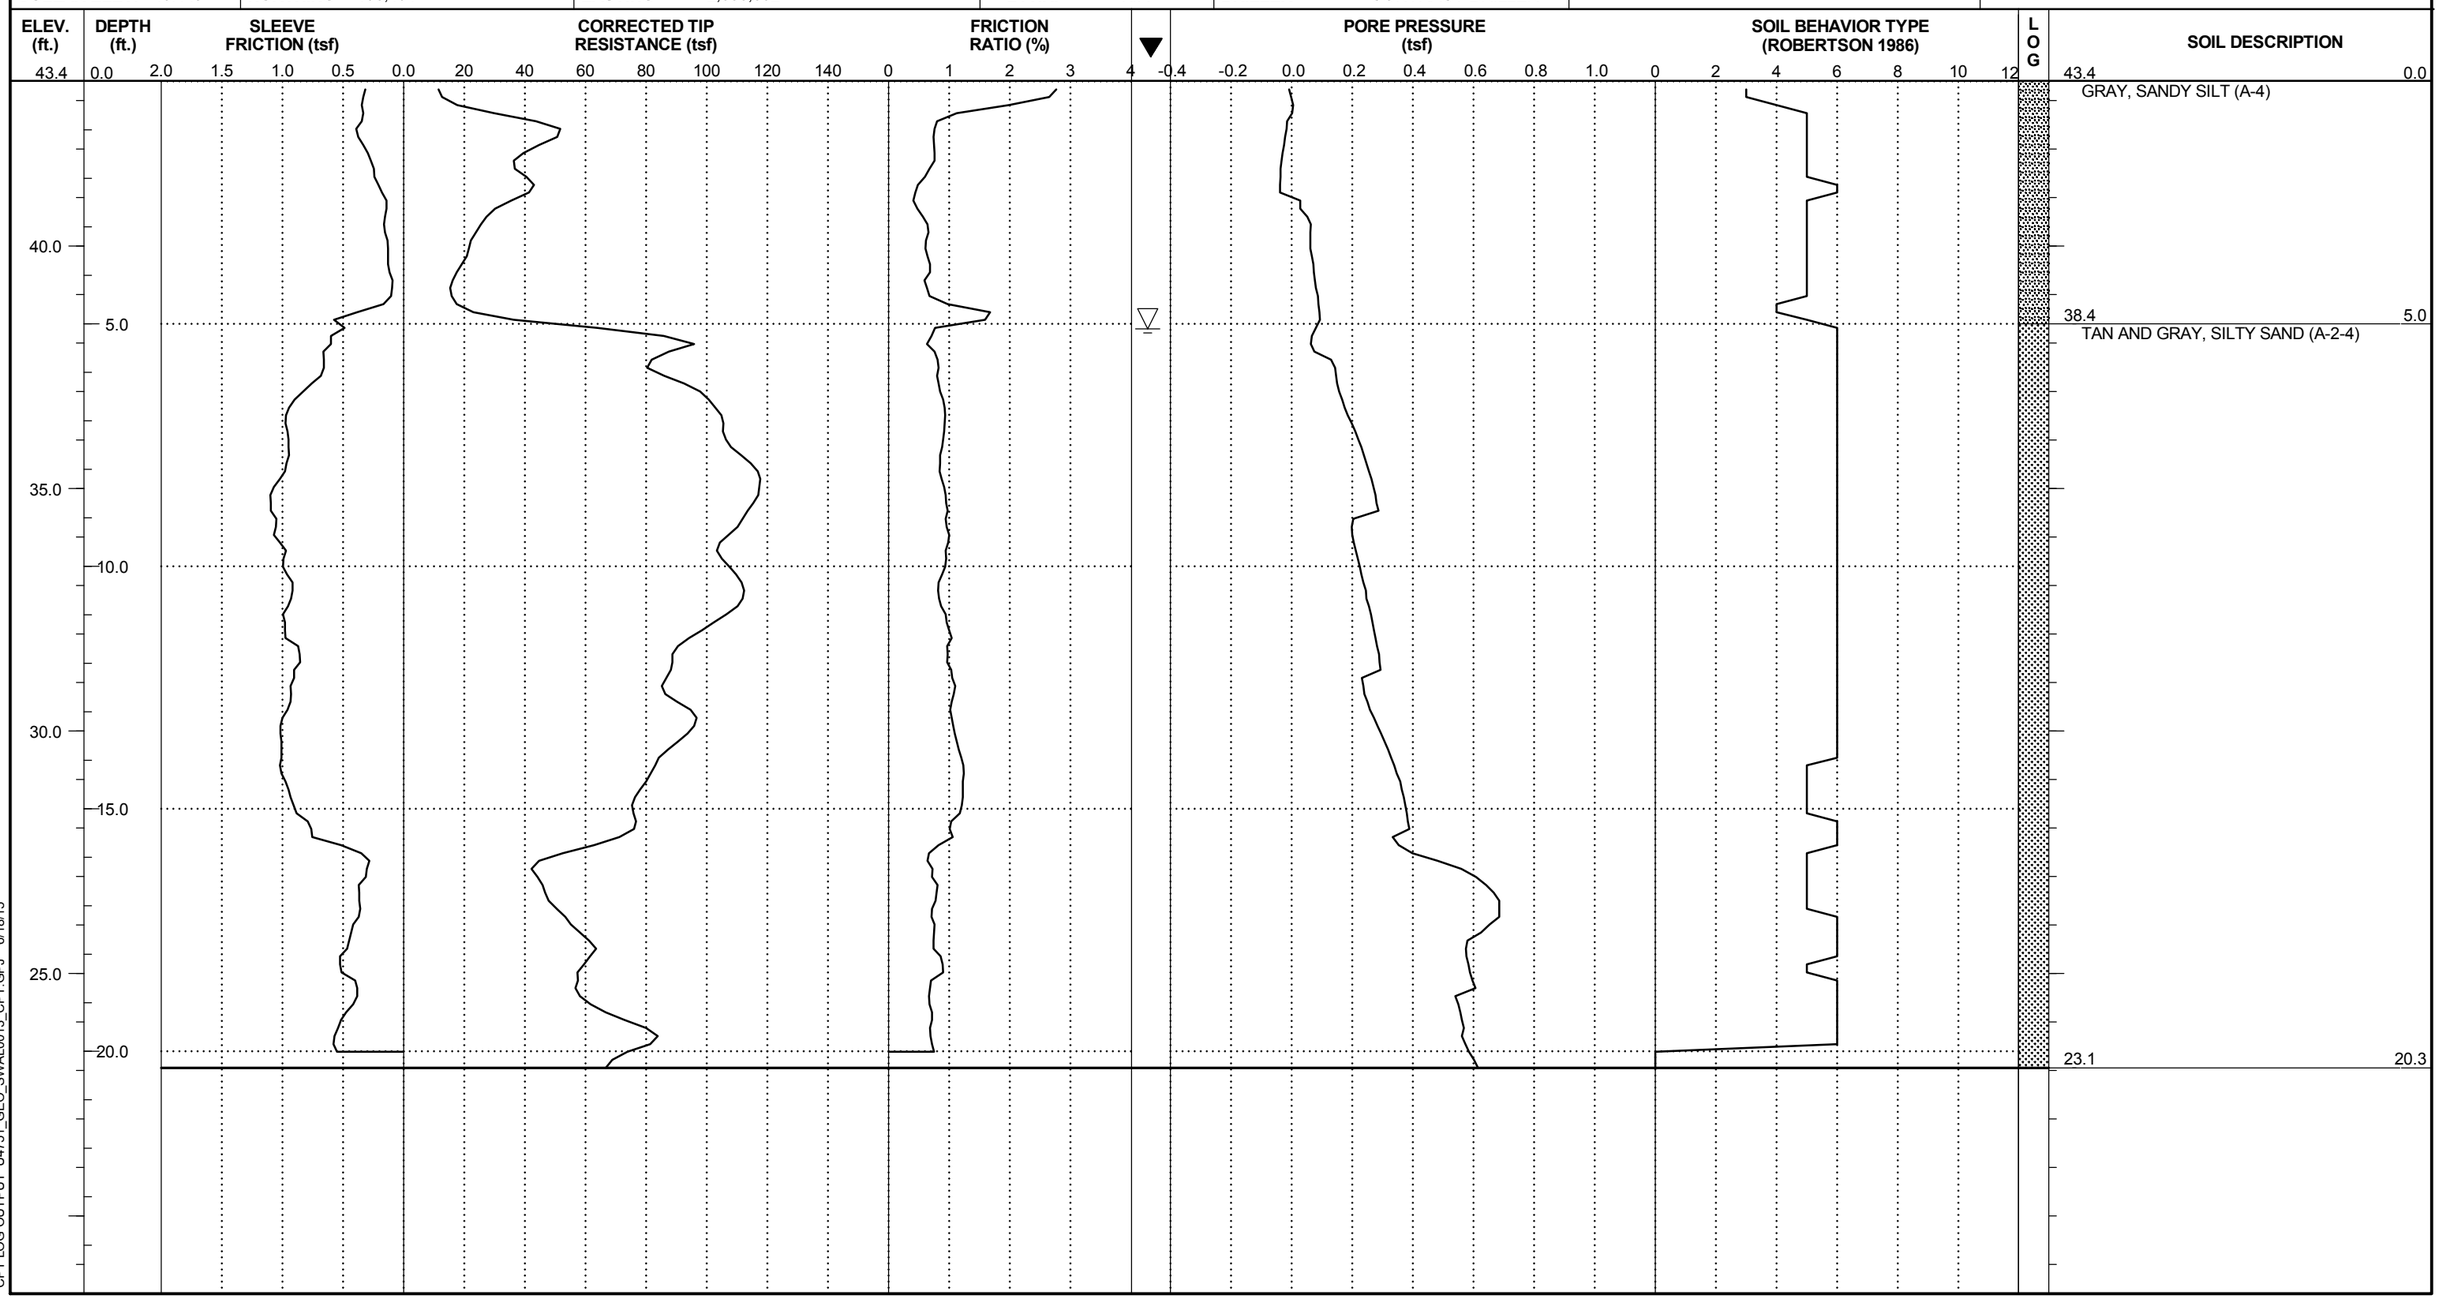

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-18	**BORING LOCATION** 27+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 4.7	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 43.5 ft	**NORTHING** 198,689	**EASTING** 2,355,595		**24 HR.** 3.3	**DRILLER** CONTRACT DRILLER		

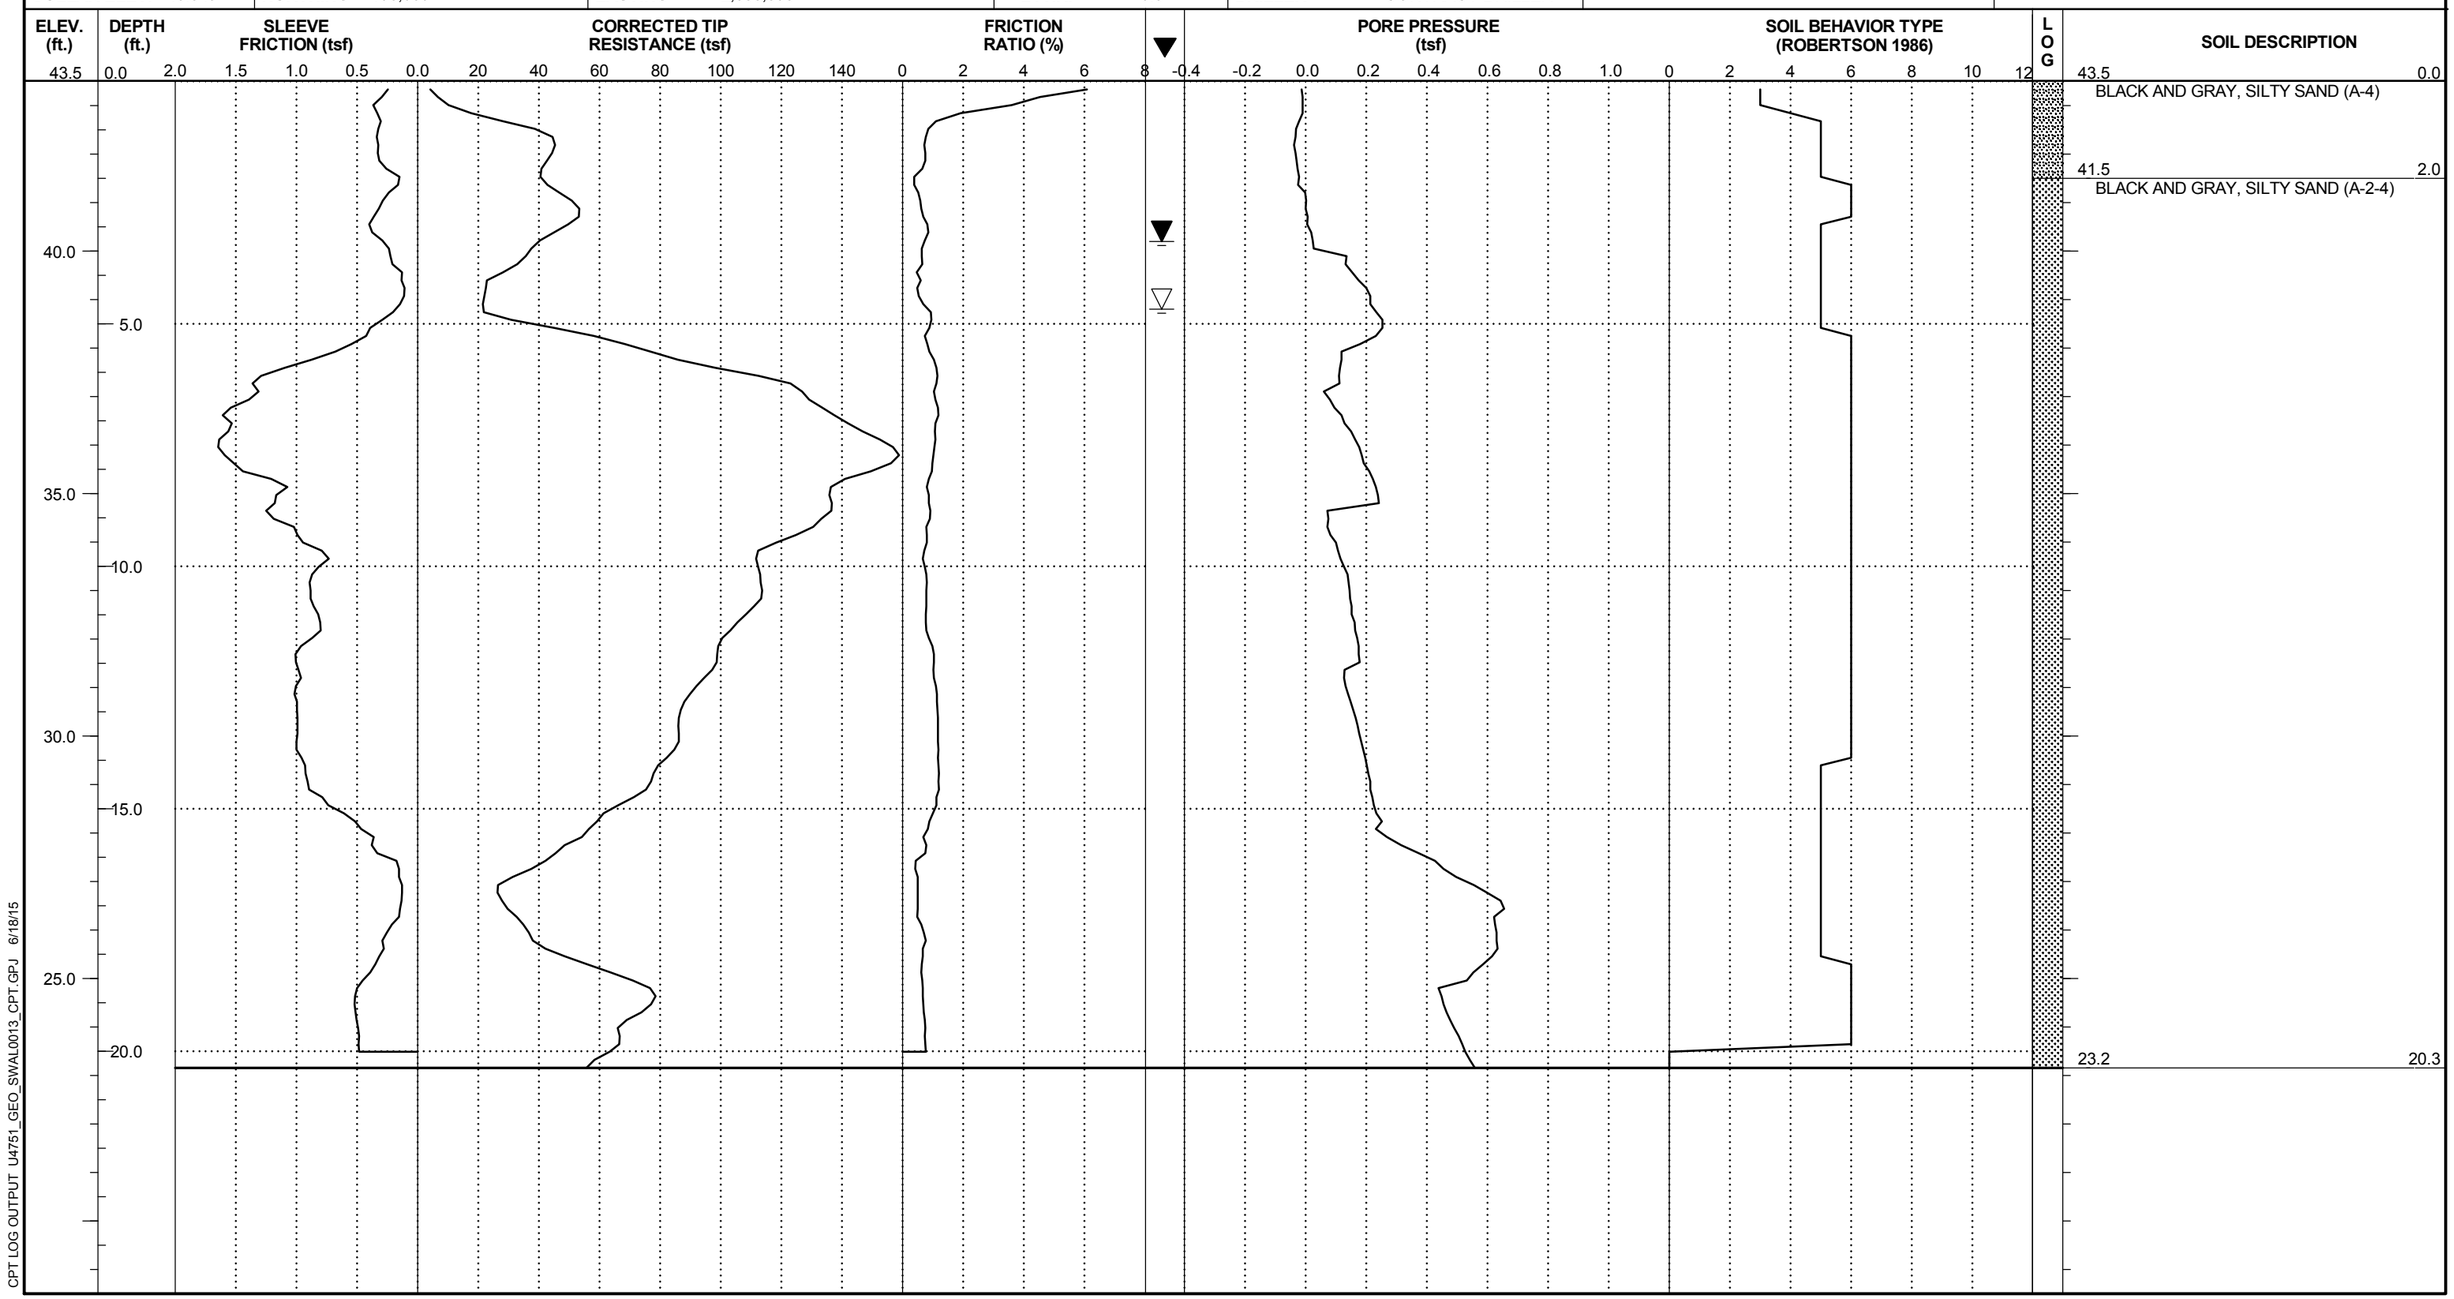

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-20	**BORING LOCATION** 29+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 10.5	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 49.2 ft	**NORTHING** 198,887	**EASTING** 2,355,623		**24 HR.** CAVED	**DRILLER** CONTRACT DRILLER		

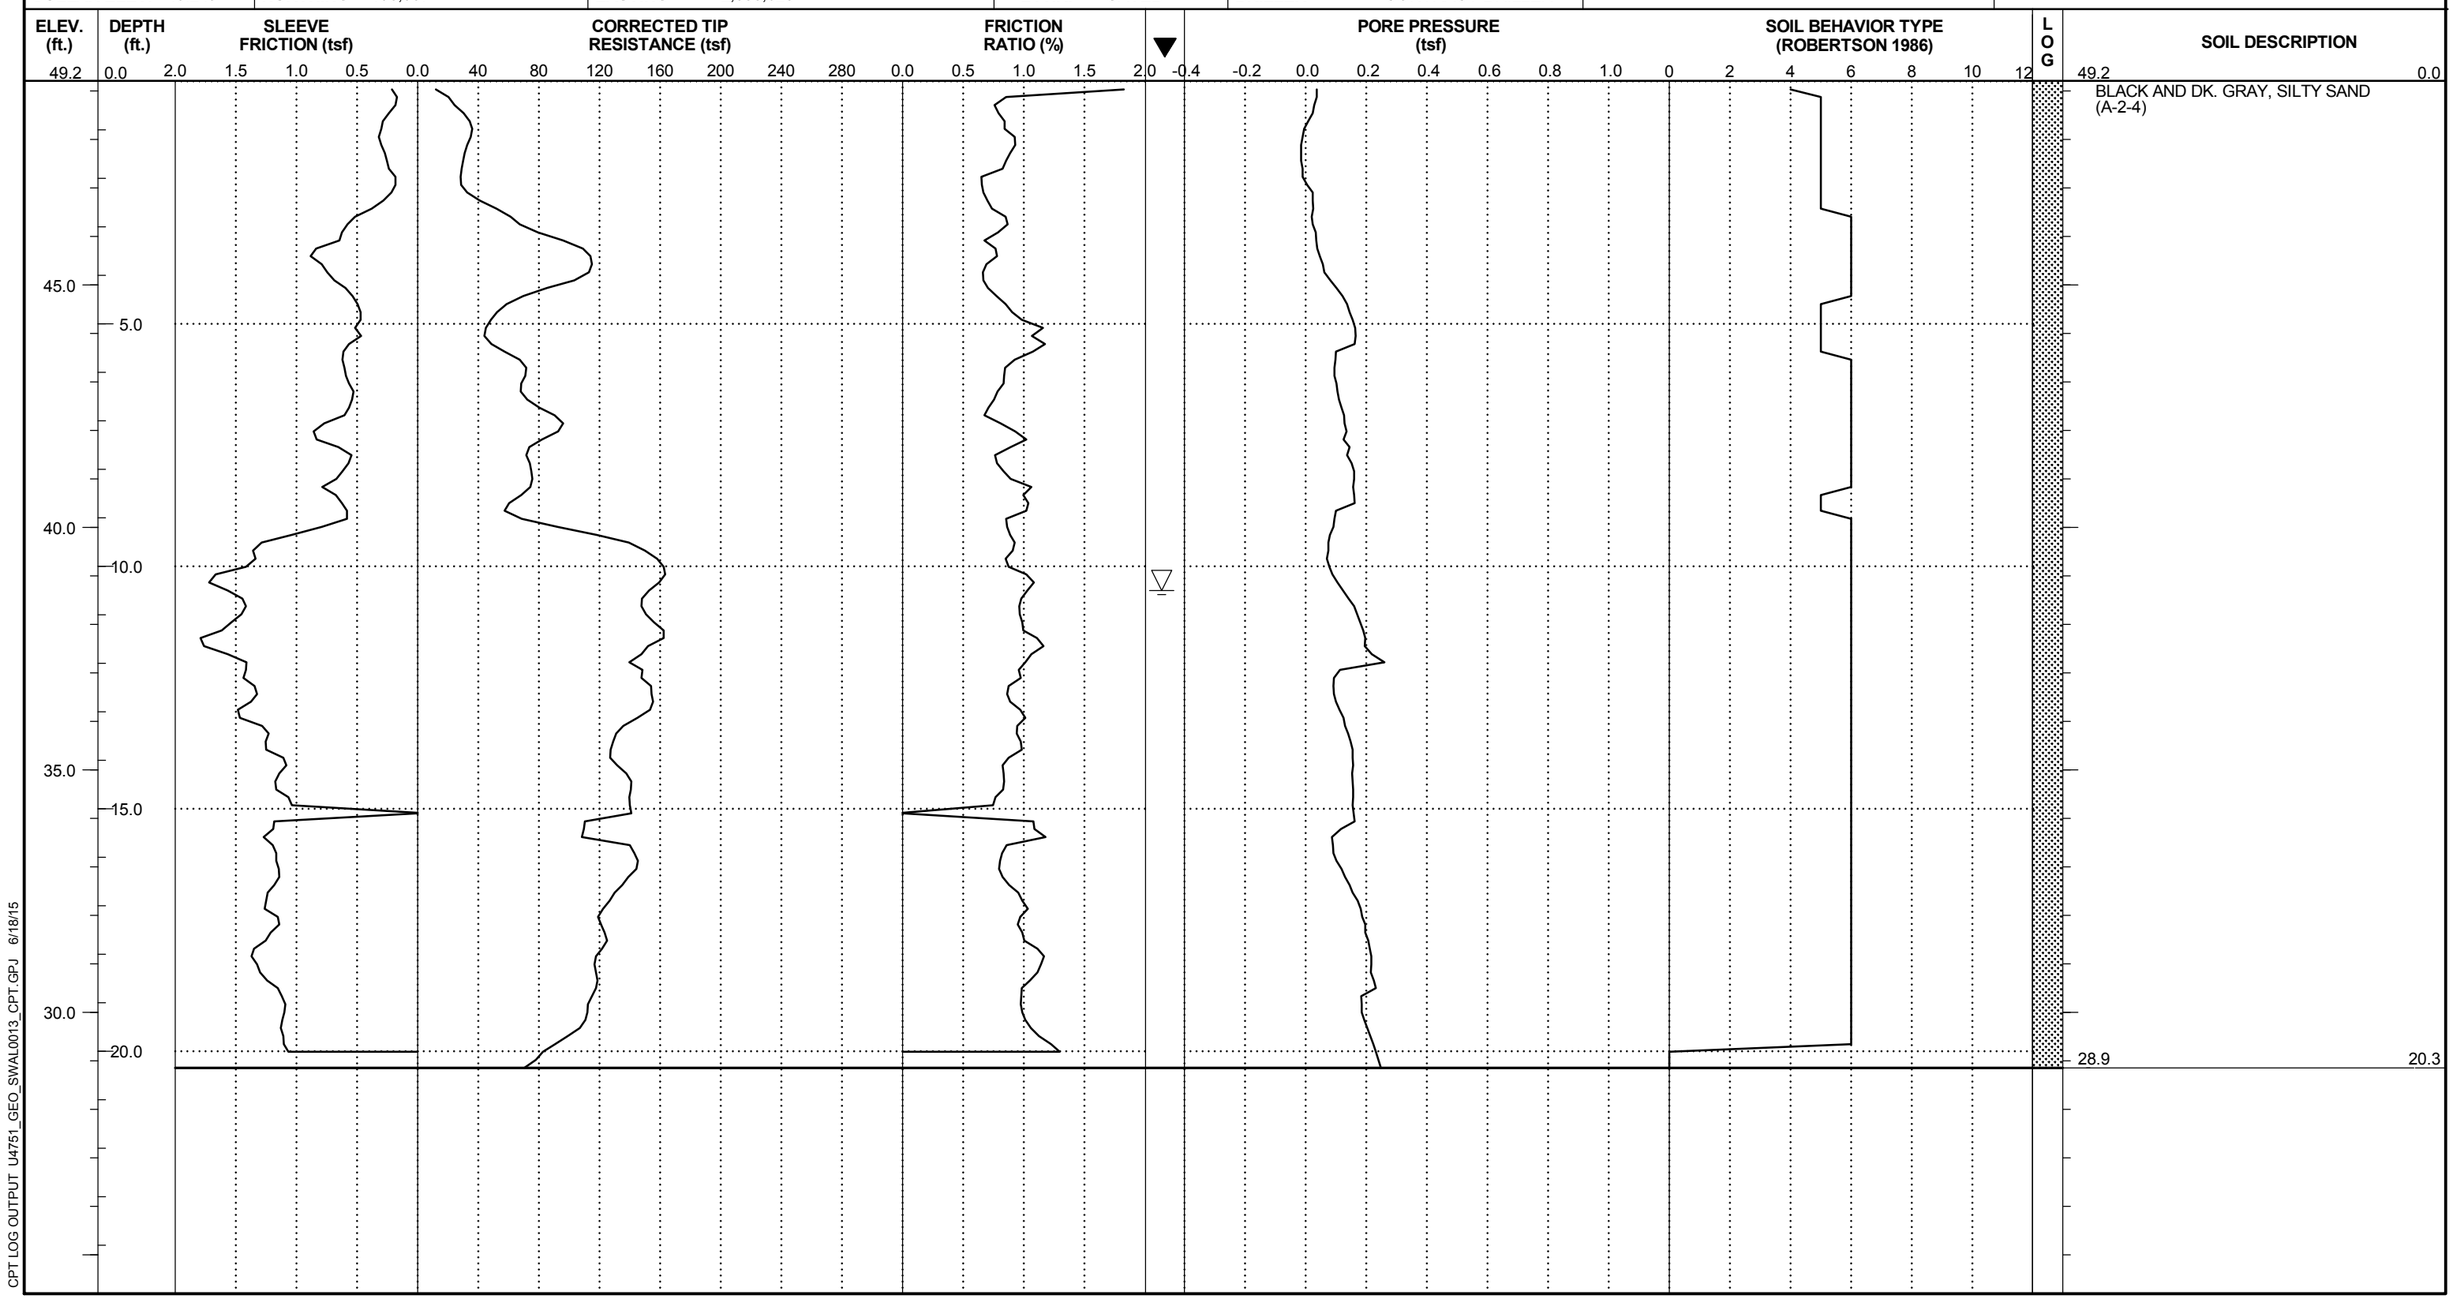

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-22	**BORING LOCATION** 31+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 4.8	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 43.9 ft	**NORTHING** 199,086	**EASTING** 2,355,625		**24 HR.** CAVED	**DRILLER** CONTRACT DRILLER		



CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/13/15	**COMPLETED** 1/13/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-24	**BORING LOCATION** 33+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 5	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 42.4 ft	**NORTHING** 199,270	**EASTING** 2,355,633		**24 HR.** 3.4	**DRILLER** CONTRACT DRILLER		

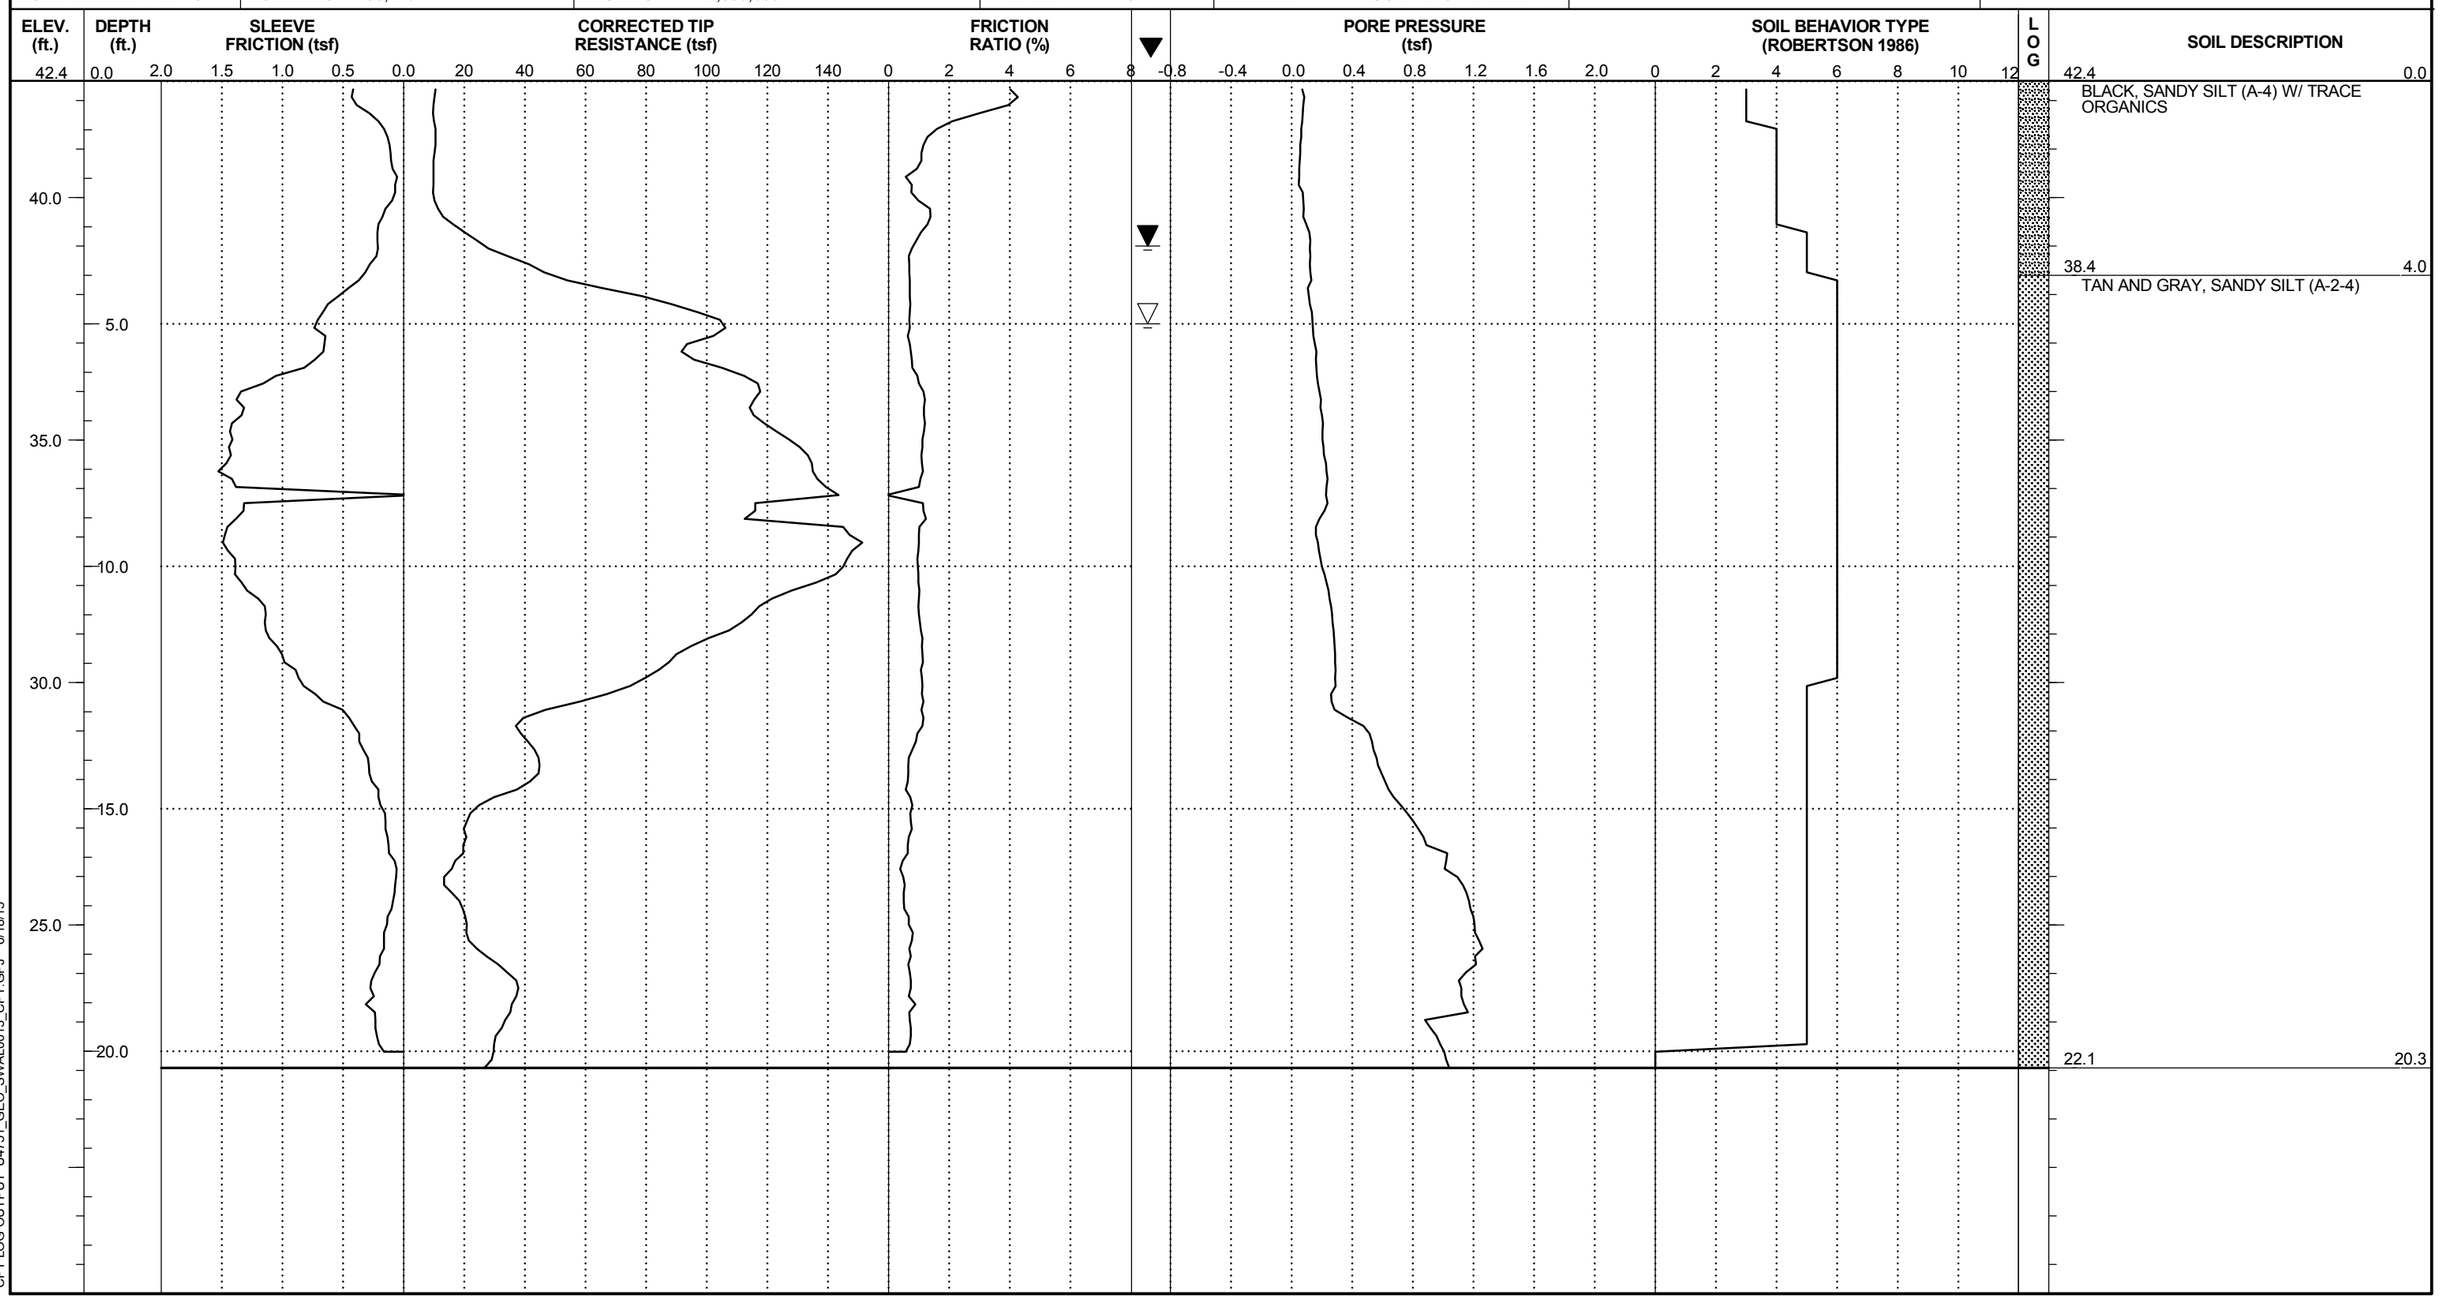

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-26	**BORING LOCATION** 35+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 2.7	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.5 ft	**NORTHING** 199,477	**EASTING** 2,355,615		**24 HR.** 2.8	**DRILLER** CONTRACT DRILLER		

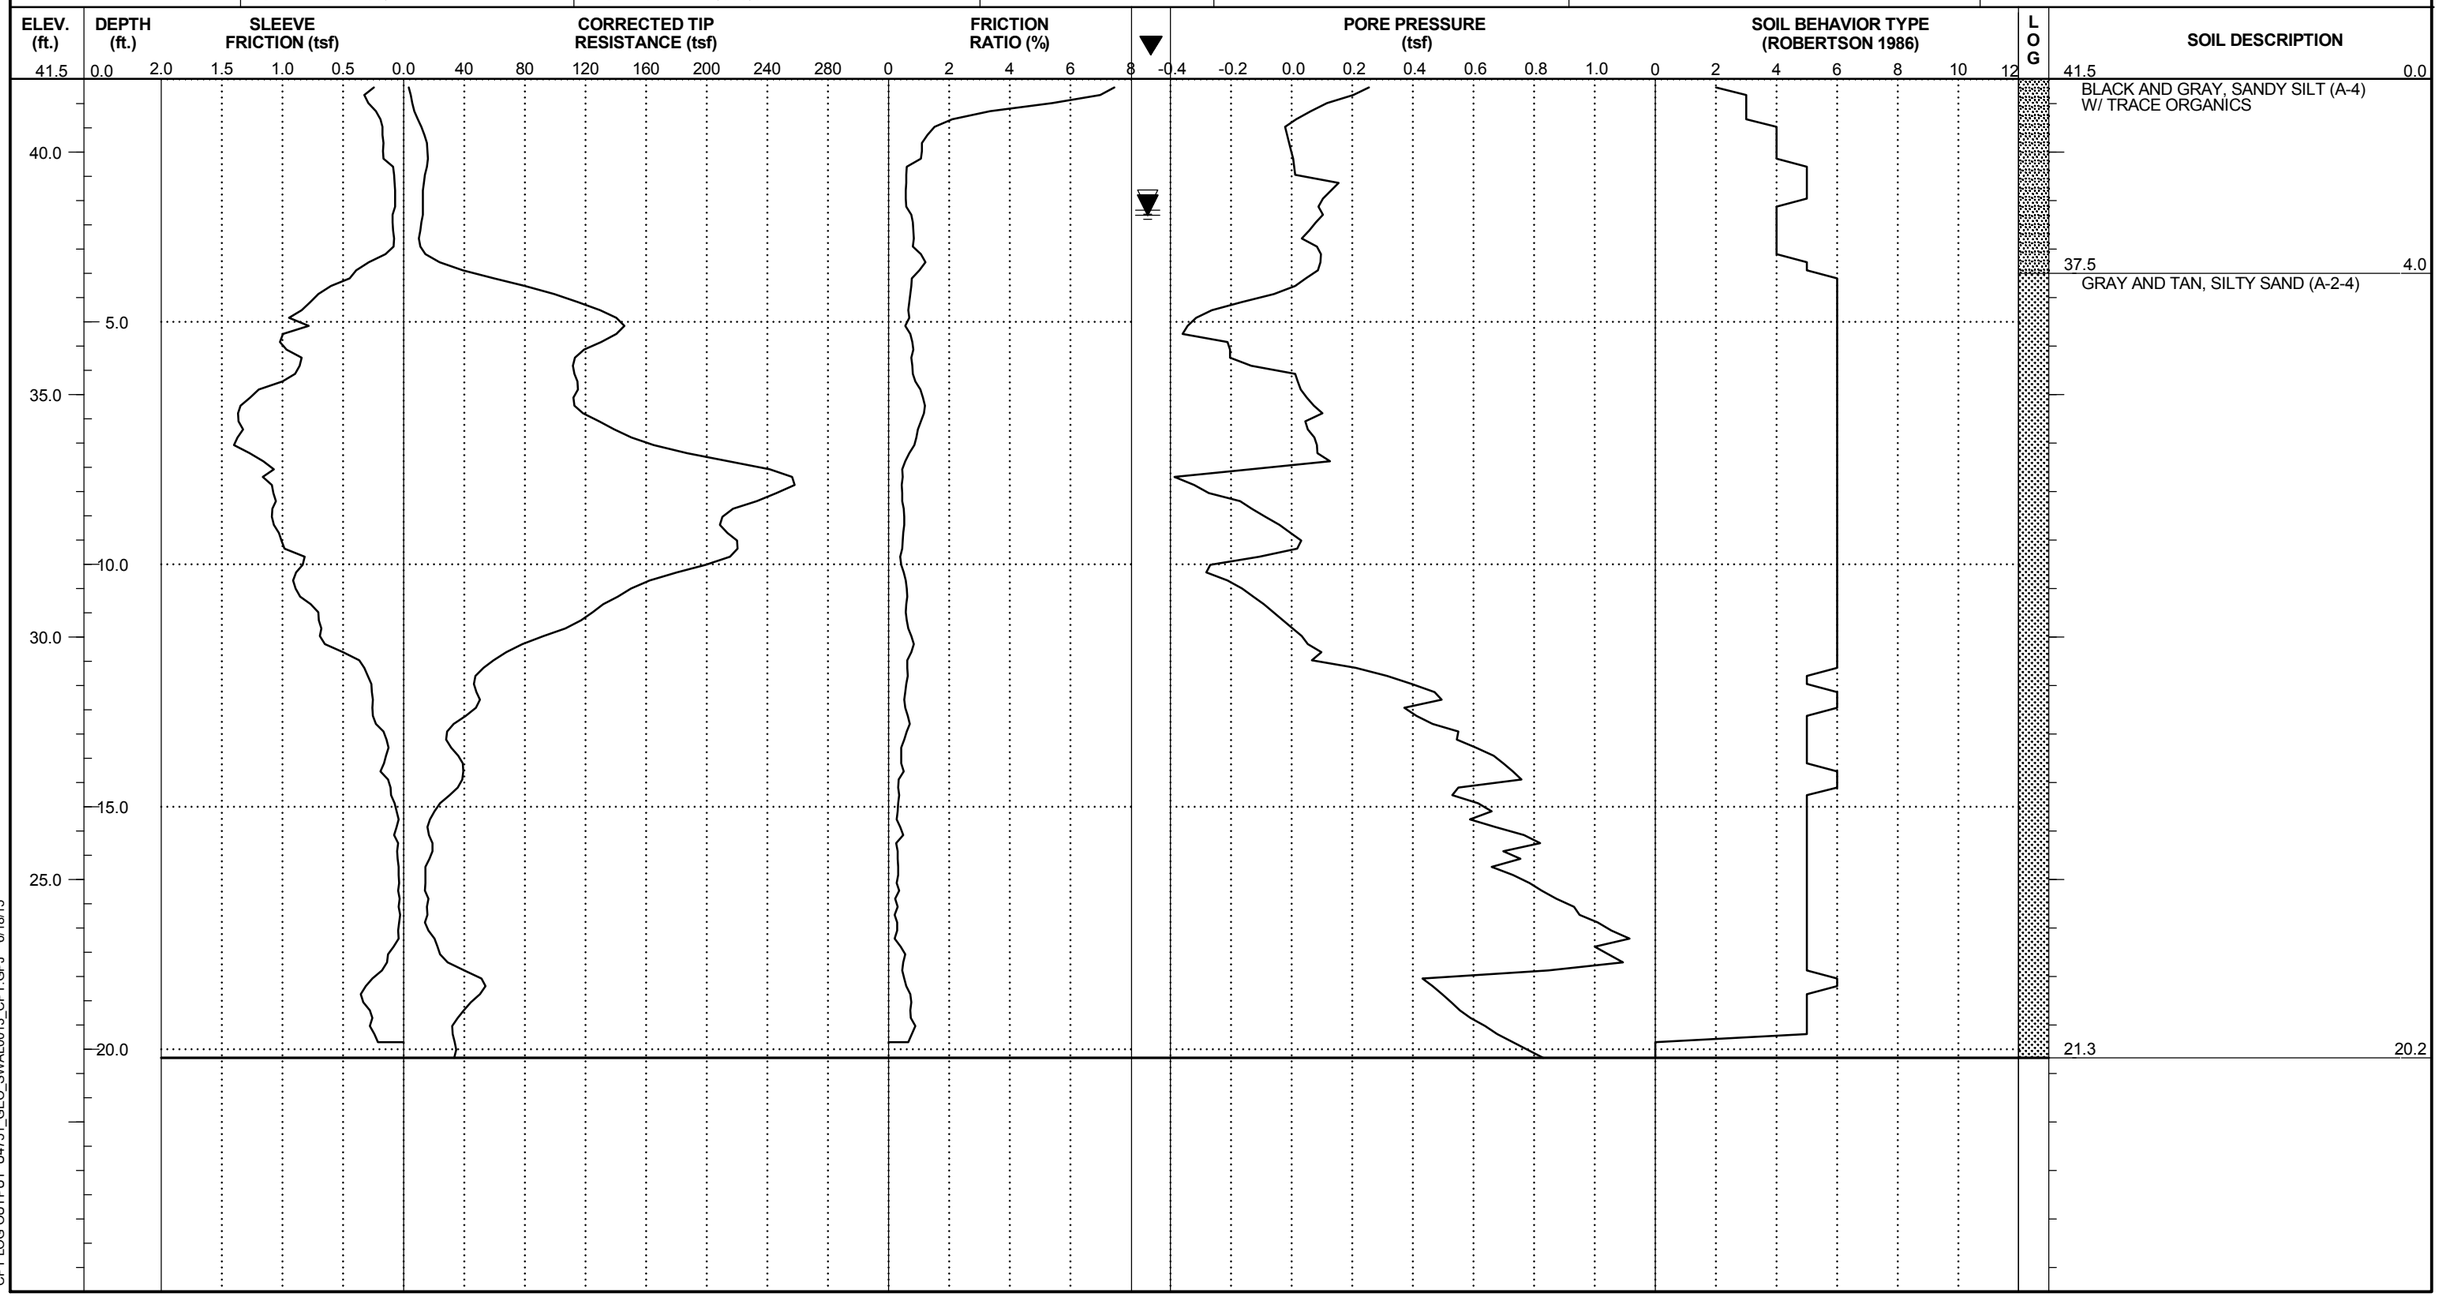

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-28	**BORING LOCATION** 37+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 1.4	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 42.1 ft	**NORTHING** 199,674	**EASTING** 2,355,581		**24 HR.** CAVED	**DRILLER** CONTRACT DRILLER		

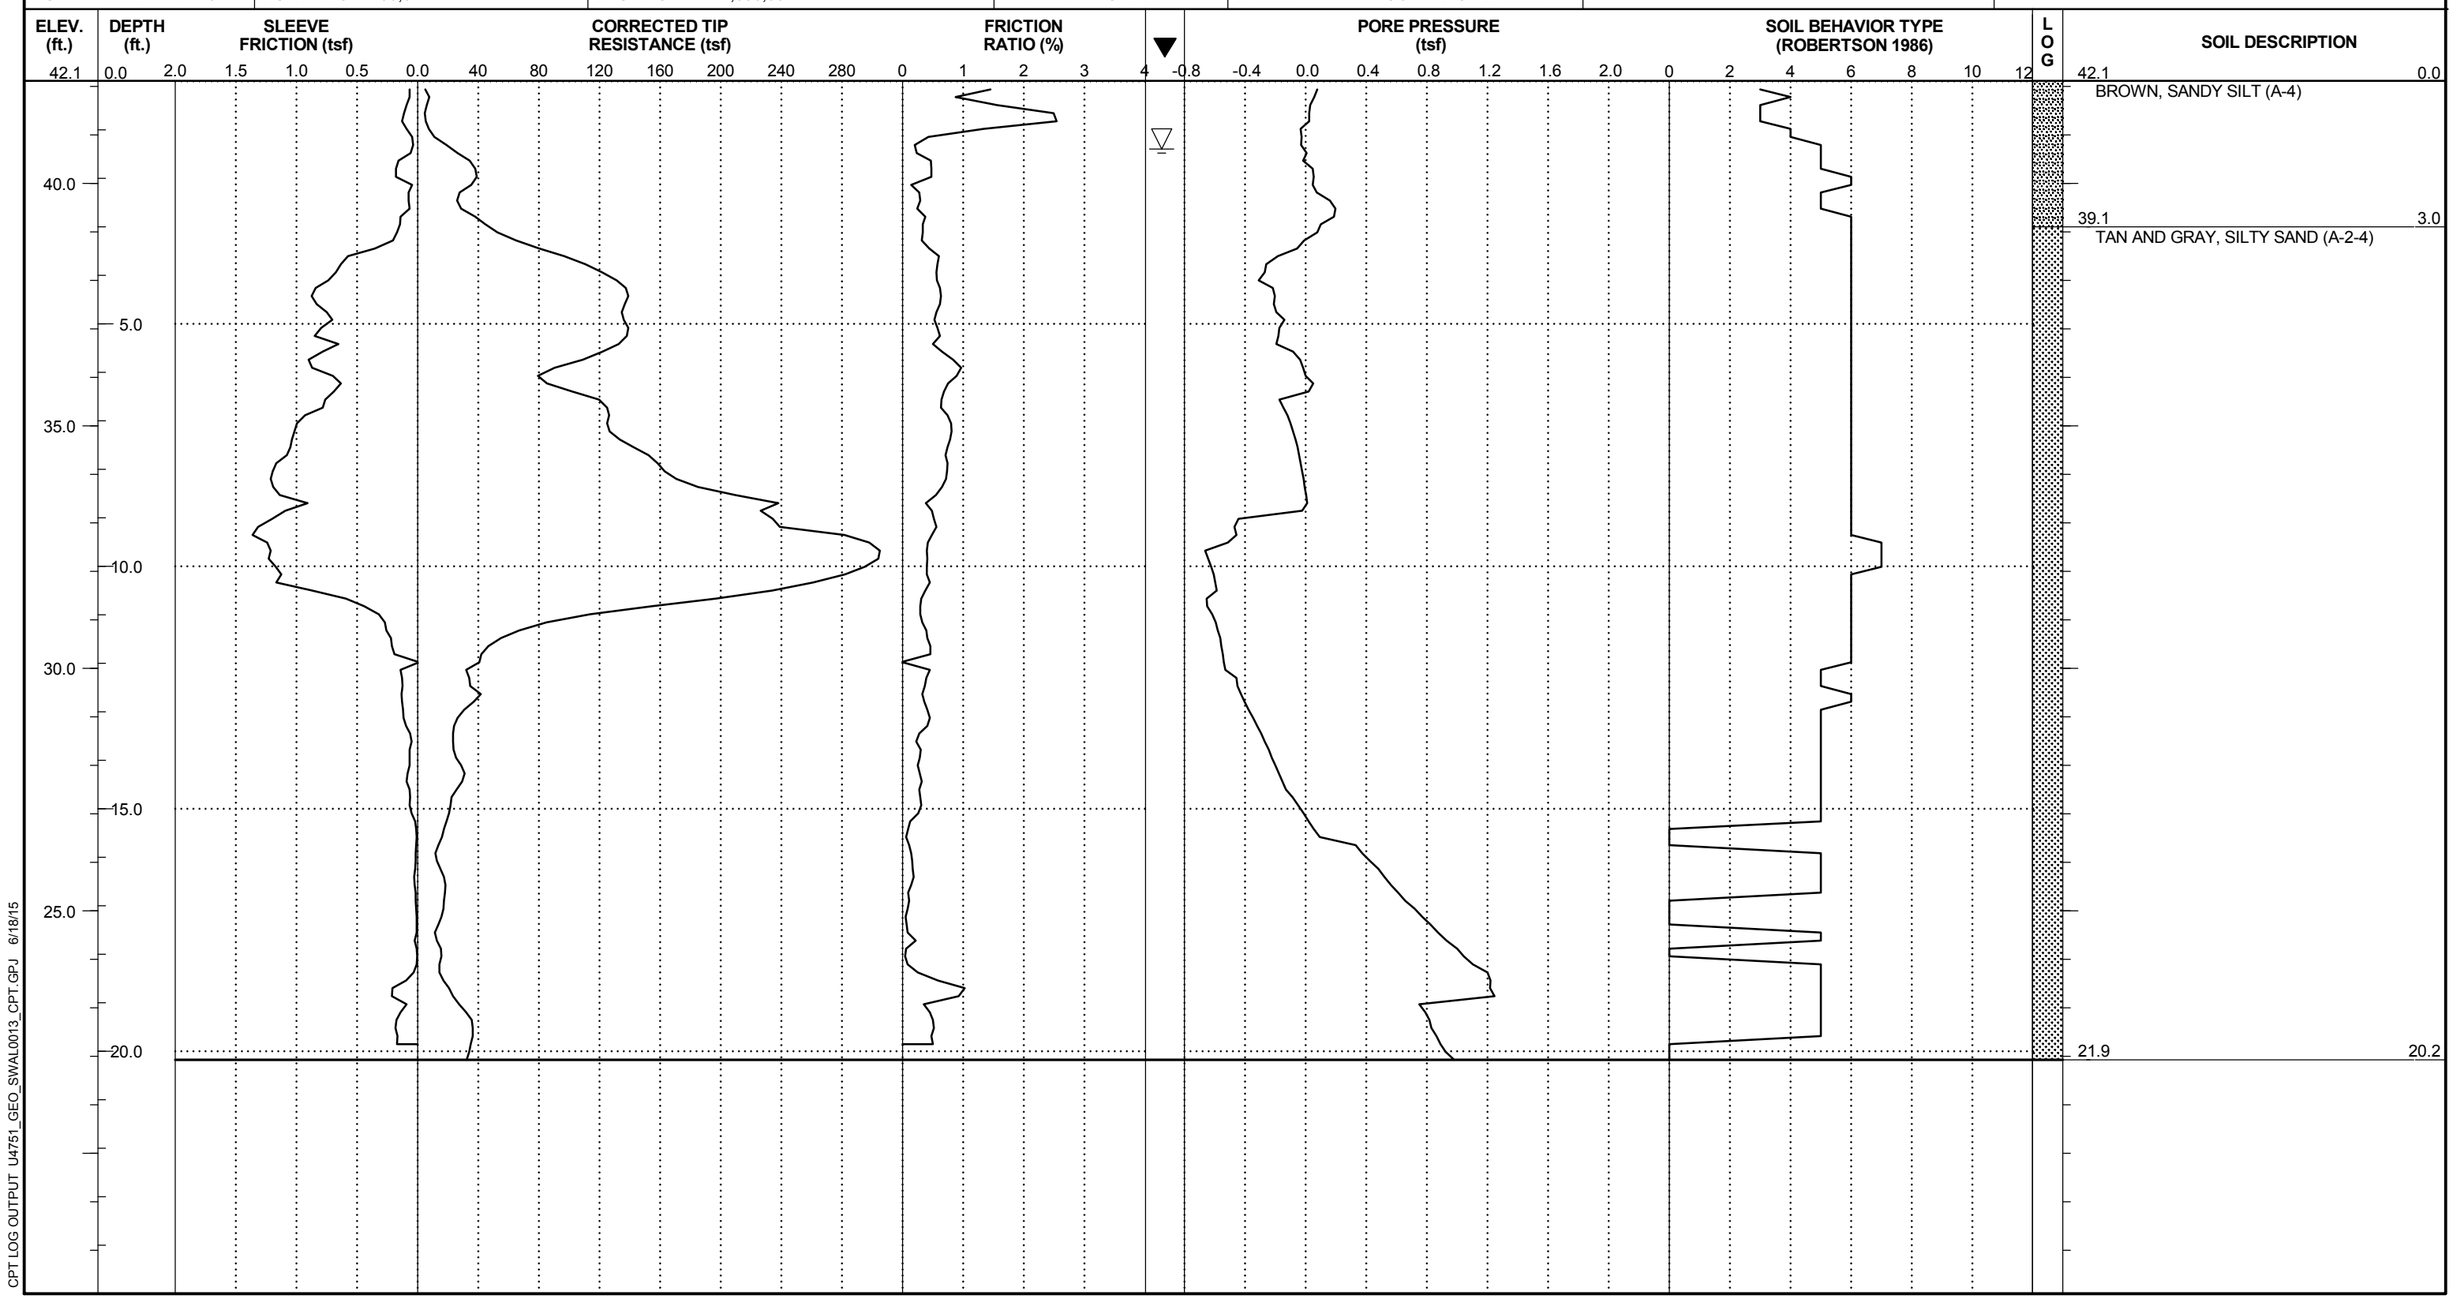

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-30	**BORING LOCATION** 39+00	**OFFSET** CL	**ALIGNMENT** -NW13-	**0 HR.** 1.1	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 42.1 ft	**NORTHING** 199,868	**EASTING** 2,355,531		**24 HR.** 1.1	**DRILLER** CONTRACT DRILLER		

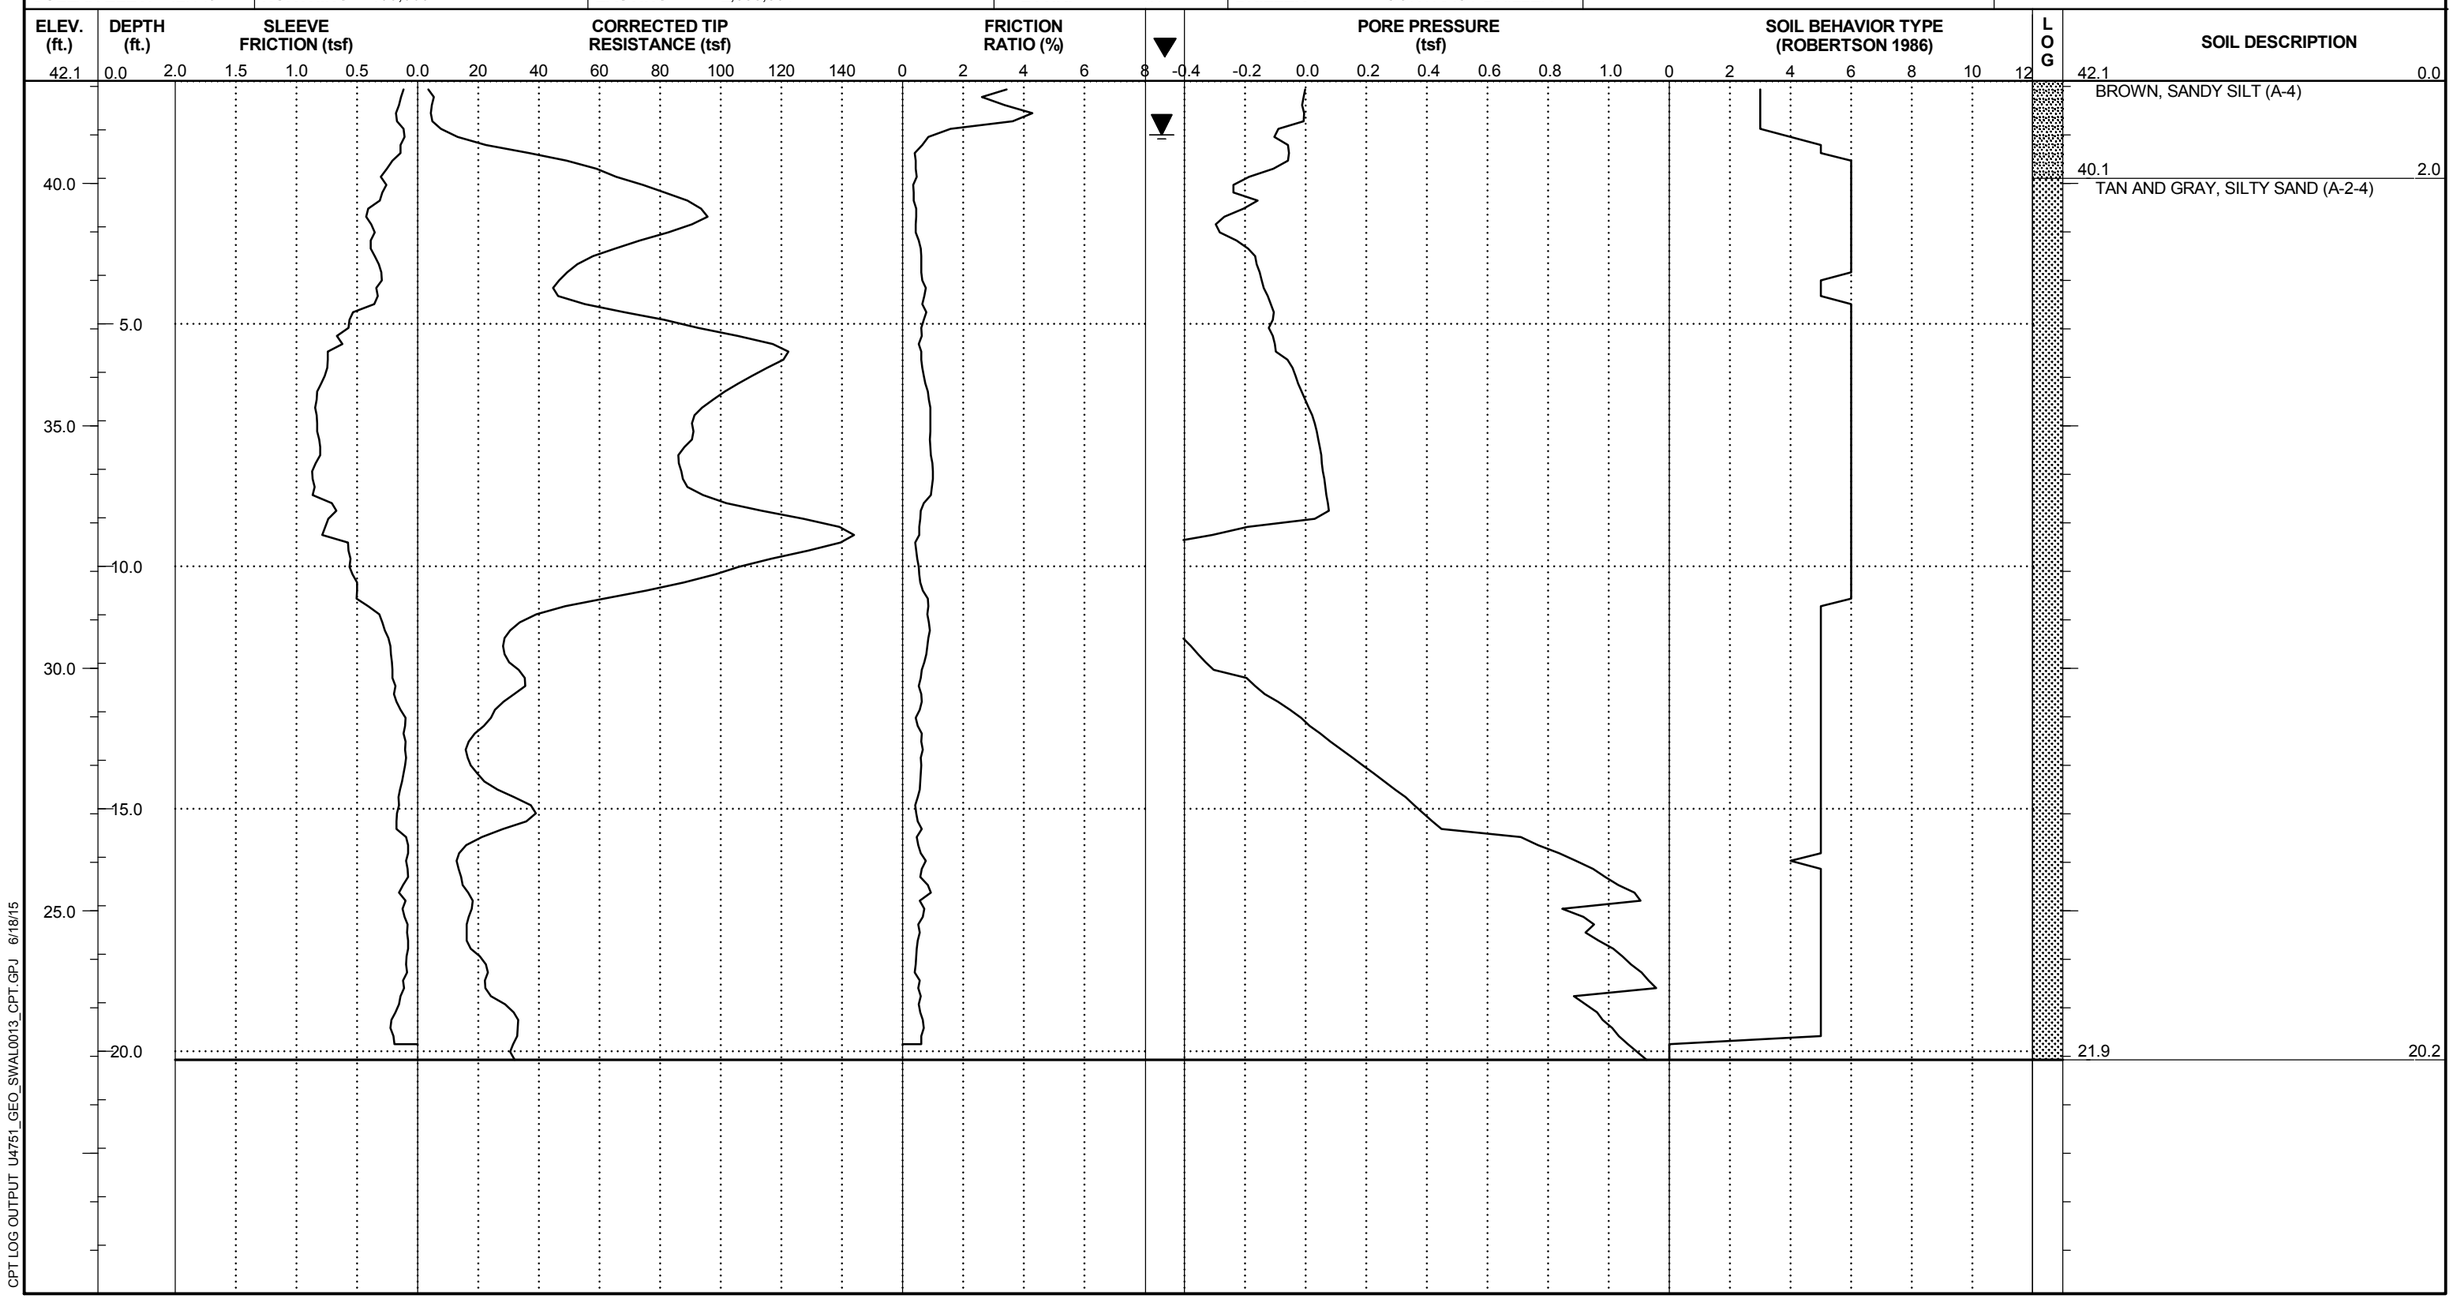

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-32	**BORING LOCATION** 159+76	**OFFSET** 65' LT	**ALIGNMENT** -L-	**0 HR.** 0.7	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 42.1 ft	**NORTHING** 200,059	**EASTING** 2,355,473		**24 HR.** CAVED	**DRILLER** CONTRACT DRILLER		

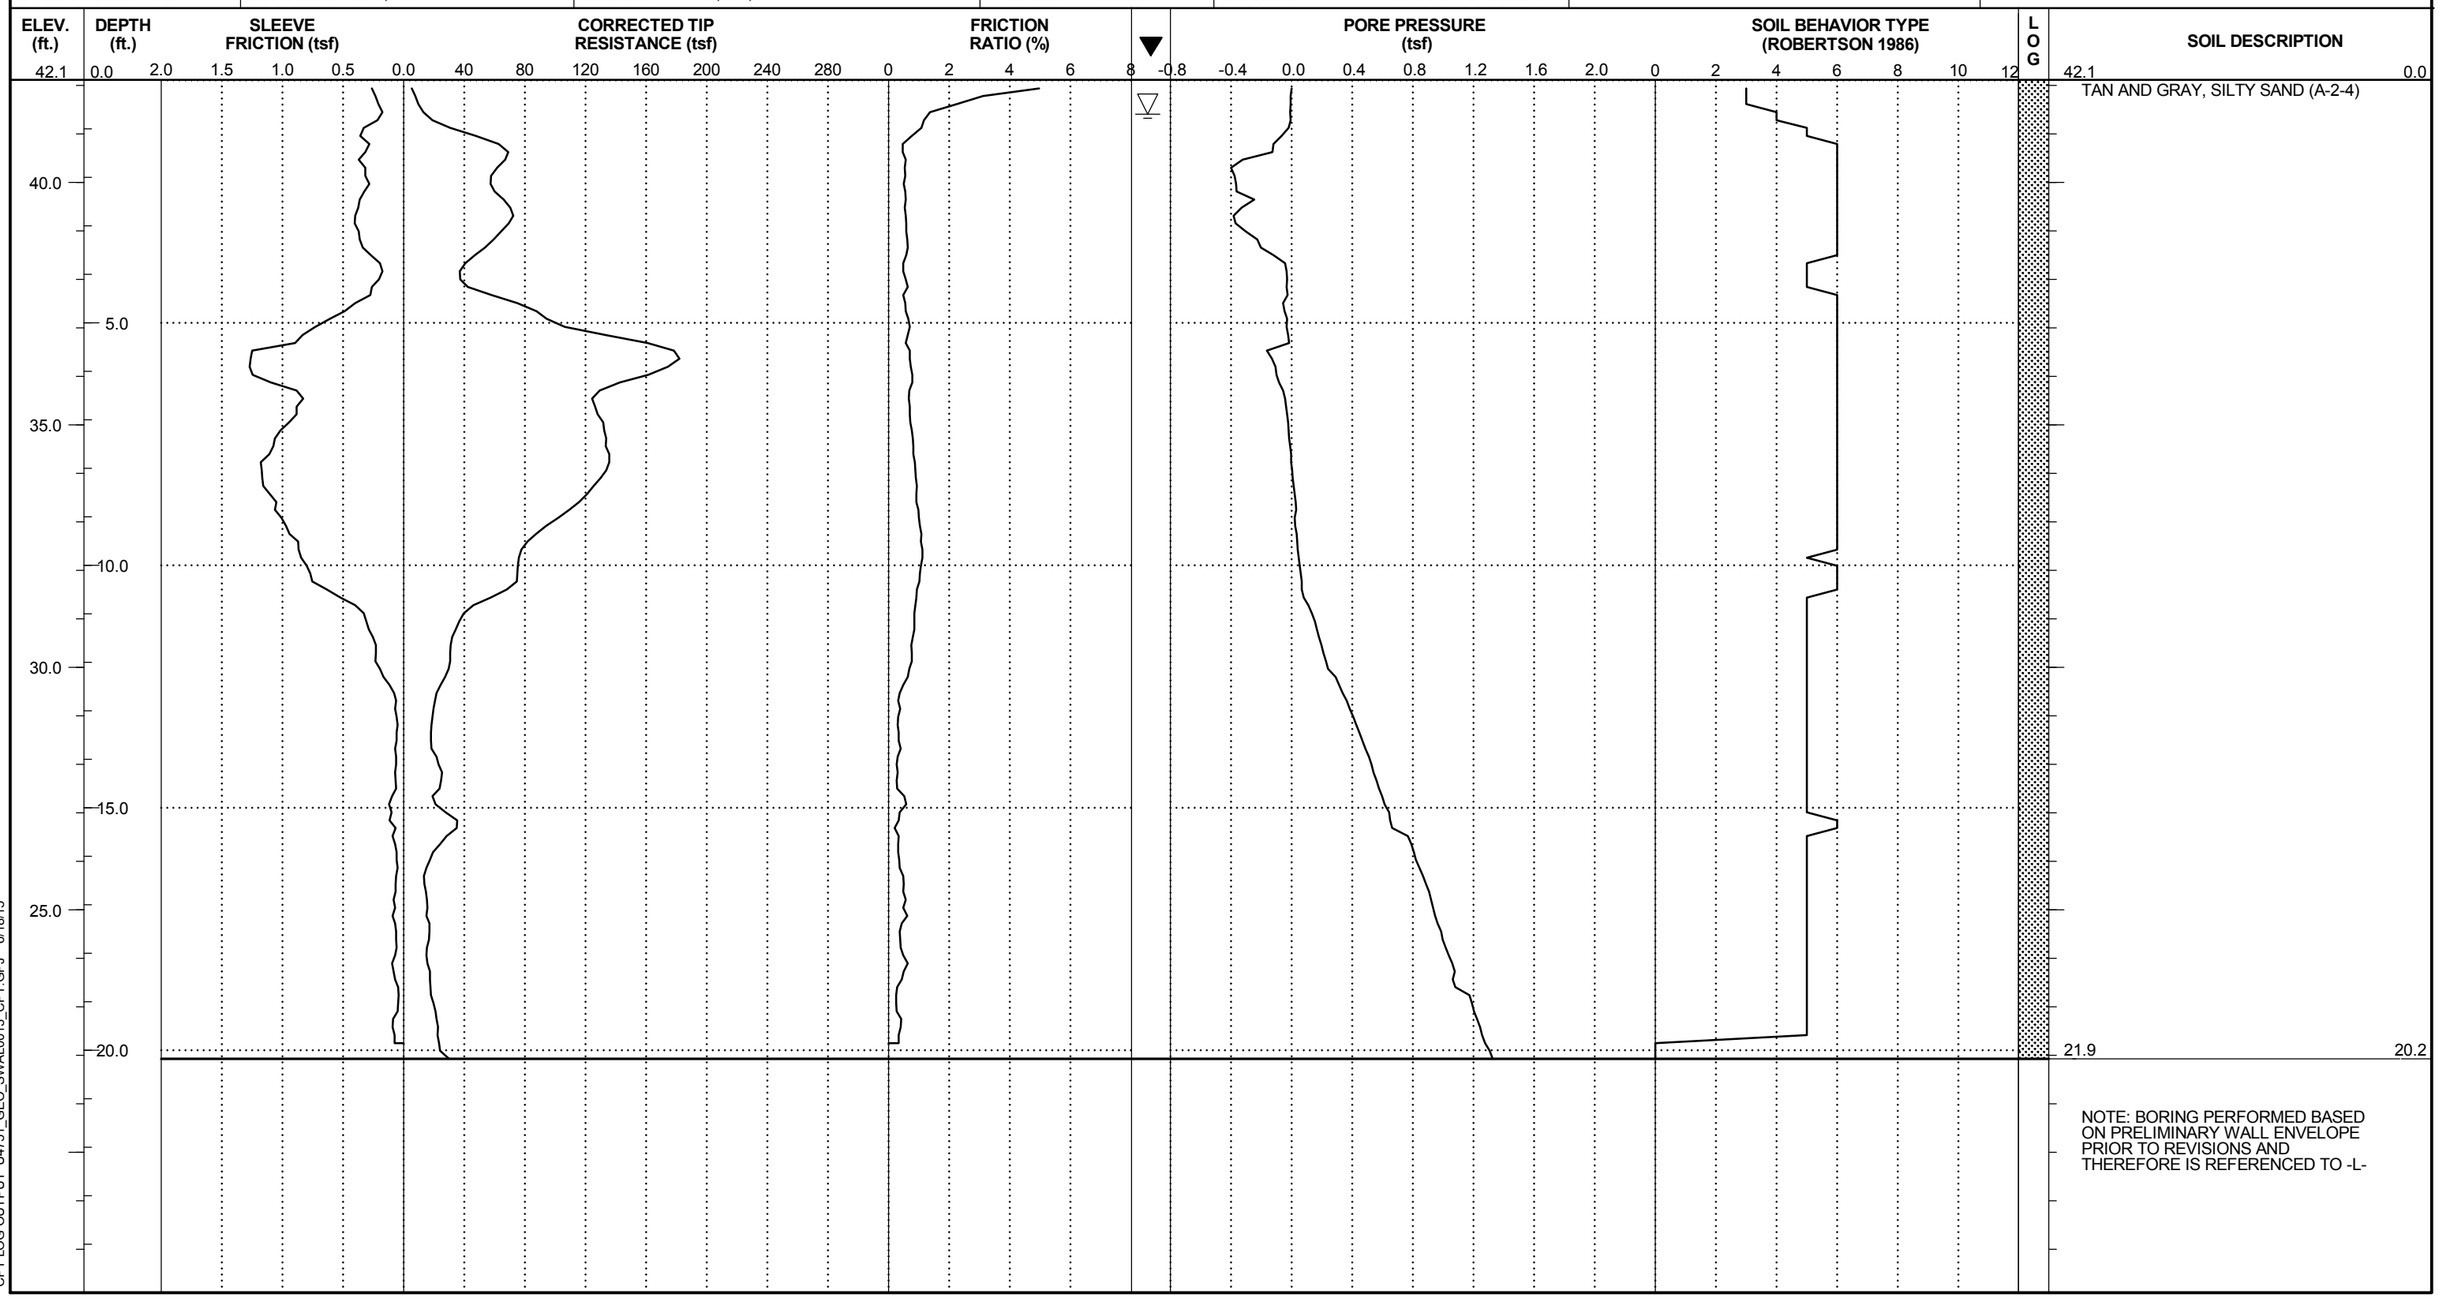

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-34	**BORING LOCATION** 161+76	**OFFSET** 65' LT	**ALIGNMENT** -L-	**0 HR.** 0.9	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 42.2 ft	**NORTHING** 200,251	**EASTING** 2,355,414		**24 HR.** 0.9	**DRILLER** CONTRACT DRILLER		

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF	
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A	
BORING NO. B-36	**BORING LOCATION** 163+76	**OFFSET** 65' LT	**ALIGNMENT** -L-	**0 HR.** 2.2	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.5 ft	**NORTHING** 200,442	**EASTING** 2,355,355		**24 HR.** 1.3	**DRILLER** CONTRACT DRILLER		

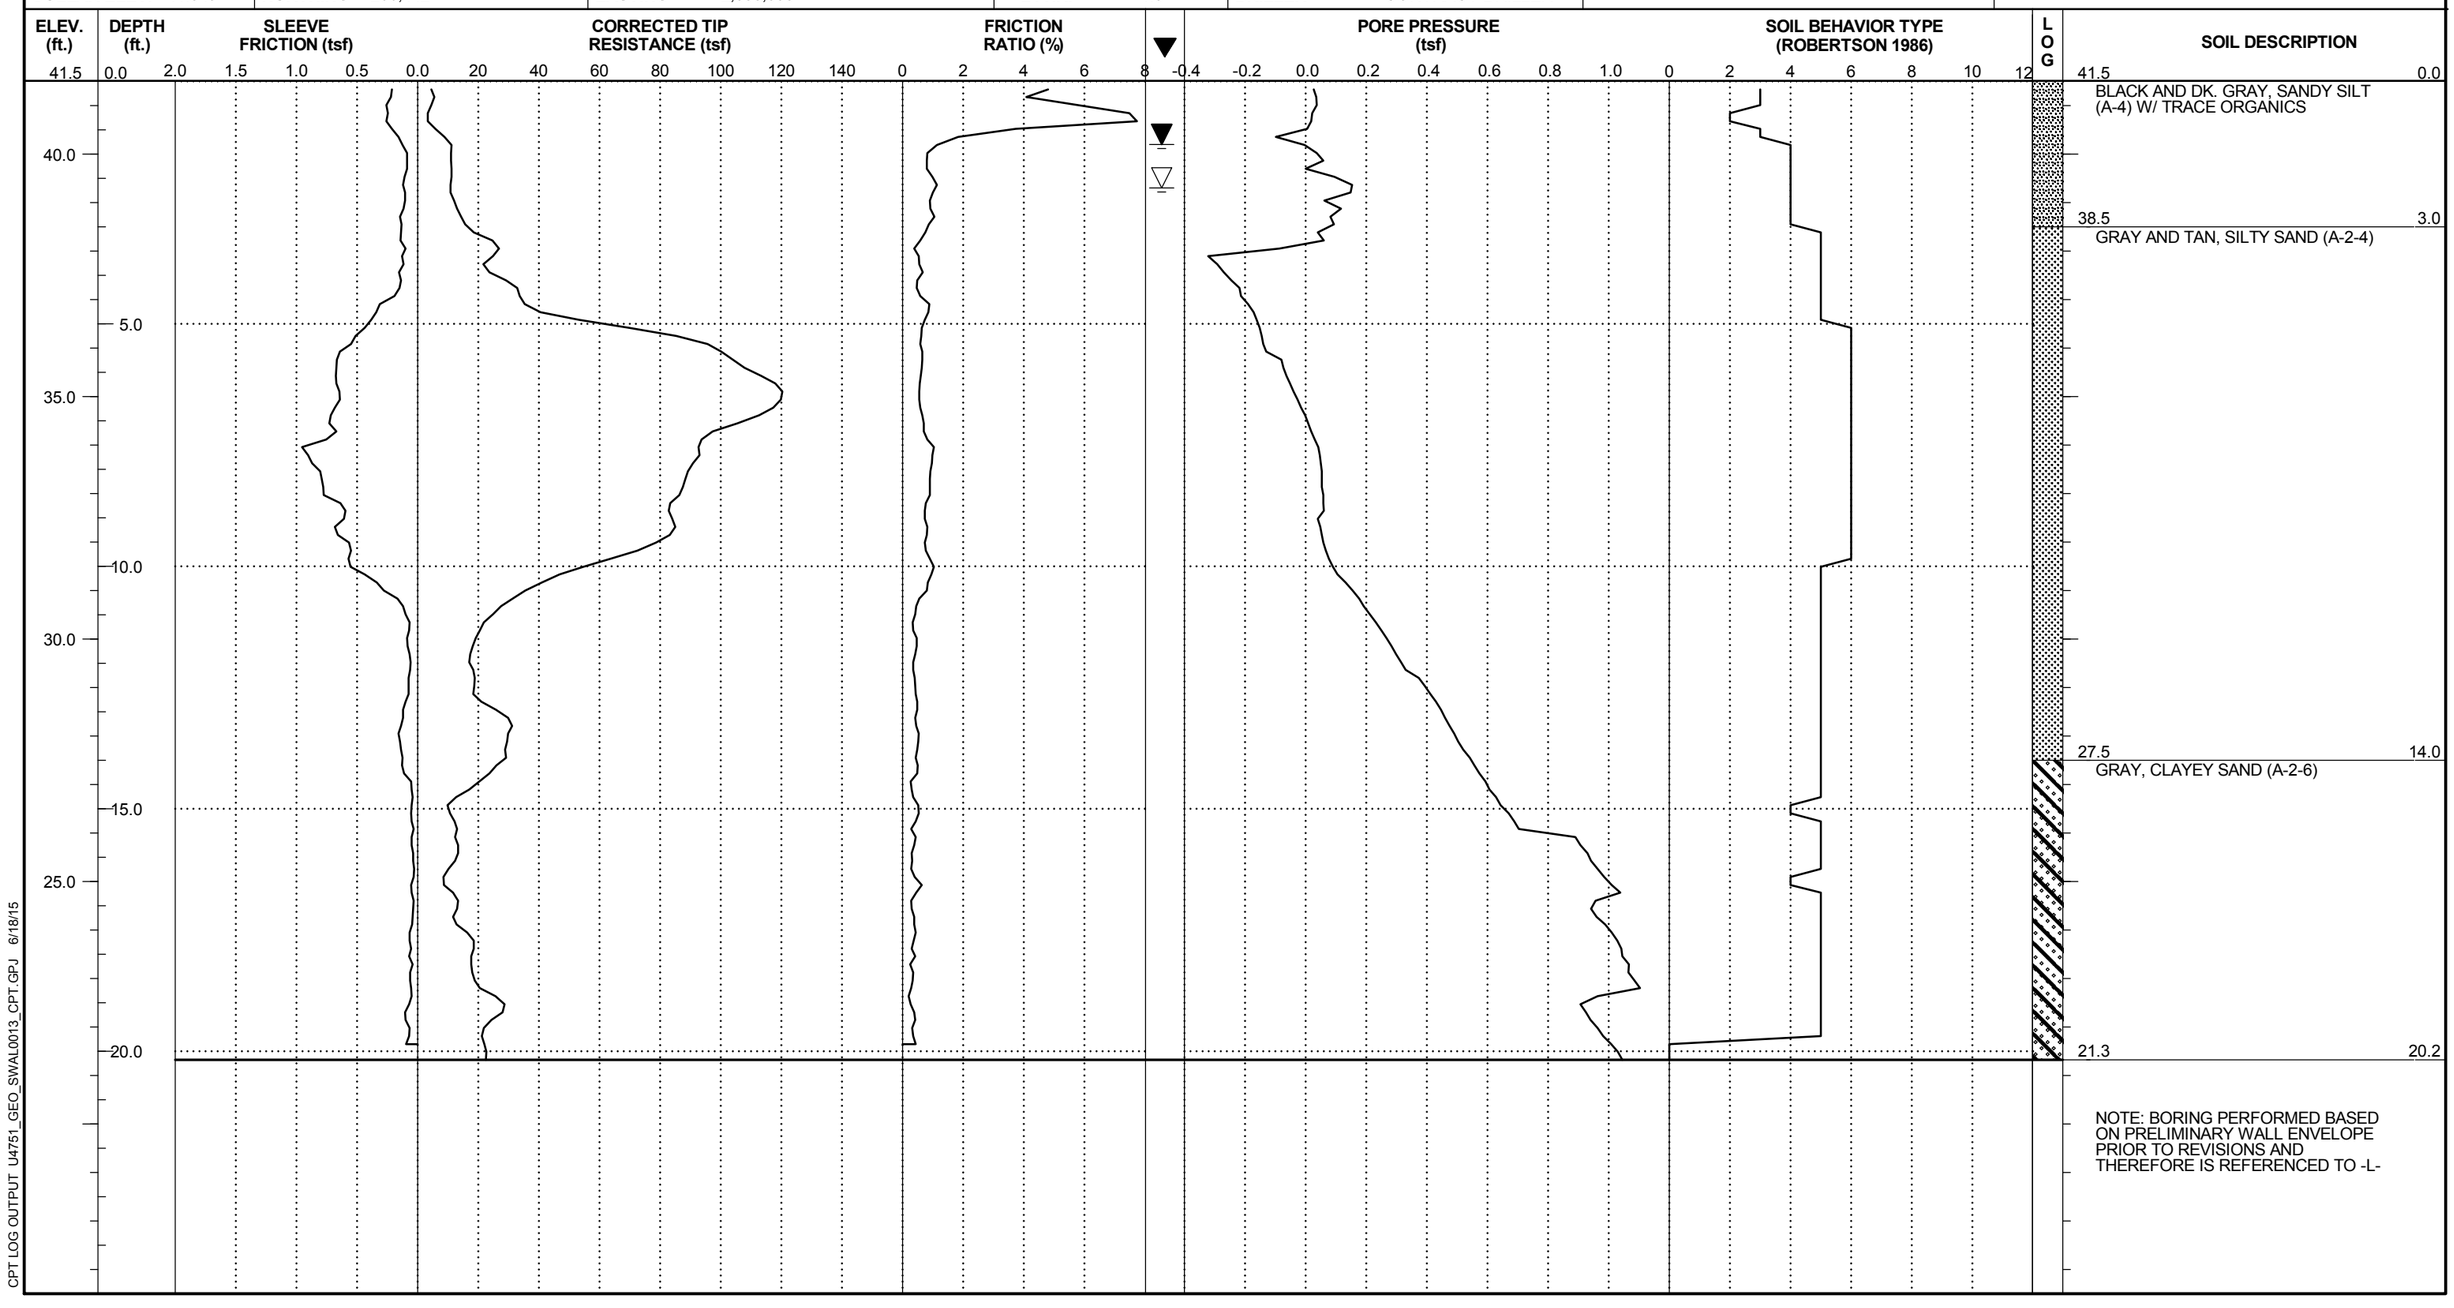

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-38	**BORING LOCATION** 165+76	**OFFSET** 65' LT	**ALIGNMENT** -L-	**0 HR.** 1.8	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.0 ft	**NORTHING** 200,633	**EASTING** 2,355,296		**24 HR.** 1.8	**DRILLER** CONTRACT DRILLER		

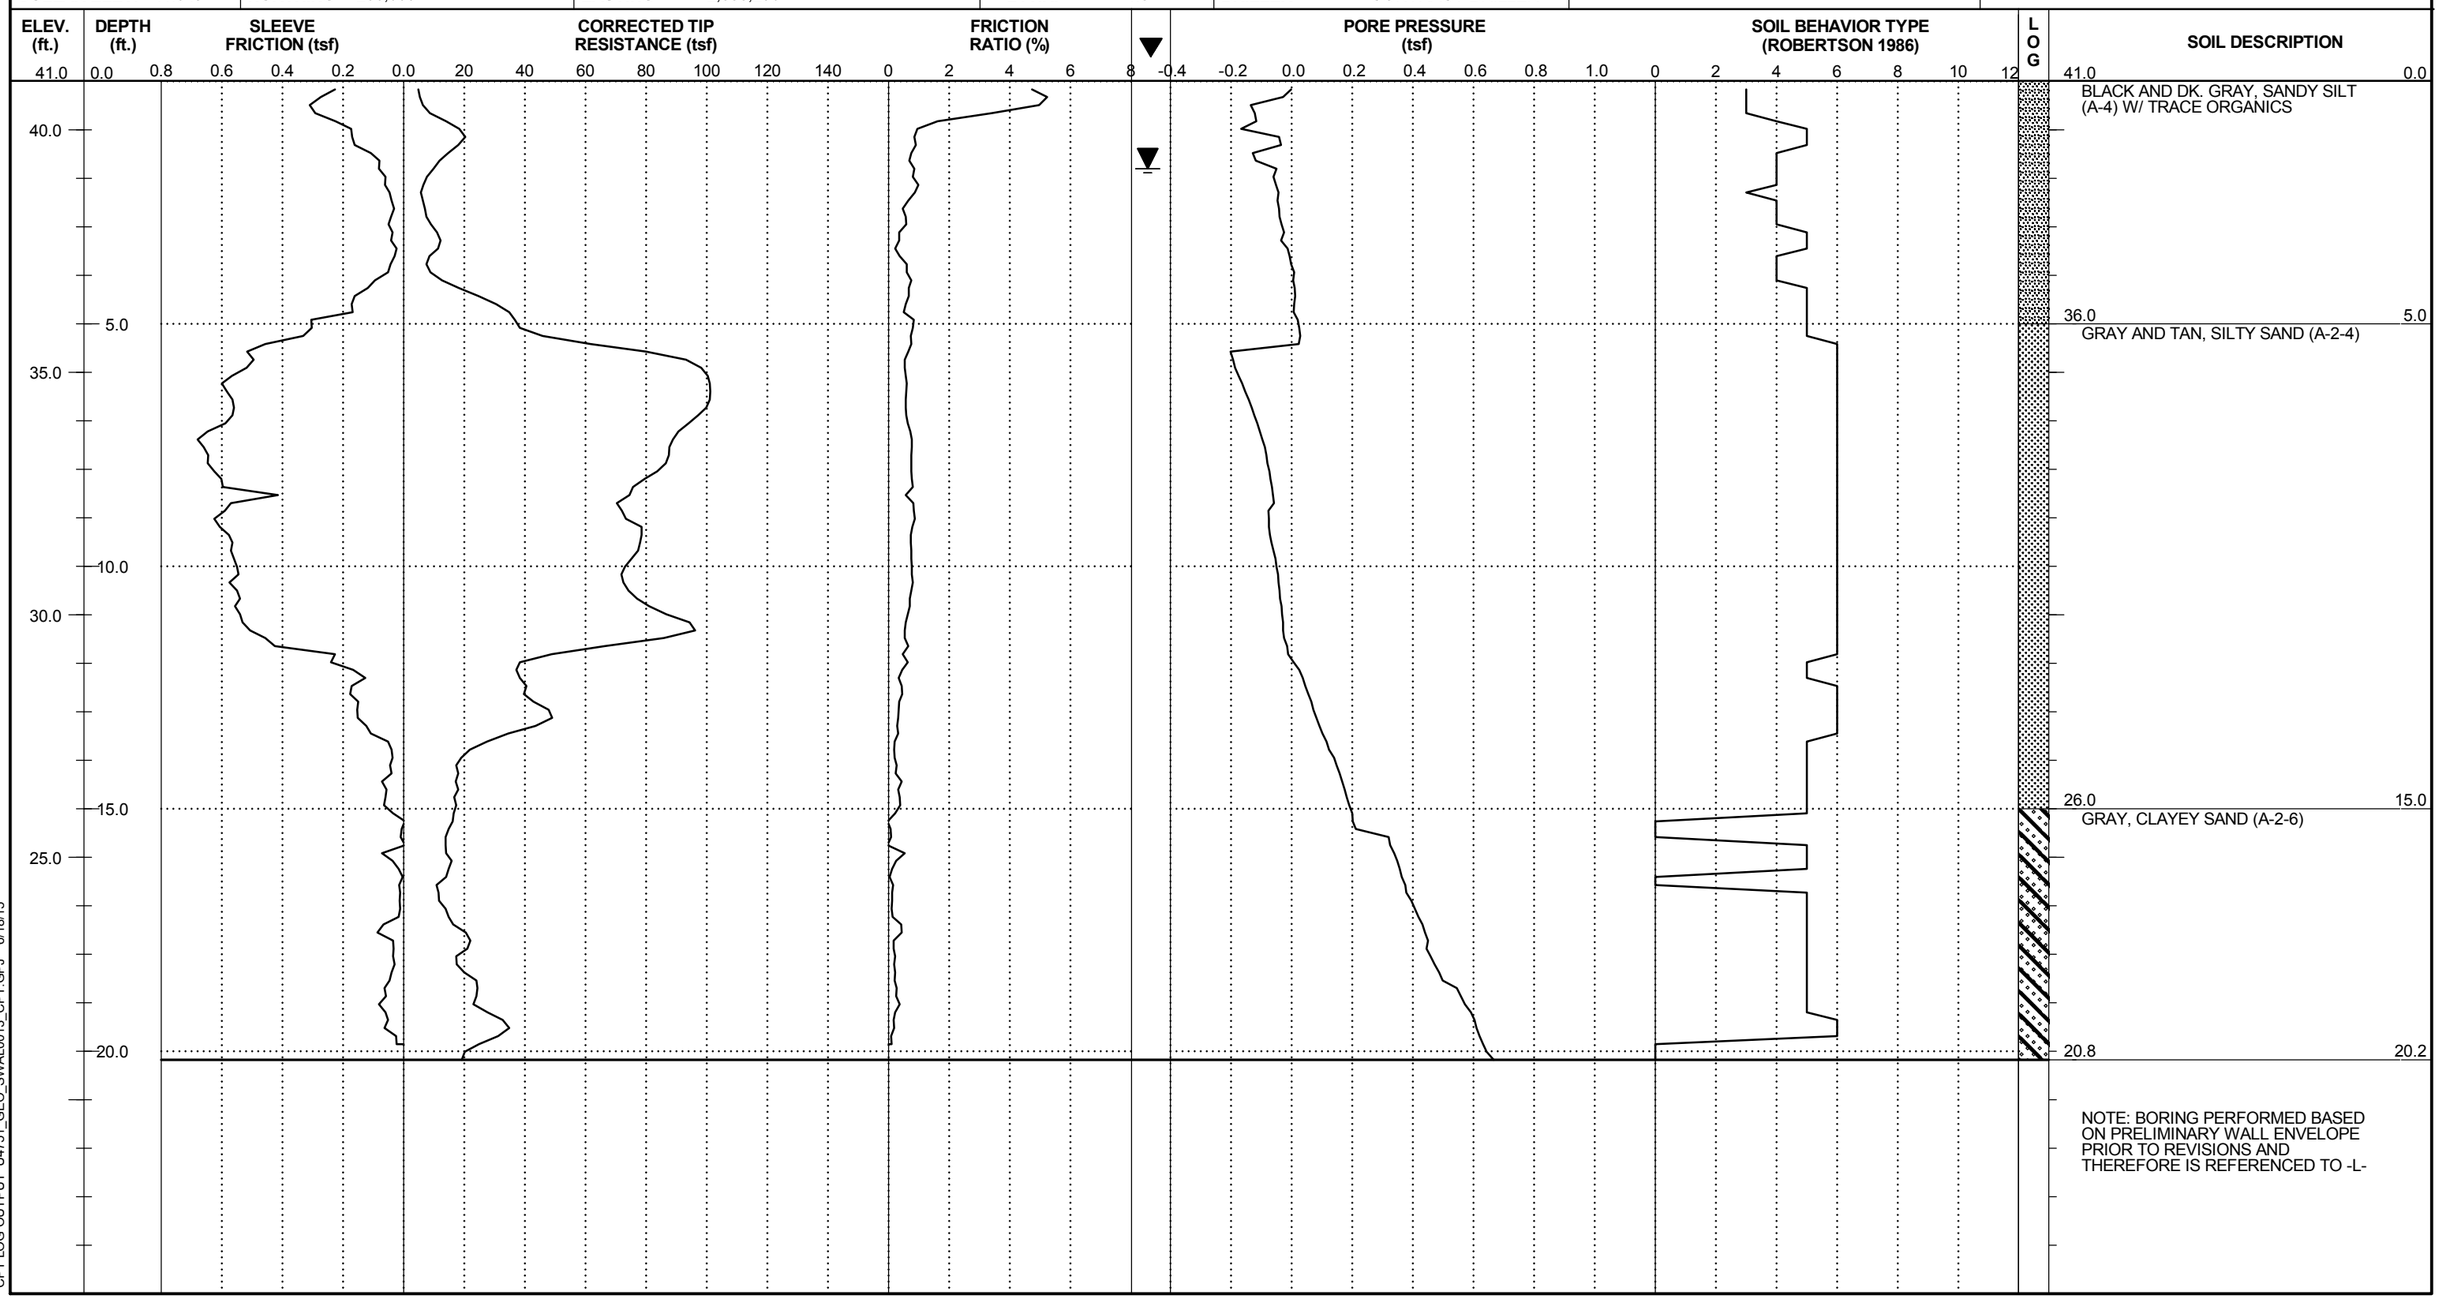

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-40	**BORING LOCATION** 167+76	**OFFSET** 66' LT	**ALIGNMENT** -L-	**0 HR.** 1.5	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.5 ft	**NORTHING** 200,824	**EASTING** 2,355,236		**24 HR.** 2.3	**DRILLER** CONTRACT DRILLER		

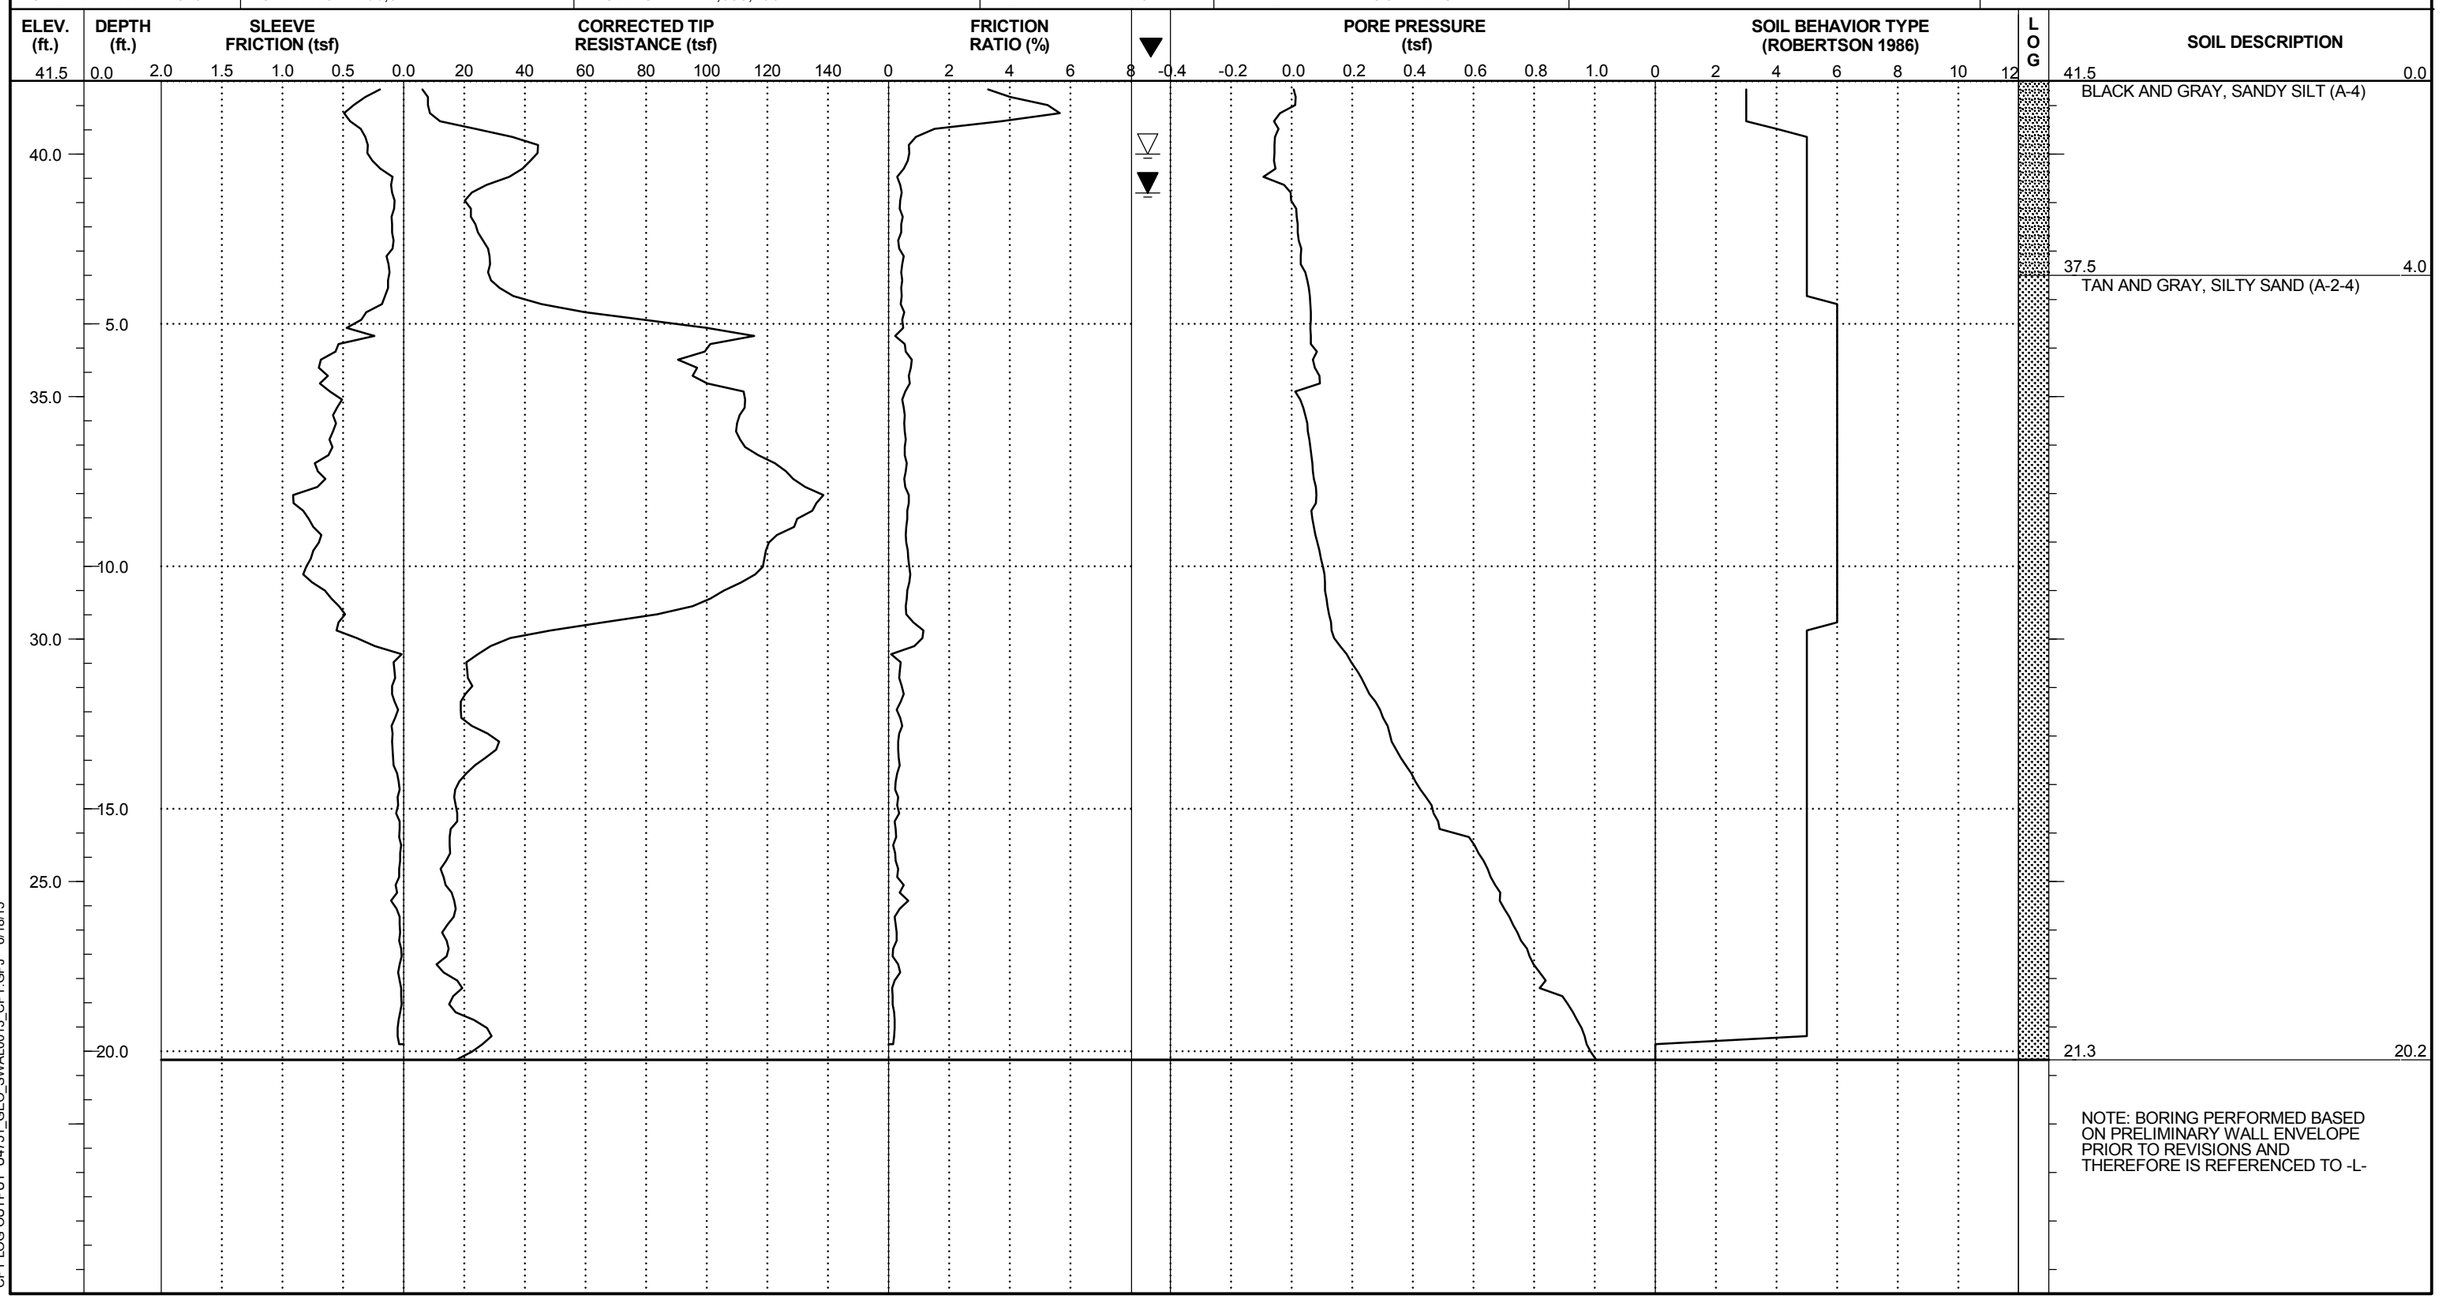

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-42	**BORING LOCATION** 169+76	**OFFSET** 70' LT	**ALIGNMENT** -L-	**0 HR.** 1.1	**TOTAL DEPTH** 20.34 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.6 ft	**NORTHING** 201,014	**EASTING** 2,355,174		**24 HR.** 2.4	**DRILLER** CONTRACT DRILLER		

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NORTH CAROLINA 27607
Phone (919) 871-0800 Fax (919) 871-0803

PROJECT NO. U-4751	**ID.** 40191.1.2	**COUNTY** NEW HANOVER	**LOGGED BY** HUNSBERGER, W. S.	**TYPE OF CONE** 10 TON CONE	**ROD TYPE** 1.4" DIA	**MAX. DOWN PRESSURE (tsf)** 900 TSF
SITE DESCRIPTION SR 1409 (MILITARY CUTOFF RD) TO US 17 IN WILIMINGTON - NOISE WALL 13			**GROUND WATER (ft.)**	**DATE STARTED** 1/14/15	**COMPLETED** 1/14/15	**SURFACE WATER DEPTH** N/A
BORING NO. B-43	**BORING LOCATION** 171+12	**OFFSET** 70' LT	**ALIGNMENT** -L-	**0 HR.** 1.5	**TOTAL DEPTH** 20.18 ft	**DRILL MACHINE** CPT TRACK	**DRILL METHOD** DIRECT PUSH
COLLAR ELEV. 41.5 ft	**NORTHING** 201,144	**EASTING** 2,355,134		**24 HR.** CAVED	**DRILLER** CONTRACT DRILLER		

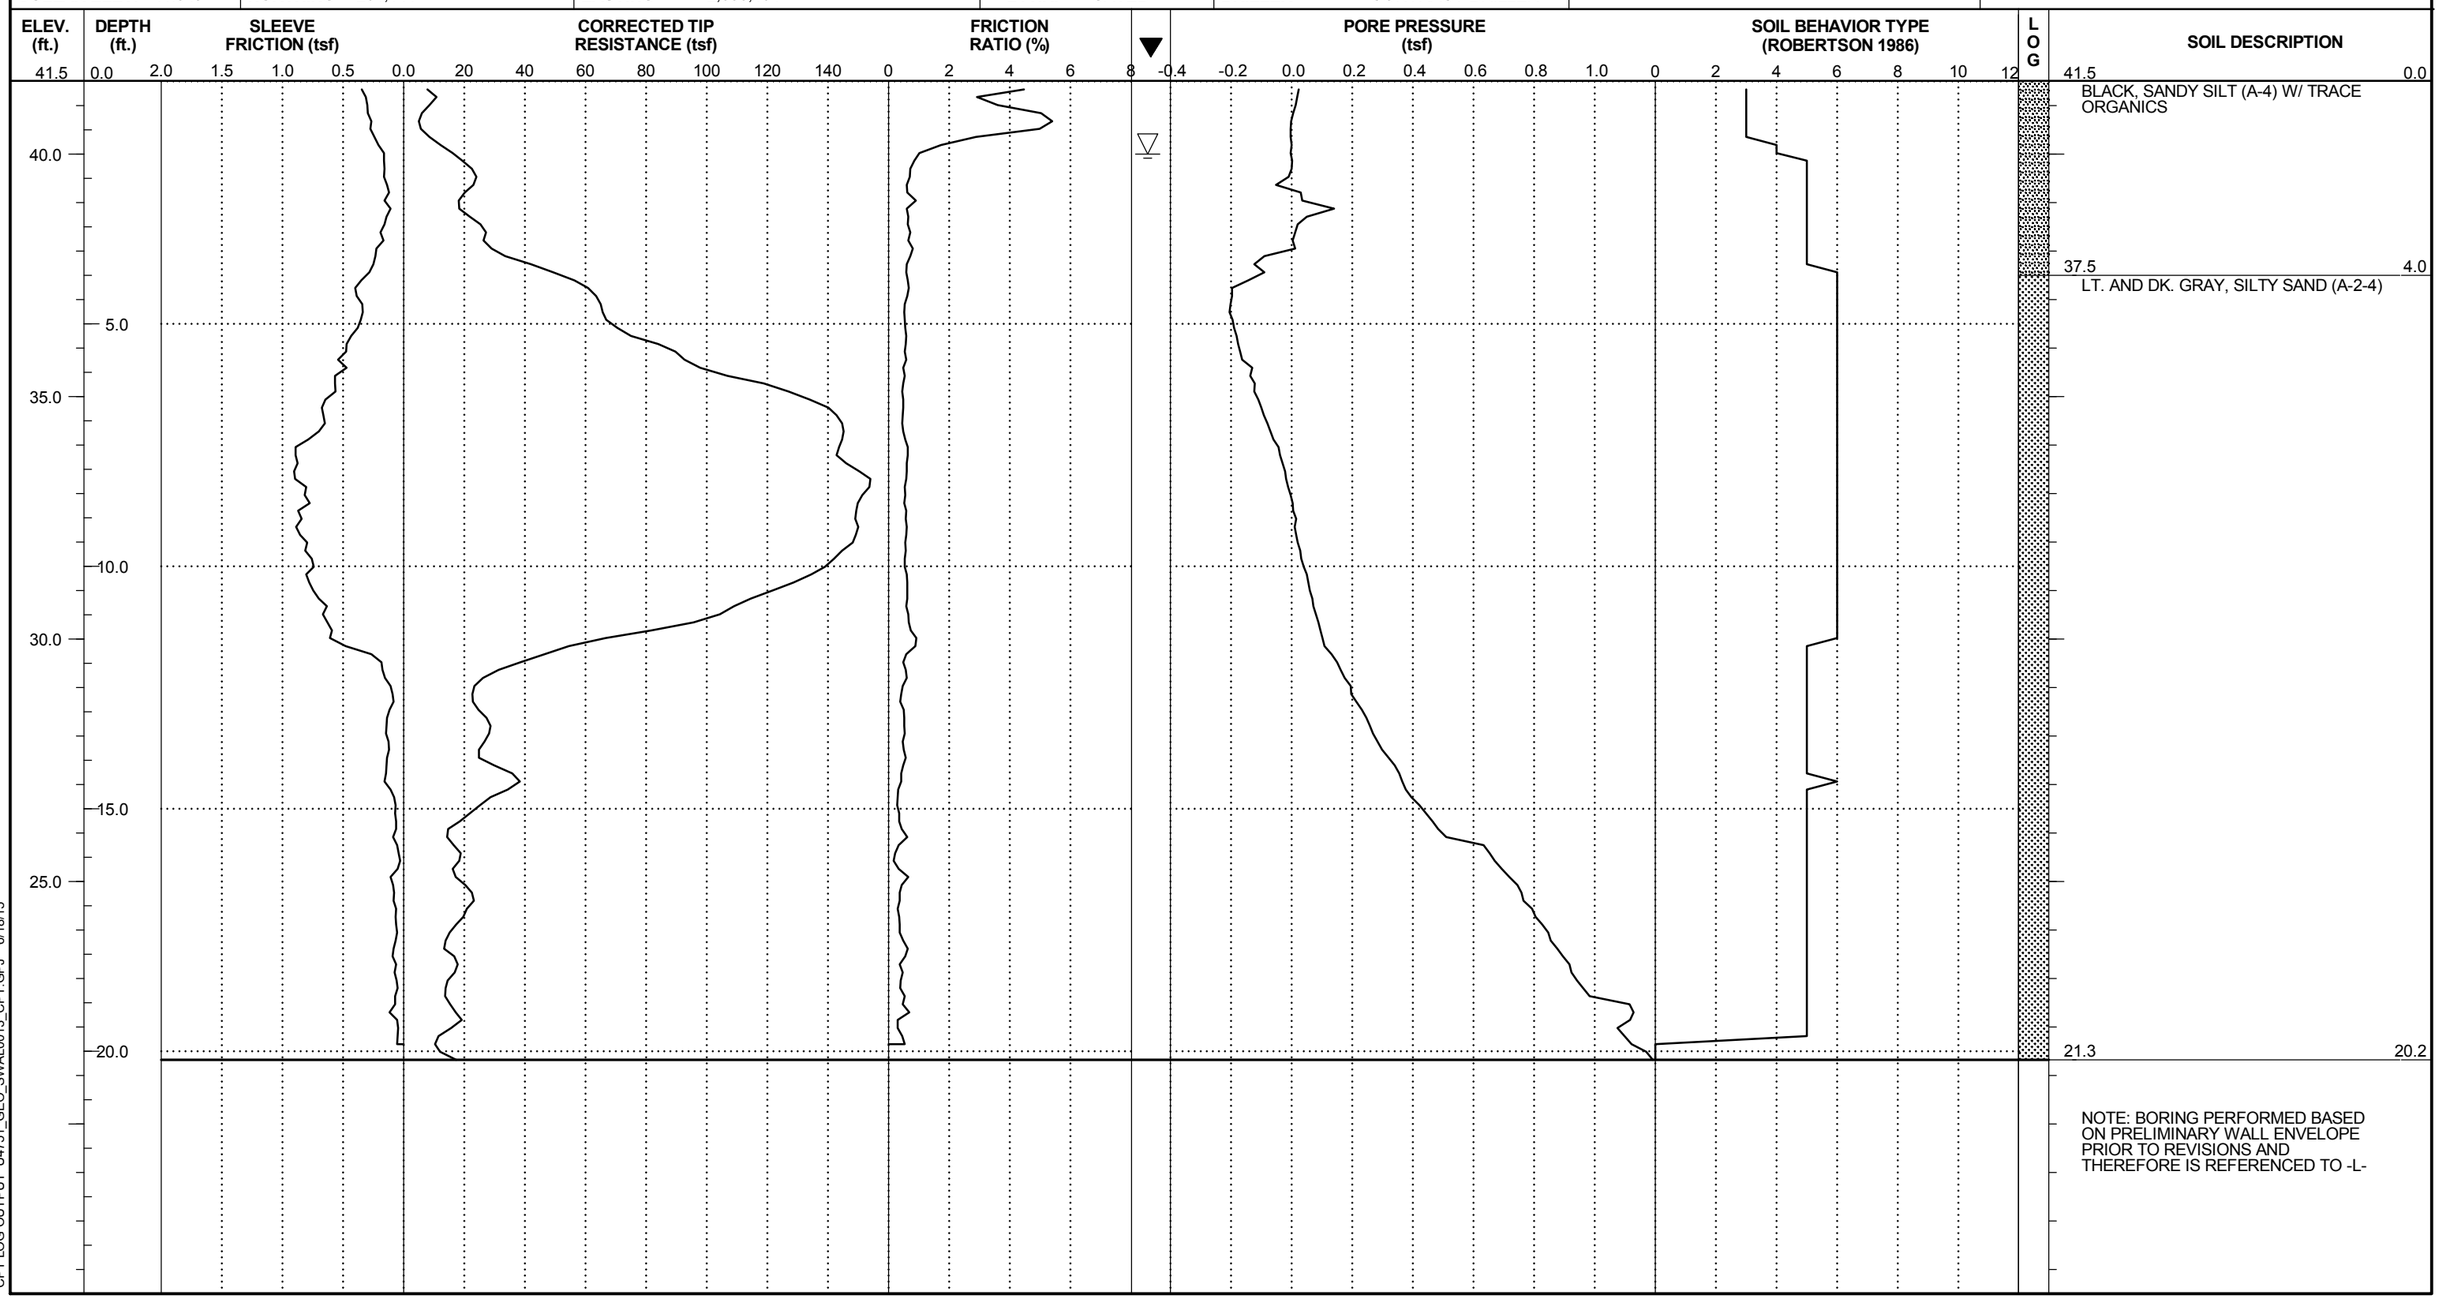

CPT LOG OUTPUT U4751_GEO_SWAL0013_CPT.GPJ 6/18/15

SPT RIG AT STAKED B-1 LOCATION

CPT RIG AT STAKED B-2 LOCATION

B-11 STAKED LOCATION

LOOKING DOWNSTATION FROM B-18 ALONG -NW_13-

FALCON ENGINEERING, INC.
1210 TRINITY ROAD, SUITE 110
RALEIGH, NC 27607
PHONE: 919.871.0800
FAX: 919.871.0803

SITE PHOTOGRAPHS

SR1409 (MILITARY CUTOFF RD) TO US 17 IN WILMINGTON
NOISE WALL 13
NEW HANOVER COUNTY, NC
WBS NO.: 40191.1.2 TIP NO.: U-4751
