3@8'X9' RCBC CONSTRUCTION SEQUENCE
STA. 1042 + 09 –L– STONY RUN (HANNAS POND)

PROJECT REFERENCE NO.	SHEET NO.
I-5878	EC-21B/CONST.21
R/W SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

PHASE III
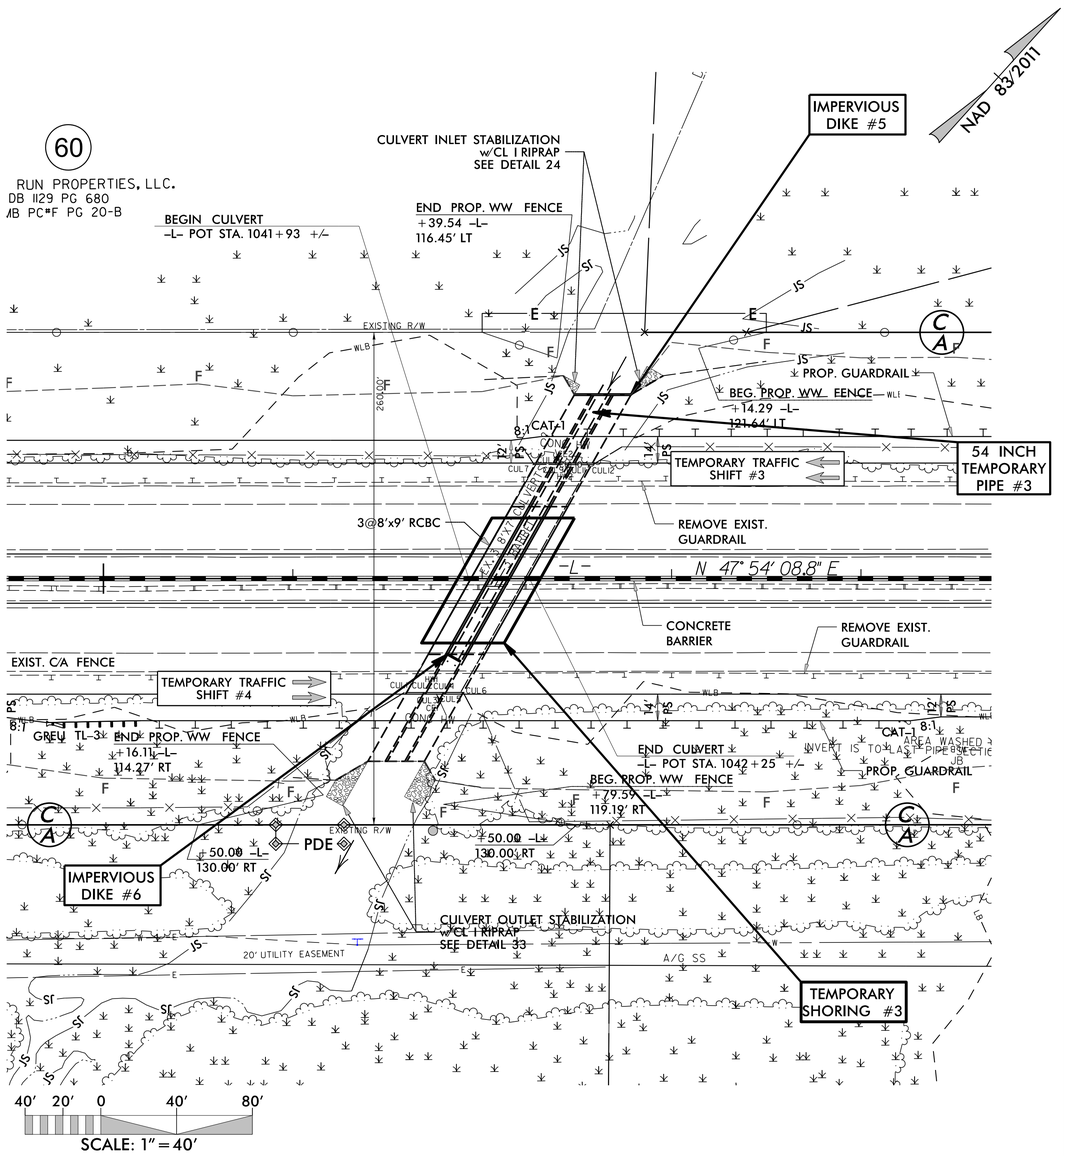
1.) UTILIZE SPECIAL STILLING BASIN(S) AS NEEDED THROUGHOUT CULVERT CONSTRUCTION.
2.) INSTALL IMPERVIOUS DIKES #5 AND #6 AND TEMPORARY 54" PIPE #3.
3.) DEWATER CONSTRUCTION AREA, UTILIZING SPECIAL STILLING BASIN(S) FOR PUMPED EFFLUENT.
4.) CONSTRUCT TEMPORARY SHORING #3 AND TEMPORARY TRAFFIC SHIFTS #3 AND #4.
5.) REMOVE REMAINDER OF EXISTING BOX CULVERT.
6.) CONSTRUCT REMAINDER OF PROPOSED BOX CULVERT.
7.) EXCAVATE ANY ACCUMULATED SILT AND DEWATER BEFORE REMOVAL OF IMPERVIOUS DIKES.
8.) REMOVE IMPERVIOUS DIKES, TEMPORARY 54" PIPE #3, AND TEMPORARY SHORING #3 AND DIVERT FLOW THROUGH 3@8'X9' RCBC.
9.) COMPLETE ROADWAY AND REMOVE TEMPORARY TRAFFIC SHIFTS #3 AND #4.
