DocuSign Envelope ID: FEC680E6-CB45-4C69-A809-6B6D3CC7F073

CULVERT CONSTRUCTION SEQUENCE STA. 113+69 –L–

PROJECT REFERENCE NO.	SHEET NO.
A-0009CA	EC-13B/CONST.J3
R/W SHEET NO.	___
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

9. INSTALL IMPERVIOUS DIKES #5 & #6 AND DIRECT FLOW THROUGH NEW P1 EXTENSION.
10. CONSTRUCT WALL 1.5 FT ABOVE FLOOR SLAB ACCORDING TO STRUCTURE PLANS.
11. REMOVE IMPERVIOUS DIKES #5 & #6 AND REESTABLISH STREAM ACCORDING TO CONST. PLANS.
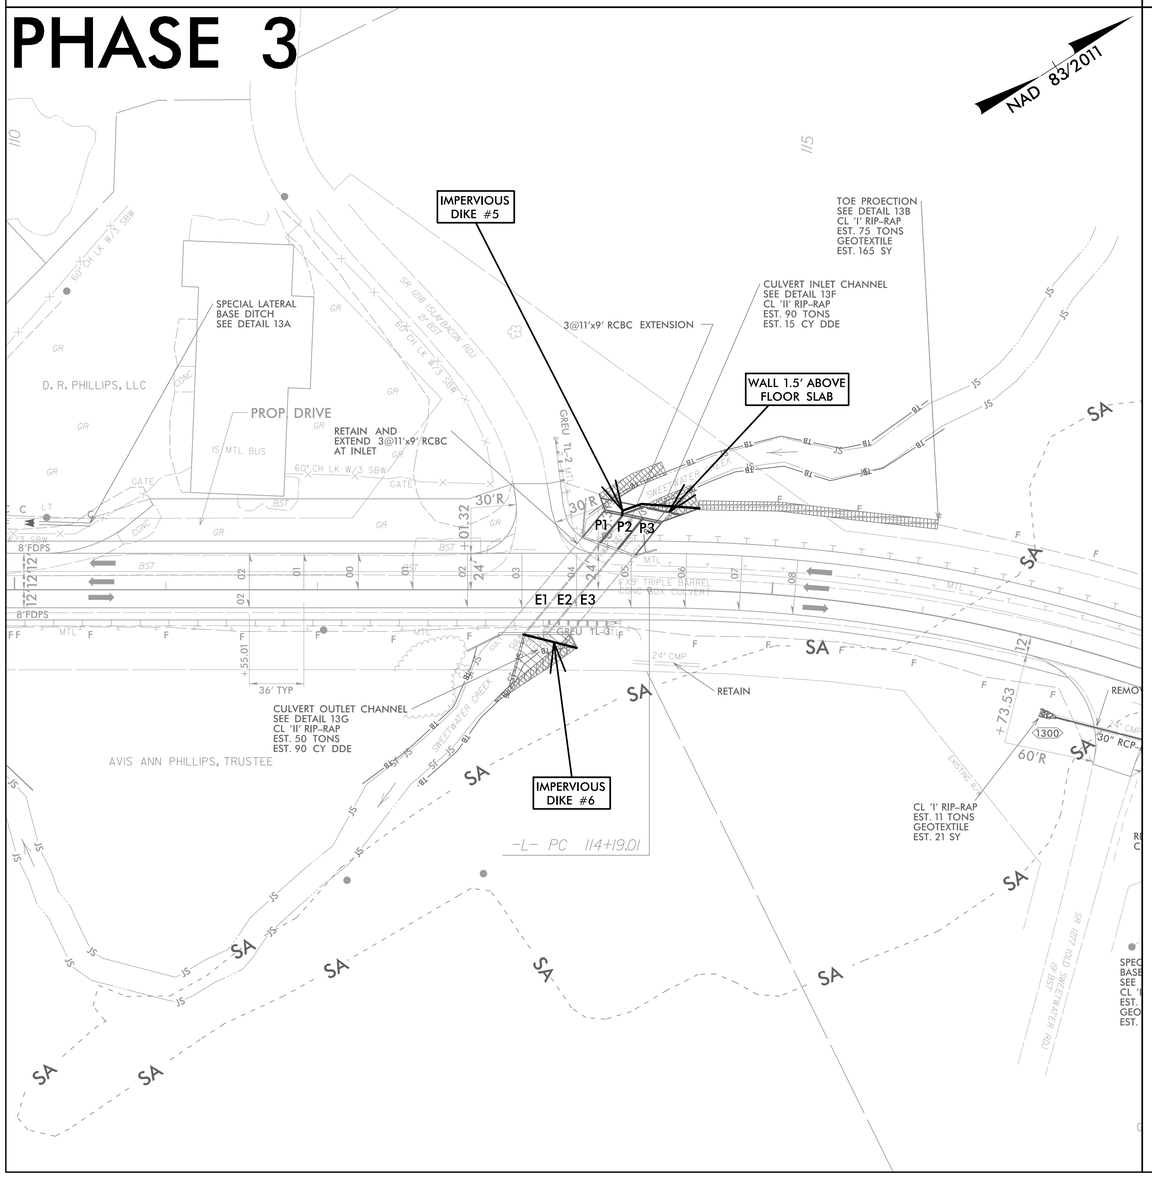
PHASE 3
