DocuSign Envelope ID: FEC680E6-CB45-4C69-A809-6B6D3CC7F073

CULVERT CONSTRUCTION SEQUENCE STA. 195+16 –L–

PROJECT REFERENCE NO.	SHEET NO.
A-0009CA	EC-19B/CONST.J9
R/W SHEET NO.	___
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

8. REMOVE IMPERVIOUS DIKES #3 & #4.
9. INSTALL IMPERVIOUS DIKES #5 & #6, DIVERTING FLOW INTO NEW 7'X8' RCBC P2.
10 REMOVE EXISTING 72" CMP E1 AND CONSTRUCT P1 WINGWALLS.
11. COMPLETE HEADWALLS AND WINGWALLS ACCORDING TO DRAINAGE AND STRUCTURE PLANS.
12. REMOVE IMPERVIOUS DIKES #5 & #6 AND RESTORE STREAM.
13. COMPLETE ROADWAY AND SHIFT TRAFFIC FROM DETOUR.
14. REMOVE DETOUR ROADWAY AND TEMPORARY 2@103"X71" CS PIPE-ARCH.
15. COMPLETE FINAL GRADING OF PROPOSED BERM.
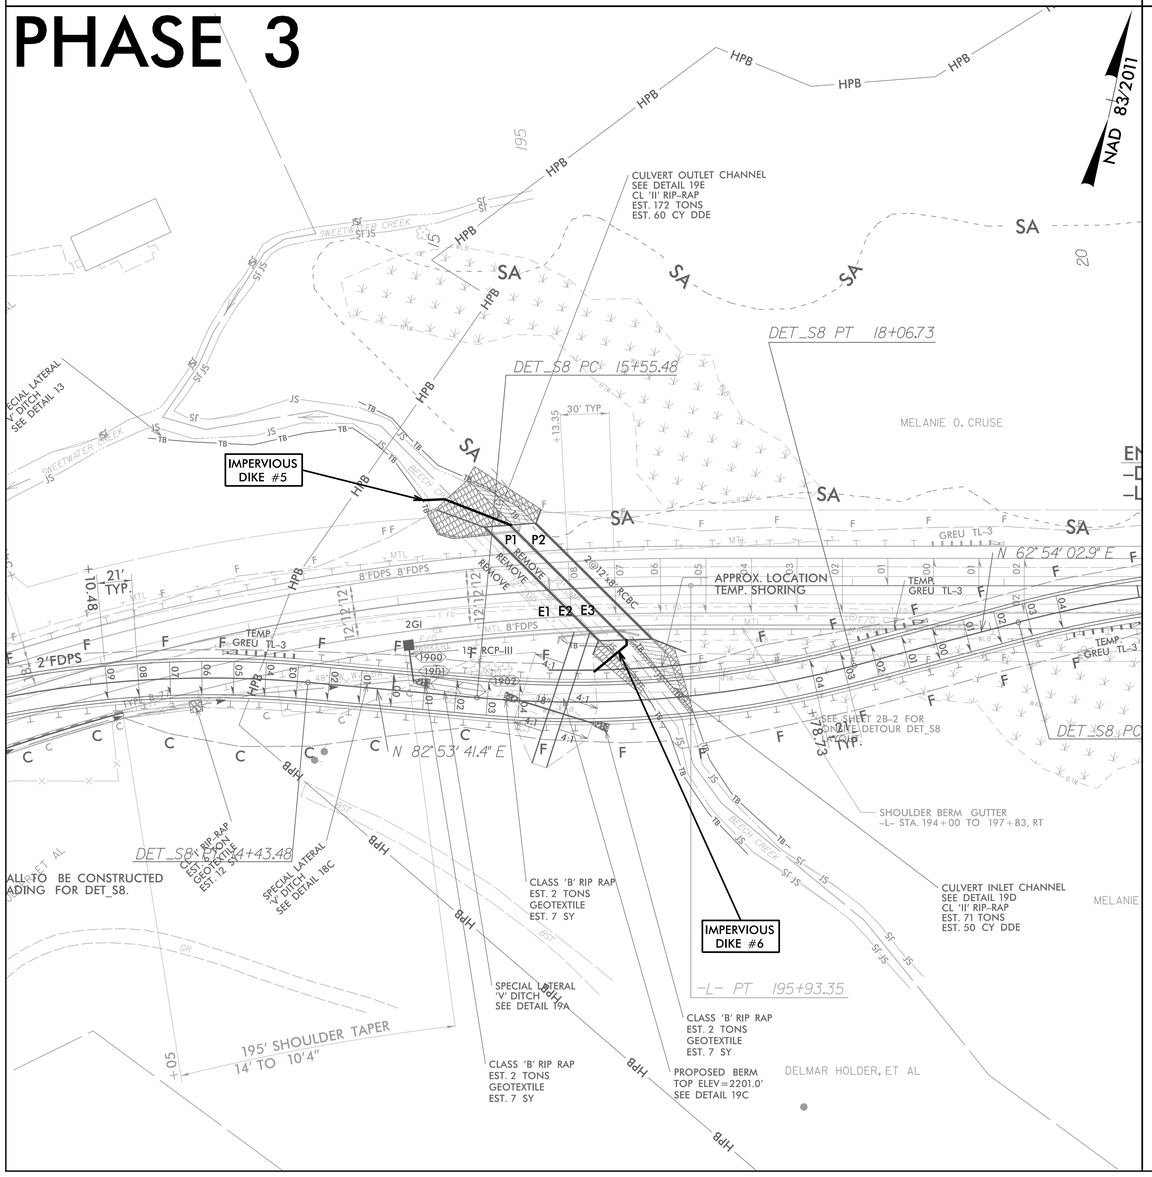
PHASE 3
