5/26/20

# *SURVEY CONTROL SHEET*

## *W/ EXISTING CENTERLINE ALIGNMENTS PRIOR TO CONSTRUCTION*

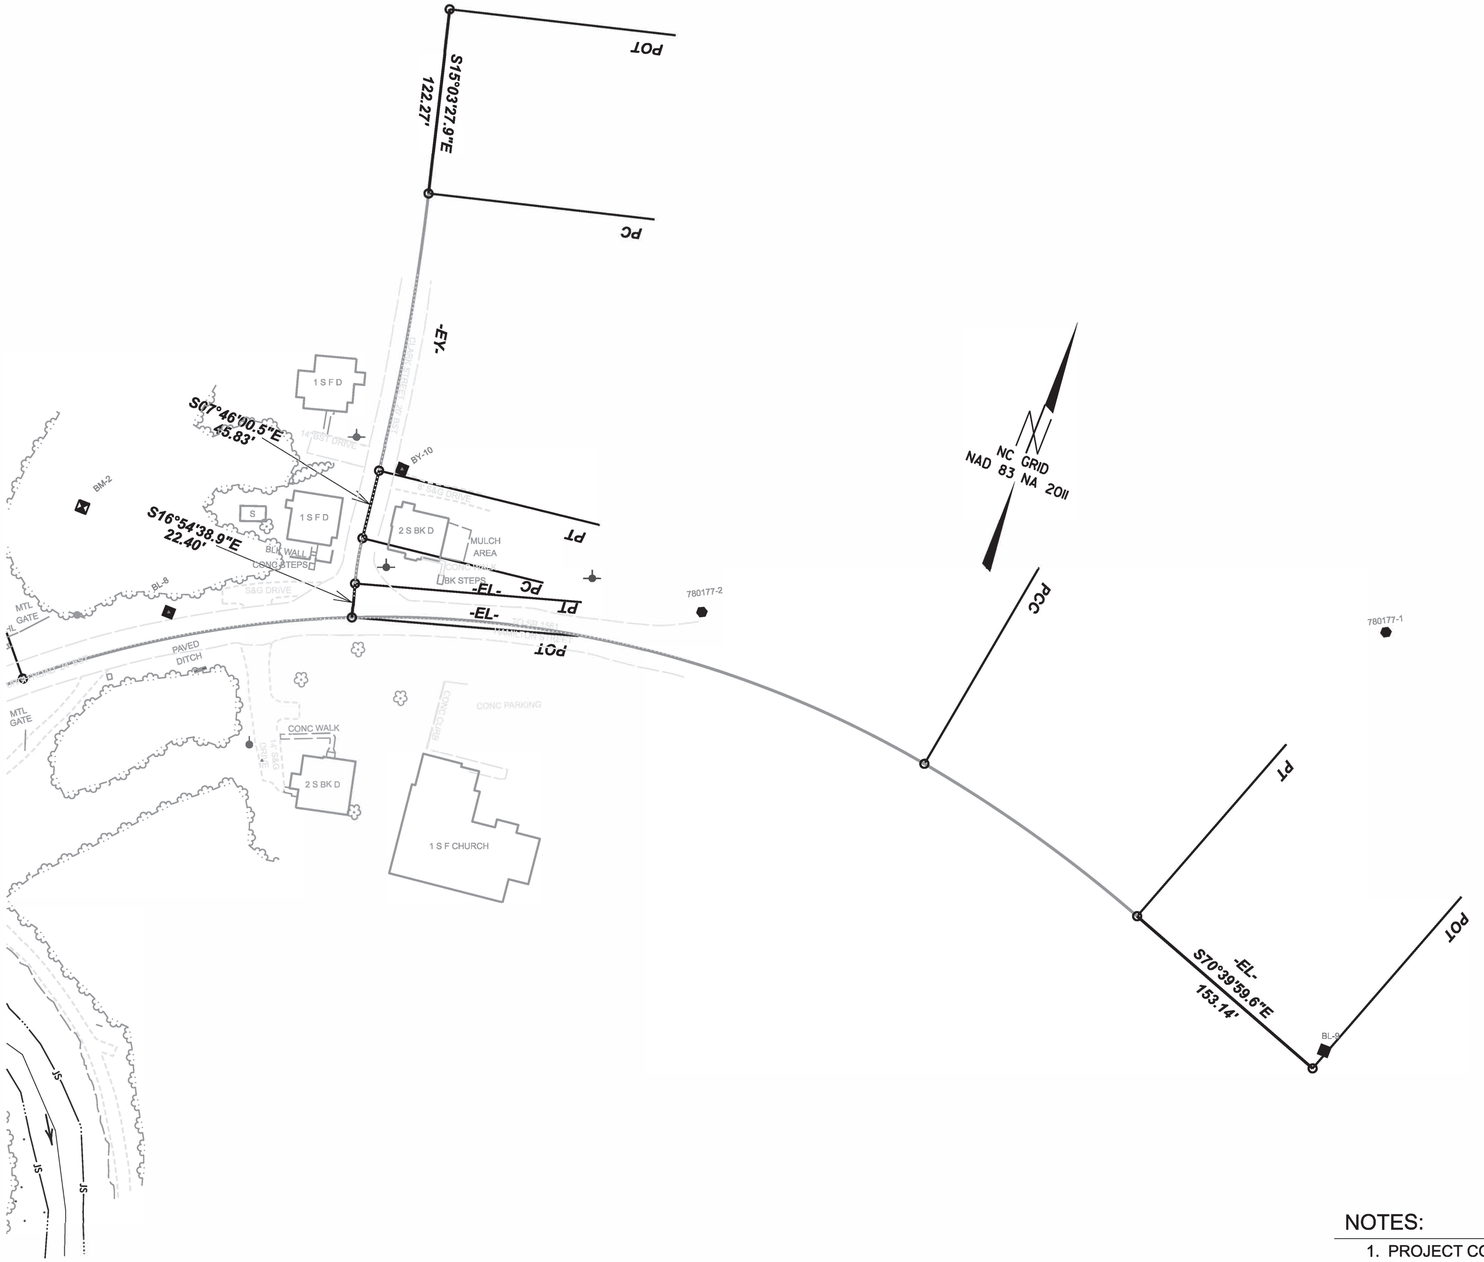


I, Parks H Icenhour Jr, PLS, certify that the Project Control was performed by others from an actual GPS survey made by others and the following information was used to perform the survey:

Class of survey: ***AA***
Type of GPS field procedure: RTN
Dates of survey: N/A
Datum/Epoch:NAD 1983/ N2011
Published/Fixed-control use: N/A
Localized around: 780177-2
Northing: 1000678.329
Easting: 1769607.838
Combined grid factor: 0.99991460
Geoid model: G12BNC
Units: US SURVEY FEET

I also certify that the Baseline Control for this project was completed under my direct and responsible charge from an actual survey made under my supervision; that all horizontal closures had a minimum ratio of precision of 1:20,000 (Class AA) and Vertical accuracy to Class A. Field work was performed from 7-27-23 to 7-31-23 , and all coordinates are based on NAD 83/2011 and all elevations are based on NAVD 88; that this survey was performed to meet the requirements of 21NCAC 56.1600 as applicable.

This 11th day of May, 2026.

Digitally signed by Parks H. Icenhour, Jr.
Date: 2026.05.11 13:18:40 -04'00'

Professional Land Surveyor L-3996

NOTES:

1. PROJECT CONTROL WAS ESTABLISHED USING GNSS, THE GLOBAL NAVIGATION SATELLITE SYSTEM.

2. THE SURVEY CONTROL DATA FOR THIS PROJECT HAS BEEN COMPILED FROM VARIOUS SOURCES. IF FURTHER INFORMATION REGARDING PROJECT CONTROL IS NEEDED, PLEASE CONTACT THE LOCATION AND SURVEYS UNIT.

HB-0035
R/W 02C-2

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION

PROFESSIONAL LAND SURVEYOR

NORTH CAROLINA PROFESSIONAL SEAL L-3996 LAND SURVEYOR PARKS H. ICENHOUR JR.

GEL ENGINEERING OF NC, INC. NO. C-1938 CERTIFICATE OF AUTHORIZATION

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES ARE COMPLETED

2024 STANDARD SPECIFICATIONS

***TIP PROJECT: HB-0035***
County: Rockingham

PREPARED FOR

LOCATION AND SURVEYS UNIT

PREPARED BY

GEL SOLUTIONS
an Affiliate of THE GEL GROUP, INC.
111 CREEK RIDGE ROAD
SUITE C
GREENSBORO,NC 27406
(336) 516-9840
WWW.GEL-SOLUTIONS.COM
