DocuSign Envelope ID: 2055D67D-2BC7-4965-A3E1-F0C75DE6942A

PROJ. REFERENCE NO.	SHEET NO.
U-3308	TMP-28

HDR Engineering, Inc. of the Carolinas
3733 National Drive, Suite 207 Raleigh, N.C. 27612
N.C.B.E.L.S. License Number: F-0116

REVISIONS

PLOT DRIVER: NCDOT_pdf_color_eng_50.plt PENTABLE: NCDOT_tcp.tbl
USER: erbrooks DATE: 5/12/2016 TIME: 4:04:33 PM
FILE: c:\pw\working\tpo\d0487729\U-3308_TMP_TMP-28.dgn

MATCHLINE -LALT- STA. 53+50, SEE SHEET TMP-27

ELM ST.

-Y16- HOPKINS ST.

-Y18- LIBERTY ST.

-Y20- EVA ST.

-Y22- HOLLOWAY ST. (US 70 BUS / NC 98)

GILBERT ST.

SAV-A-LOT

SCHOOL

SALVATION ARMY

-LALT- ALSTON AVE. (NC 55)

CONSTRUCT CONC. ISLANDS (STEP 1)

PLACE TEMPORARY MARKINGS IN THE FINAL PATTERN ON -LALT- FROM STA. 57+69 +/- TO STA. 59+12 +/- SB

CONSTRUCT CONCRETE ISLANDS (STEP 1)

PERMANENT STAMPED CONCRETE CROSSWALKS

CONSTRUCT C&G AND SIDEWALK (STEP 2)

MAINTAIN CLOSURE OF CROSSWALKS UNTIL COMPLETION OF NC 55 NB RIGHT-TURN CHANNELIZATION ISLAND (STEP 1)

COMPLETE ALL MEDIAN WORK (STEP 1), AND C&G AND SIDEWALK WORK (STEP 2)

PLACE TEMPORARY MARKINGS IN THE FINAL PATTERN ON -LALT- FROM STA. 55+21 +/- TO STA. 56+67 +/- NB

PLACE TEMPORARY MARKINGS IN THE FINAL PATTERN ON -LALT- FROM STA. 61+67+/- TO STA. 63+58 +/- NB

PLACE TEMPORARY MARKINGS IN THE FINAL PATTERN ON -LALT- FROM STA. 64+26 +/- TO STA. 67+60 +/-, -Y18-, AND -Y22-

MAINTAIN CLOSURE OF PARALLEL PARKING LANE UNTIL COMPLETION OF CONSTRUCTION OR AS DIRECTED BY THE ENGINEER. SHIFT TRAFFIC INTO PARALLEL PARKING LANE, AS NECESSARY, TO COMPLETE MEDIAN ISLAND WORK.

05-1029

05-1027

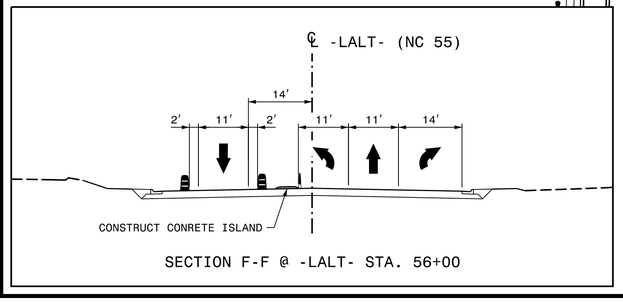

SECTION F-F @ -LALT- STA. 56+00

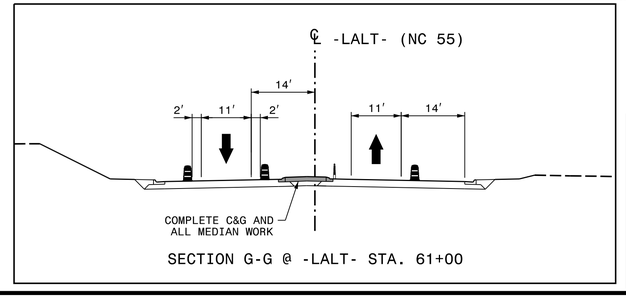

SECTION G-G @ -LALT- STA. 61+00



SECTION H-H @ -LALT- STA. 65+00

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED

APPROVED R. Erskine Brooks DATE: 5/13/2016

SEAL

NORTH CAROLINA PROFESSIONAL SEAL 032584 ENGINEER R. ERSKINE BROOKS

DIVISION OF HIGHWAYS * STATE OF NORTH CAROLINA * DEPARTMENT OF TRANSPORTATION * WORK ZONE TRAFFIC CONTROL

PHASE 3
