



PHASING

COMPLETE THE WORK IN STEP 1 AND STEP 2 IN THREE (3) CONSECUTIVE CALENDAR DAYS. SEE INTERMEDIATE CONTRACT TIMES AND LIQUIDATED DAMAGES.


- STEP 1: USING TMP-4 AND RSD 1101.02 (SHEETS 1, 2, 3, 11, AND/OR 12 OF 15), PLACE TEMPORARY PAVEMENT MARKINGS AT THE INTERSECTION OF SR 4892 (LANCASTER HWY) AND SR 4931 (CAROLINA PLACE PKWY).
- STEP 2: A) INSTALL OFF-SITE DETOUR ROUTE SIGNS & ASSEMBLIES FOR THE CLOSING OF SR -L- (SR. 4982, SOUTH POLK ST).
B) USING ROADWAY STANDARD DRAWING (RSD) NO. 1101.03 (SHEET 1 OF 9), CLOSE -L- FROM STA. 15+00± TO STA. 22+50±, BETWEEN -Y-(SABAL POINT DR) AND -EY1- (MEADOW CREEK LN).
- STEP 3: - AWAY FROM TRAFFIC, REMOVE EXISTING BRIDGE. CONSTRUCT NEW STRUCTURE AND ROADWAY UP TO BUT NOT INCLUDING THE FINAL LAYER OF SURFACE COURSE FROM -L- STA. 15+00± TO -L- STA. 22+50± (SEE ROADWAY PLANS).
- USING RSD NO. 1101.02 (SHEET 1 OF 15), CONSTRUCT SHOULDER WITH CURB AND GUTTER, AND WEDGE ROADWAY UP TO PROPOSED ELEVATION UP TO BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE ON -Y-, -EY-, FROM -L- STA. 12+00± TO -L- STA. 15+00±, AND FROM -L- STA. 22+50± TO -L- STA. 25+25± (SEE ROADWAY PLANS). PLACE TEMPORARY PAVEMENT MARKERS AS SHOWN ON FINAL PAVEMENT MARKING PLANS.
NOTE: UTILIZE DRUMS OR CONES TO MAINTAIN ACCESS TO DRIVEWAYS DURING CONSTRUCTION.
- STEP 4: - REMOVE ALL TRAFFIC CONTROL DEVICES AND OPEN -L- (SR 4982, SOUTH POLK ST) TO THE FINAL TRAFFIC PATTERN. REMOVE ALL OFF-SITE DETOUR SIGNING.
- USING RSD 1101.02 (SHEETS 1, 2, 3, 11, AND/OR 12 OF 15), MODIFY TEMPORARY PAVEMENT MARKINGS AT THE INTERSECTION OF SR 4892 (LANCASTER HWY) AND SR 4931 (CAROLINA PLACE PKWY) WITH PAINT AS SHOWN ON FINAL PAVEMENT MARKINGS PLANS OR AS DIRECTED BY THE ENGINEER.
- STEP 5: USING RSD 1101.02 (SHEETS 1, 2, 3, 11, AND/OR 12 OF 15), PLACE THE FINAL SURFACE LAYER, PAVEMENT MARKINGS, AND PAVEMENT MARKERS ON ALL ROADS (SEE ROADWAY PLANS AND FINAL PAVEMENT MARKING PLANS).

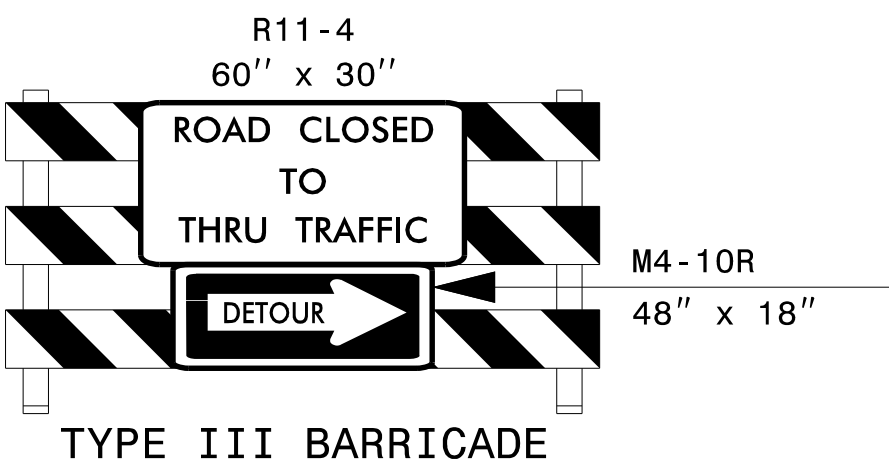


1

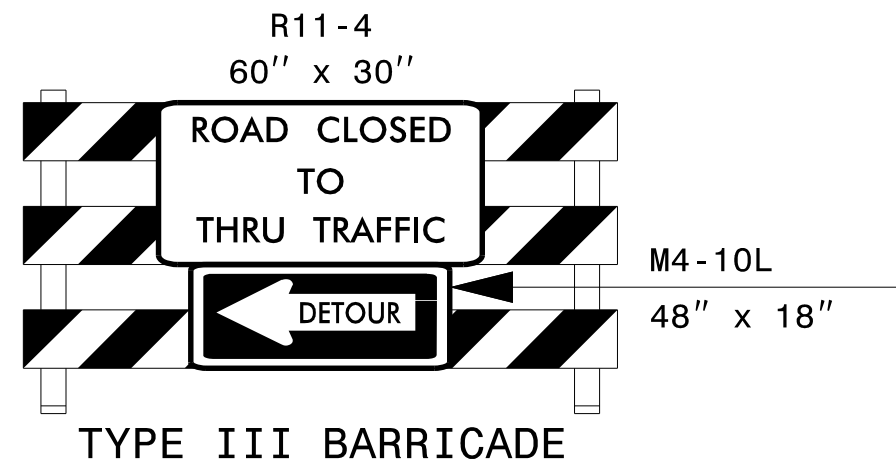


2

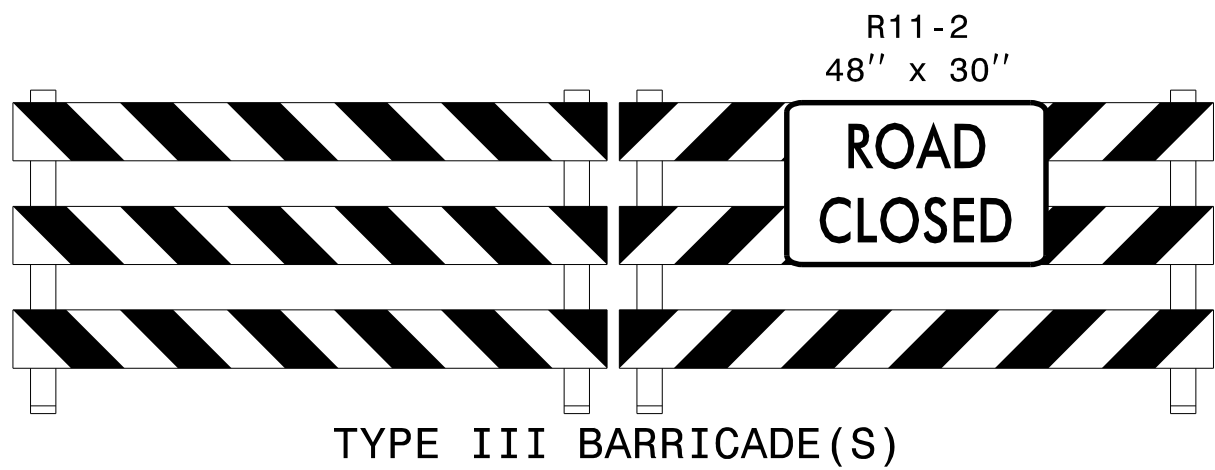


3

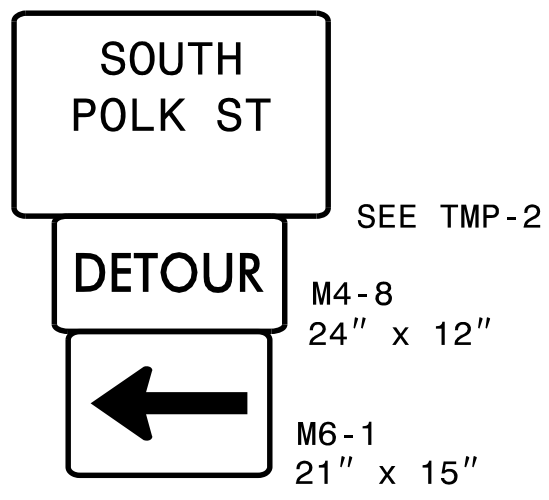


A

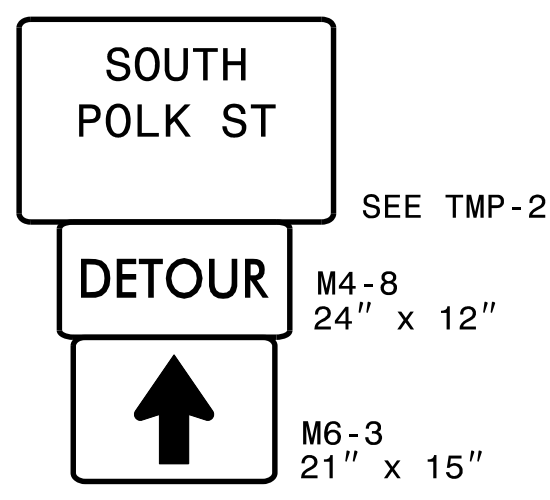

B

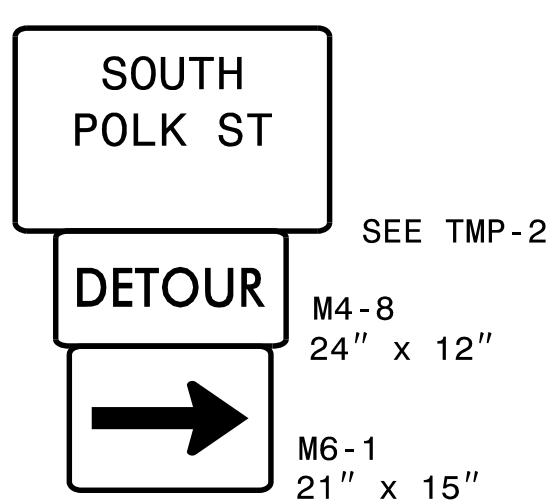

C

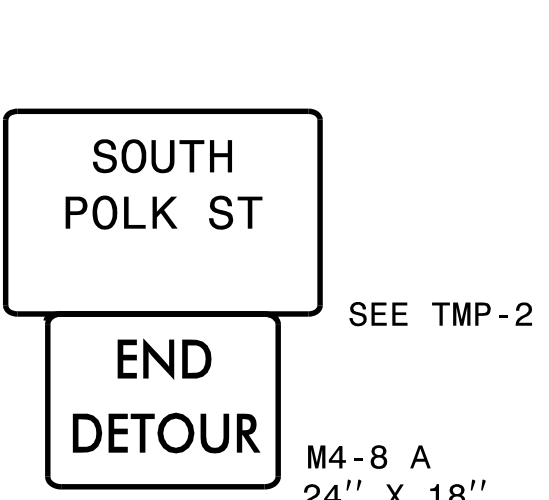

D

MESSAGE NO. 1	MESSAGE NO. 2
SOUTH POLK ST	DETOUR
CLOSED	AHEAD

CHANGEABLE MESSAGE SIGN

INSTALL 7 DAYS PRIOR TO FULL ROAD CLOSURE

REMOVE 7 DAYS AFTER FULL ROAD CLOSURE


E





F



G

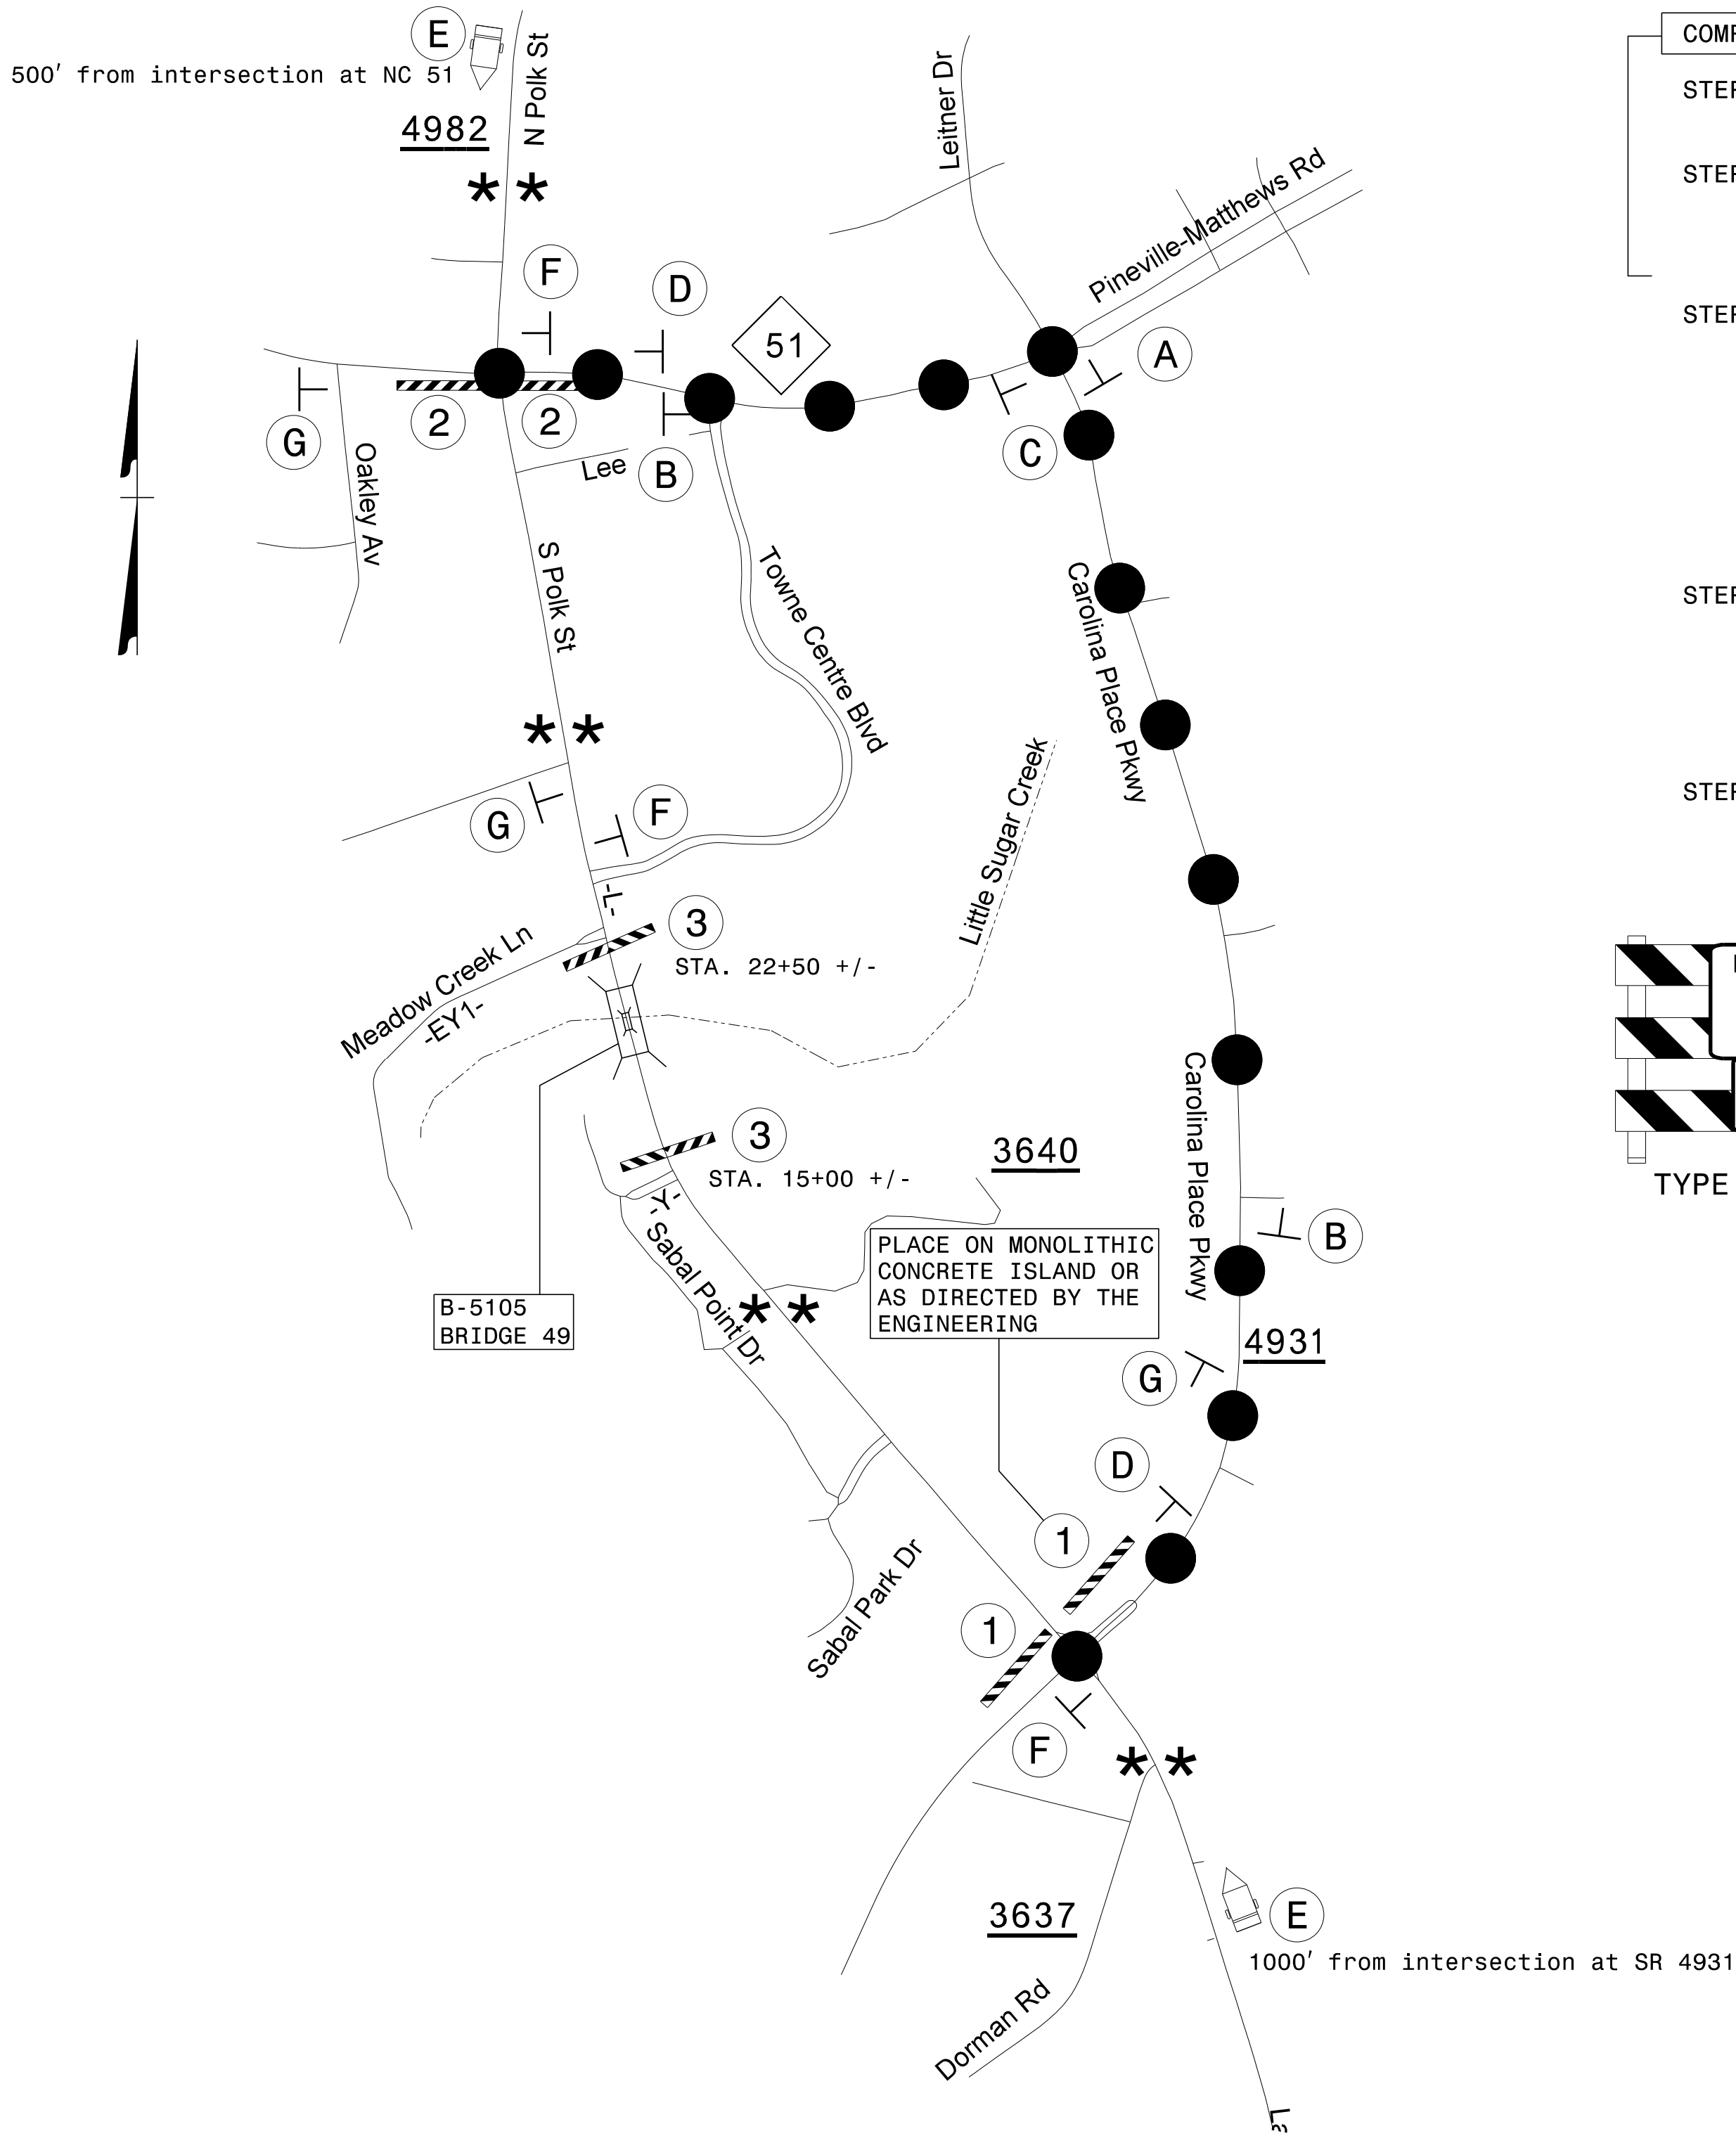

** SEE RSD 1101.03, SHEET 1 OF 9, FOR ADDITIONAL WORK ZONE SIGNS AND LOCATIONS.

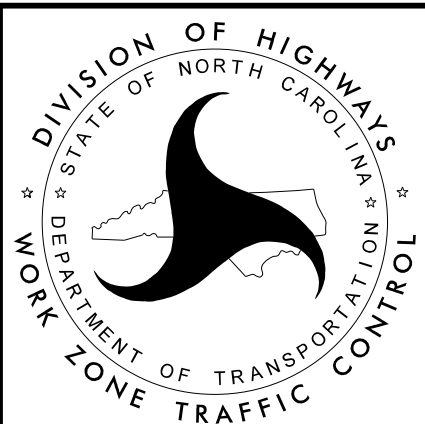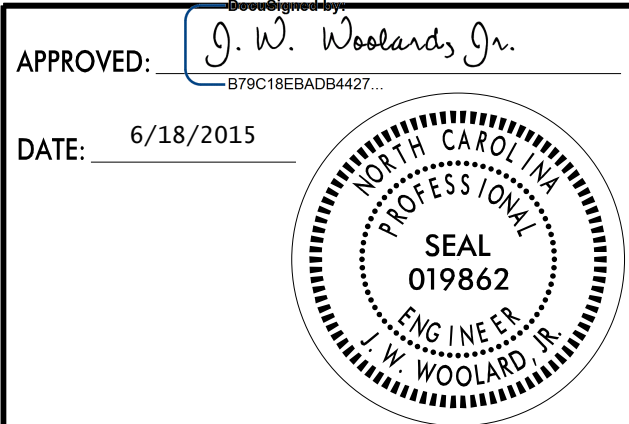

OFF-SITE DETOUR, BARRICADE PLACEMENT, AND PHASING
